

Inspection Report for flood Damage Work

Date :-

1- Name of PIUs :- R.W.D., (W) Division, Chapra - II

2- Name of Block/Road :- ~~Bara~~ Jalalpur
Chaukhra Gadhi Par se Barakageron hote huye
Savari jalalpur tak.

A. FOR ROAD

1- Damage Location/Chainage :- ~~0.010 km (10 meter)~~ / 1.950 km

2- Damage Length :- ~~0.010~~ 0.010 km (10 meter)

3- Nature of Damage :- Forcefully cut by villagers

4- Details of Restoration :-

i- Material being used in Restoration

:- Brick bats / Humet pipe
Local Sand,

ii- Equipment/Tools being used in Restoration Works

:-

iii- Procedure taken up in Restoration Works

:- Manabharal-

iv- Restored Length

:- 0.010 km (10 meter)

B. FOR BRIDGE

1- Damage Location/Chainage :-

2- Damage Length :-

3- Nature of Damage :-

4- Details of Restoration :-

i- Material being used in Restoration

:-

ii- Equipment/Tools being used in Restoration Works

:-

iii- Procedure taken up in Restoration Works

iv- Restored Length

:-

Signature of JE/AE/EE



19.11.21

E.E.

Signature
(Name of Inspector)

For JE/EE/EE
R.W.D., (W) Division,
Chapra-I




ग्रामीण कार्य विभाग

Rural Works Department, Govt of Bihar

2021-22

FLOOD DAMAGED REPORT

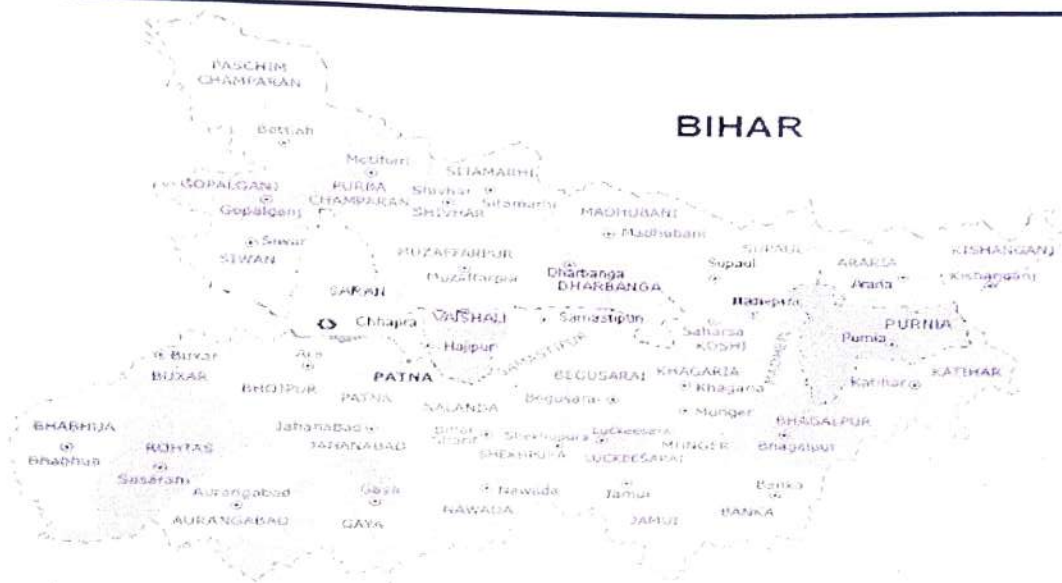

Urgent Motorable work of Road from Chaukhra Gadhi Par Se Barkagown Hote Huye Savari Jalalpur Tak

DISTRICT	:-	Chapra	
DIVISION	:-	Chapra 2	
BLOCK	:-	Jalalpur	
TOTAL LENGTH OF ROAD (Damage Length)	:-	0.010	KM
TOTAL COST OF SURFACE RENEUAL	:-	2.787	Lac
TOTAL COST OF PROJECT	:-	2.787	Lac

Date :-

1- Name of PIUs :- R.W.D., (W) Division, Chapra - II

2- Name of Block/Road :- Jalalpur / chauhara Gadhi Par se
Barkagawn note mye savori jalalpur taluk.

A. FOR ROAD

- 1- Damage Location/Chainage :- 1.950 km
- 2- Damage Length :- 0.010 km (10 meter)
- 3- Nature of Damage :- Forcely cut by villagers
- 4- Details of Restoration :-
 - i- Material being used in Restoration :- Brick beds / Hume Local Sand,
 - ii- Equipment/Tools being used in Restoration Works :-
 - iii- Procedure taken up in Restoration Works :- 1
 - iv- Restored Length :-

B. FOR BRIDGE

- 1- Damage Location/Chainage :-
- 2- Damage Length :-
- 3- Nature of Damage :-
- 4- Details of Restoration :-
 - i- Material being used in Restoration :-
 - ii- Equipment/Tools being used in Restoration Works :-
 - iii- Procedure taken up in Restoration Works :-
 - iv- Restored Length :-


Signature of JE/AE/EE


19.11.21
E.E.


Signature
Executive Engineer
(Name of Inspector)
Chapra-I

प्रतिवेदन

1. पथ का नाम :- चौखरा गदी पर से बड़का गाँव होते हुए सवरी जलालपुर तक
2. क्षतिग्रस्त भाग की लंबाई :- 0.010 कि०मी०
3. प्राक्कलित राशि :- 2.787 लाख

प्रस्तुत प्राक्कलन जलालपुर प्रखंड अंतर्गत चौखरा गदी पर से बड़का गाँव होते हुए सवरी जलालपुर तक पथ के Motorable कार्य हेतु तैयार किया गया है। जिसकी प्राक्कलित राशि 2.787 लाख रू० है। यह पथ पूर्व में मुख्यमंत्री ग्राम संपर्क योजना (विश्व बैंक संपोषित) से निर्मित है। यह पथ वर्तमान में द्वितीय वर्ष के अनुरक्षण अवधि में है, इस पथ की कुल लंबाई 5.729 कि०मी० है। इस पथ के दोनो ओर का जल-जमाव क्षेत्र (Catchment Area) काफी बड़ा चंवर के रूप में है। वर्ष 2021 के बाढ़/अतिवृष्टि के कारण पथ के Up Stream भाग में जल-जमाव होने के कारण चौखरा एवं आस-पास के गाँव में बाढ़ की स्थिति उत्पन्न हो गयी थी। जिसके कारण अज्ञात ग्रामीणों द्वारा रात्रि प्रहर में पथ को दस मीटर की लंबाई में एवं पुरी गहराई में JCB मशीन द्वारा काट दिया गया था। जिसकी सूचना कार्यपालक अभियंता, ग्रामीण कार्य विभाग, कार्य प्रमंडल, छपरा-2 के द्वारा V.C. के माध्यम से उच्चाधिकारियों को दी गयी एवं MIS पर कारण सहित पथ का फोटोग्राफ के साथ Upload भी कर दिया गया।


पथ के इस भाग में निर्माण के समय मूल प्राक्कलन में 1 x 1000 mm आकार का Hume Pipe पुलिया का प्रावधान था। लेकिन पथ के निचले भाग (Down Stream) के ग्रामीणों द्वारा पुलिया का निर्माण का विरोध किया गया एवं पुलिया का निर्माण नहीं हो सका।

उक्त पथ के क्षतिग्रस्त भाग का Motorable कार्य करने के लिए सर्वप्रथम 10 मीटर लंबाई, औसतन 6 मीटर चौड़ाई में एवं 0.600 मीटर मोटाई Brick Bats डाला गया। तत्पश्चात Brick Bats के उपर 2.5 मीटर लंबाई एवं 0.600 मीटर आकार के 2 x 2 = 4 नग NP3 Hume Pipe डालकर शेष भाग को (औसतन 1.80 मीटर मोटाई में) Brick Bats से भर दिया गया है। Brick Bats सतह पर 0.150 मीटर मोटाई में Local Sand का प्रावधान भी किया गया है। Motorable का यह कार्य तीव्र गति से बहते हुए पानी में किया गया है। वर्तमान में भी पथ में पानी का बहाव तेज गति से हो रहा है।

यह पथ पूर्ण रूप से Endeavour Infratech & Consultancy Pvt. Ltd. द्वारा किये गये एकरारनामा के अनुसार करवाया गया है एवं प्राक्कलन में प्रस्तावित दर विभाग द्वारा किये गये निविदा के आधार पर न्यूनतम दर पर स्वीकृत/अनुमोदित दर के अनुरूप तैयार किया गया है। इस पथ के प्राक्कलन की तकनीकी एवं प्रशासनिक स्वीकृति अपेक्षित है।


J.E.
R.W.D.
Chapra-2


A.E.
R.W.D.
Chapra-2


E.E.
R.W.D.
Works Division,
Chapra-2

FLOOD DAMAGED REPORT

GENERAL ABSTRACT OF COST

Block:-- Jalalpur District:- Chapra

Length of Road:-- 0.010 KM

Name of Road:-- Urgent Motorable work of Road from Chaukhra Gadhi Par Se Barkagown
Hote Huye Savari Jalalpur Tak

Sl. No.	Item of Work	Amount
A	TOTAL COST OF CONSTRUCTION :	2.787 Lacs
	TOTAL :	2.787 Lacs

M. S. S.
29/10/21

Junior Engineer

—

Asstt. Engineer

(Signature)
29.10.21

Executive Engineer

आधीन कार्य विभाग
कार्य प्रबंधक, जलपुर

SE
RWD

GENERAL ABSTRACT OF COST FOR Motorable of Road

NAME OF ROAD :

Urgent Motorable work of Road from Chaukhra Gadhi Par Se Barkagown Hote Huye Savari Jalalpur Tak

DISTRICT

Chapra

BLOCK

Jalalpur

DIVISION

Chapra 2

LENGTH OF ROAD (in Km)

0.010

Sl. No.	DESCRIPTION	Amount	1 % Labour Cess	12 % GST	1% Labour Cess & 12% GST AMOUNT (LAKHS)
PART-A	INITIAL RECTIFICATION INCLUDING SURFACE RENEWAL				
1	Brick Bats	2.193	0.022	0.263	2.478
2	Local Sand	0.016	0.000	0.002	0.018
3	HPC 600mm	0.258	0.003	0.031	0.291
	SUB TOTAL OF SURFACE RENEWAL	2.466	0.025	0.296	2.787
	TOTAL COST OF PROJECT IN LACS =	2.466	0.025	0.296	2.787

M. M. R. 29/10/24

JE
RWDAE
RWD29.10.24
RWD
RWD
RWD

Analysis of Rates (FORMAT F8)

Sl. No.	SDB Sl. No.	MORD Ref No.	DESCRIPTION	Unit	Quantity	Rate	Amount in Rs
26	OLD SOR		Providing brick bats including spreading laying hand packing and compacting with C.I. Hammer in layers not exceeding 75 mm thick including cost of light barriers, danger signals, chowkidar, taxes, royalty etc. all complete job as per specification and direction of E/I including carriage cost of bricks.				
	8.1.3.2 (iii)		Unit = cum Assuming- 2.832 Cum				
	a)		Labour (Unskilled)				
			i) Carrying, spreading, laying & Packing	nos	1.50	304.00	456.00
			ii) Compaction brick bats with C.I. Hammer.	nos	0.67	304.00	203.68
			iii) Brick Bat	Cum	2.83	1006.00	2848.99
			iv) Local Sand	Cum	0.63	141.75	89.59
			Over Heads @ 12 % on (a+b+c)				431.79
			C. Profit @ 10 % on (a+b+c+d)				403.00
	d)		Cost for 2.832 cum = a+b+c+d				4433.05
	e)		Rate Per cum = (a+b+c+d)/2.832	cum			1565.34
			<u>CARRIAGE</u>				
			Carriage for Brick (1 cum Bats = 300 nos Bricks)	nos	0.300	776.64	233.10
			Rate per cum with carriage				1798.45
			Total Cost	CUM			1,798.45
27	OLD SOR		Providing & Laying Local sand on brick bats with rolling etc completed				
			Unit = cum Assuming- 2.832 Cum				
	a)		Labour (Unskilled)				
			i) Carrying, spreading, laying & Packing	nos	1.50	386.00	579.00
			Over Heads @ 12 % on (a+b+c)				69.48
			C. Profit @ 10 % on (a+b+c+d)				64.85
	d)		Cost for 2.832 cum = a+b+c+d				713.33
	e)		Rate Per cum = (a+b+c+d)/2.832	cum			251.88
			<u>CARRIAGE</u>				
			Carriage for Sand	cum	0.040	185.01	7.40
			Rate per cum with carriage				259.28
			Total Cost	CUM			259.28

Mans
29/10/24
(J.E)

29.10.24
कार्यवाही परीक्षण
आनीय कार्य दिवस
आवेदन संख्या, 100/2024

Analysis of Rates (FORMAT F8)

Sl. No.	SDB Sl. No.	MORD Ref No.	DESCRIPTION	Unit	Quantity	Rate	Amount in Rs
3 (1)	9.30	1100	Providing and Laying Reinforced Cement Concrete Pipe NP3 as per design in Single Row Providing and laying reinforced cement concrete pipe NP3 for culverts on first class bedding of granular material in single row including fixing collar with cement mortar 1:2 but excluding excavation, protection works, backfilling, concrete and masonry works in head walls and parapets Clause 1106. A. 600 MM DIA Unit =m Taking output =7.5 m (3 pipes of 2.5 m length each) a) Material i) RCC pipe NP 4 pipe including collar at site b) Labour Mate Mason (1st class) Mazdoor (Unskilled) Overheads @ 20% d)Contractor's profit @ 10% on (a+b+c) Cost for 7.5m = (a+b+c) Rate per m =(a+b+c)/7.5				
				m	7.50	1905.50	14291.25
				day	0.04	321.00	12.84
				day	0.12	408.00	48.96
				day	0.96	304.00	291.84
							2928.98
							1757.39
							19331.25
							2577.50
			Total Cost	M			2577.50

Mms
29/10/24
(J.E)

29.10.24
जारीकर्ता अधिकारी
आसीर जॉई रिपोर
जॉई एंगेज, जयपुर

Sl. No.	SDB SL.NO	MORD Ref.No	Description	Unit	NOS	LENGTH	WIDTH	HEIGHT	QUANTITY	RATE	AMOUNT (In Rs.)
1			Brick Bats Providing brick bats including spreading laying hand packing and compacting with C.I. Hammer in layers not exceeding 75 mm thick including cost of light barriers, danger signals, chowkidar, taxes, royalty etc. all complete job as per specification and direction of E/I including carriage cost of bricks.								
				Cum	1	10.00	6.00	0.60	36.00		
				Cum	1	10.00	5 avg	1.80	90.00		
				Cum				=	126.00		
			Less for Hume Pipe		2	3.14	0.13 avg	5.0	4.08		
				Cum					121.92	1,798.45	2,19,263.00
2			Providing & Laying Local sand on brick bats with rolling etc completed								
				Cum	1	10.00	4.00	0.15	6.00		
				No.					6.00	259.28	1,556.00
3			HPC 600mm	Nos	2	2.00	2.50		10.00	2,577.50	25,775.00
A) SUB TOTAL OF CRUST =											2,46,594.00

M. K. Singh
29/10/24
(J.E)



29.10.24
कार्यवाही
समीक्षा
आवेदन, जल संयंत्र

Restoration/plot table of road form.

MBN03443

Schedule XLV-Form No. 134

Chaukhara Gadhi Por Se Borka Gawan Hote hae
Savri Jalalpur tak.

Contractor.

DIVISION

Sri. Himanshu Shekhar Prasad A.E.

SUB-DIVISION

Jalalpur.

Measurement Book

INDEX

PAGE

प्रमाणित किया जाता है कि इस माप पुस्तक में
मशीन मुद्रित 50 (पचास) पन्ने हैं जो श्री
हिमाशु शेरर-प्रसाद स्वयं क अभियंता तथा
का. वि. का. 03 पर प्रमाणित जलालपुर की
निर्गत किया जाता है

10/10/14

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, लखनऊ

10/10/21

INDEX

PAGE

Record Entry

Time to work— 1
 Situation of work—
 Agency by which work is executed—
 Date of measurement—
 No. and date of agreement.
 (These four lines should be repeated at the commencement of the measurements relating to each work.)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
N/W:- Urgent Motorable					
Work of Road from					
Chaukhara Gadhi Par se					
Barkaganh hata huye					
Savari Jalalpur tak.					
Name of Agency—					
Date of measurement— 12.10.2014					
Total length of Road— 5.729					
Damaged length of Road— 0.010 ^{km}					
(10m)					

Items of work.

- ① P/V & Laying brick bats
 Including spreading, hand
 packing & compacting
 below Hume pipe.
 $1 \times 10.00 \text{ m} \times 6.00 \text{ m} \times 0.60 \text{ m} = 36.00 \text{ m}^3$

mm
 12/10/14
 (J.E.)

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L	B	D	
N/W:- Urgent - measurable Work of Road from chauhmagadhi to se. Barbagawn hole huge Saveri Jalapputak Under PDR.					
N/Agency:-					
Total length of Road - 5.729 Km					
Length of Damage part - 0.010 Km (10 m)					
Date of measured - 17.12.21					

Abstract of Cost

- ① P/V & Laying brick bats including compacting, spreading, hand packing & compaction etc. completed.

36.00 m³ wide t.mol-1

85.92 m³, wide t.mol-2

121.92 m³

@ Rs 1798.45/m³ Rs 2,19,267.00

- ② P/V & Laying of R.C.C. Pipe of dia 600mm,

10.00 m, wide t.mol-2

@ Rs 2572.50/m Rs 25,725.00

Rs 2,45,042.00

Continuation

Columns	Details of actual measurement				Contents of area
	No.	L	B	D	
			81/2	1/2	219,262.00 2,45,042.00

3) Plv 2 measuring Pucca sand on brick batts with filling etc. completed.

6.00 m³ vide TMB-3

① Rs 259.28/m³ - Rs 1556.00

Total Rs 270,823.00

Rs 2,46,598.00

Add 12% GST + Rs 29,592.00

Add 1% LCW + Rs 2,466.00

Total Rs 2,78,656.00

(Rupees) Two Lakh, Seventy eight thousand, six hundred & fifty six only.

CBP

OKM

17/12/21
(J.E)

20/12/21
BR

