

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग कार्य प्रमंडल फुलपरास।

पत्रांक 308

दिनांक ~~28/20/2022~~
28/02/2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, फुलपरास।

सेवामें,

अपर मुख्य कार्यपालक पदाधिकारी- सह- सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:- शीर्ष NEW MAINTENANCE POLICY-2018 (MR-3054) में आवंटन उपलब्ध कराने के संबंध में।


महाशय,

उपरोक्त विषय के संबंध में कहना है शीर्ष NEW MAINTENANCE POLICY - 2018 (MR-3054) योजना अन्तर्गत पथ में संलग्न विवरणी के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय ताकि संवेदक का भुगतान किया जा सके।

अनु०:-

1. अधियाचना प्रमाण पत्र 1 पृष्ठ में।
2. उपयोगिता प्रमाण पत्र एक प्रति में।

विश्वासभाजन



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, फुलपरास।

Subhas
28/2/2022

FORM GFR 19-A

(See Government of India's Decision (I) below Rule-150)

Form of Utilisation Certificate Upto the month of 28 February-2022

New Maintenance policy - 2018

PIU – Executive Engineer, R.W.D (W) Division, Phulparas

SL. No	Name of Scheme	Sanction No. & Date with Amount (In Rs. lacs)	Amount Received (In Rs. lacs)	Particulars
1	Construction of Rural roads under New maintenance policy-2018	Authorization letter No-10 dt- 21/02/2022. Rs. 1395.92752.	1395.92752	Certified that out of 1395.92752 Lakh received during the years up to 2021-22 in favour of Ex. Engineer, RWD (W) Division Phulparas, Madhubani, Bihar, a sum of Rs.1381.69131 Lakh has been utilized for the purpose of New maintenance policy- 2018 as given in the margin for which the balance of Rs 14.23621 Lakh remaining unutilized at the end of the period under.

2. Certified that I have satisfied my self that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised :-

- I. Works have been supervised by Executive Engineer/Superintending Engineer.
- II. Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- III. Construction materials have been tested.
- IV. Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/Executive Engineer.
- V. All other codal formalities have been observed.


3. Physical Progress achieved :-

- I. Construction of Road Works.
- II. Construction of CD Works.



Executive Engineer
R.W.D (W) Division
Phulparas
28/2/22

Format of Requisition under Head New Maintenance policy - 2018 (MR- 3054) for the month of 28 February - 2022.
 Name of Division :- RWD (W) Division phulparas.

SI No.	Package No.	Name of road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (In Lakh)	up-to-date expenditure as per MIS (In Lakh)	Requisition against work done (In Lakh)	Remarks
					Length (In km)	Amount of (In lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Year Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/MA/PHU/20/000	PARSA NH-57 - LAKSENA	31909802069	7387 / 04.10.2019	3.380	120.474	104.340	30.33030	12MBD/2021-22/ 24.08.2021	23.08.2022	12.12.2021	2332.6	25	5	74.00495	74.00495	0.00000	Work Completed
2	RM/MA/PHU/20/000	MURLICHOWK - MATHOUR	31909802059	7387 / 04.10.2019	1.960	71.965	62.405	18.67560	12MBD/2021-22/ 24.08.2021	23.08.2022	19.02.2022	4312.63	25	5	0.00000	0.00000	43.54923	Work Completed
Total						192.439	166.745	49.006							74.00495	74.00495	43.54923	


 30/02/22
 Executive Engineer
 R.W.D(W)Div. Phulparas

Name of Customer: Sanjay kumar Jha , Machine no: 19210 , Road: Murli Chowk to Mahthaur , Date: 18-02-22 , Section No: 12 , Equation: $Y=0.940X + 239.3$

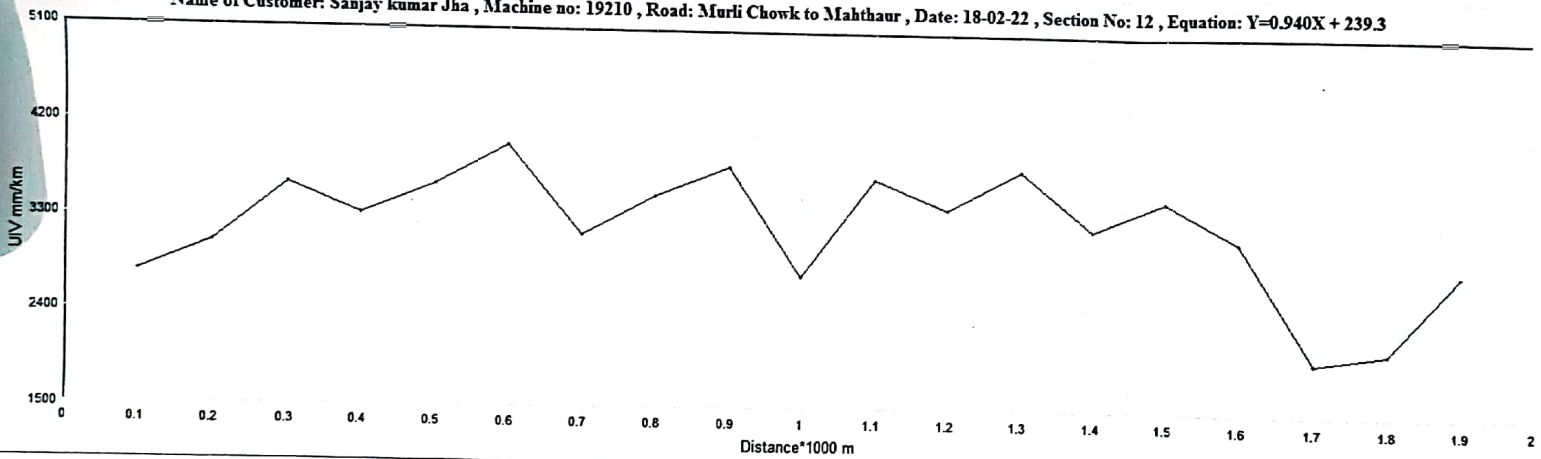

[Signature]
28/2/22
Executive Engineer
Rural Works Department
Works Division Phulparas
Subd. 28/2/22

Name of work : Muri Chowk to Mahthaur		
Name of customer : Sanjay kumar Jha		
(R) Rural Road		
Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
18/02/22	11:17:27	1	100	100	27.0 cm	11.5 Km/Hr	2700.0 mm/Km	2777	3.76	Good	26.3934336	N	86.5018396	E	Normal
18/02/22	11:17:49	1	100	200	30.0 cm	16.5 Km/Hr	3000.0 mm/Km	3059	4.1	Good	26.3943605	N	86.5020533	E	Normal
18/02/22	11:18:08	1	100	300	36.0 cm	19.0 Km/Hr	3600.0 mm/Km	3623	4.77	Good	26.3951998	N	86.5023127	E	Normal
18/02/22	11:18:23	1	100	400	33.0 cm	23.1 Km/Hr	3300.0 mm/Km	3341	4.44	Good	26.3961267	N	86.5025721	E	Normal
18/02/22	11:18:39	1	100	500	36.0 cm	22.7 Km/Hr	3600.0 mm/Km	3623	4.77	Good	26.3970518	N	86.5027857	E	Normal
18/02/22	11:18:54	1	100	600	40.0 cm	23.4 Km/Hr	4000.0 mm/Km	3999	5.21	Good	26.3979425	N	86.5029612	E	Normal
18/02/22	11:19:09	1	100	700	31.0 cm	25.4 Km/Hr	3100.0 mm/Km	3153	4.21	Good	26.3987684	N	86.5032206	E	Normal
18/02/22	11:19:23	1	100	800	35.0 cm	23.9 Km/Hr	3500.0 mm/Km	3529	4.66	Good	26.3997202	N	86.5035486	E	Normal
18/02/22	11:19:37	1	100	900	38.0 cm	26.4 Km/Hr	3800.0 mm/Km	3811	4.99	Good	26.4006433	N	86.5038080	E	Normal
18/02/22	11:19:51	1	100	1000	27.0 cm	25.7 Km/Hr	2700.0 mm/Km	2777	3.76	Good	26.4015436	N	86.5040369	E	Normal
18/02/22	11:20:06	1	100	1100	37.0 cm	24.3 Km/Hr	3700.0 mm/Km	3717	4.88	Good	26.4023848	N	86.5042505	E	Normal
18/02/22	11:20:22	1	100	1200	34.0 cm	22.9 Km/Hr	3400.0 mm/Km	3435	4.55	Good	26.4028044	N	86.5043497	E	Normal
18/02/22	11:20:37	1	100	1300	38.0 cm	23.4 Km/Hr	3800.0 mm/Km	3811	4.99	Good	26.4039927	N	86.5046549	E	Normal
18/02/22	11:20:53	1	100	1400	32.0 cm	23.1 Km/Hr	3200.0 mm/Km	3247	4.32	Good	26.4048262	N	86.5048838	E	Normal
18/02/22	11:21:27	1	100	1500	35.0 cm	10.9 Km/Hr	3500.0 mm/Km	3529	4.66	Good	26.4059458	N	86.5051966	E	Breaker
18/02/22	11:21:52	1	100	1600	31.0 cm	14.2 Km/Hr	3100.0 mm/Km	3153	4.21	Good	26.4068251	N	86.5054407	E	Normal
18/02/22	11:22:20	1	100	1700	19.0 cm	16.8 Km/Hr	1900.0 mm/Km	2025	2.84	Good	26.4077196	N	86.5054407	E	Normal
18/02/22	11:23:46	1	100	1800	20.0 cm	15.5 Km/Hr	2000.0 mm/Km	2119	2.95	Good	26.4071627	N	86.5046549	E	Normal
18/02/22	11:24:16	1	100	1900	28.0 cm	12.8 Km/Hr	2800.0 mm/Km	2871	3.87	Good	26.4071627	N	86.5046549	E	Normal

Corrected UI -
Average - 3242.052632
Cont - 19
Sum - 61599

IRI
Average - 4.312631579
Cont - 19
Sum - 81.94

Executive Engineer
Rural Works Department
Works Division Phulparas
18/2/22

ii) M/R-3054 ମିଆଁନ ଗ୍ରାମପଞ୍ଚାୟତ - ମୁନ୍ଦା ଚକ୍ରବର୍ତ୍ତୀ-ମାତୁରୀ

Schedule XLV-Form No. 134

ସମ୍ମୁଖିକା **DIVISION**

ସମ୍ମୁଖିକା **SUB-DIVISION**

M.B.No-277.
2021-22

MEASUREMENT BOOK

ମିଆଁନ ଗ୍ରାମପଞ୍ଚାୟତ - ମୁନ୍ଦା ଚକ୍ରବର୍ତ୍ତୀ-ମାତୁରୀ

પ્રમાણિત ભિન્ન બાજુ જે ભાગ દર્શાવે તે માપવામાં આવે
 પાંત-જે-મણીના દ્વારા માપેલું છે-100(પગલાં)
 યુદ્ધ જે બી મહાભારત અભિયાનમાં, ગામીયુદ્ધ
 બાળક વિભાગ, બાળક ગ્રામીય યુવાઓ, પ્રમુખ
 બી મણી છે.

૩૪૩૭૨
 ૨૪/૮/૨૧
 Executive Engineer
 Rural Works Department
 Works Division Phulparas
 24.8.21

Sch. XLV - Form No. 134

ગામીયુદ્ધ DIVISION

ગામીયુદ્ધ SUB-DIVISION

Measurement Book

No. 277.
 2021-22

Name of Officer Executive Engineer
Rural Works Department
Works Division Phulparas
 24.8.21

Date of first entry _____

Date of last entry _____

(ii) M/R-3054 મીનાર ગ્રામીય-મુન્દીચનૌક-મોતમૌર

Name of Work—
 Situation of Work—
 Agency by which work is executed—
 Date of Measurement—
 No. and date of agreement

(These four lines should be repeated at the commencement of the measurement relating to each work)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of Work:- Const ⁿ of Road & CD work from Murlidhar to Mathaur under MP 3054.					
Agency:- Sanjay Kumar Jha.					
Agreement No 12 MBD/2021-22					
Date of commencement:- 24.08.2021					
Date of completion :- 23.08.2022 As per agreement.					
Date of Measurement:-					

Date:- 01.02.2022					
(1) clearing & Grubbing					
Road land (By Manual Means) ----- E/I					
$2 \times 1960 \text{ M} \times 1.00 \text{ M (av)} = 3920 \text{ M}^2$					
OR 0.3920 Hect					
(2) Const ⁿ of Granular					
Sub-base by Providing					
Grading Materials - E					
CH. 0.00 M to 1.00 KM					
$1 \text{ NM} \times 3.00 \times 1.80 \times 0.100 = 0.54 \text{ M}^3$					
$4 \text{ NM} \times 4.00 \times 1.50 \times 0.100 = 2.40$					
$1 \text{ NM} \times 3.00 \times 1.70 \times 0.100 = 0.51$					
$1 \text{ NM} \times 4.00 \times 1.50 \times 0.100 = 0.60$					
4.05 M ³					

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Abstract of cost:-					
(1) Clearing & Grubbing of Road land including uprooting ----- E1					
0.3920 Hect		Vide TMB			
			P-1		
@ 5113 = 76/4 Hect					20044.90
(2) Consol of granular sub base by Providing grading & Making - E1					
71.77 M ³		Vide TMB			
			P. 4		2,40,184.00
@ 3346.52/M ³ - R.					2,07,987.00
(3) Providing stone Molar WBM road spreading & compacting --- E1					
110.6325 M ³		Vide TMB			
			P-5		
@ 4221.34/M ³ R					4,67,017.00
(4) Providing & laying - Prime coat - - - E1					
1475.10 M ²		Vide TMB			
			P-7		
@ 44.69/M ² - R.					65,922.00
(5) Providing & applying Thick coat with bitumen emulsion - - - E1					
1475.10 M ²		Vide TMB			
			P. 7		
7423.50 M ²			P-8		
8898.60 M ²					
@ 15.20/M ² - R.					1,35,259.00

Rs 8,76,229.00
9,28,426.00

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
				3F-R 9	28,426.00
(56) Providing & laying M/s					
7					
2cm Surfacing					
1475.10 m ²				Vide TMB	
				P-7	
				@ 232.00/m ² -R	342223.00
(57) Providing & laying					
8					
25mm thick S.D.B.C					
- - -					
185.5875 m ³				Vide TMB	
				P-8	
				@ 1183.52/m ³ -R	2196339.00
(58) Providing & fixing M/s					
9+10					
Grade 4/10 metre stone					
				Vide TMB / P 10	
(11) 4M Stone					
3 Nos				@ 240.9295/each-R	7230.00
(11) 200M Stone					
3 Nos				@ 629.37/each-R	5035.00
(9) Painting 1m, dash Arrow					
11					
on Road in 2 covt					
19.60 m ²				Vide TMB	
				P-9	
				@ 77.72/m ² - R	1523.00
(10) Providing & fixing					
(12+13+14)					
at retroreflective sign					
(i) 600mm squl/4krd Triangles					
6 Nos				@ 3776.06/Mos R	226562.00
(11) 600 mm Circular					
2 Nos				@ 3935.37/each-R	7871.00

R 3479106.00

Continuation

35,11303.00

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
			BF & 35		11,303.00
(11) 60mm x 45mm Rectangular					
4 No @ 2800 x 96 / No. - R					15,204.00
(11) Providing & fixing					
15 M/S grade Boundary					
Pillars					
24 Nos			Vide TMB		
			P-9		
@ 8 522.72 / No. - R					12,547.00
(12) Planting of trees by					
18 the road side.					
196 Nos			Vide TMB		
			P-9		
@ 8 819.72 / each. R					160,704.00
(13) Providing & laying hot					
18 applied thermoplastic					
compound.					
392 M ²			Vide TMB		
			R-9		
@ 8 735.44 / M ² R.					2,88,292.00
(14) Providing & fixing of					
19 Typical MR 305 info					
metry Signboard - E.					
02 Nos			Vide TMB		
			P-11		
@ 8 736.425 / each R					18,729.00
(15) Constn of earthen shoulder					
2 with approved Material					
1176 M ³			Vide TMB		
			P-9		
@ 1 176.86 / M ³ - R					207,987.00

R. 41,82,509.00

Continuation

42,14,766.00

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
					BF-R 42,14,766.00
(16) Brick Masonry in cm	20				
(123) in Propel					
14.90M ²		Vide TMB			
	@ 8	5213.721	M ³ -R		75,078.00
(17) Plastering with cm (1:4)	21				
97.84M ²		Vide TMB			
	@ 9	178.20/M ²	- R.		17,791.00
(18) Painting 2 coat on	22				
new surface.					
99.84M ²		Vide TMB			
	@ 2	97.13/M ²	- R.		9702.00
					R. 43,17,337.00
					R. 42,85,140.00
					5,18,080.00
Add G.S.T 12 % - R.					5,14,217.00
					43,173.00
Add L.C - 1 % - R.					42,851.00
					2,83,65.00
Add S. Fee - R.					49,06,955.00
					R. 48,70,573.00
					5,52,032.00
Less 11.25% as per agreement					R. 5,47,939.00
					R. 43,22,634.00
					R. 43,54,923.00
Ldny 19.2.022 JE					

Continuation
