

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल छपरा 2

पत्रांक

469अनु०

छपरा/दिनांक 08/03/2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, छपरा-2

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
बिहार ग्रामीण पथ विकास अभिकरण (ब्राडो),
बिहार, पटना।

विषय:-

नई अनुरक्षण नीति 2018 (Head - 3054) योजना मद में आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि नई अनुरक्षण नीति 2018 (Head - 3054) योजना अंतर्गत 02 (दो) पथों में राशि का अधियाचना विहित प्रपत्र में तैयार कर माप पुस्त की छायाप्रति एवं Bump Indecator का Reading संलग्न कर आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अतः अनुरोध है कि पत्र के साथ संलग्न अधियाचना प्रपत्र में अंकित राशि उपलब्ध कराने की कृपा की जाय ताकि संवेदक के विपत्र का भुगतान किया जा सकें।

अनु०:- यथोक्त।

विश्वासमाजन

(Signature)
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, छपरा 2

AS
8/3/22


Requisition Format for Scheme Head :- MR (3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Name of Division :- Rural Works Department, Works Division, Chapra-2

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)	Length (In km)	Amount (In Lakh)	Agreement Amount (In Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/19-20 Chapra-2/10	Hanumanganj to Telindih	31306302037	Lt. No. 3388 Dated 02.08.19	1.062	35.76380	23.30764	9.92450	86/MBD/2020-21	22.09.21	08.01.22	1242.545	25.00	5%	0.00	0.00	19.01221	MB No. 3399, Page No. 01 to 08
2	MR-N/19-20 Chapra-2/14	T05 to Ithari	31306302098	Lt. No. 3388 Dated 02.08.19	5.000	176.22790	114.16861	49.65183	29/MBD/2020-21	11.08.21	05.01.22	1276.580	25.00	5%	0.00	0.00	100.63519	MB No. 3397, Page No. 01 to 13


 Executive Engineer
 Rural Works Department,
 Works Division, Chapra-2
 AEP
 8/13/22

File : F:\New folder\cpr\Bachcha singh\T05 - ITHARI\05011033.Xls, Section No. :97, Eqn : $Y = 0 * X^2 + 0.816 * X - 262$
 Name of Customer : Bachcha Singh, Name of Work/ Road : T05 - ITHARI, Lab Job number :97

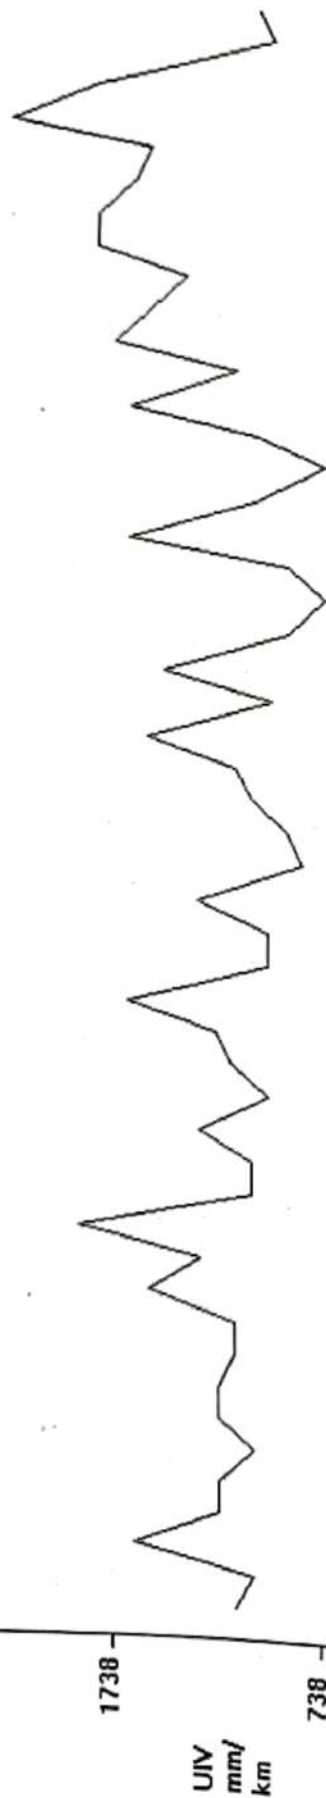

Distance * 1000 m

6/10/2022
 JE

[Signature]
 Executive Engineer
 R.W.D. Works Div.
 Chapra-2

Lab Job number :97

Date :05-01-2022

Name of Customer :Bachcha Singh

Name of Work/ Road :T05 - ITHARI

Sr.no Location of Corrected U.I Road category
test(in km) value(mm/km)

2	0.1	1146 G
3	0.2	1064 G
4	0.3	1636 G
5	0.4	1228 G
6	0.5	1228 G
7	0.6	1064 G
8	0.7	1228 G
9	0.8	1228 G
10	0.9	1146 G
11	1	1146 G
12	1.1	1554 G
13	1.2	1309 G
14	1.3	1880 G
15	1.4	1064 G
16	1.5	1064 G
17	1.6	1309 G
18	1.7	983 G
19	1.8	1146 G
20	1.9	1228 G
21	2	1636 G
22	2.1	983 G
23	2.2	983 G
24	2.3	1309 G
25	2.4	820 G
26	2.5	901 G
27	2.6	1064 G
28	2.7	1146 G
29	2.8	1554 G
30	2.9	983 G
31	3	1472 G
32	3.1	901 G
33	3.2	738 G
34	3.3	901 G
35	3.4	1636 G
36	3.5	1064 G
37	3.6	738 G
38	3.7	1064 G
39	3.8	1636 G
40	3.9	1146 G
41	4	1717 G
42	4.1	1554 G
43	4.2	1391 G
44	4.3	1799 G

Gyini
05/01/2022
JE

RPSm
5-1-2022
AE

10/1/22

Executive Engineer
R.W.D. Works Div.
Chapra-2

Scanned with CamScanner

45	4.4
46	4.5
47	4.6
48	4.7
49	4.8
50	4.9
51	5

1799 G
1636 G
1554 G
2207 G
1799 G
983 G
1064 G

Gsingh
05/01/2022
JE

RPSm
5-1-2022
AE


10.1.22
Executive Engineer
R W.D. Works Div.
Chapra-2

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI CATEGORY ROAD	Latitude	ongitude	Event
5/1/22	11:8:2	97	0.1	110	10.1	1100	1146 G	25.99742	84.44202	Normal
5/1/22	11:8:37	97	0.1	100	20.2	1000	1064 G	25.99832	84.44224	Normal
5/1/22	11:9:14	97	0.1	170	20.2	1700	1636 G	25.99913	84.44242	Normal
5/1/22	11:9:14	97	0.1	120	30.3	1200	1228 G	26.23	84.44261	Normal
5/1/22	11:9:49	97	0.1	120	30.3	1200	1228 G	26.753	84.44281	Normal
5/1/22	11:10:0	97	0.1	100	10.1	1000	1064 G	26.1548	84.44306	Normal
5/1/22	11:10:10	97	0.1	120	30.3	1200	1228 G	26.2282	84.44364	Normal
5/1/22	11:10:44	97	0.1	120	30.3	1200	1228 G	26.2878	84.44431	Normal
5/1/22	11:11:0	97	0.1	110	30.3	1100	1146 G	26.348	84.44487	Normal
5/1/22	11:11:35	97	0.1	110	10.1	1100	1146 G	26.4077	84.44527	Normal
5/1/22	11:11:45	97	0.1	160	20.2	1600	1554 G	26.458	84.44561	Normal
5/1/22	11:12:0	97	0.1	130	30.3	1300	1309 G	26.5035	84.44579	Normal
5/1/22	11:12:10	97	0.1	200	20.2	2000	1880 G	26.5447	84.44591	Normal
5/1/22	11:12:28	97	0.1	100	20.2	1000	1064 G	26.6225	84.44611	Normal
5/1/22	11:12:46	97	0.1	100	20.2	1000	1064 G	26.6677	84.44621	Normal
5/1/22	11:13:0	97	0.1	130	20.2	1300	1309 G	26.7162	84.44648	Normal
5/1/22	11:13:11	97	0.1	90	30.3	900	983 G	26.788	84.44673	Normal
5/1/22	11:13:27	97	0.1	110	20.2	1100	1146 G	26.892	84.44717	Normal
5/1/22	11:13:47	97	0.1	120	10.1	1200	1228 G	26.9528	84.44746	Normal
5/1/22	11:13:59	97	0.1	170	20.2	1700	1636 G	26.10362	84.4479	Normal
5/1/22	11:14:0	97	0.1	90	40.4	900	983 G	26.11202	84.4482	Normal
5/1/22	11:14:12	97	0.1	90	40.4	900	983 G	26.1222	84.44855	Curve
5/1/22	11:14:25	97	0.1	130	40.4	1300	1309 G	26.12672	84.44828	Normal
5/1/22	11:14:42	97	0.1	70	30.3	700	820 G	26.1307	84.44838	Normal
5/1/22	11:14:55	97	0.1	80	30.3	800	901 G	26.1361	84.44857	Normal
5/1/22	11:15:0	97	0.1	100	30.3	1000	1064 G	26.14102	84.44869	Normal
5/1/22	11:15:6	97	0.1	110	30.3	1100	1146 G	26.1499	84.44867	Speed Breaker
5/1/22	11:15:16	97	0.1	160	30.3	1600	1554 G	26.15357	84.4486	Normal
5/1/22	11:15:41	97	0.1	90	30.3	900	983 G	26.15943	84.4487	Normal
5/1/22	11:16:0	97	0.1	150	40.4	1500	1472 G	26.16677	84.44889	Normal
5/1/22	11:16:16	97	0.1	80	30.3	800	901 G	26.17425	84.44916	Normal
5/1/22	11:16:36	97	0.1	60	10.1	600	738 G	26.18293	84.44939	Speed Breaker
5/1/22	11:16:52	97	0.1	80	20.2	800	901 G	26.1903	84.44955	Normal
5/1/22	11:17:0	97	0.1	170	20.2	1700	1636 G	26.20005	84.44995	Normal
5/1/22	11:17:10	97	0.1	100	30.3	1000	1064 G	26.20838	84.45022	Normal

$$Y = 0 * X^2 + 0.816 * X + 249$$

$$X = 1905$$

$$Y = 1765$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

R.P.Gm.
5-1-2022
AE

6/21/2022
05/10/2022
JE

Executive Engineer
R.W.D. Works Div.
Chanra.2

5/1/22	11:17:18	97	0.1	60	30.3	600	738 G	26.21598	84.45054	Normal
5/1/22	11:17:27	97	0.1	100	20.2	1000	1064 G	26.22357	84.45081	Normal
5/1/22	11:17:37	97	0.1	170	20.2	1700	1636 G	26.23853	84.45076	Normal
5/1/22	11:17:45	97	0.1	110	10.1	1100	1146 G	26.2426	84.45094	Speed Breaker
5/1/22	11:18:2	97	0.1	180	10.1	1800	1717 G	26.25135	84.45125	Normal
5/1/22	11:18:21	97	0.1	160	10.1	1600	1554 G	26.25995	84.4516	Normal
5/1/22	11:18:32	97	0.1	140	20.2	1400	1391 G	26.26607	84.45165	Normal
5/1/22	11:18:37	97	0.1	190	20.2	1900	1799 G	26.2687	84.45162	Normal
5/1/22	11:18:47	97	0.1	190	20.2	1900	1799 G	26.27655	84.45158	Normal
5/1/22	11:19:0	97	0.1	170	10.1	1700	1636 G	26.28787	84.45215	Speed Breaker
5/1/22	11:19:13	97	0.1	160	10.1	1600	1554 G	26.28887	84.45219	Normal
5/1/22	11:19:33	97	0.1	240	10.1	2400	2207 G	26.29438	84.45237	Normal
5/1/22	11:19:53	97	0.1	190	20.2	1900	1799 G	26.30098	84.45251	Normal
5/1/22	11:20:0	97	0.1	90	20.2	900	983 G	26.31173	84.45283	Normal
5/1/22	11:20:10	97	0.1	100	20.2	1000	1064 G	26.2968	84.44537	Normal

6/15/22
05/01/2022
JE

Executive Engineer
R W.D. Works Div.
Chapra-2

MR. N/19.20 Chapra. 2/14 MR. N/10-3397

Schedule XLV-Form No. 134

105 से सरेरी पप

पेकमाना सं. 29/5BD/20-21

DIVISION

सपक-सि अरु सि

सि अरु सि सि सि सि सि

SUB-DIVISION

पेकमाना

MEASUREMENT BOOK

MR. N/10-3397

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
8.10 x 2.25 x 0.175 =					3.189
26.70 x 3.10 x 0.175 =					14.484
4.12 x 2.50 x 0.175 =					1.803
22.75 x 3.25 x 0.175 =					12.939
7.38 x 3.55 x 0.175 =					4.585
32.39 x 3.15 x 0.175 =					17.85
4.26 x 3.55 x 0.175 =					2.647
18.28 x 2.95 x 0.175 =					9.437
14.13 x 2.50 x 0.175 =					6.182
32.45 x 3.20 x 0.175 =					18.172
40.30 x 2.38 x 0.175 =					16.784
12.39 x 3.45 x 0.175 =					7.480
4.52 x 1.50 x 0.175 =					1.187
4.26 x 3.05 x 0.175 =					2.274
8.29 x 3.05 x 0.175 =					4.425
6.15 x 2.0 x 0.175 =					2.153
4.26 x 3.25 x 0.175 =					2.423
12.39 x 3.15 x 0.175 =					6.830
9.41 x 3.25 x 0.175 =					5.352
16.28 x 2.25 x 0.175 =					6.410
11.67 x 3.45 x 0.175 =					7.046
3.74 x 2.5 x 0.175 =					1.636
16.51 x 3.55 x 0.175 =					10.257
35.40 x 3.10 x 0.175 =					19.204
				Total	236
					263.243m ³
					Limit to 259.214m ³

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
2. Construction of Water Bound Macadam					
with stone screening Gr - II					
(WB4 - Gr II)					
2.4 x 2.75 x 0.075					7.012
8.4 x 2.6 x 0.075					1.638
8.49 x 3.35 x 0.075					2.133
13.61 x 3.35 x 0.075					2.420
7.11 x 2.60 x 0.075					1.386
10.54 x 3.35 x 0.075					2.648
10.35 x 2.35 x 0.075					1.824
6.37 x 2.60 x 0.075					1.242
9.63 x 3.65 x 0.075					2.636
6.51 x 3.65 x 0.075					1.782
16.38 x 2.60 x 0.075					3.194
14.64 x 3.55 x 0.075					3.898
6.77 x 1.60 x 0.075					0.812
6.51 x 3.15 x 0.075					1.538
10.54 x 3.15 x 0.075					2.490
8.40 x 2.10 x 0.075					1.323
6.51 x 3.35 x 0.075					1.636
14.64 x 3.25 x 0.075					3.569
11.66 x 3.35 x 0.075					2.930
15.53 x 2.35 x 0.075					3.266
13.92 x 3.55 x 0.075					3.706
5.99 x 2.60 x 0.075					1.168
18.76 x 3.65 x 0.075					5.126
18.76 x 2.60 x 0.075					3.658

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
8.49 x	3.35	x	0.075	=	2.133
19.98 x	2.35	x	0.075	=	3.521
16.12 x	3.45	x	0.075	=	4.171
11.25 x	3.10	x	0.075	=	2.616
14.95 x	3.35	x	0.075	=	3.756
14.64 x	2.10	x	0.075	=	2.306
10.25 x	2.45	x	0.075	=	1.883
19.72 x	2.35	x	0.075	=	3.476
5.25 x	2.6	x	0.075	=	1.024
9.63 x	3.65	x	0.075	=	2.636
10.25 x	3.65	x	0.075	=	2.806
9.87 x	2.60	x	0.075	=	1.925
5.25 x	3.55	x	0.075	=	1.398
19.98 x	1.60	x	0.075	=	2.398 0.825
3.49 x	3.15	x	0.075	=	0.825 2.295
9.87 x	3.10	x	0.075	=	2.295
40.50 x	2.40	x	0.075	=	7.290
14.95 x	3.10	x	0.075	=	3.476
12.09 x	3.35	x	0.075	=	3.038
9.87 x	3.10	x	0.075	=	2.295
39.80 x	3.28	x	0.075	=	9.790
20.03 x	2.10	x	0.075	=	3.155
14.43 x	2.45	x	0.075	=	2.652
10.35 x	2.35	x	0.075	=	1.824
			P.T.O		

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
18.06	X	2.93	X	0.075	= 1.771 m ³
11.97	X	2.93	X	0.075	= 2.630 m ³
6.27	X	2.25	X	0.075	= 1.058 m ³
10.72	X	2.93	X	0.075	= 2.355 m ³
10.47	X	3.38	X	0.075	= 2.654 m ³
17.18	X	2.07	X	0.075	= 3.853 m ³
23.12	X	2.97	X	0.075	= 5.150 m ³
26.28	X	2.74	X	0.075	= 5.401 m ³
9.39	X	2.97	X	0.075	= 2.092 m ³
36.22	X	2.29	X	0.075	= 6.221 m ³
				Total	170.757 m ³
				Limit to	165.356 m ³
					164.84 m ³

3.	WBM grading III				
	Providing, laying, spreading and compacting stone aggregates.				
	do				
	m	m	m	m	m ³
34	X	2.75	X	0.075	= 7.012
9.75	X	2.50	X	0.075	= 1.828
9.84	X	3.25	X	0.075	= 2.399
14.96	X	3.25	X	0.075	= 3.647
8.46	X	2.50	X	0.075	= 1.586
11.89	X	3.25	X	0.075	= 2.898
11.70	X	3.75	X	0.075	= 3.291
21.38	X	2.0	X	0.075	= 3.207
15.78	X	2.35	X	0.075	= 2.781

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
11.70 x	2.25	x	0.075	=	1.974
7.72 x	2.50	x	0.075	=	1.448
10.98 x	3.55	x	0.075	=	2.923
7.86 x	3.55	x	0.075	=	2.093
17.73 x	2.50	x	0.075	=	3.324
15.99 x	3.45	x	0.075	=	4.137
8.12 x	1.50	x	0.075	=	0.914
7.86 x	3.05	x	0.075	=	1.798
11.89 x	2.0	x	0.075	=	2.720
9.75 x	3.25	x	0.075	=	1.463
7.86 x	3.15	x	0.075	=	1.916
15.99 x	3.15	x	0.075	=	3.778
13.01 x	3.25	x	0.075	=	3.171
19.88 x	2.25	x	0.075	=	3.355
15.27 x	3.45	x	0.075	=	3.951
7.34 x	2.50	x	0.075	=	1.376
20.11 x	3.55	x	0.075	=	5.354
20.11 x	2.50	x	0.075	=	3.771
9.84 x	3.25	x	0.075	=	2.319
16.30 x	3.75	x	0.075	=	4.584
15.99 x	2.0	x	0.075	=	2.399
11.60 x	2.35	x	0.075	=	2.045
21.07 x	2.25	x	0.075	=	3.556
6.60 x	2.50	x	0.075	=	1.238
10.98 x	3.55	x	0.075	=	2.923
11.60 x	3.55	x	0.075	=	3.089

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
11.22 x 2.50	x	0.075	=	2.104	
6.60 x 3.45	x	0.075	=	1.708	
21.33 x 1.50	x	0.075	=	2.400	
4.84 x 3.05	x	0.075	=	1.107	
11.22 x 3.00	x	0.075	=	2.525	
16.30 x 3.00	x	0.075	=	3.668	
13.44 x 3.75	x	0.075	=	3.780	
40.50 x 3.75	x	0.075	=	7.290	
11.22 x 3.00	x	0.075	=	2.525	
21.33 x 2.25	x	0.075	=	3.591	
17.47 x 3.25	x	0.075	=	4.389	
12.60 x 3.00	x	0.075	=	2.835	
11.60 x 2.50	x	0.075	=	2.175	
11.84 x 3.65	x	0.075	=	3.241	
10.60 x 3.25	x	0.075	=	2.584	
8.60 x 2.50	x	0.075	=	1.613	
7.60 x 3.25	x	0.075	=	1.853	
8.60 x 3.75	x	0.075	=	2.419	
7.60 x 2.00	x	0.075	=	1.140	
11.60 x 2.35	x	0.075	=	2.045	
10.09 x 2.25	x	0.075	=	1.703	
12.60 x 2.50	x	0.075	=	2.363	
39.80 x 3.25	x	0.075	=	9.790	
15.27 x 3.55	x	0.075	=	4.066	
7.34 x 2.00	x	0.075	=	1.101	
11.60 x 2.35	x	0.075	=	2.045	

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
8.60 x 2.25 x 0.075 =					1.451
9.84 x 2.50 x 0.075 =					1.845
16.30 x 3.55 x 0.075 =					4.340
21.42 x 3.01 x 0.075 =					4.836
32.61 x 2.69 x 0.075 =					6.579
36.68 x 2.92 x 0.075 =					8.033
25.62 x 2.92 x 0.075 =					5.611
28.78 x 2.69 x 0.075 =					5.806
38.72 x 2.24 x 0.075 =					6.505
8.33 x 2.24 x 0.075 =					1.399
24.84 x 2.92 x 0.075 =					5.440
				Total	221.278m ³

	Limit to	215.912m ³
	=	215.912m ³

(4) clearing & grubbing
road land - do - -

$$2 \times 200 \times 25 \times 1.0 = 10000$$

$$= 10000 \text{ m}^2 = 1 \text{ hectare}$$

$$\therefore \text{cont} = 1.0 \text{ hectare}$$

(5) const. of subgrade and
earthen shoulder
- - do - -

$$2 \times 200 \times 25 \times 0.70 \times 0.30 = 2100 \text{ m}^2$$

(6) Prime coat
Providing and applying
primer coat with
bitumen emulsion SS-1
- - do - -

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Area used for prime coat is same as area used for WBM gr-III					
P-(8) item-(3)					
$\sqrt{215.912}$					
SPM 0.075					
					$= 2878.83$
					$= 2878.83m^2$
(7) Tack coat providing & applying tack coat with bitumen emulsion RS-1					
do					
Area used for					
tack coat is same as area used for					
prime coat + $2 \times 22 \times 3.75$					
$\frac{1}{2} \sqrt{2878.83 + 165}$					
					$= 3043.83m^2$
(8) Patch work over WBM using MSS--do--					
Area used for MSS is same as area used for					
tack coat P-(9)					
item-(7)					
					$= 3043.83m^2$
(9) Tack coat providing and applying tack coat with bitumen emulsion					

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
RS-1	—	do	—	—	
R.P.C.	80X	25X	3.75	=	7500m ²
	80X	25X	3.80	=	7600m ²
	20X	3.0	=		60m ²
	20X	3.3	=		66m ²
	20X	3.50	=		70m ²
R.P.C.	2X20X	3.60	=		144m ²
	4X25X	3.40	=		340m ²
	25X	3.25	=		81.25m ²
	31X25X	3.752			2906.25m ²
			Total		18767.50m ²

Limit to 18750m²

(10) Providing and laying
semidense bituminous
concrete — do —

Area used for

SPBC is same as

area used for tack

coat P- (10) item- (9)

$$R.P.C. = 18750m^2$$

∴ ent for

R.P.C.

SPBC

$$= 18750 \times 0.025 = 468.75m^3$$

$$= 468.75m^3$$

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(11) Planting of trees by the road side do					
				ent =	20 No.
(12) Providing & fixing of typical masonry informative sign board with logo - do					
				ent =	1 No.
6/11/2022 05/01/2022 AE				RPSM: 5-1-2022 AE	
					18.170 m
Abstract of cost					
(1) const. of granular subbase - do					
				ent =	259.214 m ³ P- (2)
item - (1) @ Rs 2327.69/m ³					Rs 603370:
(2) const. of WBM gr-II					
do					
				ent =	164.84 m ³ P- (3) (5)
item - (2) @ Rs 4341.97					Rs 715730 =
(3) const. of WBM gr-III					
do					
				ent =	215.912 m ³ P- (8)
item - (3) @ Rs 3880.07					Rs 8377542

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
④ clearing & grubbing road land - do - -					
2x200x25x					
amt = 1.0 hect P- (8)					
itm - (4) @ Rs 49496.70					
				2 Rs	494972
⑤ const. of subgrade & earthen shoulder - do - -					
amt = 2100 m ² P- (8)					
itm - (5) @ Rs 176.96/m ²					
				2 Rs	3716162
⑥ Prime coat - do - -					
amt = 2878.83 m ²					
P- (8) itm - (6)					
@ Rs 41.58/m ²				2 Rs	1197022
⑦ Tack coat - do - -					
amt = 3043.83 m ² P- (9)					
itm - (7) @ Rs 14.10/m ²				2 Rs	429182
⑧ Patch work over WBM using mss - do - -					
amt = 3043.83 m ² P- (9)					
itm - (8) @ Rs 230.07/m ²				2 Rs	7002932

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(9) Tack coat					
do					
cont =	18	750	m ²	P- (10)	
item - (9) @ Rs			12.26/m ²		
			= Rs	229875 =	
(10) Providing and laying					
SDBC - do					
cont =	468	75	m ²		
P- (10) item - (10)					
@ Rs	1113	91	m ³	= Rs	5209645 =
(11) Planting of trees					
by the road side					
do					
cont =	20	No.	P- (11)		
item - (11) @ Rs			800.30 =		
			Rs	16006 =	
(12) Providing & fixing of					
typical masonry					
informational signboard					
with 10 go - do					
cont =	1	No.	P- (11)		
item - (12) @ Rs			9364 =	Rs	9364 =
			Total Rs	8905770 =	
Add GST -	12.1	(+)	Rs	1068692 =	
Add labour	1	(+)	Rs	89057 =	
			Total Rs	10063519 =	

Gsingh
05/10/2022
JE

RPSm
5-1-2022
Continuation
AE

10.1.22
AM
