

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, आरा ।

पत्रांक 32331नु०

आरा, दिनांक 04/03/2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, आरा ।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
ग्रामीण कार्य विभाग
बिहार, पटना ।

विषय:- बिहार ग्रामीण पथ अनुरक्षण नीति-2018 के तहत पथों की
अधियाचना के संबंध में ।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि बिहार ग्रामीण पथ अनुरक्षण
नीति-2018 के तहत पथों के भुगतान हेतु संलग्न विवरणी के अनुसार रू०-258.15001
लाख रू० की आवश्यकता है ।

अतः अनुरोध है कि यथाशीघ्र उक्त राशि को आवंटित करने की कृपा
की जाय, जिससे संवेदक का भुगतान किया जा सकें ।

अनु० यथोक्त ।

04/03/2022

विश्वासभाजन

04/03/22
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, आरा ।

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in km)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/19-20/Ara/05	Strengthening Manikpur to Long Babu ke Mathiya Road	10401603139	1833/24.06.2019	3.14	111.895	65.323	27.62121	10/MR 3054/MBD/2019-20	21-Aug-20	25.02.2022	3144	25mm	5.0	0.00	0.00	65.00160	Completed
2	MR-N/19-20/Ara/05	Strengthening of Nalbandpur to Charar Road	10401603145	1833/24.06.2019	1.35	91.263	51.749	22.30895	10/MR 3054/MBD/2019-20	21-Aug-20	25.02.2022	3198	25mm	5.0	0.00	0.00	51.35655	Completed
3	MR-N/19-20/Ara/06	Strengthening to Manikpur Road	10401601027	1833/24.06.2019	2.15	75.179	42.878	18.16524	11/MR 3054/MBD/2019-20	21-Aug-20	25.02.2022	3146	25mm	5.0	0.00	0.00	42.55606	Completed
4	MR-N/19-20/Ara/05	Babura - Sahalpur	NEA22000797	1833/24.06.2019	2.2	78.776	45.404	19.68121	10/MR 3054/MBD/2019-20	21-Aug-20	25.02.2022	3055	25mm	5.0	0.00	0.00	44.91468	Completed
5	MR-N/19-20/Ara/06	Kolhanpur Bus Stand - Mahatampur Charar tola Path	NEA22000824	1833/24.06.2019	2.5	47.499	27.57	11.9767	11/MR 3054/MBD/2019-20	21-Aug-20	25.02.2022	3357	25mm	5.0	0.00	0.00	27.24254	Completed
6	MR-N/19-20/Ara/06	Semra - Bandhu Chhapra	NEA22000835	1833/24.06.2019	1.3	46.786	27.406	11.43158	11/MR 3054/MBD/2019-20	21-Aug-20	23.02.2022	3152	25mm	5.0	0.00	0.00	27.07858	Completed
Total																	258.15001	

1. Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.
2. Up-to date Physical Progress has been uploaded in MIS.

24/08/2022

Executive Engineer
Rural Works Department
Ara Division, Ara

24/08/22

FORM GFR 19-A
(See Government of India's Decision (1) below Rule-150)
Form of utilisation Certification up to month of Feb, 2022
MR Maintenance Policy- 2018
R.W.D. Works Division-Ara (Bhojpur)

Sl. No.	Name of Scheme	Sanction No & Date with Amount (In Rs. Lacs)	Amount Received (In Rs. Lacs)	Particulars
1.	Construction of Rural Road under MR Maint. Policy- 2018	Letter No-10 we Date- 21.02.2022	268932530.00	Certified that out of Rs. 268932530.00 Lacs of grant in aid received during the Year 2021-22 in favour of Executive Engineer, RWD Bihar R.W.D. Ara. A sum of Rs. 259895417.00 Lacs has been utilized for the purpose of MR Maint. Policy- 2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 9037113.00 Lacs remaining unutilized at the end of the period under.
		Total	268932530.00	

2. Certified that I have satisfied myself that the conditions on which the grants-in aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised:-

- I. Works have been supervised by Executive Engineer/ Superintending Engineer.
- II. Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- III. Construction materials have been tested.
- IV. Measurements have been recorded in the MBS and test check conducted by the Assistant Engineer/Executive Engineer.
- V. All other codal formalities have been observed.

3. Physical progress achieved:

- i. Construction of Road Works.
- ii. Construction of CD Works.

[Signature]
D.A.O-I
Rural Works Department
Works Div-Ara

[Signature]
04/03/22
Executive Engineer
Rural Works Department
Works Div. Ara
04/03/22

Name of Customer: SANJAY KUMAR SINGH

Name of Work/Road: BABURA TO SABALPUR ROAD

Lab Job number:

Date: 23-02-2022


Section No. 74

Test Date: <u>23-02-2022</u>	Road Name: <u>BEURA TO SABALPUR ROAD</u>
Machine No: <u>384</u>	Road Type: <u>(R) RURAL ROAD</u>
Start S No: <u></u>	Side: <u></u>
Start E No: <u></u>	Interval <u></u>
Weather: <u></u>	UIV Range: <u>1577</u> To <u>5000</u> <u>1000</u> mm/km
Start Location: <u>BABURA</u>	Dist Range: <u>0</u> To <u>2.3</u> <u>0.1</u> * 1000 m
End Location: <u>SABALPUR</u>	Equation: <u>$Y = 0 * X^2 + 0.984 * X + 510.70$</u>

Print Generate Report and Graph

Redraw Graph

Map View

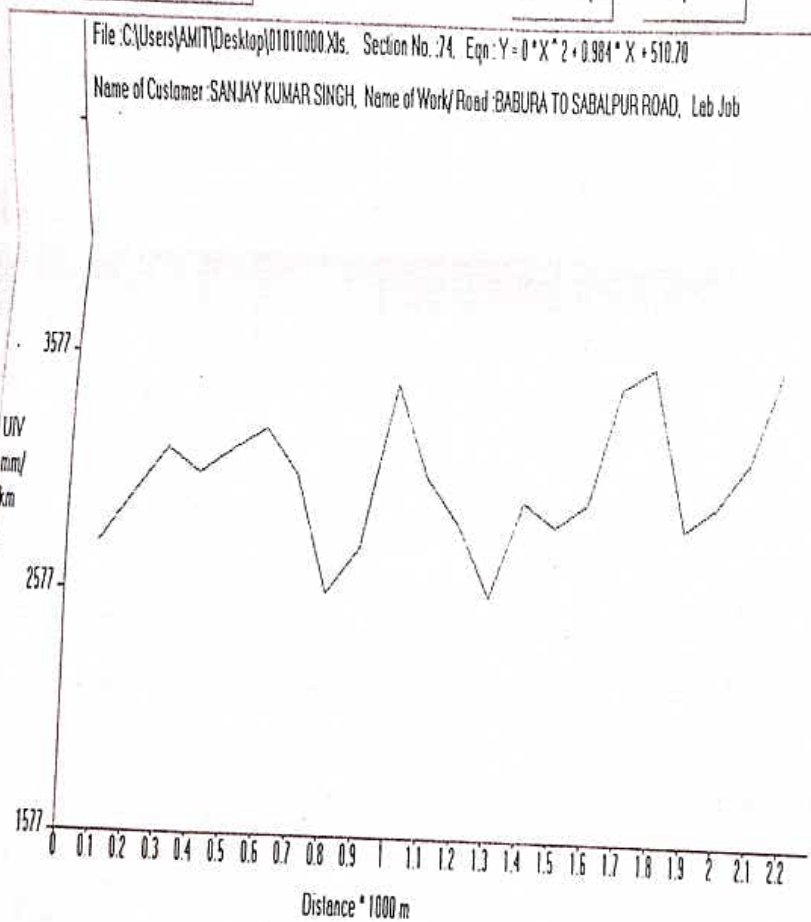

Chandra
25/02/2022
JE

Chandra
25/02/22
A.E

R2
25/02/22

ROAD NAME BABURA TO SABALPUR ROAD CONTRACTOR NAME - SANJAY KUMAR SINGH									
Date	Time	Section	Length	Bumps	Speed	OR	IRI, I CATEGORY	Latitude, longitude	Event
No.		in km	in mm	Rate	mm/km	mm/km	ROAD		
23-02-22	16:18:7	74	0.1	230	0	2300	2773 G	25.4854	84.45252 Normal
23-02-22	16:18:7	74	0.1	250	30.3	2500	2970 G	25.48627	84.45268 Normal
23-02-22	16:18:7	74	0.1	270	31.2	2700	3167 G	25.48718	84.45337 Curve
23-02-22	16:18:42	74	0.1	260	32.5	2600	3069 G	25.48799	84.45572 Normal
23-02-22	16:19:0	74	0.1	270	30.3	2700	3167 G	25.48886	84.45875 Speed Bre (R) RURAL ROAD
23-02-22	16:20:0	74	0.1	280	30.3	2800	3265 G	25.48948	84.45337 Curve
23-02-22	16:21:3	74	0.1	260	31.2	2600	3069 G	25.4901	84.45982 Normal
23-02-22	16:21:39	74	0.1	210	32.5	2100	2577 G	25.49092	84.4505 Normal
23-02-22	16:22:14	74	0.1	230	30.3	2300	2773 G	25.49148	84.4547 Curve
23-02-22	16:23:0	74	0.1	300	31.2	3000	3462 G	25.49236	84.45318 Speed Breake
23-02-22	16:23:24	74	0.1	260	30.3	2600	3069 G	25.49323	84.4537 Normal
23-02-22	16:24:0	74	0.1	240	30.3	2400	2872 G	25.49325	84.4508 Speed Breake
23-02-22	16:24:17	74	0.1	210	30.3	2100	2577 G	25.45708	84.17087 Normal
23-02-22	16:24:35	74	0.1	250	31.2	2500	2970 G	25.4568	84.16127 Curve
23-02-22	16:24:52	74	0.1	240	32.5	2400	2872 G	25.45599	84.15757 Normal
23-02-22	16:25:09	74	0.1	250	30.3	2500	2970 G	25.45528	84.15168 Normal
23-02-22	16:25:26	74	0.1	300	31.2	3000	3462 G	25.45446	84.14797 Normal
23-02-22	16:25:43	74	0.1	310	32.5	3100	3561 G	25.45361	84.14545 Speed Breake
23-02-22	16:25:59	74	0.1	240	30.3	2400	2872 G	25.45315	84.13753 Speed Breake
23-02-22	16:26:16	74	0.1	250	30.3	2500	2970 G	25.45324	84.1338 Normal
23-02-22	16:26:43	74	0.1	270	30.3	2700	3167 G	25.45321	84.14275 Curve
23-02-22	16:27:00	74	0.1	310	31.2	3100	3561 G	25.45396	84.1468 Normal
LENTH - 2200 MTR.					AVERAGE - 3055				


 25/02/2022
 JE

GUNWAL
 45.12.16


 25/02/22

$$Y = 0.0 * X^2 + 0.984 * X + 510.70$$

X = 5300
 Y = 5725

Good Average Poor
 <4000 4001-5000 >5001

प्रमाण पत्र

शीर्ष:- 3054एम0आर0 (बिहार ग्रामीण पथ अनुरक्षण 2018)

योजना:- Babura - Sabalpur

1. मापी पुस्त पर इस आशय का प्रमाण पत्र दर्ज है कि कार्य गुणवत्ता पूर्ण कराया गया है।
2. कराये गये कार्यों के सभी अवयवों के अवयववार 100 प्रतिशत कार्य का दर्ज मापी का सत्यापन कनीय अभियंता, 50 प्रतिशत मापी का सत्यापन सहायक अभियंता एवं 10 प्रतिशत मापी का सत्यापन कार्यपालक अभियंता द्वारा किया गया है।

(Signature)
25/02/2022

कनीय अभियंता
कार्य प्रशाखा, बड़हरा

(Signature)
25/02/22

सहायक अभियंता
कार्य अवर प्रमंडल, बड़हरा

(Signature)
25/02/22

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, आरा।
