

**कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, गोगरी।**

E-mail ID.- eerwdgogri@gmail.com

पत्रांक 1917(अ) प्रमंडल गोगरी, दिनांक 17-10-2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, गोगरी।

सेवा में,

नोडल पदाधिकारी,
3054(MR)
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:- शीर्ष New Maintenance Policy-2018 under MR-3054 योजना अन्तर्गत राशि का अधियाचना समर्पित करने के संबंध में।

महाशय,

उपर्युक्त विषयक संबंध में कहना है कि शीर्ष New Maintenance Policy-2018 under MR-3054 योजना अंतर्गत कुल मो 110.12024 लाख (एक करोड़ दस लाख बारह हजार चौबीस) रुपये मन्त्र उपलब्ध कराने की कृपा की जाए। इस पत्र के साथ विहित प्रपत्र में अधियाचना राशि समर्पित की जा रही है।

सूचनार्थ सादर समर्पित।

अनु०- यथोक्त

विश्वासभाजन

Atul
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, गोगरी।

FORM GFR 19-A
(See Government of India's Decision (I) below Rule-150)
Form of Utilization Certificate up to the 17 Oct. 2022
RWD, Works Divisio, Gogri

Sr. No	Name of Scheme	Sanction No. & Date with Amount (in lacs Rs.)	Amount Received (in lacs Rs.)	Particulars
1	Construction of Rural roads Maintenance Policy-2018 under MR-3054	Previous Allotment	Rs. 1512.55447 Lakh	Certified that out of Rs. 2361.33128 lacs of grants-in-aid sanctioned during the years 2019-20 in favors of E-in-C, RWD Bihar, Patna a sum of Rs. 2361.33128 lacs has been utilized for the purpose of MR(3054) Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 0.00 Lacs remaining unutilized at the end of the period under report.
		01. Letter No-26, Date -15.04.21	Rs. 126.73585 Lakh	
		02. Letter No-30, Date -21.05.21	Rs. 211.26975 Lakh	
		03. Letter No-60, Date -09.01.21	Rs. 83.54087 Lakh	
		04. Letter No-02, Date -03.01.22	Rs. 185.7605 Lakh	
		05. Letter No-05, Date -25.01.22	Rs. 66.66837 Lakh	
		-----	Rs.-11.03089 Lakh	
		06. Letter No-20, Date -14.03.22	Rs. 103.32400 Lakh	
		07. Letter No-22, Date -16.03.22	Rs. 17.36849 Lakh	
		08. Letter No-35, Date -13.10.22	Rs. 43.07.809 Lakh	
		Total :-	Rs.- 2361.33128 Lakh	

18. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised :-

- Works have been supervised by Executive Engineer/ Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/ Executive Engineer.
- All other codal formalities have been observed.

19. Physical Progress achieved :-

- Construction of Road Works.
- Construction of CD works


D.A.O.
RWD Works, Division, Gogri


Executive Engineer
RWD Works, Division, Gogri

Requisition Formate for Scheme Head - MIR(305-4) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Gogri

Name of Works Division : - Gogri																			
SI No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval(AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Alloted Amount (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks	
					Length (In km)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)											
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	
1	RMNHGO G-21/0001	Satish Nagar to Korchhaka	20904603003	Lt No.- 181 Dated 13.01.2022	2.214	148.03000	110.12024	20.34909	05 MBD /2022-23 19.05.2022	18.02.2023	On- Going	2198.545	25.00	5.06	0.00	0.00	110.12024	Work Complete	

1. Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.

2. Up-to-date Physical Progress has been uploaded in MIS.

प्रमाणित
13/10/22
प्र. 0 ले 0 पदा 0
प्र. 0 का 0 बि 0
काय प्र. 0. गंगने

Executive Engineer
RWD, Works Division,
Gogri

Road Name- Satish nagar to Korchhaka, Contractor-Pritam Sagar Infratech Pvt. Ltd

Project ID-20904603003

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEG ORY	Latitude	Longitude	Event
27/9/22	13:0:8	14	0.1	210	0	2100	2095 G	ROAD	25.40269	86.23418	Normal
27/9/22	13:0:41	14	0.1	170	40.4	1700	1739 G		25.40217	86.82366	Normal
27/9/22	13:0:41	14	0.1	190	30.3	1900	1917 G		25.40113	86.82378	Curve
27/9/22	13:0:41	14	0.1	180	40.4	1800	1828 G		25.40037	86.82364	Culvert
27/9/22	13:0:41	14	0.1	250	40.4	2500	2450 G		25.39956	86.82365	Culvert
27/9/22	13:1:16	14	0.1	200	30.3	2000	2006 G		25.39883	86.82384	Culvert
27/9/22	13:1:16	14	0.1	170	20.2	1700	1739 G		25.39855	86.82539	Culvert
27/9/22	13:1:16	14	0.1	200	30.3	2000	2006 G		25.39845	86.82637	Culvert
27/9/22	13:1:51	14	0.1	190	40.4	1900	1917 G		25.39806	86.82733	Normal
27/9/22	13:1:51	14	0.1	220	40.4	2200	2184 G		25.39503	86.82793	Normal
27/9/22	13:1:51	14	0.1	190	40.4	1900	1917 G		25.39686	86.82884	Normal
27/9/22	13:1:51	14	0.1	190	50.5	1900	1917 G		25.3963	86.82928	Normal
27/9/22	13:2:26	14	0.1	150	40.4	1500	1561 G		25.39616	8.829482	Normal
27/9/22	13:2:26	14	0.1	190	40.4	1900	1917 G		25.39495	86.83037	Normal
27/9/22	13:2:26	14	0.1	160	40.4	1600	1650 G		25.39412	86.83094	Normal
27/9/22	13:2:26	14	0.1	130	40.4	1300	1383 G		25.393	86.8315	Normal
27/9/22	13:3:2	14	0.1	170	30.3	1700	1739 G		25.39248	86.83199	Culvert
27/9/22	13:3:2	14	0.1	380	20.2	3800	3606 G	Speed Breaker	25.39248	86.83199	Speed Breaker
27/9/22	13:3:2	14	0.1	390	20.2	3900	3695 G		25.39185	86.83297	Culvert
27/9/22	13:3:37	14	0.1	310	20.2	3100	2984 G		25.39067	86.83655	Speed Breaker
27/9/22	13:3:37	14	0.1	310	20.2	3100	2984 G		25.39067	86.83466	Speed Breaker
27/9/22	13:4:12	14	0.052	170	20.2	3269	3134 G		25.3887	86.8344	Normal
							Total IRI	48368			
							Average IRI	2198.545			

Y = 0 * X^2 + 0.889 * X + 228.2
X = 3269
Y = 3134

(R) RURAL ROAD

Good Average Poor
4000 4001-5000 >5001

DRS
27/9/2022

JE

AE


27/9/2022

27/9/2022

Executive Engineer
Rural Works Department
Works Division, Gogari

Name of Customer :	Pritam Sagar Infratech Pvt. Ltd
Name of Work/ Road :	Salish nagar to Korchhaka
Lab Job number :	20904603003
Date :	27-09-2022
Section No. :	14

Test Date :	27-09-2022	Road Name :	Salish nagar to Korchhaka
Machine No :	403	Road Type :	(R) RURAL ROAD
Start S No :	0.00 KM	Side :	
Start E No :	2.214 KM	Interval	
Weather :	Normal	UIV Range :	383 To 5000 mm/km
Start Location :		Dist Range :	0 To 2.3 1000 m
End Location :		Equation :	$Y = 0 \cdot X^2 + 0.889 \cdot X + 228.2$

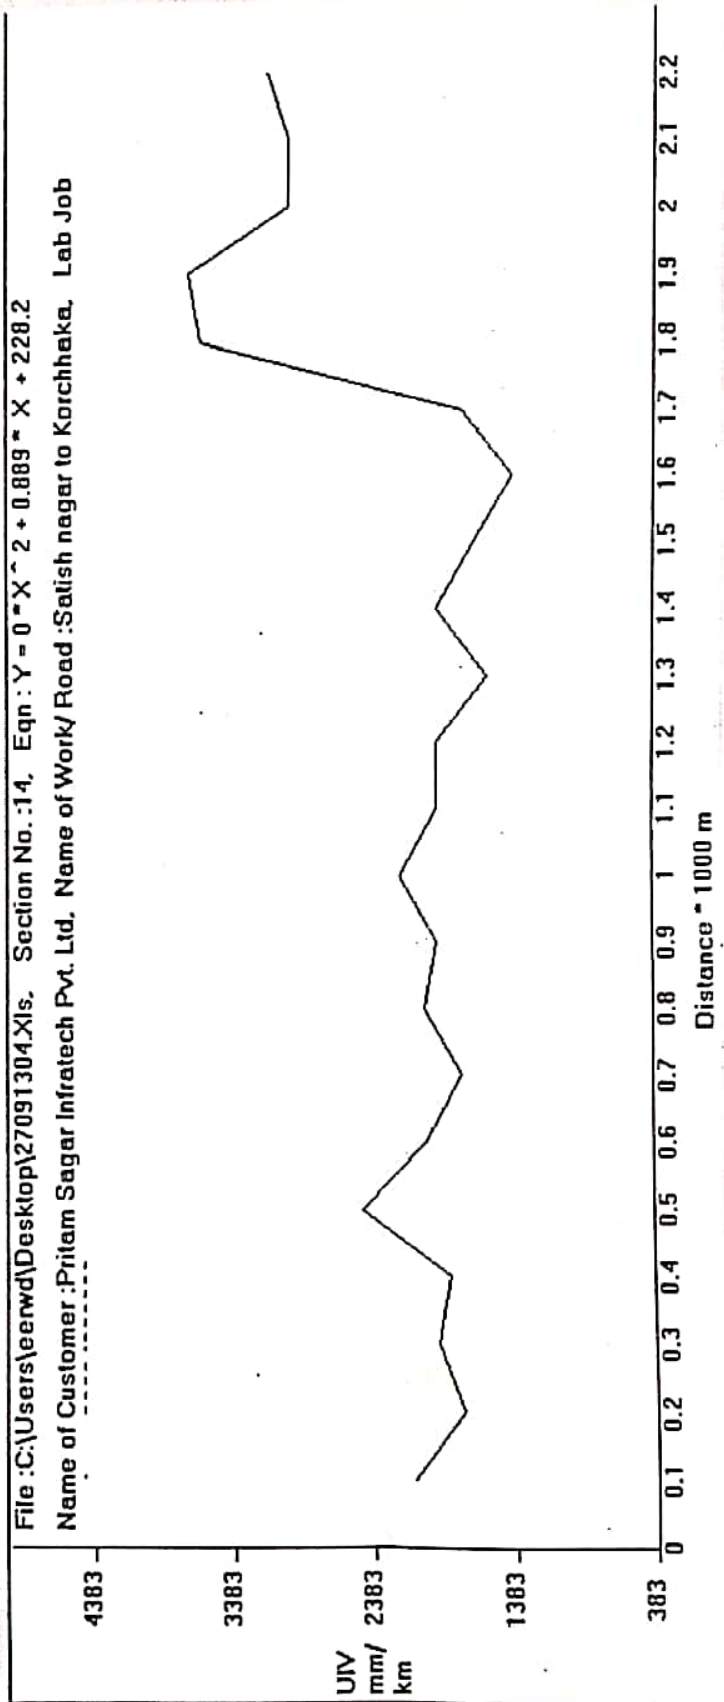

Kund
Executive Engineer
R.W.D. Works Div.
Gogri

27/9/22
A.E

27/09/22
J.E

MR-3054 (New)

MB No. 561

12.22

Schedule XLV Form No. 134.

Satish Nagar se Korchakra Path

गुप्त. गोरक्ष

DIVISION

गुप्त गुप्त गुप्त

SUB-DIVISION

M.B No-561

Measurement Book

Pritham Sagar

प्रमाणित किया जाता है कि इस
मापी पुस्तक में मशीन द्वारा अंकित
कुल - 100 (एक सौ) पन्ने हैं जिसमें
सहायक अभियंता, ग्रामीण कार्य
विभाग, कार्य अवर प्रमंडल,
परबला का निर्वाह किया
गया है।

H. Kumar
Executive Engineer
R.W.D. Works Div.
Gogri
20/5/22

Sch. XLV - Form No. 134

ग्रामीण, गोगरी DIVISION

अवर ग्रामीण, परबला SUB-DIVISION

Measurement Book

561 No.

Name of Officer _____

Date of first entry _____

Date of last entry _____

Name of Work-
 Situation of Work-
 Agency by which work is executed-
 Date of Measurement-
 No. and date of agreement

(These four lines should be repeated at the commencement of the measurement relating to each work)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of work:-	Const. of Road from				
	Chhalish Nagar (Sathish nagar) se				
	Korcha kka Path tak Path EWM				
	Puliyā ke Nisamon				
Agency:-	Paitam sagar, Jharkhand Pvt.				
	Ltd, Add - Vill - Manaul, P.S - Bhatpur, P.O -				
	Marianpur, Dist:- Bhagalpur (Bihar)				
Agg. no:-	05 MBN/2022-23				
Date of commencement:-	19-5-2022				

Date of completion:-

Date Approved - 10.5.22 below

Record Measurement

① Clearing and grubbing road

land including uprooting

wild vegetation - all compds

$$2 \times 68 \times 30m \times 1m = 4080m^2$$

$$2 \times 3 \times 30m \times 1.20m = 216m^2$$

$$2 \times 2 \times 30m \times 1.10m = 132m^2$$

$$\text{all} = 4428m^2$$

$$\text{OR} = \frac{4428}{10000} \text{ Hect}$$

$$= 0.44 \text{ Hect.}$$

40-P-19/T.M.B

Continuation

23/5/2022
J.G

cost = 15470

(24) P/V and fixing of typical masonry

/MR sandor masonry sign board - all comp. job

cost - 470

~~PK~~
12/9/2022
J.E.

~~JK~~
12/9/22
A.E.

Abstract of cost

(1/1) clearing and grubbing
road land including up
rooting wild vegetation

--- all comp. job

Qty vide P. no ① item no

① = 0.44 hect.

B/F 1/TMB

@ 59726.3/hect — R 26279 =

(2/2) construction of subgrade

and E/shoulder with

approved material obtained

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
form borrow pits - all comp. job					
on vide P. no (4) item					
no (2) = 2241.065 m ³					
@ 252.62/m ³					R 563897 = 00
(3/3) const. of W.B. B. str-2					
by providing well graded					
material - all comp. job					
on vide P. no (5) item					
(5) = 112.08 m ³					
@ 2449.80/m ³					R 274574 = 00
(4/4) P/v and laying bedding					
compacting stone aggregate					
at specific size to					
water bound macadam spec					
(WBM str-2)					
ification - all comp. job					
on vide P. no (8) item					
no (4) = 105.86 m ³					
@ 4323.80/m ³					R 457717 = 00
(5/5) P/v laying spreading					
and compacting stone					
aggregate at specific size					
to water bound maca					
(WBM str-3)					
- dam - all comp. job					
on vide P. no (5) item					
no (5) = 168.130 m ³					
@ 4010.35/m ³					R 674260 = 00

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(6/6) P/v and applying primer					
coat with bitumen emulsion					
(SSS) -- all comb job					
Qty vide P. no (12) item					
no (6) = 2241.68 m ²					
@ 60' 2/m ² ----- R 134770 = 2					
(7/7) P/v and applying tack					
coat with bitumen emul					
- sion pressure distributor					
at the rate of 0.25 to 0.30					
kg / sqm -- all comb job					
Qty vide P. no (12) item					
no (7) = 2241.68 m ²					
@ 20.46/m ² ----- R 45865 = 2					
(8/8) P/v laying and rolling					
of class graded premix					
surfacing material -- all comb					
Qty vide P. no (12) item					
no (8) = 2241.68 m ²					
@ 240.52/m ² ----- R 539169 = 2					
(9/9) P/v and applying tack					
coat with bitumen em					
- ulsion pressure distributor					
at the rate of 0.25 m to					
0.30 kg / sqm -- all comb job					
Qty vide P. no (14) item					
no (9) = 16771.05 m					

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Q 16771.05 m ² @ 20.46/m ²					1343136 =
(10/10) P/v and laying semi dense bituminous macadam concrete with 100-20 TP Batch Type H.M.P. - - all comp 205 Qty vide P.no (15) item no (10) = 423.43 m ³					
@ 9742.14/m ³					4125140 = 4125114 =
(11/11) P/v and laying semi dense bituminous concrete with 100-120 TP Batch Type H.M.P. - - all comp 205 Qty vide P.no (15) item no (11) = 211.71 m ³					
@ 12758.99/m ³					2701206 =
(12/12) P/v Reinforced cement concrete mix grad from Stone and 200m Stone - - all comp 205 Qty vide P.no (15) item no (12)(1) km stone = 4 no					
@ 2584.45/Each					10338 =
and 200m Stone P.no (15) item 12(1) = 9 No					
@ 742.10/each					6679 =
(13/13) Direction and place Identification sign with					

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Size more than 0.9 sqm					
Size board - - all comp cob					
Qty vide P. no (15) item					
no (13) = 1.92 m ²					
@ 12938 13/m ² ———				n	24841 =
(14) Painting line, surface					
-rous etc on roads two					
coats on old work - —					
- - - all comp cob					
Qty vide P. no (15) item					
no (14) = 1.80 m ²					
@ 88.82/m ² ———				n	160 =
(15) P/V and fixing of retro					
reflectorised cautionary,					
mandatory and interon					
-atory sign - - all comp cob					
Qty vide P. no (16) item					
no (15) (i) 600 mm Δ					
triangle = 12 no					
@ 3762.65/each ———				n	45164 =
and item no (15) (ii)					
600 mm $\bigcirc$ circular					
= 10 no					
@ 3779.89/each ———				n	37799 =
and item no 15 (iv) 600 mm					
x 450 mm $\square$ = 8 NO					
@ 3653.81/each ———				n	29230 =
(16) P/V and fixing Thermoplastic compound					
road strip - - - all comp cob					
Item no (16) = 20 @ 237.15/each				n	4743 =

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(17/21) R.C.C. 15' grad. bound dark pillars/local stone at standard depth design --- all comp. work					
Qty vide P. no (16) item no (17) = 104 no					
@ 629.67/cab. --- m 65486 =					
(18/22) Printing new letter and figure at every shade with synthetic --- all comp. work					
Qty vide P. no (16) item no (18) = 792 cm @ 0.60/cm --- 475 =					
(19/24) P.V. and laying at hot hot abbed thermoplastic compound 25mm thick including reflector e.e. glass --- all comp. job.					
Qty vide P. no (18) item no (19) 446.60 m ² @ 762.51/m ² --- 340537 =					
(20/25) Brick masonry work in C.M (1:3) in parapet excu ding pointing and plastering --- all comp. work					
Qty vide P. no (20) item no (20) = 23.034 m ³ @ 6040.25/m ³ --- 139131 =					

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(28/8) Plastering with cement mortar (1:4) on brick work					
- - - - - all work on h.					
Qty vide P. no (18) Item					
no (28) = 161.28 m ²					
@ 192.53/m ²					Rs 31051 =
(29/8) Painting two coats in					
- including primer coat after filling the surface - all work on					
Qty vide P. no (18) Item no					
(29) = 468.48 m ²					
@ 110.32/m ²					Rs 51683 =
(30/8) painting of tree and					
their maintain for one year - - all work on					
Qty vide P. no (19) Item no (22)					
111 No @ 1033.45/each					Rs 115379 =
(31/8) P/V panel fixing of typical					
concrete sign board - all work on					
Qty vide P. no (19) Item no (23)					
= 4 no @ 10297.03/each					Rs 41188 =
Add 12% C.S.T					Rs 10825168 =
					Rs 1299620 =
					Rs 12129455 =
					Rs 12124188 =
Add 1% L.C					Rs 12124188 =
					Rs 108299 =
					Rs 12245430 =
					Rs 12237754 =
Add Sdg. fee					90234 =
					Rs 12335664 =
					Rs 12327988 =

C.O ↓

Continuation

material statement	
① Earth work	2241.065m ³
