

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, रक्सौल।

पत्रांक :- 1245 0130

रक्सौल, / दिनांक :- 10/10/2022

प्रेषक :-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
ग्रामीण कार्य विभाग, बिहार, पटना।


विषय :- बिहार ग्रामीण पथ अनुरक्षण नीति-2018 अन्तर्गत पाँच वर्षीय रूटीन अनुरक्षण कार्य मद योजना अन्तर्गत आवंटन निर्गत करने हेतु अधियाचना के संबंध में।
महाशय,

उपर्युक्त विषयक बिहार ग्रामीण पथ अनुरक्षण नीति-2018 अन्तर्गत पाँच वर्षीय रूटीन अनुरक्षण कार्य मद में संलग्न सूची के अनुसार आवंटन अधियाचना संबंधित प्रपत्र में भरकर आवश्यक कार्रवाई हेतु समर्पित किया जाता है।

अनुलग्नक :- संलग्न सूची

1. पथों का आवंटन अधियाचना प्रपत्र।
2. Bump Integrator Report

विश्वासभाजन,


10/10/22
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, रक्सौल।

Standard Format For Roads Quarterly Statement (2nd Quarter)

Plt Name:- Rural Works Department, (Works) Division, Raxaul

1	Name of the Road	REO Road to Piparia		
2	Batch No.	RM/EA/RAX/20/0011		
3	Project ID	31708202198		
4	Total Length of Road (In Km)	2.210		
5	Length of Road to Meet Required Service Level [Completed Length] (In Km) [1]	2.210		
6	No. of Total Quarter (i.e. 3 Months as a unit) in 5 Years	20		
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] (in Lakh)	22.53605		
8	Quarterly Payment: 1/20 of ordinary Maintenance Cost as per Schedule (in Lakh) [2]	1.12680		
Compliance Criteria	Standard Job Description	Non Compliance		Reduction Payment [6] = [3]/[1]*[2]*[4]
		Length Non Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	Paved Roads (Carriageway)	0	60%	0.00000
II	Shoulders and Embanments	0	10%	0.00000
III	Cross Drainage Including Culverts and Bridge	0	15%	0.00000
IV	Signage and Road Safety	0	10%	0.00000
V	Vegataion	1	5%	0.02549
Total Payment Reduction For the Quarterly (In Lakh) [5]				0.02549
To be Paid for the Quarter / Demand (In Lakh) [6]				1.10131

Date of Inspection by E/I or his agent 10/10/2022

Prepared by Contractor's self Control Unit

ABHISHEK KUMAR, AE

Name and Designation of person inspecting road

Abhishek Kumar
10/10/22
(Signature)

Date:

Abhishek Kumar
10-10-2022
J-E
Signature of person inspecting road

Certify by E/I [Signature] Date

Abhishek Kumar
10/10/22
Executive Engineer
Rural Works Department
Works Division, Raxaul



Rural Works Department, Works Division, Raxaul
Government of Bihar

OM01Q

Rural Works Department

Road From: REO Road

To: Piparia

(Package No. RM/EA/RAX/20/0011)

Length of Road: 2.210 Km

Period: From 26.04.2021 to 25.07.2021

Inspector: A.E., RWD, Works Sub Division, Raxaul

Position: Good

2nd Quarter

Summary of Ordinary Maintenance Inspection Report

Date 10/10/2022

Standard Work Item		Work	Unit of work required in each Kilometre										Comments
No	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM100 Scaled Pavement													
OM101	Pothole Patching	m ²	Nil	Nil	Nil								No Pot Hole Found
OM102	Surface Depression and Rut Patching	m ²	Nil	Nil	Nil								No Surface Depression and Rut Patching Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil								No Crack Sealing Found
OM104	Surface Treatment												
	(a) Loss of Aggregate (Surface Ravelling)	m ²	Nil	Nil	Nil								No Loss of Aggregate (Surface Ravelling) Found
	(b) Bleeding / Flushing	m ²	Nil	Nil	Nil								No Bleeding / Flushing Required
	(c) Crocodile Cracking	m ²	Nil	Nil	Nil								No Crocodile Cracking Found
OM105	Edge Repair	m ²	Nil	Nil	Nil								No Edge Repair Required
OM106	Digouts	m ²	NA	NA	NA								
OM107	Concrete Pavement	m ³	NA	NA	NA								
	Other activities												
OM200 Shoulder													
OM201	Unsealed Shoulder												No Edge Drop-off Required
	(a) Edge Drop-off	Lm	Nil	Nil	Nil								Not Required
	(b) Roughness, Scouring or Pothles	Lm	Nil	Nil	Nil								No Holding Water Found
	(c) Holding Water	Lm	Nil	Nil	Nil								Not Required
OM202	Embankment Repair	m ³	Nil	Nil	Nil								
	Other activities												



Standard Work Item		Work	Unit of work required in each Kilometre										Comments
No	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM300 Drainage including culverts major and minor bridges													
OM301	Surface Drains & Verge	Lm	NA	NA	NA								Not Required
OM302	Culvert Cleaning	Lm	Nil	Nil	Nil								Not Required
OM303	Culvert and Pit Repair	m ³	Nil	Nil	Nil								Not Required
	Other activities												Not Required
OM400 Vegetation													
OM401	Grass Control												Not Required
	(a) Roadside General Tidy	Ha	Nil	Nil	Nil								Not Required
	(b) Clear near safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil								Not Required
OM402	Tree and Shrub Management	Ha	Nil	Nil	Nil								Not Required
	Other activities												
OM500 Signage and Road Safety													
OM501	Signs Maintenance	No	Nil	Nil	Nil								Not Required
OM502	Guard stones	Lm	NA	NA	NA								Not Required
OM503	Distance Stones	No	NA	NA	NA								Not Required
OM504	Road Markings	No	Nil	Nil	Nil								Not Required
	Other activities												

← *बिडर*
Bidder

Appendix
Appendix

Executive Engineer,
Executive Engineer,
RWD, Works Division, Raxaul
10/10/22

Name of Road:- REO Path To Pipriya
Name of Contractor:-Rohan Construction Private Limited

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	UIV	CATEGORY ROAD	Latitude	Longitude	Event
9/3/22	17:46:10	62	0.1	330	0	3300	3402 G		26.94065	84.74884	Normal
9/3/22	17:46:40	62	0.1	240	20.2	2400	2504 G		26.94121	84.74926	Normal
9/3/22	17:47:10	62	0.1	320	20.2	3200	3303 G		26.94158	84.7501	Normal
9/3/22	17:47:35	62	0.1	280	20.2	2800	2903 G		26.94225	84.75072	Normal
9/3/22	17:48:05	62	0.1	230	30.3	2300	2404 G		26.94314	84.75089	Normal
9/3/22	17:48:30	62	0.1	240	30.3	2400	2504 G		26.94403	84.75103	Curve
9/3/22	17:49:0	62	0.1	270	20.2	2700	2804 G		26.94435	84.75042	Curve
9/3/22	17:49:35	62	0.1	320	20.2	3200	3303 G		26.94493	84.74978	Curve
9/3/22	17:50:05	62	0.1	260	20.2	2600	2704 G		26.94509	84.74891	Normal
9/3/22	17:50:30	62	0.1	240	20.2	2400	2504 G		26.94558	84.7481	Curve
9/3/22	17:51:00	62	0.1	250	20.2	2500	2604 G		26.94598	84.74732	Curve
9/3/22	17:51:20	62	0.1	300	20.2	3000	3103 G		26.94544	84.74678	Curve
9/3/22	17:51:56	62	0.1	250	20.2	2500	2604 G		26.94458	84.7468	Curve
9/3/22	17:52:20	62	0.1	280	20.2	2800	2903 G		26.9439	84.74618	Normal
9/3/22	17:52:50	62	0.1	280	20.2	2800	2903 G		26.94352	84.74522	Normal
9/3/22	17:53:21	62	0.1	280	10.1	2800	2903 G		26.94375	84.74426	Normal
9/3/22	17:53:51	62	0.1	280	10.1	2800	2903 G		26.94451	84.74392	Normal
9/3/22	17:54:20	62	0.1	300	10.1	3000	3103 G		26.94505	84.74318	Normal
9/3/22	17:54:50	62	0.1	300	10.1	3000	3103 G		26.9456	84.74237	Normal
9/3/22	17:55:22	62	0.1	340	10.1	3400	3502 G		26.94612	84.74162	Normal
9/3/22	17:55:52	62	0.1	300	20.2	3000	3103 G		26.94642	84.74062	Normal
9/3/22	17:56:20	62	0.1	340	10.1	3400	3502 G		26.94695	84.7398	Normal
9/3/22	17:56:57	62	0.1	280	20.2	2800	2903 G		26.94697	84.73965	Normal

Total IRI	67474
Average IRI	2933.652

$$Y = 0 * X^2 + 0.998 * X + 109.5$$

$$X = 18462$$

$$Y = 18534$$

(R) RURAL ROAD
 Good Average Poor
 <4000 4001-5000 >5001

Signature
 10-10-2022
 J-E

Signature
 10/10/22
 AE

Signature
 10/10/22
 Executive Engineer
 Rural Works Department
 Works Division

Name of Customer : Rohan Construction Private Lim
 Name of Work/ Road : REO Path To Pipriya
 Lab Job number : 23
 Date : 09-03-2022
 Section No : 62


Test Date : 09-03-2022 Road Name : REO Path To Pipriya
 Machine No : 378 Road Type : (R) RURAL ROAD
 Start S No : 0 000 km Side :
 Start E No : 2 210 km Interval
 Weather : Normal IIV Range : 1404 To 5000 1000 mm/km
 Start Location : REO Path Dist Range : 0 To 24 01 1000 m
 End Location : Pipriya Equation : $Y = 0 \cdot X^2 + 0.998 \cdot X + 1095$

Print

Generate Report and Graph

Redraw Graph

Map View

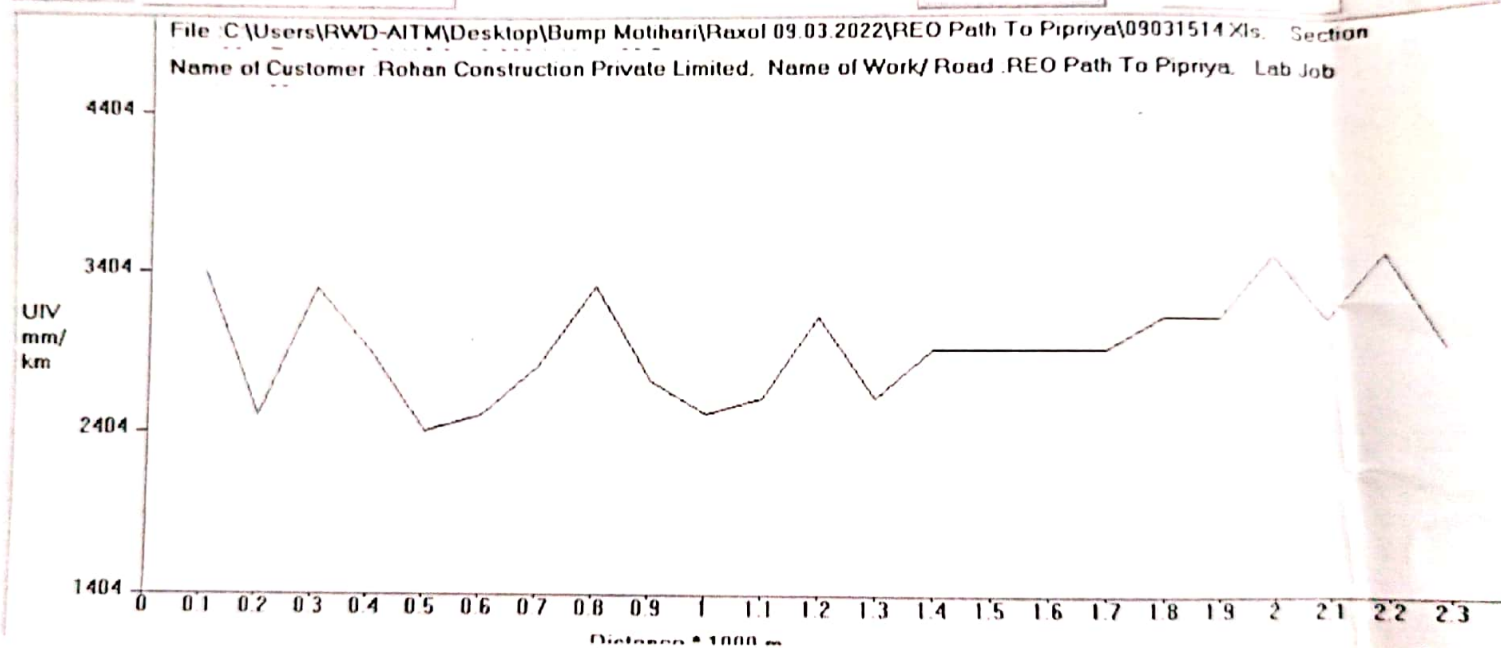

Signature
 10-10-2022
 J-E

Signature
 10/10/22
 AE

Signature
 10/10/22
 Executive Engineer
 Rural Works Department
 Works Division, Raxaul
 10/10



मुख्यमंत्री ग्रामीण पथ अनुरक्षण कार्यक्रम

योजनाकानामः आर. ई.ओ. पथ से पिपरिया
पथकी लम्बाई: 2.21 K.M., बिटुमिनस पथांशः 2.21 K.M., पो.सी.सी. पथांशः
प्राक्कलित राशि: 48.24 लाख
पाँच साल तक रस्-रखाव की राशि: 19.85 लाख
पुलिया: 2 कॅजवे: पुलः
कार्य आरंभ की तिथि: 08-08-2020, कार्य समाप्ति की तिथि: 07-05-2021
संवेदक कानामः रोहन कन्सट्रक्शन प्रा. लि. हवाई अड्डा रोड, परेडो बार्डन: 01, रक्सौल
कार्यकारी एजेंसी: कार्यपालक अभियंता, ग्रामीण कार्य विभाग, कार्य प्रमंडल, रक्सौल


Latitude: 26.94486
Longitude: 84.74711
Elevation: 107.91±52 m
Accuracy: 67.8 m
Time: 04-09-2022 15:11
Note: REO Road, piparia

Powered by NoteCam




Latitude: 26.945824
Longitude: 84.751632
Accuracy: 2400.0 m
Time: 04-09-2022 15:01
Note: REO Road, piparia

Powered by NoteCam

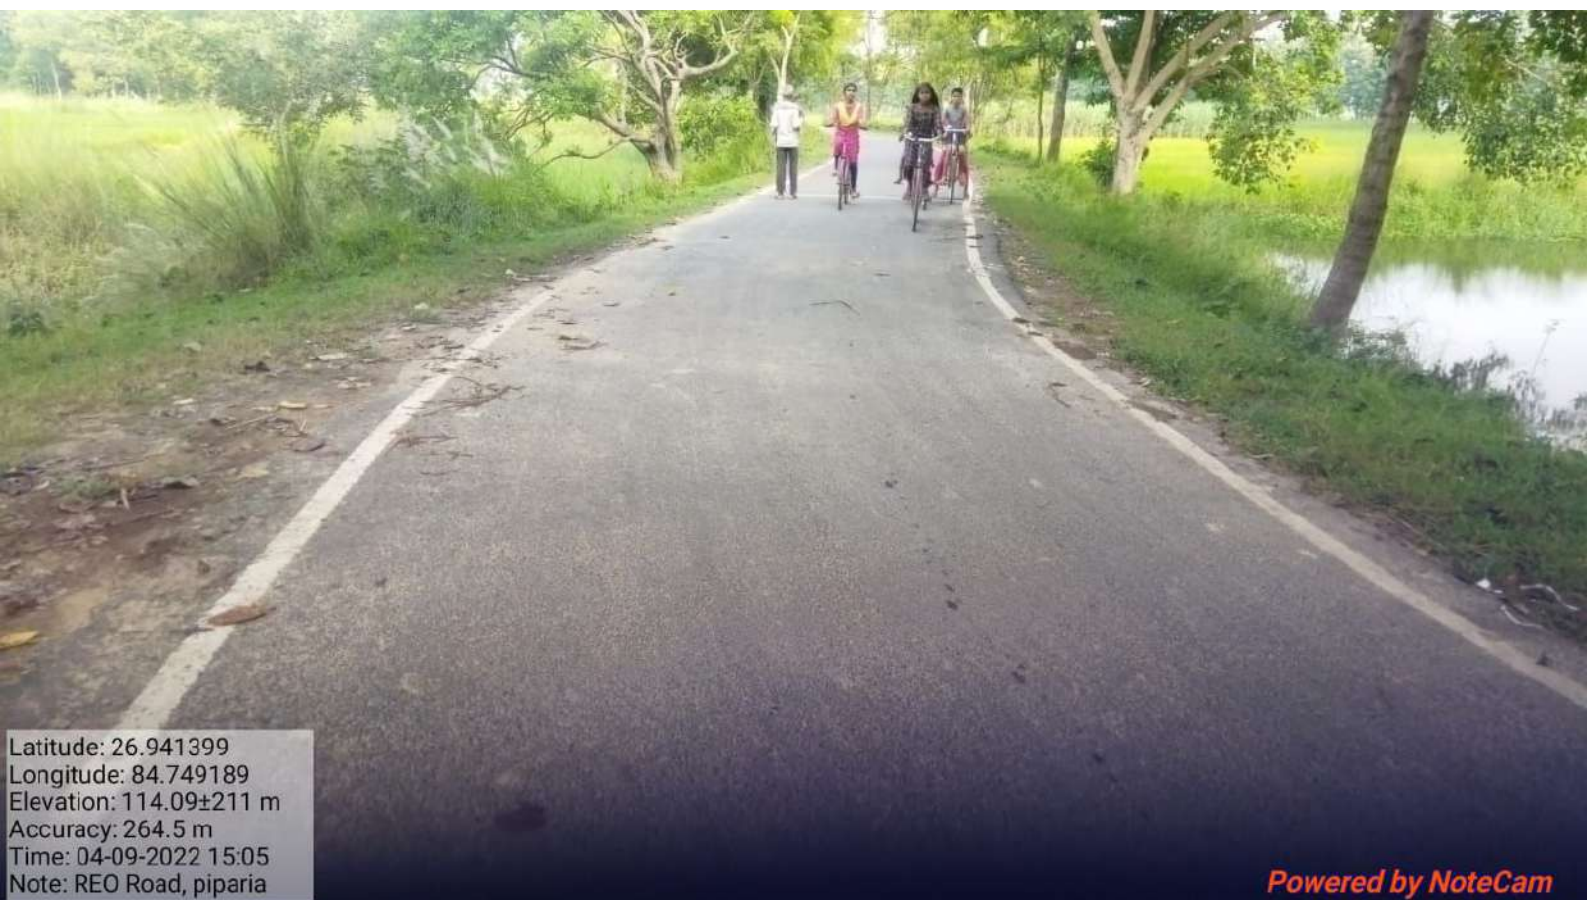

Latitude: 26.941399
Longitude: 84.749189
Elevation: 114.09±211 m
Accuracy: 264.5 m
Time: 04-09-2022 15:05
Note: REO Road, piparia

Powered by NoteCam

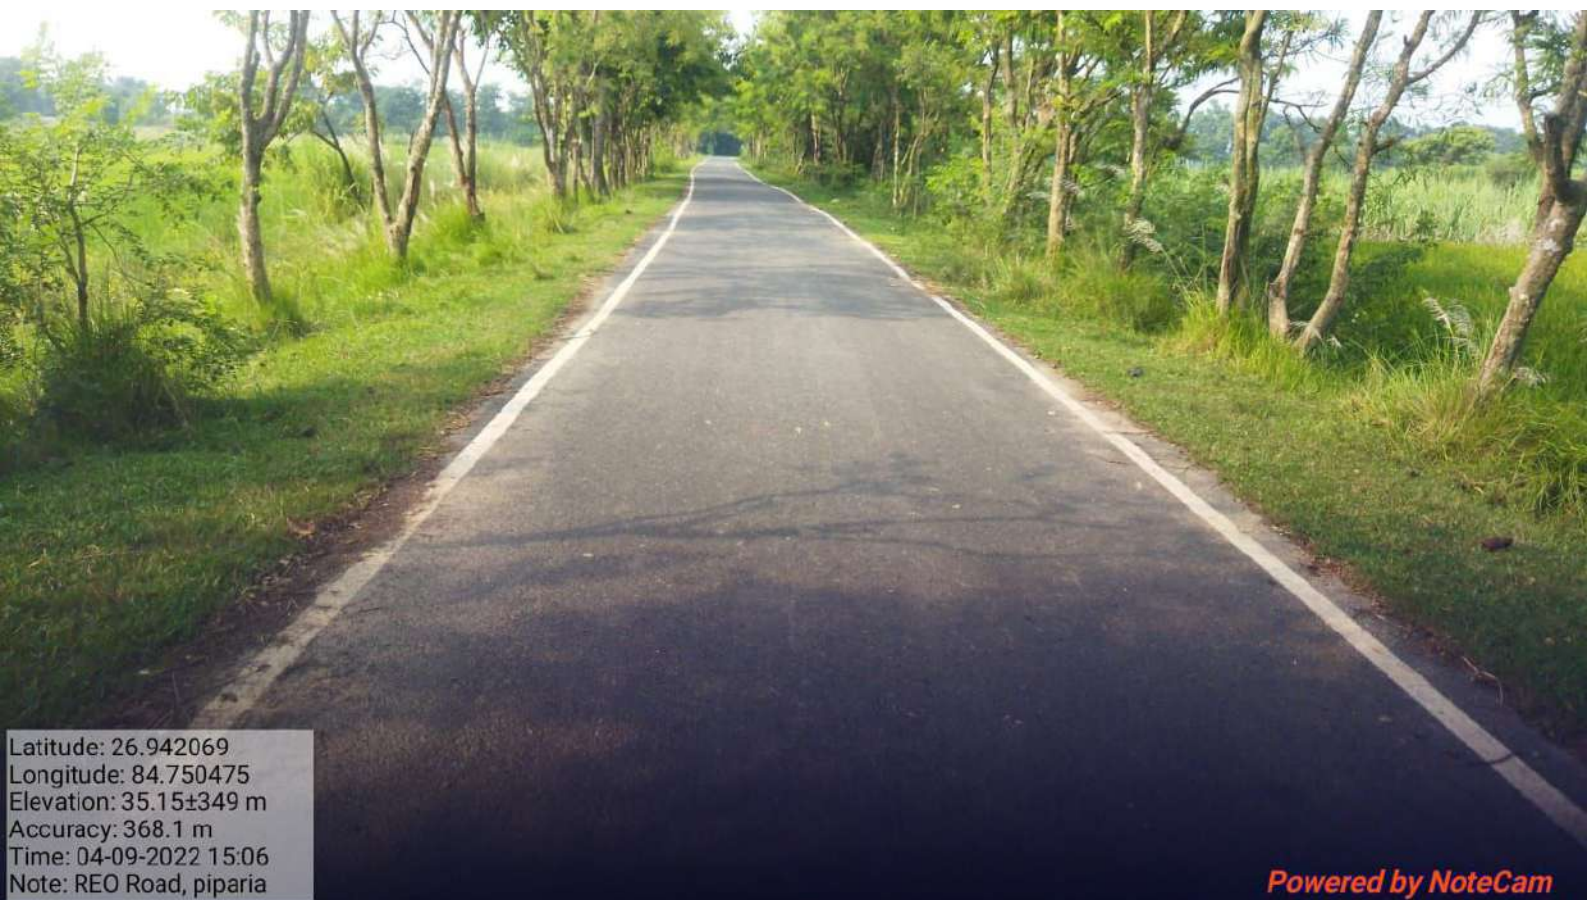

Latitude: 26.942069
Longitude: 84.750475
Elevation: 35.15±349 m
Accuracy: 368.1 m
Time: 04-09-2022 15:06
Note: REO Road, piparia

Powered by NoteCam



Latitude: 26.944896
Longitude: 84.74641
Elevation: 77.4±347 m
Accuracy: 245.7 m
Time: 04-09-2022 15:09
Note: REO Road, piparia

Powered by NoteCam
