

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, जयनगर

पत्रांक 1221 अनु०

जयनगर, दिनांक 15-09-2022

प्रेषक :- कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, जयनगर

सेवा में,
नोडल पदाधिकारी (3054)
ग्रामीण कार्य विभाग
ब्राडा, पटना।


विषय :- MR-3054 (NMP) योजनान्तर्गत चल रहे योजनाओं हेतु आवंटन उपलब्ध कराने के सम्बंध में।


महाशय,

उपर्युक्त विषयक के सम्बंध में कहना है कि MR-3054 (NMP) योजना हेतु अधियाचना विहित प्रपत्र में आवश्यक कार्रवाई हेतु समर्पित की जाती है।

अनु०- यथोक्त।

विश्वासभाजन


कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, जयनगर


15.9.22

MR(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division. Jaynagar

Sl No	Package No	Name of the Road Project (English)	Project ID as per MIS	Administrative Approval (AA) Letter no Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/Km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allied Amount (in Lakh)	Up to Date Expenditure as per MIS	Requirement against work done (in Lakh)	Remarks
					Length (in Km)	Amount of Lakh	Initial Rectification and Surface Renewal (in Lakh)	Five Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/MA/JAY/22/0001	T04 to Chilmilla	31910002081	Lt-102 Dt-03/06/2022	2.249	107.10000	81.263	17.70221	06/MIB/22-23 26/07/2023	25/07/2023	-	2868	25 mm	5%	0.00000	0.00000	80.15004	

1 Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed

2 Up-to-date Physical Progress has been uploaded in MIS

[Signature]
15/9/22

[Signature]
Executive Engineer
RWD, Works Division, Jaynagar

FORM GFR -19 -A

(see Govt. of India's decision (i) below rule 150)

Form of Utilisation Certificate upto August

Rural Road Maintenance policy-2018

PIU:- R.W.D. Works, Division , Jaynagar

Sl. No.	Name of Scheme	Sanction No.& Date with amount (in Rs. Lakh)	Amount Received (in Rs. Lakh)	Particulars
1	2	3	4	5
1	Construction of Road Under Rural Road Maintenance policy-2018	1436.94319	1436.94319	Certified that out of Rs.1436.94319 Lakh received till date in favour of Ex.Engineer, R.W.D. Works Division, Jaynagar a sum of Rs.1422.77780 Lakh has been utilized for the purpose of Rural Road Maintenance policy-2018 Scheme as given in the margine for which it was sanctioned and that the balance of Rs.14.165390 Lakh remaining unutilized at the end of the period under the time of completion.
		1436.94319	1436.94319	

- 2 Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the propose for which it was sanctioned.

Kind of Checks Exercised :-

- (i) Workers have been supervised by Executive Engineer/ Superintending Engineer
- (ii) Periodical inspection has been conducted by Executive Engineer/Superintending Engineer
- (iii) Construction materials have been tested.
- (iv) Measurments have been recorded in the MB's and test check conducted by the Assistant
- (v) All other codal formalities have overserved

Handwritten signature
7/8/19

Handwritten signature
15/8/19
Executive Engineer
Rural works Department
Works Division, Jaynagar

प्रमाण-पत्र

शीर्ष :- 3054 एम0 आर0 (बिहार ग्रामीण पथ अनुस्क्षण निति-2018)


योजना :- T04 to Chilmilla (Package No.- RM/MA/JAY/22/0001)

1. मापीपुरत पर इस आशय का प्रमाण-पत्र दर्ज है कि कार्य गुणवत्तापूर्ण कराया गया है।
2. कराये गये कार्यो के सभी अवयवों के अवयववार 100 प्रतिशत कार्य का दर्ज मापी का सत्यापन कनीय अभियंता, 50 प्रतिशत मापी का सत्यापन सहायक अभियंता एवं 10 प्रतिशत मापी का सत्यापन कार्यपालक अभियंता द्वारा किया गया है।




15/09/2022

कनीय अभियंता
कार्यप्रशाखा, बासोपट्टी



15/09/2022

सहायक अभियंता
कार्य अवरप्रमंडल, बासोपट्टी



15/09/2022

कार्यपालक अभियंता
ग्रामीण कार्यविभाग
कार्यप्रमण्डल, जयनगर

Name of work : 104 to Chilimilla

Name of customer : Om Construction

(R) Rural Road

Good

Average

Poor

< 4000

4001 - 5000

> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUM(cm)	Speed(Km/Hr)	Ultrasonic(Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
06/09/22	16:55:26	59	0	0	0.0 cm	0.0 Km/Hr	0.0 mm/Km	196	0.35	Good	26.5423422	N	86.004043	E	Normal
06/09/22	16:56:33	59	100	100	36.0 cm	1.2 Km/Hr	3600.0 mm/Km	3534	4.66	Good	26.5608644	N	86.0076532	E	Normal
06/09/22	16:56:52	59	100	200	31.0 cm	19.4 Km/Hr	3100.0 mm/Km	3070	4.11	Good	26.5607920	N	86.0071115	E	Normal
06/09/22	16:57:13	59	100	300	21.0 cm	17.0 Km/Hr	2100.0 mm/Km	2143	2.98	Good	26.5602179	N	86.0082739	E	Normal
06/09/22	16:57:32	59	100	400	34.0 cm	18.1 Km/Hr	3400.0 mm/Km	3348	4.44	Good	26.5597195	N	86.0055170	E	Normal
06/09/22	16:57:47	59	100	500	36.0 cm	24.9 Km/Hr	3600.0 mm/Km	3534	4.66	Good	26.5593023	N	86.0051126	E	Normal
06/09/22	16:58:02	59	100	600	29.0 cm	24.1 Km/Hr	2900.0 mm/Km	2885	3.89	Good	26.5580568	N	86.0041208	E	Normal
06/09/22	16:58:15	59	100	700	38.0 cm	26.2 Km/Hr	3800.0 mm/Km	3719	4.88	Good	26.5574999	N	86.0036936	E	Normal
06/09/22	16:58:29	59	100	800	29.0 cm	26.2 Km/Hr	2900.0 mm/Km	2885	3.89	Good	26.5566740	N	86.0031595	E	Normal
06/09/22	16:58:42	59	100	900	33.0 cm	26.4 Km/Hr	3300.0 mm/Km	3255	4.33	Good	26.5566740	N	86.0031595	E	Normal
06/09/22	16:58:57	59	100	1000	37.0 cm	25.4 Km/Hr	3700.0 mm/Km	3626	4.77	Good	26.5555601	N	86.0023127	E	Normal
06/09/22	16:59:11	59	100	1100	37.0 cm	25.4 Km/Hr	3700.0 mm/Km	3626	4.77	Good	26.5541830	N	86.0014353	E	Normal
06/09/22	16:59:27	59	100	1200	34.0 cm	22.7 Km/Hr	3400.0 mm/Km	3348	4.44	Good	26.5541830	N	86.0014353	E	Normal
06/09/22	16:59:45	59	100	1300	28.0 cm	20.2 Km/Hr	2800.0 mm/Km	2792	3.78	Good	26.5541830	N	86.0014353	E	Normal
06/09/22	17:00:02	59	100	1400	21.0 cm	21.0 Km/Hr	2100.0 mm/Km	2143	2.98	Good	26.5526209	N	85.9996119	E	Normal
06/09/22	17:00:17	59	100	1500	26.0 cm	23.6 Km/Hr	2600.0 mm/Km	2607	3.55	Good	26.5519781	N	85.9988642	E	Normal
06/09/22	17:00:31	59	100	1600	29.0 cm	24.9 Km/Hr	2900.0 mm/Km	2885	3.89	Good	26.5519781	N	85.9988642	E	Normal
06/09/22	17:00:49	59	100	1700	21.0 cm	20.6 Km/Hr	2100.0 mm/Km	2143	2.98	Good	26.5497980	N	85.9980021	E	Normal
06/09/22	17:01:05	59	100	1800	36.0 cm	23.1 Km/Hr	3600.0 mm/Km	3534	4.66	Good	26.5497980	N	85.9980021	E	Normal
06/09/22	17:01:25	59	100	1900	31.0 cm	17.8 Km/Hr	3100.0 mm/Km	3070	4.11	Good	26.5486422	N	85.9973307	E	Normal
06/09/22	17:01:42	59	100	2000	24.0 cm	20.9 Km/Hr	2400.0 mm/Km	2421	3.33	Good	26.5486422	N	85.9971018	E	Normal

15/09/2022
15/09/2022

15/09/2022

15/09/2022

कार्यपालक अभियंता
श्रीमणि कार्य विभाग
कार्य प्रमण्डल, जयनगर

Name of work		T04 to Chillumilla													
Name of customer		Om Construction													
(R) Rural Road															
Good		Average					Poor								
< 4000		4001 - 5000					> 5000								
06/09/22	17:02:01	59	100	2100	29.0 cm	18.3 Km/hr	2900.0 mm/Km	2885	3.89	Good	26.5486422	N	85.9971018	E	Normal
06/09/22	17:02:41	59	100	2200	23.0 cm	18.3 Km/hr	2300.0 mm/Km	2328	3.21	Good	26.5462770	N	85.9965678	E	Normal

Average ~ 2868

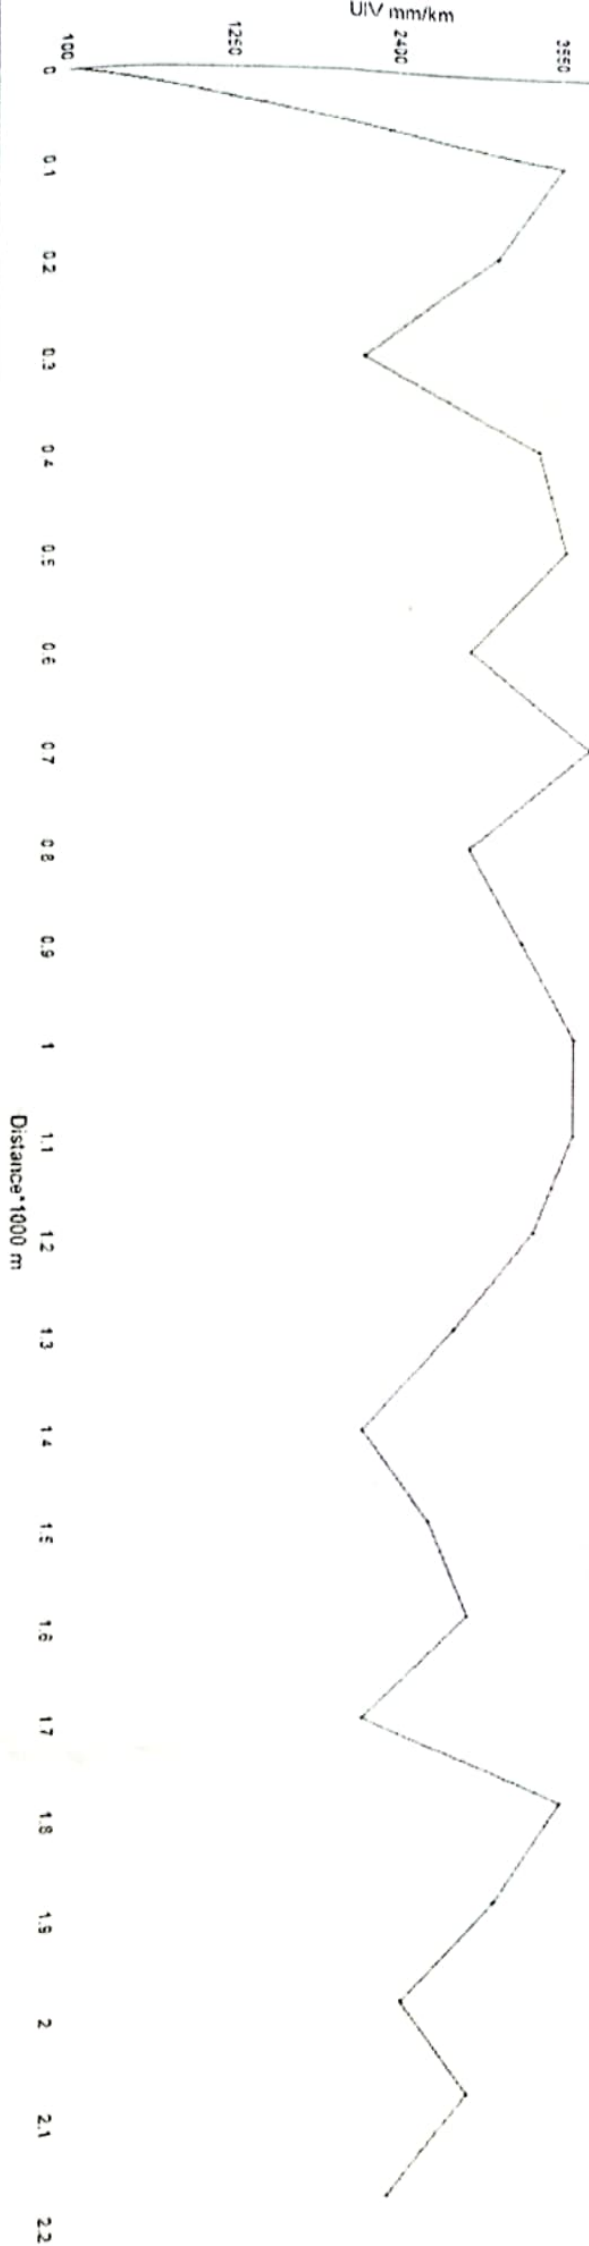
15/09/2022
JE

15-9-2022

कार्यपालक अभियंता।
प्रमाणित कार्य विभाग
कार्य प्रमण्डल, जयनगर

15/09/2022

4700

Name of Customer: Om Construction, Machine no: 19195, Road: 104 to Chilmilla, Date: 06/09/22, Section No: 59, Equation: $Y = 0.927X + 196.3$ 

15/09/2022

15/09/22

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, जयन्तनगर

15/09/22

पत्रांक - 564 (अनु०)

दरभंगा/दिनांक :- 09.09.2022

श्रेष्ठ,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
क्षेत्रीय प्रयोगशाला, दरभंगा

सेवा में,

सहायक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, बासोपट्टी

विषय :- जाँच फल प्रतिवेदन के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि आपके प्रमंडलाधीन पथों के निरीक्षण के क्रम में संग्रहित किये गये सामग्रियों के नमूनों की जाँच कर जाँच-फल प्रतिवेदन आपके आवश्यक कार्यवाही हेतु प्रेषित किया जाता है।

अनु:- यथोक्त

विश्वामाजन

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
क्षेत्रीय प्रयोगशाला, दरभंगा

09/09/2022

OFFICE OF THE EXECUTIVE ENGINEER, REGIONAL LABORATORY, R.W.D, DARBHANGA (BIHAR)

BITUMEN PERCENTAGE TEST

Name of the Scheme TDA To Chikrila (Chikrila)

Name of the works Division R.W.D. (S.D. Div. Jaynagar.

Package No 06 MAD/2022-23

Name of the work circle R.W.D. (S.D. Circle, Darbhanga.

Sample collected by Kide RA. No. 124 (S.D. Div. 16.08.2022

Name of Agency M/S. Dm Construction.

Date of sample collection At site 02.09.22

Date of test 07.09.2022

Sl No	Sample No	1	2	3
1	Wt. of mix taken before extraction (A) gm	500.160		
2	Wt. of filter paper before extraction (B) gm	4.790		
3	Wt. of mix after extraction (C) gm	472.040		
4	Wt. of filter paper after extraction (D) gm	5.680		
5	Wt. of filter collected from extract after allowing for setting (E) gm	1.700		
6	Wt. of filler collected in filter paper (D-B)=F gm	0.890		
7	Wt. of aggregate + filter paper (C+E+F)=G gm	474.630		
8	Percentage of Bitumen (in the mix) [(A-G)x100/A]	5.10%		

09/09/2022

09/09/2022

09/09/2022

09/09/22

Laboratory Assistant

Junior Engineer

Assistant Engineer

Executive Engineer

R.W.D, Regional Laboratory
Darbhanga (Bihar)

R.W.D, Regional Laboratory
Darbhanga (Bihar)

R.W.D, Regional Laboratory
Darbhanga (Bihar)

R.W.D, Regional Laboratory
Darbhanga (Bihar)

Schedule XLY-Form No. 134

TO4 to Chikewilla (MR-3054)

JAYNAGAR DIVISION

BASOPATTI SUB-DIVISION

1239

MEASUREMENT BOOK

M/S OM CONSTRUCTION

प्रमाणित किया जाता है कि इस
मापी पुरस्तीक में मशीन द्वारा मुद्रित
01 से 100 तक अंकित है, जो अवर
प्रमण्डल पदाधिकारी वासोपदी के
नाम से निगति किया जाता है।


कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, जयनगर
11/11/2022

Schedule XLV- Form No.- 134.

कार्यपालक अभियंता

ग्रामीण कार्य विभाग

कार्य प्रमण्डल, जयनगर

DIVISIUN

SUB-DIVISION

MEASUREMENT BOOK

No.

1239

Name of officer

Date of fist entry

Date of last entry

1st on A/c B/L

Name of the work-

Situation of work-

Agency by which work is executed-

Date of measurement-

No. and date of agreement-

(These four lines should be repeated at the commencement of the measurements relating to each work)

01

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of work:-					
Construction of					
Road To to Chelmiliya					
under MR (3054)					
Agency:-					
M/s Om Construction,					
Prop:-					
Om Namo Narayan,					
Ram chowk Bhavara,					
Madhubani Bihar -847212					
Agreement no-					
06 MBD/2022-23 MR(3054)					
Rate:-					
0.01%					
Date of commencement-					
26th July 2022					
Date of completion:-					
25-07-2023					

21.1/	clearing and grubbing road				
	land including uprooting --				
	-- do -- do -- all				
	complete job.				
	2x6x30x1.00			=	360.00
	2x8x30x0.90			=	432.00
	2x9x30x0.95			=	513.00
	2x13x30x1.00			=	780.00
	2x9x30x1.10			=	594.00
	2x12x30x0.90			=	648.00
	2x8x30x0.95			=	456.00
	2x9x30x1.00			=	540.00
	2x1x29x0.90			=	52.20

Continuation

= 4375.20m²

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(16)/22	Painting on parapet wall				
		du	du		
	all complete Job				
P-14	Qty-	102.40 m ²			
	@ Rs	115.90 / m ²			11868=00
(17)/23	Plastering with cement mortar (1:4) on brick work				
		du	du		
	all complete Job				
P-14	Qty-	102.40 m ²			
	@ Rs	204.00 / m ²			20,891=00

(18)/24	Brick masonry work in cement mortar (1:3)				
		du	du	all	
	complete Job.				
P-14	Qty-	14.64 m ³			
	@ Rs.	5826.74 / cum			85,303=00
					70,35,520=00
	Add GST @ 12%				8,44,262=00
	Add L. Cess @ 1%				70355=00
					= 70,50,137=00
	Add S. Fee @ 10% of M. Cost				65,668=00
					= 80,15,805=00
	Less 0.01% as per Agreement				801=00
					= 80,15,004=00

(15/09/2022) JE

Continuation
