

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग

कार्य प्रमंडल सोनपुर

पत्रांक 1482 सोनपुर, दिनांक 14/09/22

प्रेषक,

कार्यपालक अभियंता

ग्रामीण कार्य विभाग

कार्य प्रमंडल सोनपुर

सेवा में,

नोडल पदाधिकारी (3054),

ग्रामीण कार्य विभाग

बिहार, पटना।

विषय:- बिहार ग्रामीण पथ अनुरक्षण निति-2018 के तहत स्वीकृत योजना में
आवंटन उपलब्ध कराने के संबंध में।


महाशय,

उपर्युक्त विषयक ग्रामीण कार्य विभाग कार्य प्रमंडल सोनपुर के अंतर्गत बिहार
ग्रामीण पथ अनुरक्षण निति-2018 के तहत स्वीकृत योजना के क्रियान्वयन हेतु आवंटन की
मांग विहित प्रपत्र में तैयार कर भेजी जा रही है।

अनुरोध है कि उपर्युक्त योजना में आवंटन उपलब्ध कराने की कृपा की
जाये।

अनु०:-उपयोगित प्रमाण-पत्र।

विश्वासभाजन


13/9/22

कार्यपालक अभियंता

ग्रामीण कार्य विभाग

कार्य प्रमंडल सोनपुर
13/9/22

FORM GER 19-A

(See Government of India's Decision (I) below Rule-150
Form of Utilization Certificate up to the month of **September-2022**

PIU:- E.E.,R.W.D. Works Division Sonapur.

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in lacs Rs.)	Amount Received (in lac Rs.)	Particulars
1	2	3	4	5
1	Construction of Rural Roads under New Maintenance Policy-18		5536.48230	Certified that out of Rs 5536.48230 lakh received during the years 2020-21 to 2022-23 in favour of E.E.R.W.D. works division Sonapur a sum of Rs 5513.96594 Lakh has been utilized for the purpose of New Maintenance Policy-18 Scheme as given in the margin for which it was sanctioned and that the balance of Rs 22.51636 Lakh remaining unutilized at the end of the period under report.

Certified that I have satisfied that the condition of which the grants-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually for the purpose for which it was sanctioned.

Kind of Checks:-

- Words have been supervised be Executive/superintending Engineer.
 - Periodical inspection has been conducted by Executive Engineer/ superintending Engineer.
 - Construction material has been tested.
 - Measurements have been recorded in the MBS and test conducted by the Assistant Engineer/ Executive Engineer.
 - All other nodal formalities have been observed.
- 3 physical Progress achieved-
- Construction of Road Works.
 - Construction of CD works

[Signature]
13.9.22
D.A.O

R.W.D. Works Division Sonpur.

[Signature]
13/9/22
EXECUTIVE ENGINEER

R.W.D. Works Division Sonpur.

Advertisement Formate for Scheme Head - MR-3054 Under Bihar Rural Road Maintenance Policy 2018 (In Rectification and surface Renewal)

Division Name:- Rural Works Department, Works Division- Sonpur

Sl.No	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA)	Administrative Approval (AA)	Agreement Amount (in Lac)	Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in Km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content In %	Previous Total Allocated Amount (in Lac)	Upto date expenditure as per MIS (in Lac)	Requisition against Work Done (in Lac)	Remarks		
1	RM/SA/SON/20/0004	NH-19 - Jhaua(Goraiपुर) Pakauliya	NEA220001812	5138 24.09.19	2.900	114.570	58.33165	25.96345	22/MBD/21-22	19.12.2022	-	1315	25.00	5.02	0.00	0.00	57.90118	
TOTAL																57.90118		

R.W.D Works Div- Sonpur

[Signature]
D.A.O

[Signature]
Executive Engineer
R.W.D Works Div- Sonpur
13/11/22

कार्यपालक अभियंता का कार्यालय


ग्रामीण कार्य विभाग

कार्य प्रमंडल सोनपुर

का0आ0सं0...1479.....सोनपुर, दिनांक 13/09/2022

कार्यालय आदेश


प्रमाणित किया जाता है कि बिहार ग्रामीण पथ अनुरक्षण निती-2018 योजनान्तर्गत एन0एच0-19 झौवा (गोराईपुर) पकुलियों पथ का कार्य गुणवत्ता एवं विशिष्टियों के अनुरूप पूर्ण कराया गया है। पथ के मापीपुस्त की जॉच मेरे द्वारा 25 प्रतिशत एवं सहायक अभियंता के द्वारा 50 प्रतिशत एवं कनीय अभियंता के द्वारा शत प्रतिशत किया गया है।



कनीय अभियंता

ग्रामीण कार्य विभाग

कार्य अवर प्रमंडल दिघवारा



सहायक अभियंता

ग्रामीण कार्य विभाग

कार्य अवर प्रमंडल दिघवारा



कार्यपालक अभियंता

ग्रामीण कार्य विभाग

कार्य प्रमंडल सोनपुर

13/9/22

Name of work : NH-19 - Jhausa (Goraiapur) Pakauliya

Name of customer : Deepu Construction Prop-Ram Pukar Singh

(R) Rural Road

Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUM(Plcm)	Speed(Km/Hr)	Ulimm(Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction	Remarks
28/08/22	13:41:21	80	100	100	11.0 cm	11.4 Km/Hr	1100.0 mm/Km	1148	1.71	Good	25.7488241	N	84.5407775	E	Normal
28/08/22	13:41:41	80	100	200	17.0 cm	18.0 Km/Hr	1700.0 mm/Km	1705	2.43	Good	25.7495203	N	84.5407206	E	Normal
28/08/22	13:42:09	80	100	300	25.0 cm	12.4 Km/Hr	2500.0 mm/Km	2447	3.36	Good	25.7501802	N	84.5410334	E	Normal
28/08/22	13:42:50	80	100	400	11.0 cm	19.2 Km/Hr	1100.0 mm/Km	1148	1.71	Good	25.7513266	N	84.5414912	E	Normal
28/08/22	13:43:18	80	100	500	12.0 cm	12.7 Km/Hr	1200.0 mm/Km	1241	1.83	Good	25.7516127	N	84.5419927	E	Normal
28/08/22	13:43:38	80	100	600	26.0 cm	18.3 Km/Hr	2600.0 mm/Km	2540	3.47	Good	25.7524595	N	84.5412318	E	Normal
28/08/22	13:43:59	80	100	700	16.0 cm	16.7 Km/Hr	1600.0 mm/Km	1612	2.31	Good	25.7527437	N	84.5407263	E	Normal
28/08/22	13:44:41	80	100	800	12.0 cm	19.0 Km/Hr	1200.0 mm/Km	1241	1.83	Good	25.7529383	N	84.5389964	E	Normal
28/08/22	13:45:15	80	100	900	12.0 cm	10.1 Km/Hr	1200.0 mm/Km	1241	1.83	Good	25.7530565	N	84.5381648	E	Normal
28/08/22	13:45:40	80	100	1000	23.0 cm	14.5 Km/Hr	2300.0 mm/Km	2262	3.13	Good	25.7531748	N	84.5370814	E	Normal
28/08/22	13:46:03	80	100	1100	30.0 cm	15.6 Km/Hr	3000.0 mm/Km	2911	3.92	Good	25.7533617	N	84.5360056	E	Normal
28/08/22	13:46:39	80	100	1200	21.0 cm	10.2 Km/Hr	2100.0 mm/Km	2076	2.9	Good	25.7534590	N	84.5350291	E	Normal
28/08/22	13:47:08	80	100	1300	6.0 cm	22.1 Km/Hr	600.0 mm/Km	684	1.08	Good	25.7535086	N	84.5341670	E	Normal
28/08/22	13:47:44	80	100	1400	7.0 cm	10.1 Km/Hr	700.0 mm/Km	777	1.21	Good	25.7535009	N	84.5331065	E	Normal
28/08/22	13:48:13	80	100	1500	19.0 cm	12.2 Km/Hr	1900.0 mm/Km	1890	2.67	Good	25.7534800	N	84.5320641	E	Normal
28/08/22	13:48:30	80	100	1600	20.0 cm	20.6 Km/Hr	2000.0 mm/Km	1983	2.78	Good	25.7534761	N	84.5314433	E	Normal
28/08/22	13:49:03	80	100	1700	2.0 cm	10.5 Km/Hr	200.0 mm/Km	313	0.54	Good	25.7533617	N	84.5299784	E	Normal
28/08/22	13:49:39	80	100	1800	7.0 cm	10.8 Km/Hr	700.0 mm/Km	777	1.21	Good	25.7532473	N	84.5290247	E	Normal
28/08/22	13:50:09	80	100	1900	4.0 cm	11.0 Km/Hr	400.0 mm/Km	499	0.81	Good	25.7531824	N	84.5284525	E	Normal
28/08/22	13:50:39	80	100	2000	22.0 cm	12.8 Km/Hr	2200.0 mm/Km	2169	3.02	Good	25.7528620	N	84.5269872	E	Normal
28/08/22	13:51:25	80	100	2100	6.0 cm	17.8 Km/Hr	600.0 mm/Km	684	1.08	Good	25.7526045	N	84.5258662	E	Normal

8.08.22

Deepu

Deepu

Deepu

Name of work		: NH-19 - Jhausa(Goraiapur)Pakauliya													
Name of customer		: Deepu Construction Prop-Ram Pukar Singh													
(R)Rural Road															
Good		Average						Poor							
< 4000		4001 - 5000						> 5000							
28/08/22	13.51.45	80	100	2200	4.0 cm	16.5 Km/Hr	400.0 mm/Km	499	0.81	Good	25.7527876	N	84.9254237	E	Normal
28/08/22	13.52.03	80	100	2300	4.0 cm	21.2 Km/Hr	400.0 mm/Km	499	0.81	Good	25.7540789	N	84.9254994	E	Normal
28/08/22	13.52.34	80	100	2400	9.0 cm	11.2 Km/Hr	900.0 mm/Km	962	1.46	Good	25.7544451	N	84.9254923	E	Normal
28/08/22	13.52.52	80	100	2500	7.0 cm	20.6 Km/Hr	700.0 mm/Km	777	1.21	Good	25.7544451	N	84.9254923	E	Normal
28/08/22	13.53.14	80	100	2600	6.0 cm	16.5 Km/Hr	600.0 mm/Km	684	1.08	Good	25.7568121	N	84.9255534	E	Normal
28/08/22	13.53.50	80	100	2700	5.0 cm	29.8 Km/Hr	500.0 mm/Km	591	0.94	Good	25.7570410	N	84.9245615	E	Normal
28/08/22	13.54.20	80	100	2800	10.0 cm	22.0 Km/Hr	1000.0 mm/Km	1055	1.59	Good	25.7571058	N	84.9238596	E	Normal
28/08/22	13.54.47	80	100	2900	17.0 cm	13.9 Km/Hr	1700.0 mm/Km	1705	2.43	Good	25.7571248	N	84.9226923	E	Normal


Barinder Singh
29/08/22

Deepu Singh
29/08/22
A.E.

Deepu Singh
29/08/22

4.31

Name of Customer: Deepu Construction Prop Ram Pakar Singh, Machine no: 19205, Road: NH-19 - Jhau(Goripur)/Pakauli, Date: 28.08.22, Section No: 80, Equation: $Y=0.928X+127.3$

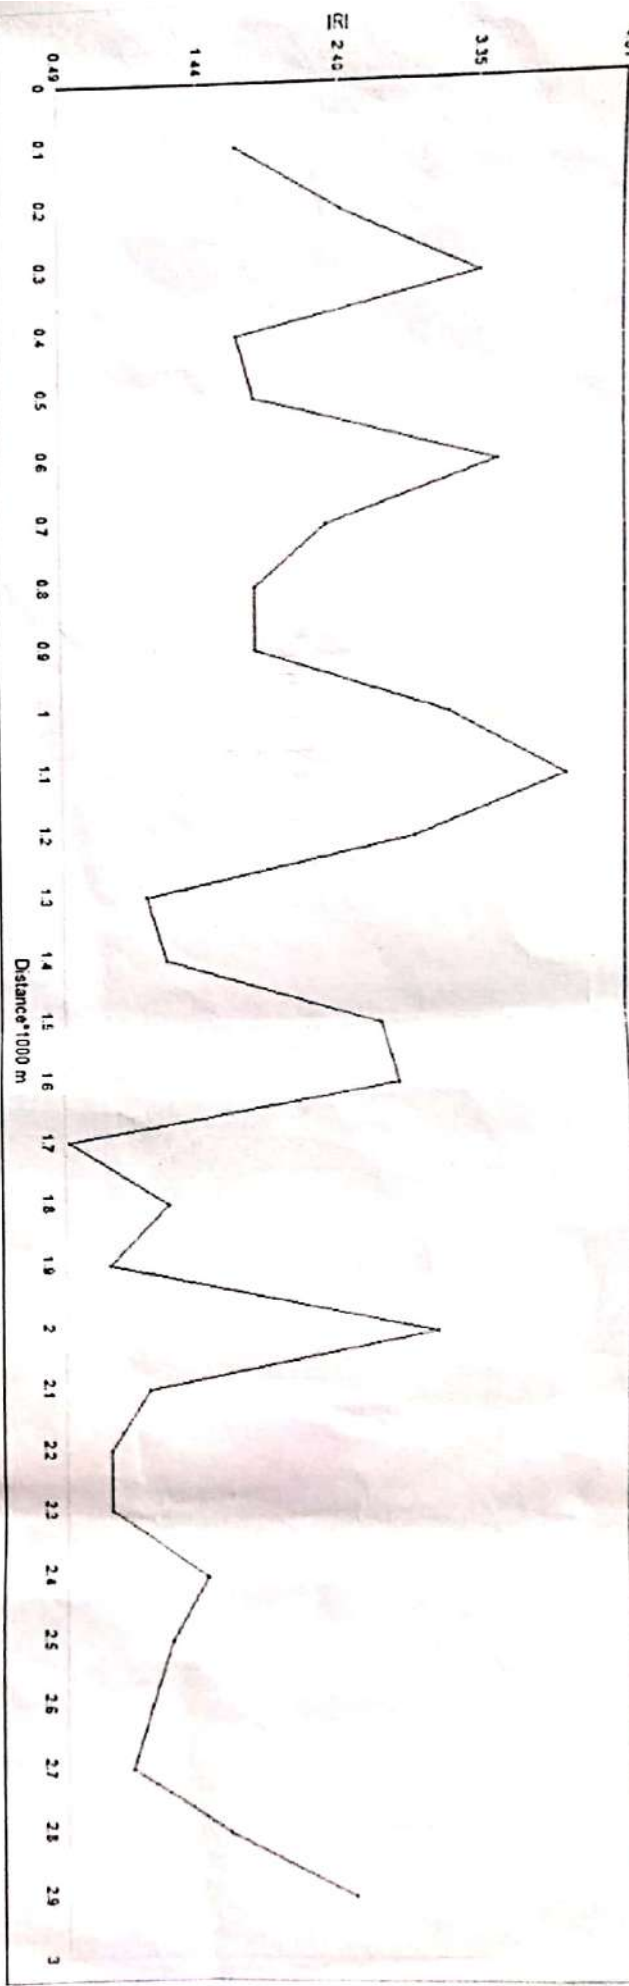

Signature
28/8/22

Signature
29/8/22
A.E.

Signature
29/8/22

1st and final Bill

Name of work—
 Situation of work—
 Agency by which work is executed—
 Date of measurement—
 No. and date of agreement.
 (These four lines should be repeated at the commencement of the measurements relating to each work.)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of Work—					M.R. to NH-19
					Jharkhand (Gorakhpur) Pakauliya
Package No—					M.R. N/19-20
					Scoopur/13.
Name of Agency—					Dipu
					Construction.
Agreement No—					22 MBD/2021-22
D.O.S—					20.12.2021
D.O.C—					19.12.2022
Date of Entry—					10.6.2022
① Clearing and grubbing					
road Land—40—40					
etc.					
	2	15	30	1.00	900.00
	2	30	30	1.00	1800.00
	2	8	30	1.00	480.00
	2	10	1.00		20.00
	2	20	30	1.00	1200.00
	2	20	30	1.00	1200.00
	2	3	30	1.00	180.00
	2	10	1.00		20.00
					5800.00
					= 0.58 Hek

Continuation

Sch. XLV—Form No. 134

Sch. XLV—Form No. 134					Contents of area
Particulars	Details of actual measurement				
	No.	L.	B.	D.	
<u>ABSTRACT OF COST</u>					
(1) clearing and grubbing					
Road Land.					
vide T.M.B.P. — (1)					
0.584 Hec	of	49496.70/Hec			28708.00
(2) construction of sub-					
grade and earthen					
shoulder.					
etc					
vide T.M.B.P. —					
(14)					
2131.00	of	176.75/4 ³			376654.00
2067.00					365342.00
(3) construction of G.S.B.					
and					
all complete for					
vide T.M.B.P. — (2)					
97.146	of	2534.26/4 ³			246193.00
(4) providing and laying					
W.B.M. gully					
etc					
vide T.M.B.P. — (5)					
99.989	of	4892.98/4 ³			489244.00
(5) providing and laying					
W.B.M. gully					
vide T.M.B.P. — (8)					
138.93	of	4284.53/4 ³			595250.00
Continuation					

Continuation

Cost 1736049.00

Sch. XLV—Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	Q.	
			B.P.		Rs 1736045.00
(6) providing and applying primer coat.					
vide T.M.B.P. (9)					
1852.40 sq m^2 C.B.		41.35 m^2			Rs 76597.00
(7) providing and laying tack coat.					
vide T.M.B.P. (9)					
1852.40 sq m^2 C.B.		14.02 m^2			Rs 25971.00
(8) providing and laying and rolling of close road primer surface					
to etc. patch work on L.B.M. surface					
vide T.M.B.P. (9)					
1852.40 sq m^2 C.B.		229.85 m^2			Rs 425774.00
(9) providing and applying tack coat over B.P. surface to etc.					
vide T.M.B.P. (10)					
10867.50 sq m^2 C.B.		12.19 m^2			Rs 132475.00
(10) providing and laying S.D.B.C. to etc.					
vide T.M.B.P. (11)					
271.69 sq m^2 C.B.		1152593 m^2			Rs 3131503.00
(11) providing and applying R.C.C. K.M. stone					

Continuation

Cof 5528369.00

