

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, बारसोई (कटिहार)

Mob. No- 8986915775

E-Mail Id :- rwd.barsoi@gmail.com

पत्रांक632...../

बारसोई, दिनांक.....26/04/2023/

प्रेषक:- कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बारसोई, (कटिहार)

सेवा में,
अपर मुख्य कार्यपालक पदाधिकारी
BRRDA, 3rd Floor भूमि विकास बैंक भवन,
बिहार, पटना।

विषय : शीर्ष 3054 अंतर्गत बिहार ग्रामीण पथ अनुरक्षण नीति-2018 के तहत स्वीकृत कार्यों का आवंटन उपलब्ध कराने के सम्बन्ध में।

प्रसंग:- भवदीय का पत्रांक 4843 दिनांक 06.12.2021

महाशय,

उपर्युक्त विषयक एवं प्रासंगिक पत्र के आलोक में ग्रामीण कार्य विभाग, कार्य प्रमंडल, बारसोई, कटिहार के अधीन शीर्ष 3054 अंतर्गत बिहार ग्रामीण पथ अनुरक्षण नीति-2018 के तहत स्वीकृत कार्यों में निधि उपलब्ध कराने हेतु अधियाचना विहित प्रपत्र में तैयार कर आपके अग्रेतर कार्रवाई हेतु समर्पित किया जाता है।

अतः आप से अनुरोध है कि आवंटन शीघ्र उपलब्ध कराने की कृपा की जाय।
अनु०- यथोक्त।

विश्वास भाजन



कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बारसोई, कटिहार



26/4/23

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, बारसोई (कटिहार)

Mob. No- 8986915775

E-Mail Id :- rwd.barsoi@gmail.com

पत्रांक/

बारसोई, दिनांक...../

प्रेषक:-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बारसोई, (कटिहार)

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी
BRRDA, 3rd Floor भूमि विकास बैंक भवन,
बिहार, पटना।

विषय :

शीर्ष 3054 अंतर्गत बिहार ग्रामीण पथ अनुसंधान नीति-2018 के तहत स्वीकृत कार्यों का
आवंटन उपलब्ध कराने के सम्बन्ध में।

प्रसंग:-

भवदीय का पत्रांक 4843 दिनांक 06.12.2021

महाशय,

उपर्युक्त विषयक एवं प्रासंगिक पत्र के आलोक में ग्रामीण कार्य विभाग, कार्य प्रमंडल,
बारसोई, कटिहार के अधीन शीर्ष 3054 अंतर्गत बिहार ग्रामीण पथ अनुसंधान नीति-2018 के तहत
स्वीकृत कार्यों में निधि उपलब्ध कराने हेतु अध्याचना विहित प्रपत्र में तैयार कर आपके अग्रेतर
कार्रवाई हेतु समर्पित किया जाता है।

अतः आप से अनुरोध है कि आवंटन शीघ्र उपलब्ध कराने की कृपा की जाय।

अनु0- यथोक्त।

विश्वास भाजन

६०

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बारसोई, कटिहार

ज्ञापांक632..... दिनांक26/04/2023

प्रतिलिपि - नोडल पदाधिकारी, 3054 MR, ग्रामीण कार्य विभाग, बिहार पटना को सूचनार्थ एवं
आवश्यक कार्रवाई हेतु समर्पित।




कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बारसोई, कटिहार
26/4/23

Rural Works Department, Works Division, Barsoi, Katihar.

MIR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Initial Rectification and Surface Renewal)

Name of Division :- Barsoi (Katihar)

Sl No	Package No.	Name Of Road	Project ID as per MIS	Administrative Approval (AA) Letter No./ Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of Bitumen Layer (in mm)	Thicknes ss of Bitumen Layer (in mm)	Value of Bitumen content in Percentage	Previous Tola Allotted Amount (In Lkh)	up-to-date expenditure as per MIS (In Lakh)	Total Value of Measurement (In Lakh)	Requisition against work done. (In Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20
1	MR-N/22-23 BARSOI/08	DASGAON - UDAIPUR	21105502034	2011 / 02.05.2022	2.130	207.91300	146.71290	26.93509	27 MBD/2022-23	08.12.23	On Going	-	-	-	0.00	0.000	0.000	0.00	
		BELAURI-SONALI R.C.D. ROAD AT DUKHRA - SISIA (Bishanpur)	21105502026		3.985	337.82100	197.59457	54.41640			On Going	2703.62	25mm	5.1%	0.00	0.000	107.87012	107.87012	
		Khidirpur Chunari Tola to Khidirpur Dhum tola	21105612012		2.296	94.94500	57.49574	24.56466			On Going	2783.09	25mm	5.1%	0.00	0.000	39.29002	39.29002	
		Chandi Chowk to Rampur Ghat Ajannagar Sima Tak	21105612020		3.398	134.99200	79.51239	37.13808			On Going	2811.94	25mm	5.1%	0.00	0.000	59.45220	59.45220	
2	MR-N/22-23 BARSOI /01	L051-T02 Bariol to Chapakhori	21105602100	1304 / 23.03.2022	2.348	99.20700	54.45394	29.23061	13 MBD/2022-23	18.08.23	On Going	-	-	-	0.00	0.000	0.000	0.00	
		Govindpur Machuya Tola to Balrampur Bargach.	21105612013		0.944	66.65100	46.84564	10.52601			On Going	-	-	-	0.00	0.000	0.000	0.00	
		Imadpur Hat to Raghunathpur Begam Chowk.	21105613005		4.448	236.57200	155.13395	46.84045			On Going	-	-	-	0.00	0.000	0.000	0.00	
					19.549	1178.10100	737.74913	229.65130							0.00000	0.00000	206.61234	206.61234	
				Total :-															


 Executive Engineer
 R.W.D. Works Division
 Barsoi, Katihar



EXECUTIVE ENGINEER, RURAL WORKS DEPARTMENT, WORKS DIVISION, BARSOI, KATIHAR

FROM GFR 19 - A

(See Government of India's Decision (I) Below Rule - 150)
Form of Utilisation Certificate

Sl. No.	Name of Scheme	Sanctioned No. Date with Amount (in Lacs Rs.)	Amount Received (in Lacs Rs.)	Particulars
1	2	4	5	6
1	MR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Year-2021-22 & 2022-23)	MR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Year- 2021-22 & 2022-23) Lt. No. 32 Dt- 28.05.2021 Lt. No. 40 Dt- 14.06.2021 Lt. No. 05 Dt- 25.01.2022 Lt. No. 10 Dt- 21.02.2022 Lt. No. 49 Dt- 27.04.2022 Lt. No. 22 Dt- 08.08.2022 Lt. No. 12 Dt- 03.02.2023 Lt. No. 35 Dt- 14.03.2023 Lt. No. 42 Dt- 20.03.2023	1255.83725	Certified that out of Rs.- 1255.83725 Lakh of grants in aid sanctioned during the Years 2021-22 & 2022-23 In Favour of Executive Engineer, Rural Works Department, Works Division, Barsoi sum of Rs.- 1250.71249 Lakh has been utilized for the purpose of MR(3054) under Bihar Rural Road Maintenance Policy- 2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs.- 5.12476 Lakh remaining unutilized at the end of the period under report purpose.
	Total -		1255.83725	

- 2 Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose fo

Kind of Checks Exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test checks conducted by the Assistant Engineer/ Executive Engineer.
- All other codal formatities have been observed.

3 **Physical Progress achieved :-**

- Construction of Road Works.
- Construction of CD. Works.

W
26/4/23

[Signature]
26/4/23
Executive Engineer
Rural Works Department
Works Division, Barsoi, Katihar
26/4/23

MR-N 22-23 BASOI / 01

(1) Khidirpur chinnu tula to khidir Durgam

Schedule XLV-Form No. 134

(1) ~~Chinnu tula to Khidir Durgam~~ ~~to Khidir Durgam~~

(1) ~~lost~~

13-5-B-D-22-23
Durgam
Durgam

DIVISION

SUB-DIVISION

MEASUREMENT BOOK

1982

Khidirpur MR - Barpoic Block

Name of work—

1

Situation of work—

Agency by which work is executed—

Date of measurement—

No. and date of agreement.

(These four lines should be repeated at the commencement of the measurements relating to each work.)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
1st on A/c bill					
Name of Work: ^{conf. and measurement of} Khidirpur Chunarri					
Tola to Khidirpur Ghum					
Tola					
Agency: Jawahar Lal Yadav					
Agreement No - 13 MBO/2022-23					
Date of start - 19.8.2022					
Date of Completion - 18.8.2023					
Date of Measurement - 05.04.2023					
1. Providing and fixing logo					
of project --- etc					
01 No.					
2. Clearing and grubbing					
of road land --- etc					
$2 \times 18 \times 30.0 \text{ m} \times 1.0 \text{ m} = 1080.0 \text{ m}^2$					
$2 \times 14 \times 30.0 \text{ m} \times 1.0 \text{ m} = 840.0 \text{ m}^2$					
$2 \times 19 \times 30.0 \text{ m} \times 1.0 \text{ m} = 1140.0 \text{ m}^2$					
$2 \times 17 \times 30.0 \text{ m} \times 1.0 \text{ m} = 1020.0 \text{ m}^2$					
$2 \times 8 \times 30.0 \text{ m} \times 1.0 \text{ m} = 480.0 \text{ m}^2$					
$2 \times 16.0 \text{ m} \times 1.0 \text{ m} = 32.0 \text{ m}^2$					
$\frac{4592.0 \text{ m}^2}{100} = 0.4592 \text{ Hae.}$					
3. Construction of granular					
Sub-base (CISB grading - II					
Material) --- etc					

Continuation

Continuation

**Executive Engineer
Rural Works Department
Works Division, Barsoi**

Lab Job number :13

Date :23-04-2023

Name of Customer :Jawahar Lal Yadav

Name of Work/ Road :Khidirpur Chunari Tola To Khidirpur Dhum Tola

Sr.no	Location of test (in km)	Corrected U.I value (mm/km)	Road catagory
1	0.100	2690	G
2	0.200	2884	G
3	0.300	3078	G
4	0.400	2981	G
5	0.500	2787	G
6	0.600	2884	G
7	0.700	2593	G
8	0.800	2884	G
9	0.900	2400	G
10	1.000	2690	G
11	1.100	2884	G
12	1.200	3175	G
13	1.300	2787	G
14	1.400	2981	G
15	1.500	3078	G
16	1.600	2497	G
17	1.700	2690	G
18	1.800	2787	G
19	1.900	2400	G
20	2.000	2303	G
21	2.100	3078	G
22	2.200	2593	G
23	2.300	2887	G
Average IRI Value		2783.09	

[Signature]
25.04.2023
OT

[Signature]
25-04-23
AC

[Signature]
26/04/23
Executive Engineer
Rural Works Department
Works Division, Barsoi

Lab Job number :13
Date :23-04-2023

Name of Customer :Jawahar Lal Yadav

Name of Work/ Road :Khidilpur Chunari Tola To Khidilpur Dhum Tola

Date	Time	Section No.	Length ih km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
23/4/23	9:3:0	13	0.1	270	0	2700	2690	G	25.59424	87.92955	Speed Breaker
23/4/23	9:3:48	13	0.1	290	10.1	2900	2884	G	25.59379	87.92884	Normal
23/4/23	9:4:23	13	0.1	310	10.1	3100	3078	G	25.59374	87.92783	Normal
23/4/23	9:5:0	13	0.1	300	10.1	3000	2981	G	25.59305	87.92724	Normal
23/4/23	9:6:9	13	0.1	280	10.1	2800	2787	G	25.59263	87.92658	Normal
23/4/23	9:7:0	13	0.1	290	10.1	2900	2884	G	25.59176	87.92660	Normal
23/4/23	9:7:19	13	0.1	260	10.1	2600	2593	G	25.59086	87.92687	Normal
23/4/23	9:7:19	13	0.1	290	10.1	2900	2884	G	25.58994	87.92684	Culvert
23/4/23	9:8:0	13	0.1	240	10.1	2400	2400	G	25.58902	87.92673	Normal
23/4/23	9:8:0	13	0.1	270	20.2	2700	2690	G	25.58813	87.92660	Culvert
23/4/23	9:8:30	13	0.1	290	10.1	2900	2884	G	25.58745	87.92689	Normal
23/4/23	9:8:30	13	0.1	320	10.1	3200	3175	G	25.58678	87.92736	Curve
23/4/23	9:9:5	13	0.1	280	20.2	2800	2787	G	25.58670	87.92840	Curve
23/4/23	9:9:5	13	0.1	300	20.2	3000	2981	G	25.58730	87.92904	Normal
23/4/23	9:10:0	13	0.1	310	10.1	3100	3078	G	25.58814	87.92928	Normal
23/4/23	9:10:50	13	0.1	250	10.1	2500	2497	G	25.58835	87.93000	Normal
23/4/23	9:11:25	13	0.1	270	10.1	2700	2690	G	25.58737	87.93017	Normal
23/4/23	9:11:25	13	0.1	280	10.1	2800	2787	G	25.58639	87.93030	Normal
23/4/23	9:12:0	13	0.1	240	10.1	2400	2400	G	25.58568	87.93072	Normal
23/4/23	9:12:35	13	0.1	230	10.1	2300	2303	G	25.58517	87.93152	Normal
23/4/23	9:13:11	13	0.1	310	10.1	3100	3078	G	25.58459	87.93241	Normal
23/4/23	9:13:11	13	0.1	260	10.1	2600	2593	G	25.58422	87.93322	Culvert
23/4/23	9:14:0	13	0.093	270	10.1	2903	2887	G	25.58350	87.93382	Normal

$$Y = 0 \cdot X^2 + 0.969 \cdot X + 74.60$$

$$X = 2903$$

$$Y = 2887$$


(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

25-04-2023
52

25-04-23
95 KC

Executive Engineer
Rural Works Department
Works Division, Barsol

File : E:\RAM KUMAR\MISC Files\Bump integrator\Barson\Khidirpur Chunari Tola To Khidirpur Dhum
 Name of Customer : Jawahar Lal Yadav, Name of Work/ Road : Khidirpur Chunari Tola To Khidirpur Dhum Tola Lab

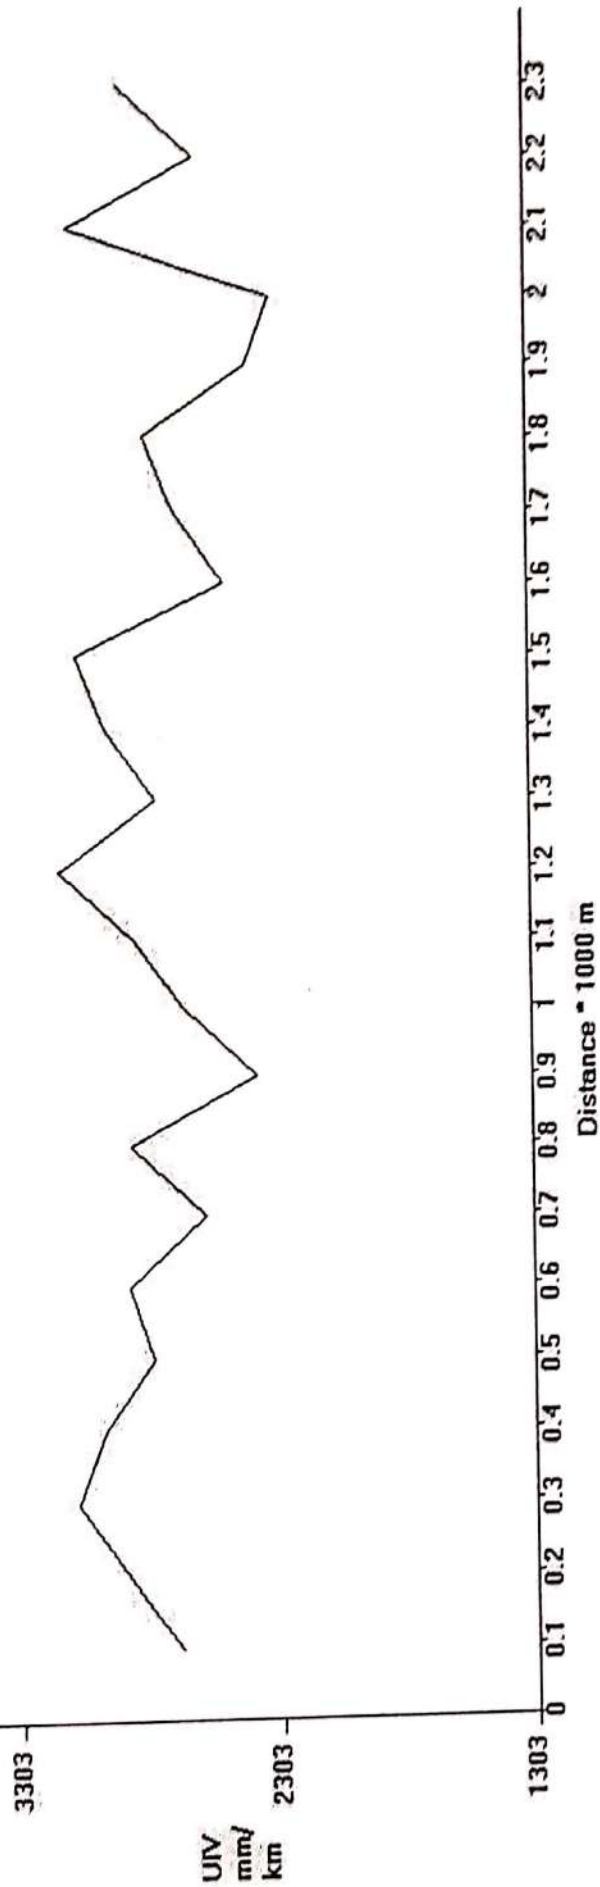

Handwritten signature
 25.04.2019
 22

Handwritten signature
 Executive Engineer
 Rural Works Department
 Works Division, Barsol
