

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग कार्य प्रमंडल, बेनीपट्टी।

पत्रांक...07/95

दिनांक...03.1.2023

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बेनीपट्टी।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय:-

शीर्ष **NEW MAINTENANCE POLICY - 2018 (MR - 3054)** में आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में कहना है शीर्ष **NEW MAINTENANCE POLICY - 2018 (MR-3054)** अन्तर्गत पथ में संलग्न विवरणी के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय ताकि संवेदक का भुगतान किया जा सके।

अनु०:-

1. अध्याचना प्रमाण पत्र 1 पृष्ठ में।
2. उपयोगिता प्रमाण पत्र एक प्रति।

विश्वासभाजस

2036/
29/1/22
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बेनीपट्टी।

Formate of Requisition under Head New Maintenace policy - 2018 (MR- 3054) for the month of December- 2022

Name of Division :- Benipatti

SI No.	Package No.	Name of road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Alloted Amount (In Lakh)	up-to-date expenditure as par MIS (In Lakh)	Requisition against work done (In Lakh)	Remarks
					Length (In km)	Amoun of (in lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Year Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/MA/BEN/19/ 0003	Paraul to Ghuskipatti	31910002058	1859/ 24.06.2019	3.090	112.92940	68.38029	26.90769	17MBD/21-22 23.09.2021	22.09.2022	22.12.2022	2957	25	5	0.00	0.00	68.20067	Work Completed
Total					3.090	112.92940	68.38029	26.90769	—	—	—	2957	25	5	0.00000	0.00000	68.20067	

Divisional Account Officer,
R.W.D(W)Div. Benipatti

Executive Engineer
R.W.D(W)Div. Benipatti

FORM GFR 19-A

(See Government of India's Decision (I) below Rule-150)

Form of Utilisation Certificate Upto the month of 30 November 2022

New Maintenance policy - 2018

PIU – Executive Engineer, R.W.D (W) Division, Benipatti

SL. No	Name of Gen.heme	Sanction No. & Date with Amount (In Rs. lacs)	Amount Received (In Rs. lacs)	Particulars
1	Construction of Rural roads under New maintenance policy - 2018	Authorization letter No. 48 we dt- 30.11.2022 Rs.222.06922	1298.31049	Certified that out of Rs.1298.31049 Lakh received during the years up to 2022-23 (30 November2022) in favour of Ex. Engineer, RWD (W) Division Benipatti, Madhubani, Bihar, a sum of Rs. 1075.62660 Lakh has been utilized for the purpose of New maintenance policy-2018 as given in the margin for which the balance of Rs 222.68389 Lakh remaining unutilized at the end of the period under.

2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer/Executive Engineer.
- All other codal formalities have been observed.

3. Physical Progress achieved:-

- Construction of Road Works.
- Construction of CD Works.


Divisional Account Officer,
R.W.D (W) Division
Benipatti



Executive Engineer
R.W.D (W) Division
Benipatti

OFFICE OF THE EXECUTIVE ENGINEER
RWD WORKS DIVISION
BENIPATTI

Name of Scheme:- Construction of Paraul to Ghuskipatti. , Package No. - RM/MA/BEN/19/ 0003


Project ID - 31910002058

**Certified that all item wise 100%
measurement has been taken by
me**


30/12/22
Junior Engineer

**RWD Work Section Benipatti-1
Works Division Benipatti**

**Certified that all item wise 50%
measurement has been Cheked by
me**


30/12/2022

**Assistant Engineer
RWD Work Sub Division Benipatti
Works Division Benipatti**

**Certified that all item wise 10%
measurement has been Cheked by
me**


30/12/22
Executive Engineer

**RWD Works Division
Benipatti**

Name of work :	PARAUL TO GHUSKIPATTI
Name of customer :	SUSHEEL KUMAR CHAUDHARI
(R)Rural Road	
Good	Average
< 4000	4001 - 5000
	Poor
	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
21/12/22	14:40:57	12	100	100	28.0 cm	0.0 Km/Hr	2800.0 mm/Km	2921	3.93	Good	26.460042	N	86.026308	E	Normal
21/12/22	14:41:17	12	100	200	29.0 cm	18.5 Km/Hr	2900.0 mm/Km	3014	4.04	Good	26.459808	N	86.027252	E	Normal
21/12/22	14:41:47	12	100	300	24.0 cm	12.4 Km/Hr	2400.0 mm/Km	2550	3.49	Good	26.459586	N	86.028136	E	Normal
21/12/22	14:42:13	12	100	400	25.0 cm	13.2 Km/Hr	2500.0 mm/Km	2643	3.6	Good	26.459622	N	86.028894	E	Normal
21/12/22	14:42:40	12	100	500	20.0 cm	13.5 Km/Hr	2000.0 mm/Km	2180	3.03	Good	26.459173	N	86.029485	E	Normal
21/12/22	14:43:00	12	100	600	23.0 cm	17.6 Km/Hr	2300.0 mm/Km	2458	3.37	Good	26.458693	N	86.030587	E	Normal
21/12/22	14:43:19	12	100	700	29.0 cm	19.2 Km/Hr	2900.0 mm/Km	3014	4.04	Good	26.459433	N	86.030923	E	Normal
21/12/22	14:43:44	12	100	800	32.0 cm	14.8 Km/Hr	3200.0 mm/Km	3291	4.38	Good	26.460174	N	86.030626	E	Normal
21/12/22	14:44:27	12	100	900	27.0 cm	8.5 Km/Hr	2700.0 mm/Km	2828	3.82	Good	26.46315	N	86.031538	E	Normal
21/12/22	14:47:03	12	100	1000	22.0 cm	8.5 Km/Hr	2200.0 mm/Km	2365	3.26	Good	26.460536	N	86.033101	E	Normal
21/12/22	14:47:54	12	100	1100	31.0 cm	3.3 Km/Hr	3100.0 mm/Km	3199	4.27	Good	26.460579	N	86.033656	E	Normal
21/12/22	14:48:26	12	100	1200	26.0 cm	11.2 Km/Hr	2600.0 mm/Km	2736	3.71	Good	26.460989	N	86.034529	E	Normal
21/12/22	14:48:48	12	100	1300	22.0 cm	16.0 Km/Hr	2200.0 mm/Km	2365	3.26	Good	26.461514	N	86.035702	E	Normal
21/12/22	14:49:10	12	100	1400	24.0 cm	16.3 Km/Hr	2400.0 mm/Km	2550	3.49	Good	26.461868	N	86.0364	E	Normal
21/12/22	14:49:37	12	100	1500	32.0 cm	13.8 Km/Hr	3200.0 mm/Km	3291	4.38	Good	26.462313	N	86.037296	E	Normal
21/12/22	14:50:15	12	100	1600	35.0 cm	9.3 Km/Hr	3500.0 mm/Km	3569	4.7	Good	26.462334	N	86.03812	E	Normal
21/12/22	14:50:44	12	100	1700	34.0 cm	12.0 Km/Hr	3400.0 mm/Km	3476	4.6	Good	26.462551	N	86.039191	E	Normal
21/12/22	14:51:03	12	100	1800	31.0 cm	17.8 Km/Hr	3100.0 mm/Km	3199	4.27	Good	26.462401	N	86.039943	E	Normal
21/12/22	14:51:21	12	100	1900	22.0 cm	21.0 Km/Hr	2200.0 mm/Km	2365	3.26	Good	26.46325	N	86.040913	E	Normal
21/12/22	14:51:54	12	100	2000	27.0 cm	10.2 Km/Hr	2700.0 mm/Km	2828	3.82	Good	26.462942	N	86.041575	E	Normal
21/12/22	14:58:37	12	100	2100	21.0 cm	3.1 Km/Hr	2100.0 mm/Km	2273	3.14	Good	26.463636	N	86.041914	E	Normal

dy.
J.F

td
A.E.

31/12/22
20/1/23
E.E.

Name of work : PARAUL TO GHUSKIPATTI		
Name of customer : SUSHEEL KUMAR CHAUDHARI		
(R)Rural Road		
Good	Average	Poor
< 4000	4001 - 5000	> 5000

21/12/22	14:59:08	12	100	2200	24.0 cm	11.7 Km/Hr	2400.0 mm/Km	2550	3.49	Good	26.464253	N	86.041875	E	Normal
21/12/22	14:59:55	12	100	2300	30.0 cm	7.5 Km/Hr	3000.0 mm/Km	3106	4.16	Good	26.464349	N	86.041769	E	Normal
21/12/22	15:00:44	12	100	2400	33.0 cm	7.3 Km/Hr	3300.0 mm/Km	3384	4.49	Good	26.465171	N	86.04092	E	Normal
21/12/22	15:01:12	12	100	2500	35.0 cm	12.8 Km/Hr	3500.0 mm/Km	3569	4.7	Good	26.466399	N	86.041109	E	Normal
21/12/22	15:01:30	12	100	2600	37.0 cm	20.0 Km/Hr	3700.0 mm/Km	3754	4.92	Good	26.467217	N	86.041127	E	Normal
21/12/22	15:01:53	12	100	2700	31.0 cm	15.2 Km/Hr	3100.0 mm/Km	3199	4.27	Good	26.467942	N	86.041138	E	Normal
21/12/22	15:02:09	12	100	2800	29.0 cm	23.4 Km/Hr	2900.0 mm/Km	3014	4.04	Good	26.469048	N	86.041545	E	Normal
21/12/22	15:02:36	12	100	2900	28.0 cm	13.2 Km/Hr	2800.0 mm/Km	2921	3.93	Good	26.469741	N	86.04181	E	Normal
21/12/22	15:02:54	12	100	3000	37.0 cm	20.4 Km/Hr	3700.0 mm/Km	3754	4.92	Good	26.470432	N	86.041485	E	Normal
21/12/22	15:03:16	12	100	3100	32.0 cm	16.3 Km/Hr	3200.0 mm/Km	3291	4.38	Good	26.471123	N	86.041801	E	Normal

dy.

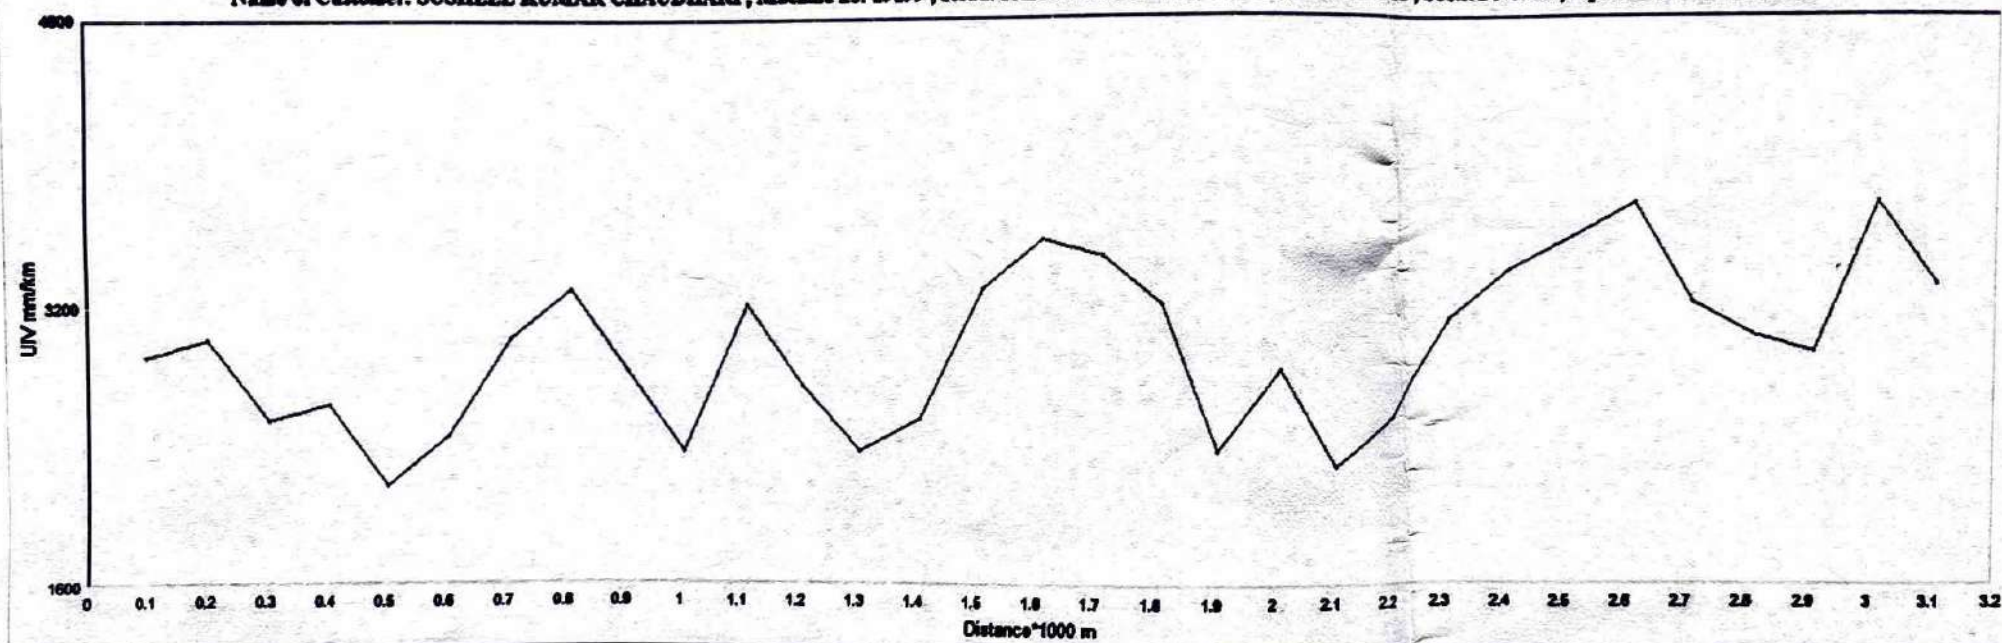
J.E.

dy.

A.E

32V
30/12/22
E.E

Name of Customer: SUSHEEL KUMAR CHAUDHARI, Machine no: 19199, Road: PARAUL TO GHUSKIPATTI, Date: 21/12/22, Section No: 12, Equation: $Y=0.926X+328.1$



[Signature]

S.E.

[Signature]

A-E

35✓
30/12/22
E.E.

1

(These four lines should be repeated at the commencement of the measurements relating to each work.)

14.12.22
JE

14.12.22
A.E

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
<u>Abstract of cost</u>					
(1/2) ^{Grading} Clearing of road land including --- dir E/I Oly vide TMB PNO - (1) 0.927 @ Rs 49496.70/Hec Rs = 45883.200					
(2/3) Cont. of ^{sub grade} SSB G-1 & earthen shoulder --- do --- job. Oly vide TMB PNO (11) 1698.75 M ³ @ Rs 176.75/M ³ Rs = 300254.200					
(3/4) Cont. of GSI G-1 by providing --- job. Oly vide TMB PNO - (3) 97.75 M ³ @ Rs 3189.47/M ³ Rs = 311771.200					
(4/5) Providing & laying spreading & compacting WBM G-3 --- job. Oly vide TMB PNO (4) 128.56 M ³ @ Rs 3907.78/M ³ Rs = 508041.200					
(5/6) P/A prime coat SS 1 --- all comp. job. Oly vide TMB PNO - (6) 1763.10 M ² @ Rs 41.21/M ² Rs = 72657.200					

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(67) P/L & rolling of close graded premix --- all complete job. Qty vide TMB PNo- (7)					
3117.04 M ² @ Rs 211.59/M ² Rs = 659534.20					
(68) P/A Tack coat RS-1 --- all complete job. Qty vide TMB PNo (9)					
14819.24 M ² @ Rs 13.98/M ² Rs = 207173.20					
(89) P/L Semidense Bituminous concrete with --- as per tech sp.					
Qty vide TMB PNo- (11)					
292.555 m ³ @ Rs 10625.43/M ³ Rs = 3108523.20					
(9/14) P&F RCC M-15 km stone --- job. Qty vide TMB PNo- (12)					
3.00 Nos @ Rs 2355.91/Each Rs = 7068.00					
(10/12) P&F 200 mtr stone precast --- Qty vide TMB PNo- (12)					
12.00 Nos @ Rs 635.92/Each Rs = 7631.00					

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(11/13) Providing & erecting direction & Place — Qty vide TMB PNo (12) 1.92m ² @ Rs 12499.99/m ² Rs = 24000=00					
(12/14) RCF retroreflect collimator, mandatory Sign --- Job. 600mm equilateral Tri. Qty vide TMB PNo (12) 37.00nos @ Rs 3707.71/Each Rs = 137185=00					
(13/15) 600mm circular Sign --- Job.					
Qty vide TMB PNo (12) 19.00Nos @ Rs 3841.43/Each Rs = 72987=00					
(14/16) P/F 600mm x 450mm Rectangular Sign --- Qty vide TMB PNo (12) 7.00Nos @ Rs 3711.02/Each Rs = 25977=00					
(15/17) P/F @ 900mm octagonal stop --- Qty vide TMB PNo - (12) 6.00Nos @ Rs 7743.74/Each Rs = 46462=00					

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(16/18) P/L rumble strip with road studs --- Qty vide TMB PNO-13 $7.50 \text{ m}^2 @ \text{Rs } 735.40/\text{m}^2 \text{ Rs} = 5516.00$					
(17/19) P/F RCC M-15 Boundary Pillar --- Qty vide TMB PNO-13 $88.00 \text{ Nos} @ \text{Rs } 528.51/\text{Each} \text{ Rs} = 46509.00$					
(18/21) Planting trees and their mainte --- Qty vide TMB PNO-13 $104.00 \text{ Nos} @ \text{Rs } 800.30/\text{Each} \text{ Rs} = 83231.00$					
(19/22) Road marking :- P/L of hot applied thermo --- job. Qty vide TMB PNO-13 $618 \text{ m}^2 @ \text{Rs } 735.40/\text{m}^2 \text{ Rs} = 454477.00$					
(20/23) P&F Typical NMGSY info. sign --- Qty vide TMB PNO-13 $2.00 \text{ Nos} @ \text{Rs } 11141.70/\text{Each}$ $\text{Rs} = 22283.00$					
(21/24) Brick masonry work with cm (1:4) --- $7.128 \text{ m}^3 @ \text{Qty vide TMB PNO-14}$ $19.256 \text{ m}^3 \text{ " " PNO-15}$ 21.384 m^3 Continuation Limit = $18.40 \text{ m}^3 @ \text{Rs } 5701.64/\text{m}^3$ $\text{Rs} = 104910.00$					

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(22/25) Plastering with Cement mortar ---					
85.76 m ² Qty vide TMB PNo (14)					
257.28 m ² " " PNo - (15)					
343.04 m ² Limit = 248.64 m ²					
@ Rs 45.01/m ² Rs = 171.82					42721.200
(23/26) Providing 1.5 mm Cement punning ---					
85.76 m ² Qty vide TMB PNo (14)					
257.28 m ² Qty vide TMB PNo (15)					
343.04 m ² Limit = 248.64 m ²					
@ Rs = 45.01/m ² Rs =					11191.200

	Rs = 63,05,984.00
Add GST @ 12% Rs = 756718.00	
Add 4/c @ 1% Rs = 63060.00	
	Rs = 71,25,762.00
Less 4.29% (-) Rs = 305695.00	
below.	Rs = 68,20,067.00

22.12.22
JE

22.12.22
A.C
