

**कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, कटिहार।**

पत्रांक :- 1151

/कटिहार, दिनांक- 21-07-23

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।

सेवा में,

अपर-मुख्य-कार्यपालक-पदाधिकारी,
BRRDA, 3री मंजिल, भूमि विकास बैंक भवन,
बिहार, पटना।


विषय :- शीर्ष New Maintenance Policy-2018 योजनान्तर्गत निर्माण हेतु आवंटन की अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष New Maintenance Policy-2018 योजनान्तर्गत ग्रा0का0वि0, कार्य प्रमंडल, कटिहार द्वारा विहित प्रपत्र में अधियाचना तैयार कर आपके अग्रेतर कार्रवाई हेतु समर्पित की जाती है।

अनु0:-यथोक्त।

विश्वासभाजन,


21/07/23


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।



ज्ञापक:- 1151


/कटिहार, दिनांक:- 21-07-23

प्रतिलिपि:- नोडल पदाधिकारी, 3054 MR, ग्रामीण कार्य विभाग, बिहार, पटना को सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।


21/07/23

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,

कार्य प्रमंडल, कटिहार।


21-07-23

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road maintenance Policy 2018 (Initial Rectification and Surface Renewal)

Name of Division : Katihar

Sl. No	Package no.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)	Agreement Amount (in Lac)			Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in percentage	Previous Total Allocated Amount (In Lac)	up to date expenditure as per MIS (In Lac)	Requisition Against work done (In lac)	Remarks
1	MR-N/22-23 KATHAR/02	NH-31 Bajrangbali Chowk to Diwandih	211551894000	1304/ 23.03.22	1.300	121.18700	105.31841	15.22950	05MBD/22-23, 06.12.2022	05.09.2023	-	2899.00	25mm	5.1%	0.00000	0.00000	105.00000	Surface Complete
															0.00000	0.00000	105.00000	

[Signature]
21.10.2023
Divisional Accounts Officer
RWD, Works Division, Katihar

[Signature]
21/7/23
Executive Engineer
RWD, Works Division, Katihar

(See Government of India's Decision (1) below Rule-150)
Form of Utilisation Certificate upto the month of June, 2023

[illegible]

Total :-

5552.86463

2. Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned

Kind of Checks exercised :-

- i. Works have been supervised by Executive Engineer/Superintending Engineer.
 - ii. Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
 - iii. Construction materials have been tested.
 - iv. Measurements have been recorded in the MBs and test check conducted by the Assistant.
 - v. All other codal formalities have been observed.
3. Physical Progress achieved -
 - i. Construction of Road Works.
 - ii. Construction of CD Works.
4. Certified that:-
 - i. Work has been done as per specification and with quality.

Divisional Accounts Officer
RWD, Works Division, Katihar

**Executive Engineer,
WD (W) Division, Katihar.**

RWD (W)
19.07.23

Lab Job number :55


Date :19-07-2023


Name of Customer :Pankaj Kumar Singh

Name of Work/ Road :NH-31 Bajrangwali Chowk To Diwandih

Sr.no	Location of test (in km)	Corrected U.I value (mm/km)	Road catagory
1	0.100	3175	G
2	0.200	2787	G
3	0.300	2593	G
4	0.400	2884	G
5	0.500	2884	G
6	0.600	3078	G
7	0.700	2981	G
8	0.800	2787	G
9	0.900	2690	G
10	1.000	2884	G
11	1.100	2497	G
12	1.200	3175	G
13	1.300	3272	G
Average IRI Value		2899.00	


JE 19.7.23


19/07/23
JC


19/07/23
Executive Engineer
R.W.D (W) Division Katihar

Lab Job number :55
Date :19-07-2023

Name of Customer :Pankaj Kumar Singh

Name of Work/ Road :NH-31 Bajrangwali Chowk To Diwandih

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
19/7/23	10:15:0	55	0.1	320	0	3200	3175	G	25.562388	87.361582	Normal
19/7/23	10:15:0	55	0.1	280	10.1	2800	2787	G	25.561682	87.362172	Normal
19/7/23	10:15:29	55	0.1	260	20.2	2600	2593	G	25.561037	87.362862	Normal
19/7/23	10:16:0	55	0.1	290	10.1	2900	2884	G	25.560200	87.363063	Normal
19/7/23	10:16:4	55	0.1	290	20.2	2900	2884	G	25.559297	87.362978	Normal
19/7/23	10:16:4	55	0.1	310	20.2	3100	3078	G	25.558393	87.362845	Normal
19/7/23	10:16:39	55	0.1	300	20.2	3000	2981	G	25.557475	87.362827	Curve
19/7/23	10:17:0	55	0.1	280	10.1	2800	2787	G	25.556837	87.363400	Normal
19/7/23	10:17:15	55	0.1	270	30.3	2700	2690	G	25.556023	87.363602	Normal
19/7/23	10:17:15	55	0.1	290	30.3	2900	2884	G	25.555045	87.363820	Normal
19/7/23	10:17:15	55	0.1	250	30.3	2500	2497	G	25.554245	87.364090	Curve
19/7/23	10:18:25	55	0.1	320	10.1	3200	3175	G	25.553410	87.364713	Culvert
19/7/23	10:19:16	55	0.1	330	10.1	3300	3272	G	25.552950	87.365690	Normal

$$Y = 0 * X^2 + 0.969 * X + 74.60$$

$$X = 3300$$

$$Y = 3272$$

(R) RURAL ROAD
Good <4000
Average 4001-5000
Poor >5001

19/07/23
19/07/23

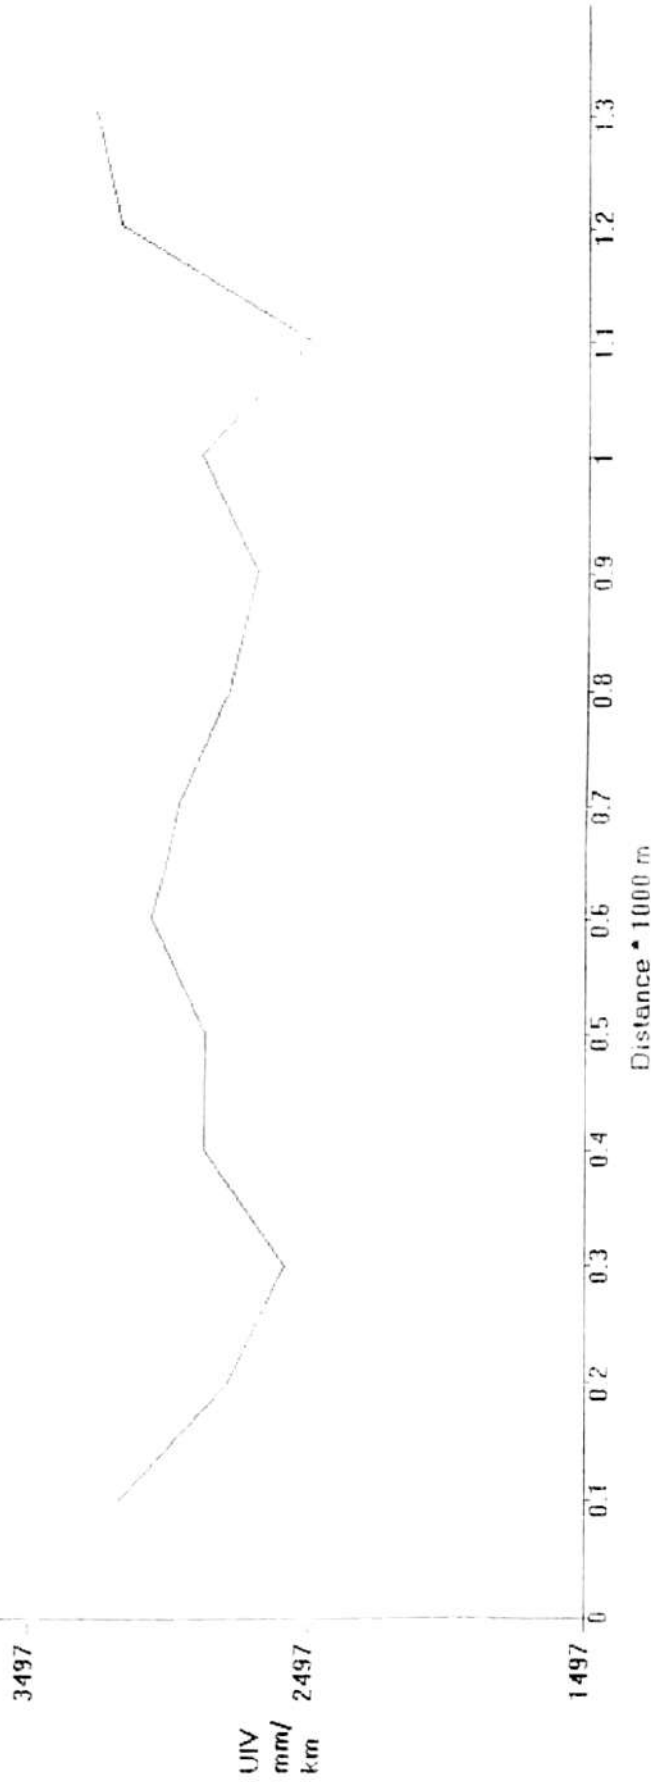
JE 19/7/23

29/07/23

Executive Engineer
R.W.D (W) Division Katihar

File E:\RAM KUMAR\MISC Files\Bump integrator\Korha\NH-31 Bajrangwadi Chowk To Diwandih\19071020.Xls.

Name of Customer Pankaj Kumar Singh, Name of Work/Road NH-31 Bajrangwadi Chowk To Diwandih, Lab Job



[Signature]
21/07/23
Executive Engineer


R.W.D (W) Division Kathihar


[Signature]
19/07/23


[Signature]
21/07/23

प्रमाण पत्र

प्रमाणित किया जाता है कि पथ— NH-31 Bajrangbali Chowk to Diwandih, Project ID- 211551894000 का सभी अवयवों की जाँच शत प्रतिशत कनीय अभियंता द्वारा किया गया है। सहायक अभियंता द्वारा सभी अवयवों की 50 प्रतिशत से अधिक जाँच किया गया है। अधोहस्ताक्षरी द्वारा 10 प्रतिशत अवयवों की जाँच की गई है।


कनीय अभियंता


सहायक अभियंता


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।
