

**कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, कटिहार।**

प्रेषक,

पत्रांक :- 912

/कटिहार, दिनांक- 8/6/23

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।

सेवा में,

अपर-मुख्य-कार्यपालक-पदाधिकारी,
BRRDA, 3रीं मंजिल, भूमि विकास बैंक भवन,
बिहार, पटना।

विषय :- शीर्ष **New Maintenance Policy-2018** योजनान्तर्गत निर्माण हेतु आवंटन की अधियाचना के संबंध में।

महाशय,


उपर्युक्त विषय के संबंध में कहना है कि शीर्ष **New Maintenance Policy-2018** योजनान्तर्गत ग्रा0का0वि0, कार्य प्रमंडल, कटिहार द्वारा विहित प्रपत्र में अधियाचना तैयार कर आपके अग्रेतर कार्रवाई हेतु समर्पित की जाती है।

अनु0:-यथोक्त।

विश्वासभाजन,


08/6/23

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।



ज्ञापांक:- 912

/कटिहार, दिनांक:- 8/6/23

प्रतिलिपि:- नोडल पदाधिकारी, 3054 MR, ग्रामीण कार्य विभाग, बिहार, पटना को सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।


08/6/23

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।



RWD, Works Division, Katihar

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road maintenance Policy 2018 (Initial Rectification and Surface Renewal)

Name of Division : Katihar

Sl. No	Package no.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in percentage	Previous Total Allocated Amount (In Lac)	up to date expenditure as per MIS (In Lac)	Requisition Against work done (In lac)	Remarks	
					Length (In Km)	Amount (in Lac)	Initial Rectification with Surface Renewal (in lac)	5 years Routine Maintenance (In lac)											
1	MR-N/22-23 KATIHAR/05	Majdia Kinara Tola Kharra Tola to Devipur Mahant Asthan	21105512023	1304/23.03.22	1.400	97.51200	82.80452	12.57410	04MBD/22-23, 22.11.2022	21.08.2023	-	3022.57	25mm	5.1%	0.00000	0.00000	82.75000	Surface Complete	
2		NH-31 Devipur to Balthi Maheshpur	21105602044	1304/23.03.22	2.036	105.44300	72.38035	27.94840	04MBD/22-23, 22.11.2022	21.08.2023	-	2848.62	25mm	5.1%	0.00000	0.00000	72.30000	Surface Complete	
3	MR-N/22-23 KATIHAR/04	Bajrangbali Chowk To Morsanda road	21105512001	1304/23.03.22	1.785	101.26600	76.91159	22.17995	03MBD/22-23, 22.11.2022	21.08.2023	-	2820.44	25mm	5.1%	0.00000	0.00000	76.90000	Surface Complete	
4		School Chowk to Nawabganj Basa tola	21105512003	1304/23.03.22	1.400	83.41200	63.02460	16.40675	03MBD/22-23, 22.11.2022	21.08.2023	-	2795.57	25mm	5.1%	0.00000	0.00000	63.02000	Surface Complete	
		Total																294.97000	

21.08.23

Divisional Accounts Officer
RWD, Works Division, Katihar

08/06/23
Executive Engineer
RWD, Works Division, Katihar

(See Government of India's Decision (1) below Rule-150)
Form of Utilisation Certificate upto the month of May, 2023

[illegible]

- i. Works have been supervised by Executive Engineer/Superintending Engineer.
 - ii. Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
 - iii. Construction materials have been tested.
 - iv. Measurements have been recorded in the MBs and test check conducted by the Assistant.
 - v. All other codal formalities have been observed.
3. Physical Progress achieved :-
 - i. Construction of Road Works.
 - ii. Construction of CD Works.
4. Certified that:-
 - i. Work has been done as per specification and with quality.

**Executive Engineer,
RWD (W) Division, Katihar.**

RWD (W) Division, Katihar.

Lab Job number :40

Date :03-06-2023

Name of Customer :Prem Kumar

Name of Work/ Road :Bajrangbali Chowk To Morsanda Road

Sr.no	Location of test (in km)	Corrected U.I value (mm/km)	Road catagory
1	0.100	2497	G
2	0.200	2690	G
3	0.300	2787	G
4	0.400	2593	G
5	0.500	2884	G
6	0.600	2787	G
7	0.700	2690	G
8	0.800	3078	G
9	0.900	2497	G
10	1.000	2884	G
11	1.100	2787	G
12	1.200	2400	G
13	1.300	2690	G
14	1.400	2787	G
15	1.500	2884	G
16	1.600	3175	G
17	1.700	2981	G
18	1.800	3677	G
Avreage IRI Value		2820.44	

Prem Kumar
JB 3.6.23

Prem Kumar
03/06/2023
AG

Prem Kumar
03/06/23
Executive Engineer
R.W.D (W) Division Kalihar

Lab Job number :40
Date :03-06-2023

Name of Customer :Prem Kumar

Name of Work/ Road :Bajrangbali Chowk To Morsanda Road

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY		Latitude	Longitude	Event
									ROAD			
3/6/23	8:23:51	40	0.1	250	0	2500	2497		G	25.49067	87.23529	Culvert
3/6/23	8:24:26	40	0.1	270	20.2	2700	2690		G	25.49184	87.23543	Normal
3/6/23	8:24:26	40	0.1	280	30.3	2800	2787		G	25.49248	87.23541	Normal
3/6/23	8:24:26	40	0.1	260	30.3	2600	2593		G	25.49325	87.23532	Culvert
3/6/23	8:25:2	40	0.1	290	30.3	2900	2884		G	25.49409	87.23542	Normal
3/6/23	8:25:2	40	0.1	280	30.3	2800	2787		G	25.49502	87.23538	Normal
3/6/23	8:25:2	40	0.1	270	20.2	2700	2690		G	25.49603	87.23503	Normal
3/6/23	8:25:37	40	0.1	310	10.1	3100	3078		G	25.49688	87.23491	Speed Breaker
3/6/23	8:26:12	40	0.1	250	10.1	2500	2497		G	25.49789	87.23443	Normal
3/6/23	8:26:12	40	0.1	290	20.2	2900	2884		G	25.49843	87.23432	Normal
3/6/23	8:26:47	40	0.1	280	20.2	2800	2787		G	25.4991	87.23397	Normal
3/6/23	8:26:47	40	0.1	240	20.2	2400	2400		G	25.49989	87.23337	Normal
3/6/23	8:27:23	40	0.1	270	10.1	2700	2690		G	25.50069	87.23331	Normal
3/6/23	8:27:23	40	0.1	280	20.2	2800	2787		G	25.50179	87.23327	Normal
3/6/23	8:27:58	40	0.1	290	10.1	2900	2884		G	25.50246	87.23324	Normal
3/6/23	8:28:33	40	0.1	320	10.1	3200	3175		G	25.50335	87.23317	Normal
3/6/23	8:29:9	40	0.1	300	10.1	3000	2981		G	25.50436	87.23292	Normal
3/6/23	8:30:0	40	0.078	290	10.1	3718	3677		G	25.50529	87.23269	Normal

$$Y = 0 * X^2 + 0.969 * X + 74.60$$
$$X = 3718$$
$$Y = 3677$$

(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

Summu
03/06/2023
APC


Summu
03.06.23

03/06/23

Executive Engineer
R.W.D (W) Division Kaihar

File :E:\RAM KUMAR\MISC Files\Bump integrator\Sameli\Bajrangbali Chowk To Morsanda Road\03060830.Xls.

Name of Customer :Prem Kumar, Name of Work/ Road :Bajrangbali Chowk To Morsanda Road, Lab Job number

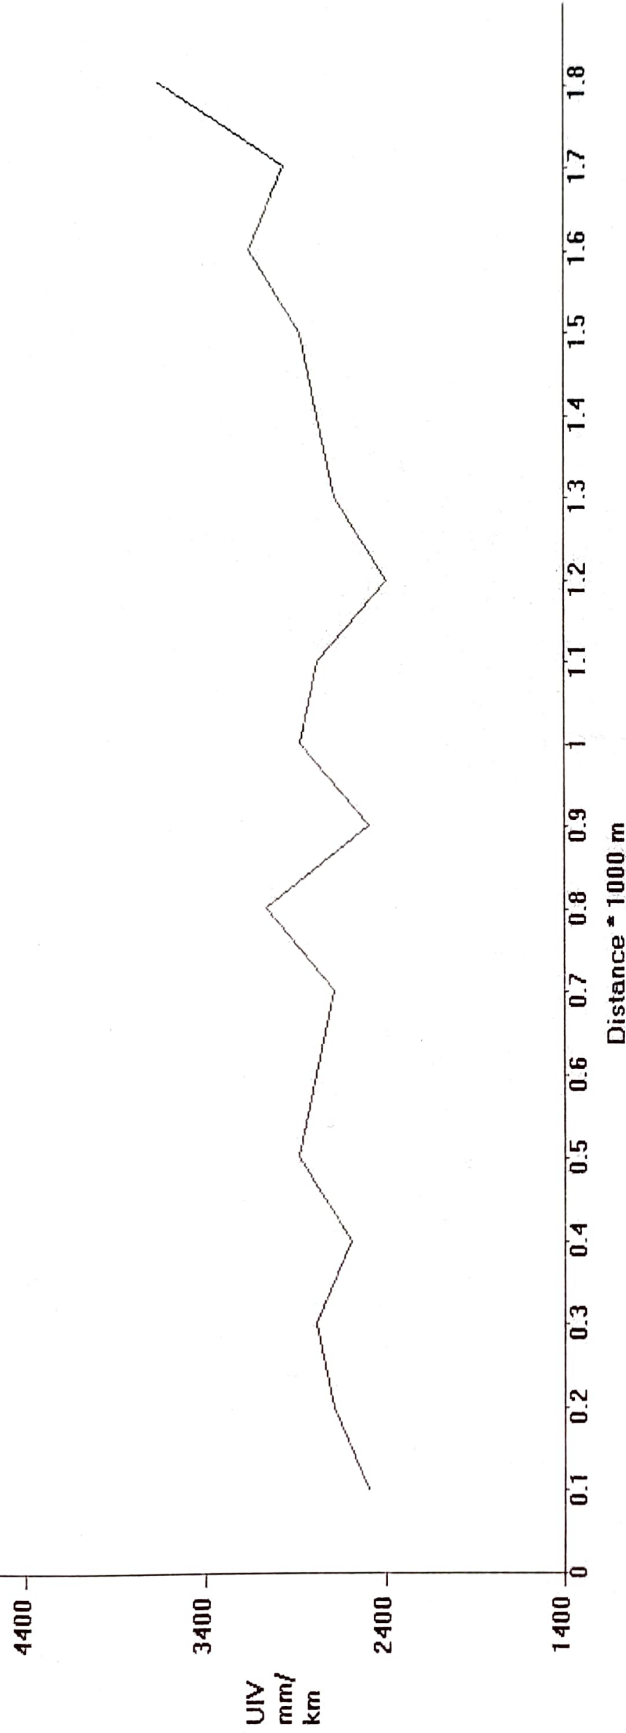

03/06/2023
AF


03/06/23


03/06/23
Executive Engineer

R.W.D (W) Division Kathbar

प्रमाण पत्र

प्रमाणित किया जाता है कि पथ— **Bajrangbali Chowk To Morsanda Road, Project ID- 21105512001** का सभी अवयवों की जाँच शत प्रतिशत कनीय अभियंता द्वारा किया गया है। सहायक अभियंता द्वारा सभी अवयवों की 50 प्रतिशत से अधिक जाँच किया गया है। अधोहस्ताक्षरी द्वारा 10 प्रतिशत अवयवों की जाँच की गई है।


कनीय अभियंता


सहायक अभियंता


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, कटिहार।
