

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, जयनगर
पत्रांक... 853 (3135) जयनगर, दिनांक... 20/06/23

प्रेषक :- कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, जयनगर
सेवा में,
नोडल पदाधिकारी (3054)
ग्रामीण कार्य विभाग
ब्राडा, पटना।

विषय :- MR-3054 (NMP) योजनान्तर्गत चल रहे योजनाओं हेतु आवंटन उपलब्ध कराने के सम्बंध में।

महाशय,

उपर्युक्त विषय के सम्बंध में कहना है कि MR-3054 (NMP) योजना हेतु अधियाचना विहित प्रपत्र में आवश्यक कार्रवाई हेतु समर्पित की जाती है।

अनु०- यथोक्त।

विश्वासभाजन
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल, जयनगर

20.6.23

MIR(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division. Jaynagar																		
Sl No	Package No	Name of the Road (English)	Project ID as per MIS	Administrative Approval (AA) Letter no Date	Administrative Approval (AA)	Agreement Amount (In Lakh)	Initial Rectification and Surface Renewal (in Lakh)	Five Years Routine Maintenance (in Lakh)	Agreement No & Date	Date Completion as per Agreement	Actual Date of Completion	Value of IRI (In mm/Km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (in Lakh)	Up to Date Expenditure as per MIS	Requisition against work done (in Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RNI/MA/JA Y/19/0005	Koriyappati - T04 (SH)	31910002042	Lt-1862 Dt-24.06.2019	3.200	86.20500	62.73675	21.70914	67/NIBD/21-22 03.01.2022	02.01.2023	-	2829	25 mm	5.85%	0.00000	0.00000	62.25793	
2	RNI/MA/JA Y/19/0005	Siriyapur - Gaus Nagar	31910002067	Lt-1862 Dt-24.06.2019	1.800	46.71500	32.88912	11.68341	67/NIBD/21-22 03.01.2022	02.01.2023	-	2860	25 mm	5.8%	0.00000	0.00000	32.86652	

Executive Engineer
RWD, Works Division, Jaynagar

[Signature]
20/6/23

[Signature]
20/6/23

FORM GFR -19 -A
(see Govt. of India's decision (i) below rule 150)
Form of Utilisation Certificate upto June - 2023
Rural Road Maintenance policy-2018

PIU:- R.W.D. Works, Division, Jaynagar

Sl. No.	Name of Scheme	Sanction No.& Date with amount (in Rs. Lakh)	Amount Received (in Rs. Lakh)	Particulars
1	2	3	4	5
1	Construction of Road Under Rural Road Maintenance policy-2018	3207.35417	3207.35417	Certified that out of Rs.3207.35417 Lakh received till date in favour of Ex.Engineer, R.W.D. Works Division, Jaynagar a sum of Rs.3148.47149 Lakh has been utilized for the purpose of Rural Road Maintenance policy-2018 Scheme as given in the margine for which it was sanctioned and that the balance of Rs.58.88268 Lakh remaining unutilized at the end of the period under the time of completion.
		3207.35417	3207.35417	

- 2 Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the propose for which it was sanctioned.

Kind of Checks Exercised :-

- (i) Workers have been supervised by Executive Engineer/ Superintending Engineer
- (ii) Periodical inspection has been conducted by Executive Engineer/Superintending Engineer
- (iii) Construction materials have been tested.
- (iv) Measurments have been recorded in the MB's and test check conducted by the Assistant
- (v) All other codal formalities have overserved

Handwritten signature
20/6/23

Handwritten signature
2.6.23

Handwritten signature
20/04/23
Executive Engineer
Rural works Department
Works Division, Jaynagar




प्रमाण-पत्र

शीर्ष :- 3054 एम0 आर0 (बिहार ग्रामीण पथ अनुस्क्षण निति-2018)

योजना :- Koriyapatti to T04 (SH) (Package No.- RM/MA/JAY/19/0005)

1. मापीपुस्त पर इस आशय का प्रमाण-पत्र दर्ज है कि कार्य गुणवत्तापूर्ण कराया गया है।
2. कराये गये कार्यों के सभी अवयवों के अवयववार 100 प्रतिशत कार्य का दर्ज मापी का सत्यापन कनीय अभियंता, 50 प्रतिशत मापी का सत्यापन सहायक अभियंता एवं 10 प्रतिशत मापी का सत्यापन कार्यपालक अभियंता द्वारा किया गया है।




कनीय अभियंता

कार्य प्रशाखा, बासोपट्टी



सहायक अभियंता

कार्य अवर प्रमंडल, बासोपट्टी



कार्यपालक अभियंता

ग्रामीण कार्य विभाग

कार्य प्रमण्डल, जयनगर

Name of work : Konyapatti To T04
 Name of customer : Ramchandra Yadav

(R) Rural Road	
Good	Average
< 4000	4001 - 5000
	Poor
	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUM(P/cm)	Speed(Km/Hr)	Ultimate(Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
17/06/23	17:42:58	24	0	0	0.0 cm	0.0 Km/Hr	0.0 mm/Km	196	0.35	Good	26.5041034	N	86.0094275	E	Normal
17/06/23	17:42:58	24	100	100	27.0 cm	24.2 Km/Hr	2700.0 mm/Km	2899	3.67	Good	26.5044534	N	86.0096565	E	Normal
17/06/23	17:41:08	24	100	200	30.0 cm	26.1 Km/Hr	3000.0 mm/Km	2977	4	Good	26.5046542	N	86.0092397	E	Normal
17/06/23	17:41:20	24	100	300	25.0 cm	27.6 Km/Hr	2500.0 mm/Km	2514	3.44	Good	26.5052012	N	86.0105926	E	Normal
17/06/23	17:41:31	24	100	400	33.0 cm	32.4 Km/Hr	3300.0 mm/Km	3255	4.33	Good	26.5056872	N	86.0112537	E	Normal
17/06/23	17:41:46	24	100	500	29.0 cm	24.2 Km/Hr	2900.0 mm/Km	2885	3.89	Good	26.5063048	N	86.0116386	E	Normal
17/06/23	17:42:00	24	100	600	35.0 cm	25.6 Km/Hr	3500.0 mm/Km	3441	4.55	Good	26.5070535	N	86.0121707	E	Normal
17/06/23	17:42:21	24	100	700	31.0 cm	22.3 Km/Hr	3100.0 mm/Km	3070	4.11	Good	26.5071515	N	86.0125907	E	Normal
17/06/23	17:42:38	24	100	800	29.0 cm	21.9 Km/Hr	2900.0 mm/Km	2885	3.89	Good	26.5074433	N	86.0142410	E	Normal
17/06/23	17:42:50	24	100	900	26.0 cm	28.2 Km/Hr	2600.0 mm/Km	2607	3.55	Good	26.5082087	N	86.0148359	E	Normal
17/06/23	17:43:01	24	100	1000	34.0 cm	31.9 Km/Hr	3400.0 mm/Km	3348	4.44	Good	26.5085737	N	86.0150409	E	Normal
17/06/23	17:43:14	24	100	1100	23.0 cm	30.6 Km/Hr	2300.0 mm/Km	2326	3.21	Good	26.5094777	N	86.0157059	E	Normal
17/06/23	17:43:29	24	100	1200	32.0 cm	26.7 Km/Hr	3200.0 mm/Km	3163	4.22	Good	26.5105537	N	86.0164309	E	Normal
17/06/23	17:43:44	24	100	1300	19.0 cm	25.9 Km/Hr	1900.0 mm/Km	1954	2.75	Good	26.5109655	N	86.0165851	E	Normal
17/06/23	17:44:02	24	100	1400	26.0 cm	32.3 Km/Hr	2600.0 mm/Km	2607	3.55	Good	26.5120711	N	86.0172834	E	Normal
17/06/23	17:44:20	24	100	1500	23.0 cm	33.9 Km/Hr	2300.0 mm/Km	2328	3.21	Good	26.5125690	N	86.0174583	E	Normal
17/06/23	17:44:38	24	100	1600	31.0 cm	32.7 Km/Hr	3100.0 mm/Km	3070	4.11	Good	26.5134420	N	86.0176738	E	Normal
17/06/23	17:44:55	24	100	1700	24.0 cm	25.5 Km/Hr	2400.0 mm/Km	2421	3.33	Good	26.5146230	N	86.0178798	E	Normal
17/06/23	17:45:09	24	100	1800	33.0 cm	31.8 Km/Hr	3300.0 mm/Km	3255	4.33	Good	26.5149579	N	86.0179083	E	Normal
17/06/23	17:45:25	24	100	1900	29.0 cm	32.3 Km/Hr	2900.0 mm/Km	2885	3.89	Good	26.5154852	N	86.0191112	E	Normal
17/06/23	17:45:38	24	100	2000	36.0 cm	33.9 Km/Hr	3600.0 mm/Km	3534	4.66	Good	26.5152415	N	86.0193438	E	Normal

6m/s
20/06/23

Executive Engineer
 Rural Works Department
 Works Division, Jaynagar

Name of work : Koriyapatti To T04
 Name of customer : Ramchandra Yadav

(R) Rural Road			
Good	Average		Poor
< 4000	4001 - 5000		> 5000


17/06/23	17.45.52	24	100	2100	27.0 cm	33.4 Km/Hr	2700.0 mm/Km	2899	3.67	Good	26.5144862	N	86.0206570	E	Normal
17/06/23	17.46.02	24	100	2200	37.0 cm	20.7 Km/Hr	3700.0 mm/Km	3626	4.77	Good	26.5148101	N	86.0210721	E	Normal
17/06/23	17.46.19	24	100	2300	32.0 cm	21.9 Km/Hr	3200.0 mm/Km	3163	4.22	Good	26.5153074	N	86.0221289	E	Normal
17/06/23	17.46.39	24	100	2400	27.0 cm	27.3 Km/Hr	2700.0 mm/Km	2699	3.67	Good	26.5156939	N	86.0232219	E	Normal
17/06/23	17.46.54	24	100	2500	34.0 cm	22.8 Km/Hr	3400.0 mm/Km	3348	4.44	Good	26.5159387	N	86.0235387	E	Normal
17/06/23	17.47.03	24	100	2600	31.0 cm	23.2 Km/Hr	3100.0 mm/Km	3070	4.11	Good	26.5162347	N	86.0252257	E	Normal
17/06/23	17.47.18	24	100	2700	24.0 cm	24.7 Km/Hr	2400.0 mm/Km	2421	3.33	Good	26.5165632	N	86.0256422	E	Normal
17/06/23	17.47.40	24	100	2800	28.0 cm	14.9 Km/Hr	2800.0 mm/Km	2792	3.78	Good	26.5152352	N	86.0260296	E	Normal
17/06/23	17.47.55	24	100	2900	36.0 cm	22.6 Km/Hr	3600.0 mm/Km	3534	4.66	Good	26.5144512	N	86.0263076	E	Normal
17/06/23	17.48.11	24	100	3000	29.0 cm	24.9 Km/Hr	2900.0 mm/Km	2885	3.89	Good	26.5140802	N	86.0265976	E	Normal
17/06/23	17.48.11	24	100	3100	29.0 cm	24.9 Km/Hr	2900.0 mm/Km	2885	3.89	Good	26.5140802	N	86.0265976	E	Normal

Ave:- 2829

6/2/2023

20/06/23

Executive Engineer
 Rural Works Department
 Works Division, Jaynagar

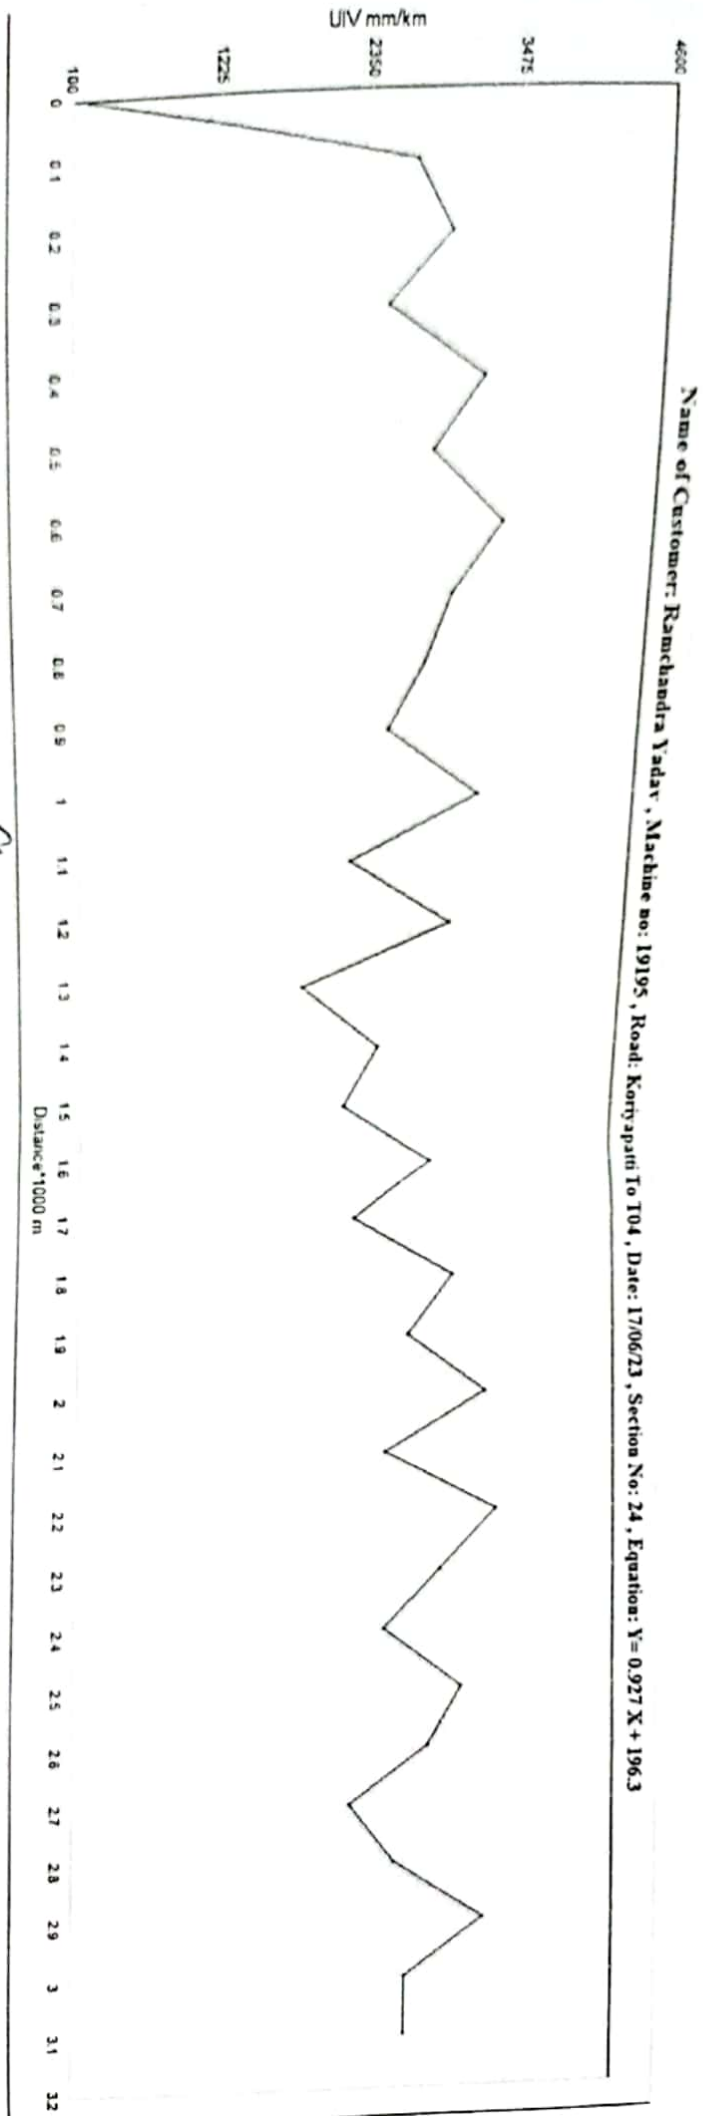

Signature
21/6/23

Signature
21/6/23

Signature
Executive Engineer
Rural Works Department
Works Division, Jaynagar

OFFICE OF THE EXECUTIVE ENGINEER, REGIONAL LABORATORY, R.W.D, DARBHANGA (BIHAR)

BITUMEN PERCENTAGE TEST

Name of the Scheme *Small of road works in Khatwa Road, Patli, etc.*
 Package No *6344AD/2-23*
 Sample collected by *Lab. Staff*
 Date of sample collection *02.05.23*

Name of the works Division *Road, Jaynagar*
 Name of the work circle *Darbhanga*
 Name of Agency *571, Kawa, Chandra, Patna*
 Date of test *02.05.23*

CH-1100M, S.O.R.C

Sl No	Sample No	1	2	3
1	Wt. of mix taken before extraction (A) gm	500.100		
2	Wt. of filter paper before extraction (B) gm	4.960		
3	Wt. of mix after extraction (C) gm	471.040		
4	Wt. of filter paper after extraction (D) gm	5.980		
5	Wt. of filler collected from extract after allowing for setting (E) gm	2.800		
6	Wt. of filler collected in filter paper (D-B)=F gm	1.020		
7	Wt. of aggregate + filter paper (C+E+F)=G gm	474.860		
8	Percentage of Bitumen (in the mix) [(A-G)x100/A]	5.05%		

10/05/2023
 Laboratory Assistant
 R.W.D, Regional Laboratory
 Darbhanga (Bihar)

10/05/2023
 Assistant Engineer
 R.W.D, Regional Laboratory
 Darbhanga (Bihar)

10/05/2023
 Executive Engineer
 R.W.D, Regional Laboratory
 Darbhanga (Bihar)

