

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमण्डल, औरंगाबाद

पत्रांक... 126/ 3150

प्रेषक,

कार्यपालक अभियंता

ग्रामीण कार्य विभाग

कार्य प्रमण्डल, औरंगाबाद।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,

—सह—सचिव, ब्राडा, पटना।

औरंगाबाद, दिनांक... 23/5/23

विषय:—

मुख्यमंत्री ग्राम सम्पर्क योजनान्तर्गत (SC) स्वीकृत पथों में आवंटन उपलब्ध कराने के संबंध में।

महाशय,

मुख्यमंत्री ग्राम सम्पर्क योजनान्तर्गत (SC) स्वीकृत पथों में आवंटन उपलब्ध कराने की कृपा की जाए।

अनु०:— आवंटन अधियाचना विहित प्रपत्र संलग्न।

विश्वासभाजन


Shri Singh
23/5/23
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल औरंगाबाद।
Shri Singh
23/5/23

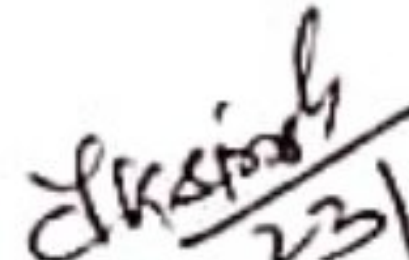
Rural Works Department
MMGSY (SC) Allotment Requisition Format

Name Of Division:- RWD, Work Division, Aurangabad

Sl. No.	Year	Name of Road	Name of Contractor	Administrative Sanction		Agreement Amount		Amount Received (in lacs)	Total Expenditure (in Lacs)	Value of Measurement (in Lacs)	Current Demand (in lac)	Remarks
				Length (in Km.)	Amount (in Lacs)	Main work	Mainta.					
1	2	3	4	5	6	7	8	9	10	11	12	13
1	2019-20	Barun Navinagar to Majhiyawa	SHARWAN AND SUNNY CONSTRUCTION PRIVATE LIMITED	1.570	116.81400	92.52000	10.80	63.23784	63.23782	91.14071	27.90287	Complete
2	2019-20	Gobardhan Pahad to Dihbarsthan	SHARWAN AND SUNNY CONSTRUCTION PRIVATE LIMITED	1.4000	98.5650	76.8100	10.3700	74.15346	74.14452	76.61165	2.45819	Completed
3	2019-20	Baghtarpa Ghorha Road to Yadubigha	SHARWAN AND SUNNY CONSTRUCTION PRIVATE LIMITED	1.6750	132.7480	105.4100	11.3500	96.30863	96.29996	104.32139	8.01276	Completed
4	2019-20	Majhauri to Sanda Baluganj Road	SHARWAN AND SUNNY CONSTRUCTION PRIVATE LIMITED	1.0200	73.0100	57.9100	6.7200	38.83847	38.83847	55.48352	16.64505	Completed
5	2019-20	Basant road to bijuliya	SHARWAN AND SUNNY CONSTRUCTION PRIVATE LIMITED	2.140	161.31100	126.80	14.66	104.04096	104.03143	124.13299	20.09203	Completed
6	2019-20	T05 TO SHIV NAGAR ROAD to MUNSHI BIGHA	SHARWAN AND SUNNY CONSTRUCTION PRIVATE LIMITED	1.925	141.99800	111.80	12.73	91.88502	91.88354	100.62081	8.73579	Completed
7	2019-20	SURHANA TO URDANA PMGSY to MISHR TENDUA	Rajesh Kumar Singh	1.010	78.95800	71.20	7.10	66.55804	66.55738	71.19178	4.63374	Completed
8	2019-20	NH98 to CHANDARDEV BIGHA	Rajesh Kumar Singh	1.220	88.43400	69.21000	9.410	55.08799	55.08797	69.19461	14.10662	Completed
9	2019-20	Madanpur deo road to badam	AURANGABAD REAL ESTATE PRIVATE LIMITED	3.370	247.12900	192.04	21.88	80.16790	80.16544	101.39308	21.22518	On-going
10	2019-20	Badam road to bhitari dhokari	AURANGABAD REAL ESTATE PRIVATE LIMITED	1.090	82.02700	72.62	7.92	55.06919	55.06913	65.53778	10.46859	Completed
11	2019-20	L028 to Runiya	AURANGABAD REAL ESTATE PRIVATE LIMITED	0.915	63.325	43.17	6.1	29.80856	29.80771	33.35914	3.55058	Completed
12	2019-20	Vakilganj to Bishunbandh	SANJAY KUMAR SINGH	1.025	80.82600	71.56	7.23	58.51845	58.51751	71.55527	13.03682	Complete

SL No.	Year	Name of Road	Name of Contractor	Administrative Sanction		Agreement Amount		Amount Received (in lacs)	Total Expenditure (in Lacs)	Value of Measurement (in Lacs)	Current Demand (in lac)	Remarks
				Length (in Km)	Amount (in Lacs)	Main work	Mainta.					
1	2	3	4	5	6	7	8	9	10	11	12	13
13	2019-20	Barun Daudnagar road to mahtha	Parmakant	1.56	124.12800	100.55	11.45	95.23064	85.38240	99.45053	4.21989	Complete
14	2019-20	MADANPUR DEO ROAD to PICHULIA	M/S MAA SHANTI CONSTRUCTION	1.470	96.70000	75.80000	11.290	66.54613	66.54520	75.74206	9.19593	Completed
15	2019-20	Shivgunj rafigunj road to arjun bigha	M/S MAA SHANTI CONSTRUCTION	1.01	76.954	68.38	7.130	61.81972	61.78750	68.11367	6.29395	Completed
16	2019-20	L037 to Sondih	M/S Bajrang Construction	0.730	49.29400	47.02000	4.840	36.95165	36.95158	42.57101	5.61936	Completed
17	2019-20	KHIRIWA PIRUTHU ROAD to GOKUL BIGHA	M/S BAJRANG CONSTRUCTION	1.200	74.04400	58.46000	7.49	38.00248	38.00248	54.28924	16.28676	Completed
18	2019-20	TANDWA GAJNA ROAD MUNGIYA to KHAJURI MAHESH	PRIYA RANJAN KUMAR SINGH	2.5100	194.4070	154.7800	18.3700	139.88578	139.88481	154.55371	14.66793	Completed
19	2019-20	T04 Jogri to Bardih	VIMLESH KUMAR SINGH	1.560	116.30800	91.45000	10.4800	85.98137	85.97210	90.97229	4.99092	Completed
20	2019-20	Madanpur deo road se saharla to kewla	VIMLESH KUMAR SINGH	1.833	132.59000	105.65000	11.72	54.39578	54.39573	95.22808	40.83230	On-going
21	2019-20	Khiriawan Pirthu to Ighunathi Par Nala	VIMLESH KUMAR SINGH	1.650	127.52900	100.18000	12.02	39.39835	39.39835	98.6494	59.25105	On-going
22	2019-20	Madanpur Kasma Path to Khajwatiya	VIMLESH KUMAR SINGH	1.775	119.02000	92.97000	12.68	39.03574	39.03000	91.7529	52.71716	Phy. Completed
23	2019-20	Balikarna More to Balikarna Bigha	Atul krishna	0.470	37.59100	30.55000	3.74	19.94188	19.54115	27.54832	7.60644	Phy. Completed
Total:-				33.640	2476.1190	1986.290	233.740	1470.9222	1460.9910	1835.8656	372.5499	


 Divisional Engineer
 RWD, Works Division
 Aurangabad (Bihar)


 Executive Engineer
 R.W.D. (W) Division, Aurangabad
