

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल- डुमरांव

पत्रांक:- 1161, डुमरांव /
प्रेषक ,

दिनांक:- 20-10-23

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, डुमरांव ।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास अभिकरण,
बुद्ध मार्ग, पटना

विषय :- मुख्यमंत्री ग्राम सम्पर्क योजना (New Maintenance Policy 2018) मद
अंतर्गत राशि की अधियाचना के संबंध में।

महाशय ,

उपर्युक्त विषय के संबंध में कहना है कि इस प्रमंडल अंतर्गत मुख्यमंत्री
ग्राम सम्पर्क योजना (New Maintenance Policy 2018) में चल विपत्र के भुगतान हेतु राशि
की आवश्यकता है जिसका अधियाचना प्रपत्र के साथ संलग्न कर भेजा जा रहा है।

अधियाचित राशि उपलब्ध कराने की कृपा की जाए ताकि कराये गये
कार्यों का भुगतान किया जा सके।

अनु०:- यथोक्त।

विश्वासभाजन

Gopal
20/10/2023
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल डुमरांव

P. H. C.
19/10/2023

FORM GFR 19-A
(SEE Government of India's Decision (I) below Rule-150)
Form of Utilisation Certificate upto the month of 19.10.2023

New Maintenance Policy 2018 Through CFMS

PIU:- RWD(WD), Dumraon

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in Rs. Lacs)	Amount Received (in Rs. Lacs)	Particulars
1	Construction of Rural Roads under New Maintenance Policy 2018	Letter No:- 140 date- 16.10.2023	2021.77126	Certified that out of Rs. 2021.77126 lacs received during the years in favour of Ex. Engineer, RWD (W), Div.- Dumraon, Bihar, a sum of Rs 1888.25731 lacs has been utilized for the purpose of MMGSY NDB Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 133.51395 lacs remaining unutilized at the end of the period under.
Total -				

2 Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised :-

- Works have been supervised by Executive Engineer/ Supertending Engineer.
- Periodical inspection has been conducted by Executive Engineer/ Supertending Engineer.
- Construction materials have been tested
- Measurements have been recorded in the MBs and test check conducted by the Assistant.
- All other codal formalities have been observed.

3 Physical Progress achieved :-

- Construction of Road works
- Construction of CD works

AS-mlb
20/10/23

Gobal
20/10/2023
Executive Engineer
R.W.D. (w) Div. Dumraon
MS
19/10/2023

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Name of Works Division : - RWD, Works Division, Dumraon.

Sl. No	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date)	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No/ Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer(in mm)	Value of Bitumen Content in Percentage	Previous Total Amount Allotted (In Lakh)	up-to-date Expenditure as per MIS (In Lakh)	Requisition against work done (In Lakh)	Remarks
					Length (in KM)	Amount (In Lakh)	Initial Rectification Surface Renewal (In Lakh)	5 Year Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RVM/BU/D UN/23/000 5	Kesath madarsa high school se katnaar	10402008042	1796/20.03.2023	2.000	113.697	82.01188	19.27730	06 MBD 2023- 24/20.07.2023	19.04.2024	ongoing	2789	25.00	5.01	0.00	0.00	80.06780	
																80.0678		

1 Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.
2 Up-to-date Physical Progress has been Uploaded in MIS.

Handwritten signature
20/10/23


Handwritten signature
20/10/2023
Executive Engineer
RWD, Works Division,
Dumraon.
19/10/2023

कार्यपालक अभियन्ता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल डुमराँव।

का०आ०सं०-.....९२..... डुमराँव दिनांक 20/10/2023

कार्यालय-आदेश


प्रमाणित किया जाता है कि बिहार ग्रामीण पथ अनुसंधान नीति-2018 योजनान्तर्गत **Kesath madarsa high school se katknaar** पथ का कार्य गुणवत्ता एवं विशिष्टियों के अनुरूप पूर्ण कराया गया है। पथ के मापीपुस्त की जाँच मेरे द्वारा 10% प्रतिशत, सहायक अभियन्ता द्वारा 50% प्रतिशत एवं कनीय अभियन्ता के द्वारा शतप्रतिशत किया गया है।


कनीय अभियन्ता
ग्रामीण कार्य विभाग
कार्य अवर प्रशाखा, केसठ।


सहायक अभियन्ता
ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल, केसठ।


कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, डुमराँव।

File :H:\shailesh\19101352(1).Xls, Section No.:36, Eqn : $Y = 0 \cdot X^2 + 0.816 \cdot X + 249$
Name of Customer :Shailesh Singh, Name of Work/ Road :Kesath Madrsa High School se Katiknar, Lab Job

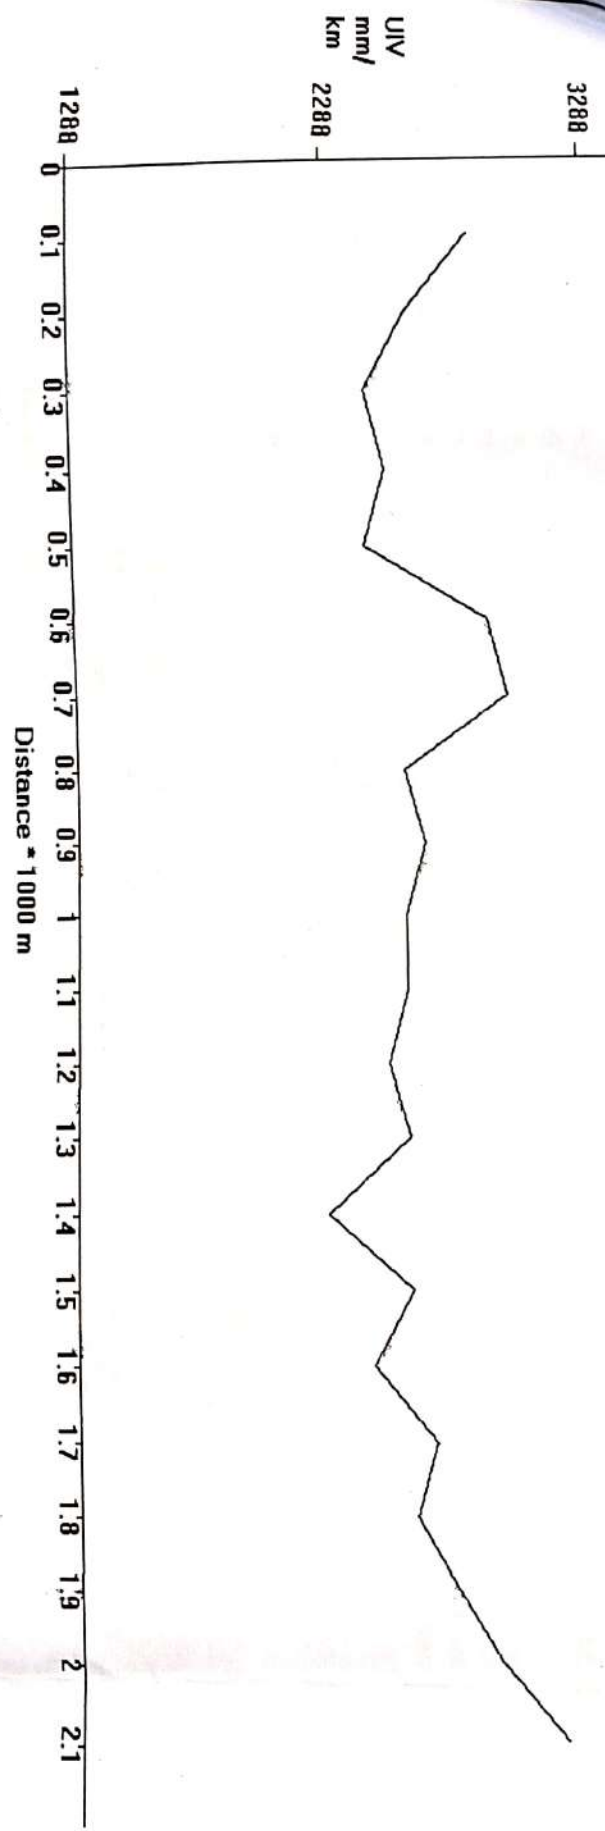

Signature
19/10/2023

Signature
19/10/2023

Signature
19/10/2023
EE

Road Name:- Kesath Madarsa High School se Katiknar Contractor Name:-Shailsh Singh

Date	Time	Section	No.	Length in km	Bumps in mm	Speed Rate	OR	IRI CATEGORY	Latitude .ongitude	Event
19/10/23	10:32:8	36	0.1	320	0	3200	2860 G	25.41912	84.23742	Normal
19/10/23	10:32:43	36	0.1	290	10.1	2900	2615 G	25.41821	84.23744	Normal
19/10/23	10:33:18	36	0.1	270	10.1	2700	2452 G	25.41754	84.23811	Normal
19/10/23	10:33:18	36	0.1	280	10.1	2800	2533 G	25.41682	84.23848	Speed Breaker
19/10/23	10:34:0	36	0.1	270	10.1	2700	2452 G	25.41597	84.23832	Normal
19/10/23	10:34:28	36	0.1	330	10.1	3300	2941 G	25.4151	84.23793	Normal
19/10/23	10:35:3	36	0.1	340	10.1	3400	3023 G	25.41432	84.23742	Speed Brez <4000
19/10/23	10:35:38	36	0.1	290	10.1	2900	2615 G	25.41365	84.23675	Curve
19/10/23	10:36:0	36	0.1	300	10.1	3000	2696 G	25.41278	84.23662	Normal
19/10/23	10:36:14	36	0.1	290	20.2	2900	2615 G	25.41181	84.23636	Normal
19/10/23	10:36:14	36	0.1	290	30.3	2900	2615 G	25.41097	84.23603	Normal
19/10/23	10:36:14	36	0.1	280	20.2	2800	2533 G	25.41005	84.23596	Normal
19/10/23	10:37:0	36	0.1	290	10.1	2900	2615 G	25.40925	84.23603	Normal
19/10/23	10:37:0	36	0.1	250	20.2	2500	2288 G	25.40875	84.23588	Curve
19/10/23	10:37:25	36	0.1	290	20.2	2900	2615 G	25.40774	84.23519	Normal
19/10/23	10:37:25	36	0.1	270	20.2	2700	2452 G	25.40699	84.235	Normal
19/10/23	10:37:25	36	0.1	300	20.2	3000	2696 G	25.4062	84.23473	Normal
19/10/23	10:38:0	36	0.1	290	10.1	2900	2615 G	25.40508	84.23473	Normal
19/10/23	10:38:0	36	0.1	310	20.2	3100	2778 G	25.4051	84.23576	Normal
19/10/23	10:38:35	36	0.1	330	20.2	3300	2941 G	25.40512	84.23668	Normal
19/10/23	10:39:0	36	0.047	170	30.3	3617	3200 G	25.40497	84.23721	Normal
				Length						
				2.00						

$$Y = 0 * X^2 + 0.816 * X + 249$$

$$X = 3617$$

$$Y = 3200$$

(R) RURAL ROAD

Good Average Poor

4001-5000 >5001

IRI Value=2789

Machine ID=415

Shailsh Singh

19/10/2023

SR

Shailsh Singh

19/10/2023

SR

Shailsh Singh

19/10/2023

SR



Lab Job number :

Date :19/10/2023

Name of Customer :Shailesh Singh

Name of Work/ Road :Kesath Madrsa High School se Katiknar

Sr.no Location of Corrected U.I Road catagory
test(in km) value(mm/km)

2	0.1	2860 G
3	0.2	2615 G
4	0.3	2452 G
5	0.4	2533 G
6	0.5	2452 G
7	0.6	2941 G
8	0.7	3023 G
9	0.8	2615 G
10	0.9	2696 G
11	1	2615 G
12	1.1	2615 G
13	1.2	2533 G
14	1.3	2615 G
15	1.4	2288 G
16	1.5	2615 G
17	1.6	2452 G
18	1.7	2696 G
19	1.8	2615 G
20	1.9	2778 G
21	2	2941 G
22	2.1	3200 G

SE
19/10/2023
SR

Devina
19/10/2023
KB

Gopal
20/10/2023



चक्र २५८८१ ३१३८२०१ से अधिक-११८३५ मी.
New Mant. Policy/MIR-3054
-2018/Length → २ K.M

Schedule XLV-Form No. 134

DATE of Start - २०.७.२३

DATE of comp- १९.५.२४

३५८१९. DIVISION

चक्र १६ SUB-DIVISION

Agreement No- ०६/२३-२४
MIR

Measurement Book

-1236

संगण-२१०१२१ असा १३६

Name of Work—
 Situation of Work—
 Agency by which work is executed—
 Date of Measurement—
 No. and date of agreement

(These four lines should be repeated at the commencement of the measurement relating to each work)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of Road—Keshari					
Madarsa High School					
To Katiyara Puh.					
Scheme—M.R.-3059					
Agency—Shailash Singh					
Vill—Bakhar, P.O.—Dulapara					
Dist.—Buxar.					
Agreement No.—06 M.R.D/2023-24					
Date of start—20.07.2023					
Date of completion—19.04.24					
(1) Clearing and grubbing road land by manual means) including as per					
15 x 30.0 x 2 x 1.00 = 900.0 m ²					
12 x 30.0 x 2 x 1.00 = 720.0 m ²					
13 x 30.0 x 2 x 1.00 = 780.0 m ²					
12 x 30.0 x 2 x 1.00 = 720.0 m ²					
15 x 30.0 x 2 x 1.00 = 900.0 m ²					
1 x 1.00 x 2 x 1.00 = 2.00 m ²					
Total = 4022.00 m ²					
= 0.4022 Hec.					
(2) Construction of concrete sub-base with reinforcement					

Continuation

35
Sch. XLV-Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
of typical information given.					
0.2 Nos. vide TMB, P-21					
@ 15335.68/Nos. ₹					30671.00
517) Earth work in excavation in foundation complete					
15.58 m ³ vide TMB, P-27					
@ 410.66/m ³ ₹					6398.00
518) Providing 14-15 cm leveling course in foundation etc.					
2.85 m ³ vide TMB, P-27					
@ 742.582/m ³ ₹					21158.00
519) Placing and compacting concrete in sub-structure					
12.61 m ³ vide TMB, P-27					
@ 8529.80/m ³ ₹					107561.00
520) Providing and laying RCC pipe no. 8 as per do.					
7.50 m. vide TMB, P-27					
@ 3427.43/m. ₹					25706.00
					Total ₹ 7410937.00
					Add GST @ 18% = ₹ 1333969.00
					Add L.C @ 1% = ₹ 74109.00
					Add S.F. 10% on material = ₹ 77407.00
					Total ₹ 8896422.00
Less agreement rate 10% below ₹ 8896422.00					
					Total ₹ 80,06,780.00

Continuation

19/10/2023
AK

19/10/2023
SR



