

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, खगड़िया ।

पत्रांक 1261 / 3730
प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, खगड़िया ।

सेवा में,

नोडल पदाधिकारी,
3054(MR)
ग्रामीण कार्य विभाग,
बिहार, पटना ।

खगड़िया, दिनांक 01-8-2024 /


विषय :- शीर्ष Maintenance Policy-2018 Under MR-3054 योजना अन्तर्गत आवंटन
उपलब्ध कराने के संबंध में ।

महाशय,

उपर्युक्त विषयांकित शीर्ष 3054(MR) के अन्तर्गत कार्यान्वित योजना हेतु मॉग
को आवंटित करने की कृपा की जाय ताकि कार्य की प्रगति सुचारु रूप से चल सके ।

अनु० - अधियाचना पत्र ।

विश्वासभाजन,


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य
प्रमण्डल, खगड़िया ।
1.8.24
Jan 1
01/08/24

FROM GFR 19-A
(See Government of India's Decision (1) below Rule-150)
Form of utilization Certificate up to the Month of 31-07-2024

PIU : Executive Engineer,
R.W.D. Works Division,
Khagaria.

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in Rs. Lacs)	Amount Received (in Rs. Lacs)	Particulars
1	MR(3054) under Bihar Rural Road Maintenance Policy - 2018	By CFMS upto Upto date	5506.11144	Certified that out of Rs. 5506.11144 Lacs received upto date 31-07-2024 in favour of Executive Engineer, RWD, Bihar Khagaria sum of Rs.5379.33010 Lacs has ben utilized for the purpose of MR(3054) under Bihar Rural Road Maintenance Policy - 2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 126.78134 Lacs remaining unutilized at the end of the period under.
	Total		5506.11144	

2 Certified that I have satisfied myself that the conditions on which the grants-in-aid wa sanctioned

Kind of Checks excresised :-

- (i) Works have been supervised by Executive Engineer/Superintending Engineer.
- (ii) Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- (iii) Construction material have been tested.
- (iv) Measurements have been recorded in the MBs and test check conducted by the Assistant.
- (v) All other codal formalities have been observed.

3 Physical Progress achieved :

- (i) Construction of Road Works.
- (ii) Construction of CD Works.

Executive Engineer,
R.W.D. Works Division,
Khagaria.

[Signature]
1-8-24
[Signature]
21/8/24


Requisition Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Khagaria

Sl No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of CC Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Alloted Amount (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/KH/KHA/2 4/0002	LOT 4-APPROACH ROAD TO RANCO (TRACK4)	20904502057	Dt. 04-12-2023	0.550	33.104	25.98974	4.84203	25/MBD/2023-24 15.03.2024	14-Dec-24	02.06.2024	3146	25.00	5.02	22.20000	22.20000	3.68977	
2	RM/KH/KHA/2 4/0001	Const. of FCC Road from Swani - Swani Tola	20904502055	Dt. 04-12-2023	0.650	37.783	29.53590	2.63273	28/MBD/2023-24 16.03.2024	15-Dec-24	Road Furniture work in progress	2675	25.00	5.02	16.50000	16.50000	12.50000	
3	RM/KH/KHA/2 4/0001	M/R to Road from the house of Gritish Singh to Barhanta Timmuhani in Bhadas north panchayat	20904508051	Dt. 04-12-2023	0.900	47.83	42.18231	6.42630	28/MBD/2023-24 16.03.2024	15-Dec-24	Road Furniture work in progress	3571	25.00	5.02	16.10000	16.10000	25.38231	
4	RM/KH/KHA/2 4/0002	South Marar to Manohar Bhagat House to PMGSY Road Via Prithvi Singh kanya Madhya vidalya and House of Shivan Poddar and Ram Toli Muhammad Balli	20904501087	Dt. 04-12-2023	1.450	82.952	69.70138	6.27223	25/MBD/2023-24 15.03.2024	14-Dec-24	Road Furniture work in progress	3062	25.00	5.02	59.70000	59.70000	8.05000	
5	RM/KH/KHA/2 4/0002	Khangaria Alauli PWD Road to Barhara	20904513011	Dt. 04-12-2023	1.600	84.171	70.33619	14.80449	25/MBD/2023-24 15.03.2024	14-Dec-24	18.07.2024	3358	25.00	5.02	65.33000	65.33000	4.87500	
6	RM/KH/KHA/2 4/0002	LOT 1-TOZ MATRIBABUR TO KAMALPUR (TRACK27)	20904502078	Dt. 04-12-2023	1.600	102.694	86.45118	784250	25/MBD/2023-24 15.03.2024	14-Dec-24	Road Furniture work in progress	3593	25.00	5.02	83.90000	82.37441	1.30000	
7	RM/KH/KHA/2 4/0002	LO66-DOWN TOLA BAI/ASS TO RAMCIANDBRA (TRACK25)	20904502075	Dt. 04-12-2023	0.570	18.224	14.07505	2.94606	25/MBD/2023-24 15.03.2024	14-Dec-24	18.06.2024	3570	25.00	5.02	12.07000	12.07000	0.74204	

8	RM/KH/KHA/2 4/0001	Bachhoua NRCC Road to Dhanuk Toll Bachhoua Madhya	20904512011	Dt. 29-03-2023	0.744	33.791	28.33608	6.19009	28/MBD/2023- 24 16.03.2024	15-Dec-24	Road Furniture work in progress	2871	25.00	5.02	27.50000	26.39439	0.81608	
9	RM/KH/KHA/2 4/0001	Bachhoua PMGSY Road To Lakshminya	20904513009	Dt. 04-12-2023	1.491	63.061	49.10735	11.47948	28/MBD/2023- 24 16.03.2024	15-Dec-24	Road Furniture work in progress	2989	25.00	5.02	41.50000	41.50000	6.50000	
10	RM/KH/KHA/2 3/0008	L032-F.W.D. ROAD TO KAMATIYAN (TRACK22)	20904502059	Dt. 04-07-2023	0.700	45.591	35.23019	6.43490	18/MBD/2023- 24 19.12.2023	18-Sep-24	Road Furniture work in progress	3025	25.00	5.02	32.23000	32.17197	1.52623	
11	RM/KH/KHA/2 4/0002	L047-BARACHAT TO BARAI (TRACK17)	20904502065	Dt. 04-12-2023	1.300	72.476	67.15461	7.96492	25/MBD/2023- 24 15.03.2024	14-Dec-24	Road Furniture work in progress	3571	25.00	5.02	0.00000	0.00000	52.50000	
12	RM/KH/KHA/2 4/0001	Barghar to Budhwan	20904512013	Dt. 04-12-2023	1.800	68.906	56.83544	13.74299	28/MBD/2023- 24 16.03.2024	15-Dec-24	Road Furniture work in progress	3400	25.00	5.02	0.00000	0.00000	52.15000	
13	RM/KH/KHA/2 3/0003	PARMANANDPUR DHALA KHAGRIYA SE MANSI TAK PATH	20904508062	Dt. 29-03-2023	6.000	358.358	332.53467	54.90672	16/MBD/2023- 24 13.09.2023	12-Jun-24		3470	25.00	5.02	328.00000	328.00000	4.52000	

- 1 Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.
- 2 Up-to-date Physical Progress has been uploaded in MIS.


 Executive Engineer
 RWD, Works Division,
 Khagaria

 15/12/24

Name of Road - Const. of PCC Road from Swani - Swani Tola

Name of Contractor -Yaduvansham Infrastructure Private Limited Batch Name - RM/KH/KHA/24/0001									
Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD	
29/5/24	8:56:41	43	0.1	220	10.1	2200	2675	G	Normal
29/5/24	8:57:16	43	0.1	230	10.1	2300	2773	G	Normal
29/5/24	8:57:52	43	0.1	210	10.1	2100	2577	G	Normal
29/5/24	8:58:0	43	0.1	200	10.1	2000	2478	G	Normal
29/5/24	8:58:27	43	0.1	270	10.1	2700	3167	G	Normal
29/5/24	8:59:2	43	0.1	180	10.1	2000	2478	G	Normal
29/5/24	8:59:38	43	0.038	210	10.1	2100	2577	G	Normal
						Total	18725		
						Average	2675		

$$Y = 0 * X^2 + 0.889 * X + 228.2$$

$$X = 2100$$

$$Y = 2577$$

(R) RURAL ROAD

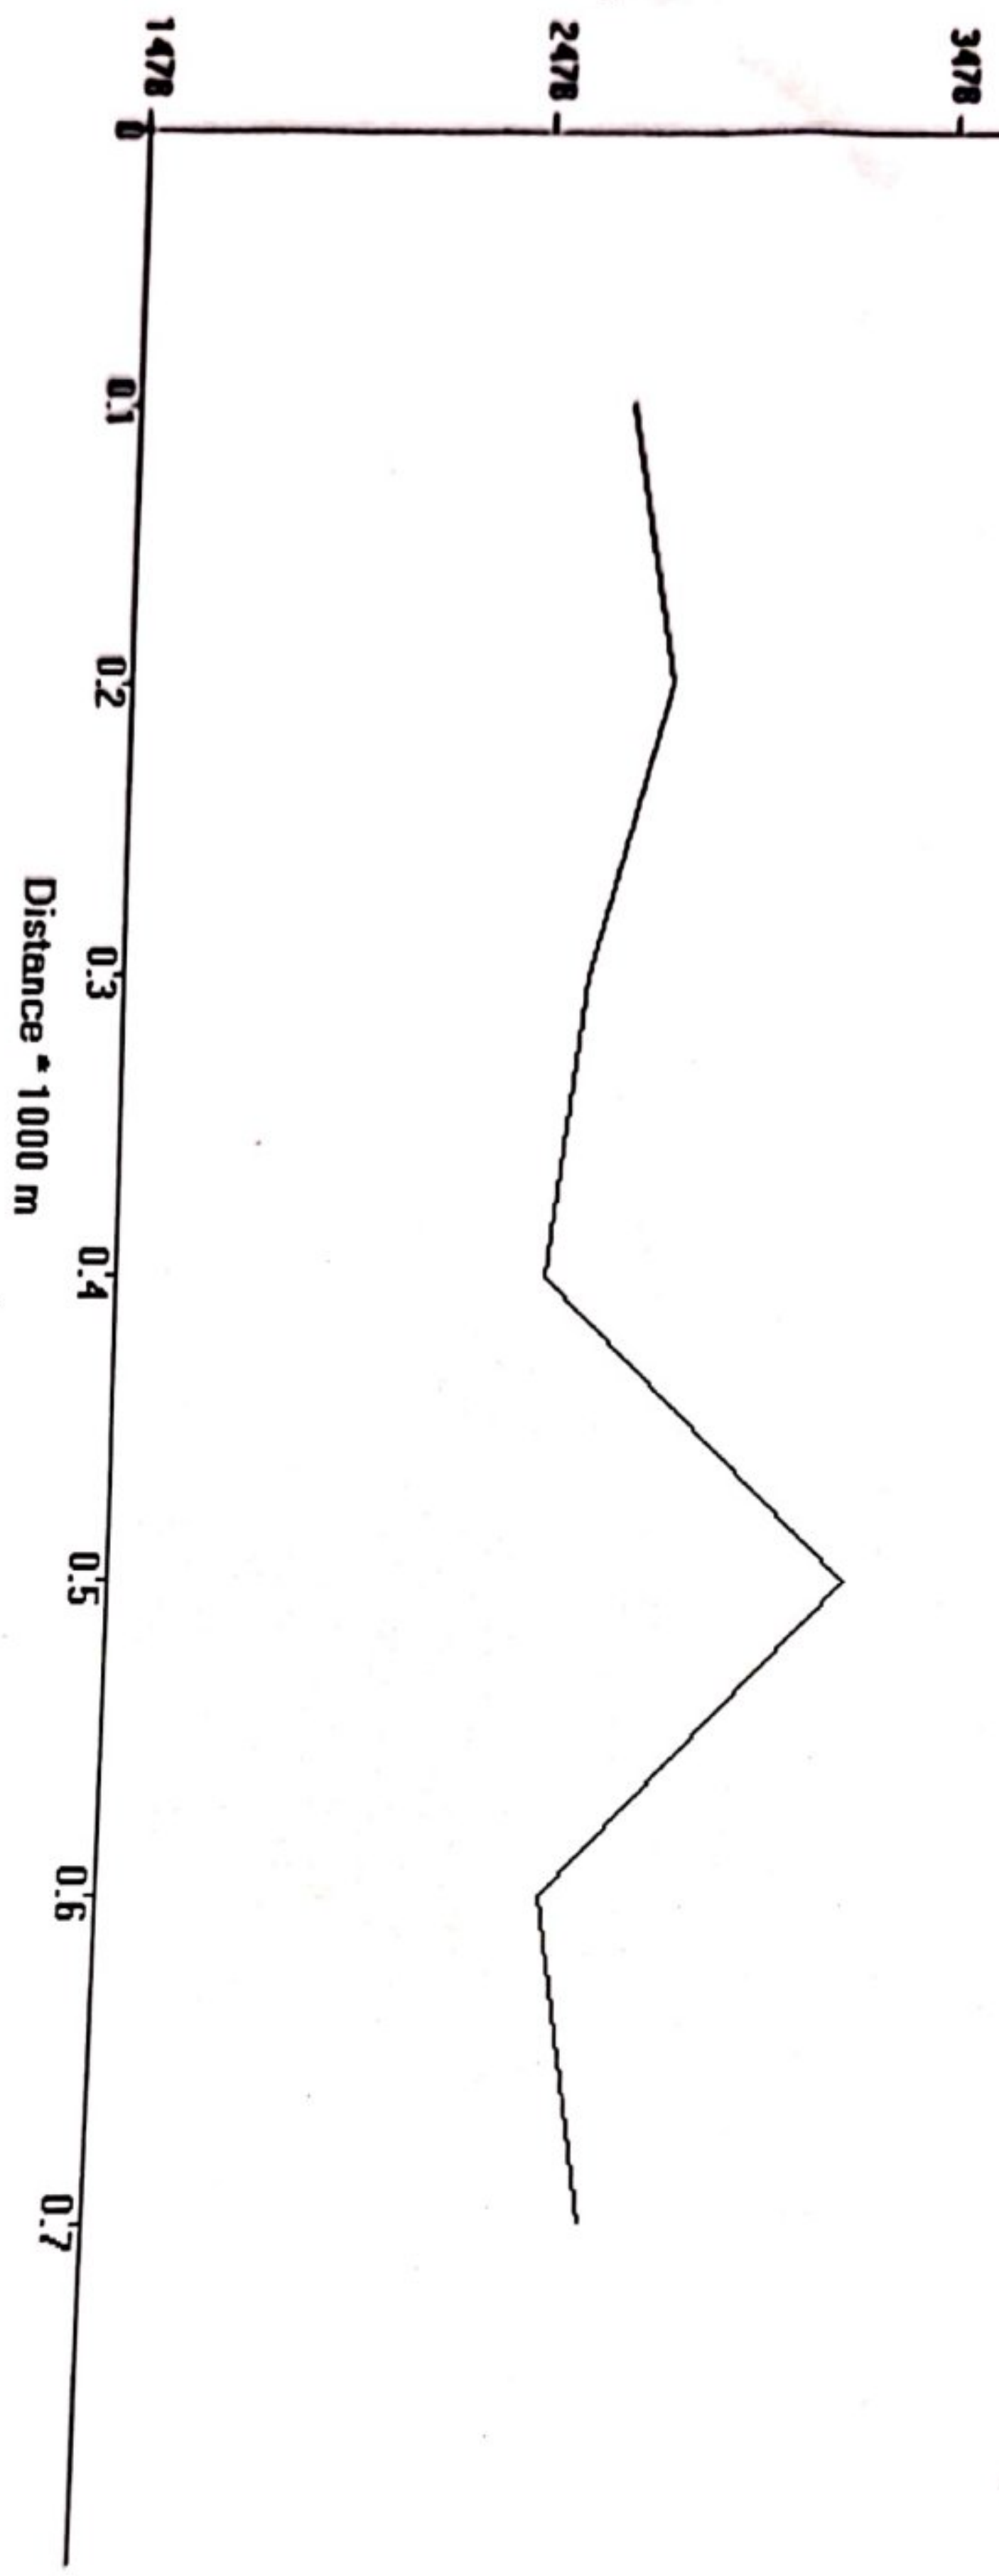
Good Average Poor
 <4000 4001-5000 >5001

[Handwritten signature]
29/5/24

[Handwritten signature]
29/5/24

[Handwritten signature]
29/5/24

File E:\BUMP INDICATOR\29050952.Xls. Section No. :43. Eqn : $Y = 0 \cdot X^2 + 0.889 \cdot X + 228.2$
 Name of Customer :Yaduvansham Infrastructure Private Ltd. Name of Work/ Road :Const. of PCC Road form Swani



Handwritten signature
 29/5/27
 are

Handwritten signature
 29/5/27
 are

Handwritten signature
 29/5/27
 are
