



कार्यपालक अभियंता का कार्यालय ग्रामीण कार्य विभाग, कार्य प्रमंडल, मढ़ौरा।

E-Mail – eerwd.marhaura@yahoo.com

पत्रांक:— 1362/अ-30

मढ़ौरा/दिनांक:— 07.08.24

प्रेषक:—

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, मढ़ौरा।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी—सह—सचिव,
बिहार ग्रामीण पथ विकास अभिकरण, बिहार, पटना।

विषय:— शीर्ष **MR-3054** योजनान्तर्गत बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत स्वीकृत पथ में कराये गये कार्य का आवंटन मॉग के संबंध में।

प्रसंग:— भवदीय के पत्रांक:-113 अनु0, दिनांक:-10-01-2020

महाशय,

उपरोक्त विषयक प्रासंगिक पत्र के संबंध में कहना है कि इस कार्य प्रमंडल, अंतर्गत शीर्ष-**3054 (MR-3054)** अंतर्गत बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत संवेदीका कुमारी शिल्पी सिंह के द्वारा पथ में किये गये कार्य का अधियाचना उक्त प्रासंगिक पत्र द्वारा प्राप्त विहित प्रपत्र में भरकर आवंटन मॉग हेतु अधियाचना—पत्र सादर समर्पित की जा रही है।

अतः अनुरोध है कि अधियाचना प्रपत्र में दर्शाये गये पथवार राशि कॉलम सं0-18 के अनुरूप पथ में आवंटन उपलब्ध कराने की कृपा की जाय ताकि संबंधित संवेदक द्वारा पथ में किये गये कार्य का भुगतान किया जा सकें।

अनु0—1) अधियाचना प्रपत्र।

2) 19 ए प्रपत्र।

3) BOMP Indicator Report संलग्न।

विश्वासभाजन

6/8/24

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, मढ़ौरा।

6/8/24

FORM GER-19-A**(See Government of India'S Decision (I) below Rule -150)****Form of Utilization Certificate up to the Month of August-2024****PIU:- Executive Engineer RWD Works Division, Marhaura**

SL No	Name of Scheme	Sanction No & Date with Amount (in Lacs Rs.)	Amount Received (in lacs Rs.)	Particulars
1	Construction of Rural Roads under MR-3054 Rural Road Maintenance Policy-2018 (Ledger ID-7069)	सचिव ब्राडा के पत्रांक-82 We दिनांक-28-06-2024	10297.16690	Certified that out of Rs-10297.16690 Lacs received during the Years, 2018-19 & 2019-20, 2020-21, 2021-22, 2022-23 & 2023-24 in favour of E.E., R.W.D. Works Division Marhaura Sum of Rs- 10287.29093 Lacs has been utilized for the Purpose of MR-3054 New Maint. Policy-2018 Scheme as given in the margin for Which it was Sanctioned and that the balance of Rs-9.87597 Lacs remaining unutilized at CFMS the end of the period under report.

Sr. DAO

R.W.D. (W) Division Marhaura

Executive Engineer

R.W.D. (W) Division Marhaura

6/8/24.

Requisition Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of works Division:- Rural Work Department, Work Division, Marhaura.

SL No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA) Total		Agreement Amount (In Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (In Lakh)	up-to-date expenditure as per MIS (In Lakh)	Requisition against work done. (In Lakh)	Remarks
					Length (In Km.)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)										
1	MR-N/22-23 Marhaura/13 RM/SA/MAR/23/0008	Tehti Dyalpur Mukh Path To Piparpati Purab Tola Tak	31306513015	Lt.- No-1797 Date-20-03-2023	3.400	227.02400	235.56405	29.54161	02/MR-3054-N/2023-24 08-09-2023	07-06-2024		3382.290	25mm	5%	212.05937	212.05937	21.39482	Work In Progress
2	MR-N/22-23 Marhaura-12 RM/SA/MAR/23/0005	Bhualpur Katsa Road To PaMMGSY[SC]him Ahir Tola Tak	31306512003	Lt.- No-1286 Date-24-02-2023	1.885	110.15000	91.01059	22.95018	08/MR-3054-N/2023-24 06-10-2023	05-07-2024		3273.730	25mm	5%	66.00143	65.35757	24.20492	Work In Progress
Total:-																	45.59974	


1. Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.
2. Up-to-date Physical Progress has been Uploaded in MIS.

6/18/24

Executive Engineer
Rural Work Department
Work Division, Marhaura
6/18/24

File : E:\BUMP\AJAY KUMAR REPORT BUMP\Bhualpur Katsa Road To PaMMGSY[SC]him Ahir Tola

Name of Customer : Kumari Shilpi Singh. Name of Work/ Road : Bhualpur Katsa Road To PaMMGSY[SC]him Ahir

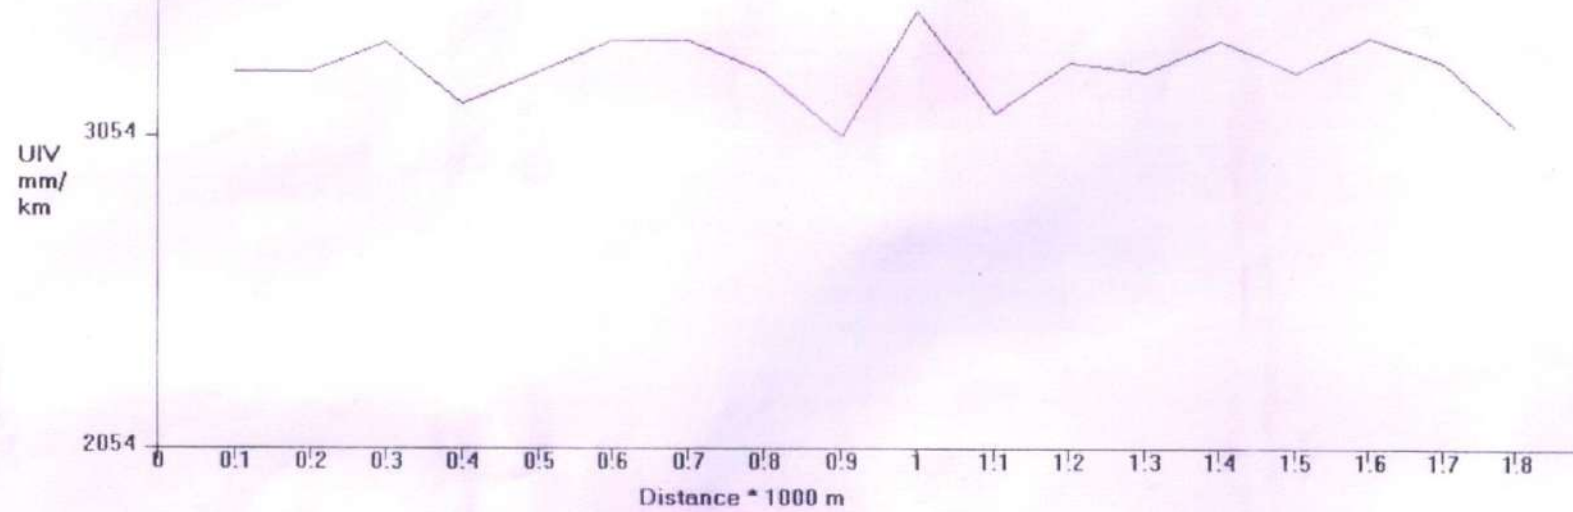

2/10/24
25/05/2024

Channarayana
25/05/24
2

25/05/24

4/5/24

Name of Customer :Kumari Shilpi Singh

Name of Work/ Road :Bhualpur Katsa Road To PaMMGSY[SC]him Ahir Tola Tak

Date	Time	Section	Length	Bumps	Speed	OR	IRI	TEGORY	Latitude	ongitude	Event
No.			in km	in mm	Rate	mm/km	mm/km	ROAD			
25/5/24	14:11:01	36	0.1	140	30.1	1400	3256	G	25.88223	84.86912	Normal
25/5/24	14:11:13	36	0.1	280	30.5	2800	3259	G	25.88189	84.86865	Normal X = 0
25/5/24	14:11:25	36	0.1	220	30.2	2200	3354	G	25.88141	84.86791	Normal Y =
25/5/24	14:11:38	36	0.1	320	30.1	3200	3156	G	25.88141	84.87	Speed Breaker
25/5/24	14:11:52	36	0.1	110	25.8	2500	3256	G	25.88133	84.86598	Normal
25/5/24	14:12:05	36	0.1	190	30.5	1900	3358	G	25.88061	84.86586	Normal (A) ASPHALTIC
25/5/24	14:12:17	36	0.1	220	30.7	2200	3356	G	25.87969	84.86557	Culvert Good Average Poor
25/5/24	14:12:29	36	0.1	270	30.3	2700	3256	G	25.87868	84.8652	Culvert <2500 2500-3500 >3500
25/5/24	14:12:42	36	0.1	270	27.9	2700	3054	G	25.87814	84.86503	Normal
25/5/24	14:12:57	36	0.1	300	25.8	3000	3452	G	25.87736	84.86471	Culvert
25/5/24	14:13:09	36	0.1	310	28.8	3100	3125	G	25.87685	84.86443	Normal
25/5/24	14:13:21	36	0.1	250	26.9	2500	3288	G	25.87629	84.86409	Culvert
25/5/24	14:13:33	36	0.1	300	25.5	3000	3256	G	25.87565	84.86354	Normal
25/5/24	14:13:45	14	0.1	300	26.8	3000	3418	G	25.88155	84.86581	Normal
25/5/24	14:13:55	36	0.1	220	30.7	2200	3356	G	25.88173	84.86377	Culvert
25/5/24	14:14:00	36	0.1	270	30.3	2700	3258	G	25.88169	84.86311	Normal
25/5/24	14:14:05	36	0.1	270	27.9	2700	3369	G	25.88172	84.86222	Normal
25/5/24	14:14:15	36	0.1	300	25.8	3000	3289	G	25.88165	84.86047	Culvert
25/5/24	14:15:05	36	0.08	310	28.8	3100	3085	G	25.8821	84.85894	Normal
Length			1.88	IRI Value		3273.73					

25/5/24
25/05/24

25/05/24
25

25/5/24

25/5/24

Lab Job number :426

Date :25-05-2024

Name of Customer :Kumari Shilpi Singh

Name of Work/ Road :Bhualpur Katsa Road To PaMMGSY[SC]him Ahir Tola Tak

Sr.no Location o Corrected U.I Road catagory
test(in km) value(mm/km)

1	0.1	3256 G
2	0.1	3259 G
3	0.1	3354 G
4	0.1	3156 G
5	0.1	3256 G
6	0.1	3358 G
7	0.1	3356 G
8	0.1	3256 G
9	0.1	3054 G
10	0.1	3452 G
11	0.1	3125 G
12	0.1	3288 G
13	0.1	3256 G
14	0.1	3418 G
15	0.1	3356 G
16	0.1	3258 G
17	0.1	3369 G
18	0.1	3289 G
19	0.08	3085 G

[Signature]
25/05/2024

[Signature]
25/05/2024
2

[Signature]
25/5/24

[Signature]
25/5/24

Matthausa Prakhanda Se bhua/pur Katsa
Schedule XLV-Form No. 134
Road Se Panchim tola Ahir tola.

कार्यपालक अभियन्ता
पञ्चिम बंगाल सरकार
कार्य प्रपत्र, १३४

23/0005

DIVISION

Matthausa

SUB-DIVISION

Kumari Shilpi Singh

MEASUREMENT BOOK

966

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of work:- Const ⁿ of Road from Marhau-					
sa - Prakhanda Me. Bhualpur Khasa					
Road So Pachim Ahiriyola Tak.					
Agency:- Kumeri Shilpi Singh					
Agreement No - 08/MR-8054-N/MBD/2023-24					
Date of commencement - 06.10.2023					
Date of completion - 05.07.2024					
Date of Measurement - 20/06, 02/07/24					
C/D work					
① E/W excavation in foundation					
— do — do — all complete job					
2x	9.10	2.30	1.60	$\frac{72.80 \text{ m}^3}{66.90 \text{ m}^3}$	
4x	1.60	2.42	1.60	24.78 m ³	
1x	6.95	1.40	0.25	2.48 m ³	
					100.06 m ³
② Pro pcc in foundation —					
— do — do — all complete job —					
2x	9.10	2.30	0.200	8.37 m ³	
4x	1.60	2.12	0.200	2.71 m ³	
					11.08 m ³
④ Pro 100 A Brick work (1:4) in founda					
— do — do — all complete job.					
2x	$\frac{8.90 + 7.90}{2}$	$\frac{2.10 + 1.50}{2}$			
					$\times 1.40 = 41.83 \text{ m}^3$
4x	$1.60 \times \frac{1.92 + 1.32}{2}$	$\times 1.40$		14.51 m ³	
					56.34 m ³
Sand filling in foundation —					
— do — all complete continuation.					
1x	7.70				

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
			B.P.P.		
12/13 Proc & Fixing RECMIS grad km & 200m					
Stone — do — do — all complete job					
11/13 Ordinary km stone					
P-19	03 Nos	of	3237.75 each		9713.00
8/14 200m stone					
P-19	07 Nos	of	884.56 each		6192.00
13/15 Proc & Fixing Direction & place indi.					
beqrd — do — do — all complete job					
P-19	1.92 m ²	of	15065.59/m ²		28926.00
14/16 Proc & Fixing Traffic sign beqrd					
— do — do — all complete job					
i/16 600mm equilateral triangle					
P-20	06 Nos	of	4526.85 each		27161.00
ii/17 600mm circular					
P-20	04 Nos	of	4445.58 each		17782.00
iii/18 600 x 450mm rectangular					
P-20	02 Nos	of	4301.84 each		8604.00
15/19 Proc & Fixing RECMIS grad Boundary pillar					
— do — do — all complete job					
P-20	12 Nos	of	764.56 each		9175.00

Continuation 5906,574.00

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
			B-1 st B		
16/21 Planting of Trees with one Year					
Maint ⁿ - do - do - all complete job					
P-20,	174 Nos	@	1230.09 each	f	214036.00
17/23 Paving & applying Hot applied Road					
Marking - do - do - all complete job					
P-20,	377.00 m ²	@	825.75/m ²	f	311308.00
18/24 Paving & fixing Log at Maintenance -					
do - do - all complete job					
P-21	02 Nos	@	11621.73 each	f	23243.00
19/25 E/W excavation in foundation					
do - do - all complete job					
P-14,	100.06 m ³	@	410.66/m ³	-f	41091.00
20/26 Sand filling in foundation					
do - do - all complete job					
P-14,	2.03 m ³ limit 2.029 m ³				
		@	591.17/m ³	-f	1197.00
21/27 Paving & fixing in foundation					
do - do - all complete job					
P-14,	11.08 m ³				
P-15,	3.16 m ³				
	14.24 m ³	@	8038.58/m ³	-f	114469.00
		@	66		11918.00

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
			B.F 68		
22/28 Pro. 100 A B/W (1:4) in Foundation					
— do — do — all complete job					
P-14,	56.34 m ³ Limit	56.32 m ³			
	@ R 6358.56/m ³				R 358,114.00
23/29 Pro 100 A B/W (1:4) in Sub-structure					
— do — do — all complete job					
P-15,	39.75 m ³ Limit	39.394 m ³			
	@ R 6643.48/m ³				R 2,61,713.00
24/30 Pro RCC/pecm 20 in Sub-structure					
— do — do — all complete job					
P-15,	4.45 m ³ Limit	4.428 m ³			
	@ R 8548.60/m ³				R 37853.00
25/31 Pro Bitumen paint over Cap &					
Dirt — do — do all complete job					
P-15, 16,	9.00 m ² @ R 20.69/m ²				R 186.00
26/32 Pro RCC m 25 in Deck Slab					
— do — do — all complete job					
P-16,	8.01 m ³ @ R 9271.69/m ³				R 74266.00
27/33 S.F.P HYSD bar reinforcement					
— do — do — all complete job					
P-15,	0.278 mt				
P-16,	0.881 mt				
	1.159 mt Limit 1.156 mt				
	@ R 83609.76/m ³				R 96,653.00
					C.O R 7440,703.00

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
28/34 Pro 8 filling joint Sealing Compound					
—d—d—d all complete job					
P-17,	15.00 m	@	57.30 / m		860.00
29/35 Pro 100 A B/W (1:3) in Parapet					
—d—d—d all complete job					
P-17,	4.32 m	@	353.55 / m		27447.00
30/36 Pro 15 mm thick C. Plaster (1:4)					
—d—d—d all complete job					
P-17	89.64 m ²	@	216.65 / m ²		19088.00
31/37 Pro 15 mm thick Cement punning.					
—d—d—d all complete job					
P-17, 18	29.76 m ²	@	68.35 / m ²		2034.00
32/38 Pro weep holes in abt & R/W					
—d—d—d all complete job					
P-17	40 Nos	@	143.25 each		5730.00
33/39 Pro 100 A B/W (1:3) in Parapet walls					
—d—d—d all complete job					
P-18	5.76 m	@	353.55 / m		2036.00
					36,596.00
34/40 Pro 15 mm thick C. plaster (1:4)					
—d—d—d all complete job					
P-18	64.36 m ²	@	216.65 / m ²		3935.00
	40.32 m ²	@	216.65 / m ²		8735.00
					C. F 75,41,193.00

Continuation

Sch. XLV—Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
35/91 Painting two coat on new farbar					
— d-d all complete for					
p. 18,	64.36 m ² of	127.28 m			8192.00
					Rs 75,49,385.00
Add 1% Labour Cess				(H) R	75,494.00
Add 18% GST				(H) R	13,58,889.00
Add S. Fees				(H)	41,380.00
				R	90,25,148.00
less 0.05% below					4513.00
				R	90,20,635.00
less Previous Payments					Rs 65,35,752.00

Rs 24,84,878.00

~~20/07/24~~

(S. K. Singh)

02/07/24

20
