

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, पालीगंज।

पत्रांक..... ४१३ डेनु पालीगंज / दिनांक 12/08/2024

प्रेषक,

ई० रवि शंकर कुमार
कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पालीगंज

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी -सह- सचिव
बिहार ग्रामीण पथ विकास अभिकरण,
ग्रामीण कार्य विभाग, पटना।

विषय:-

शीर्ष MR 3054 Under Bihar Rural Road Maintenance Policy-2018 योजना अंतर्गत
आवंटन का अधियाचना के संबंध में।


महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष MR 3054 Under Bihar Rural Road Maintenance Policy-2018 योजना अंतर्गत पथों का अधियाचना का माँग विहित प्रपत्र में तैयार कर Signed Hard Copy of Recorded IRI के साथ अधियाचना हेतु भेजी जा रही है।

अतः अनुरोध है कि उक्त योजना का आवंटन उपलब्ध करने की कृपा की जाय, ताकि संवेदक का भुगतान हो सकें।

अनु०:- यथोक्त।

विश्वासभाजन


12/8/24


12/08/24

ई० रवि शंकर कुमार
कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पालीगंज।


12-8-24

FORM GFR 19-A

(See Government of India's Decision (I) below Rule- 150
Form of Utilization Certificate up to the month- July 2024
New Maintenance Policy 2018 MR (3054)

PIU – R.W.D. Works Division Paliganj

Sl. No.	Name of Scheme	Sanction No. & Date with	Amount Received (in Lacs Rs.)	Particulars
1.	Construction of Rural Roads under New Maintenance Policy 2018 MR (3054)	Letter No. 89 & Date 31.07.2024	8396.75221	Certified that out of Rs 8396.75221 Lakhs received upto the years 23-24 in favour of Ex. Engineer, RWD Works Division, Paliganj a sum of Rs 8094.28045 lakhs has been utilized for the purpose of New Maintenance Policy 2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs 302.47176 lakhs remaining unutilized at the end of the period .
	Total		8396.75221	

2. Certified that I have satisfied may self that the conditions on which the grants in aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kinds of Checks exercised-

- Works have been supervised by Executive Engineer/ Superintending Engineer
- Periodical inspection has been conducted by Executive engineer/ Superintending Engineer
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer / Executive Engineer
- All other codal formalities have been observed.

3. Physical Progress achieved-

- Construction of Road Works
- Construction of C.D. Works

Gana
12/08/24
D.A.O.
RWD (w) Div. Paliganj

SM
12/8/24
Executive Engineer
Rural Work Department
Work Division Paliganj


SM
12/8/24
12.08.24






Requisition Format for Scheme Head-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Division : Paliganj

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of Road IRJ (in mm/Km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount of (in Lakh)	Amount (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/PA/PAL/2 4/0002	NH-98 - KARASA	10100102207	6120 & 04.12.2023	1.48	70.582	65.11524	9.33236	13/MBD/MR-3054/2023-24 & 15.03.2024	14.12.2024	01.07.2024	2692.933	25mm SDBC	5%	62.59000	62.59000	2.44188	कमाल बाबा जी द्वारा प्रस्तावित कार्य विभिन्न स्तरों पर चल रहा है। अतिरिक्त कार्य भी प्रस्तावित है। अतिरिक्त कार्य भी प्रस्तावित है। अतिरिक्त कार्य भी प्रस्तावित है।
2	RM/PA/PAL/2 4/0002	CHECHAUL - CHAK CHEAUL	10100102099	6120 & 04.12.2023	1.28	62.695	55.12721	10.10592	13/MBD/MR-3054/2023-24 & 15.03.2024	14.12.2024	22.05.2024	2898.769	25mm SDBC	5%	50.10625	49.54398	2.44628	
3	RM/PA/PAL/2 4/0002	Akwarpur - sawarchak (pradhanmantri gram sarak yojna) to Jampur - nauwarpur path khatiya dariyapur madhya	10100507020	6120 & 04.12.2023	0.77	37.578	27.08008	5.36573	13/MBD/MR-3054/2023-24 & 15.03.2024	14.12.2024	24.05.2024	2486.125	25mm SDBC	5%	25.82433	25.82433	1.17634	
4	RM/PA/PAL/2 4/0002	NAWAHI PWD - SOHRA MAHADALIT TOLA	10100102173	6120 & 04.12.2023	0.850	47.097	37.62229	6.65170	13/MBD/MR-3054/2023-24 & 15.03.2024	14.12.2024	05.07.2024	2951	25mm SDBC	5%	34.27004	34.27004	2.97296	
5	RM/PA/PAL/2 4/0002	Nagwan - Karai Main Road - Gadarpur Link Road	NEA220001585	6120 & 04.12.2023	1.525	67.165	54.78884	14.63012	13/MBD/MR-3054/2023-24 & 15.03.2024	14.12.2024	24.06.2024	2857.93700	25mm SDBC	5%	50.96659	50.96659	3.63440	
6	RM/PA/PAL/2 4/0002	Special repair of road from sadisopur road to Bihra basantchak via raunia mushari mahadalit tola	10100508057	6120 & 04.12.2023	1.025	56.507	40.92796	9.09094	13/MBD/MR-3054/2023-24 & 15.03.2024	14.12.2024	27.06.2024	2309.36300	25mm SDBC	5%	37.67246	37.67246	3.18605	


 12/08/24
 Divisonal Accounts Officer,
 Rural Work Department
 Work Division Paliganj


 12/8/24
 Executive Engineer
 RWD Works Division, Paliganj


 12-8-24

 12/08/24

Name of The Road : CHECHAUL - CHAK CHEAUL

Length : 1.280 KM

Package No.: RM/PA/PAL/24/0002

Division : Paliganj

Block : Naubatpur

Contractor Name : Progressive Engicon Private Limited

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event			
		No.	In km	In mm	Rate	mm/km	mm/km	ROAD			Y = 0 * X ^ 2 + 0.936 * X + 278.4			
10/ 04/ 24	11:25:00	60	0.1	220	0	2200	2337	G	25.499935	84.956029	Normal	X = 3000		
10/ 04/ 24	11:25:22	60	0.1	290	30.3	2900	2992	G	25.499197	84.95555	Normal	Y = 3085		
10/ 04/ 24	11:25:47	60	0.08	210	30.3	2100	2244	G	25.0499114	84.955465	Normal			
10/ 04/ 24	11:33:12	61	0.1	270	0	2700	2805	G	25.498207	84.954353	Normal			
10/ 04/ 24	11:33:38	61	0.1	210	30.3	2100	2244	G	28.498004	84.953406	Normal	(R) RURAL ROAD		
10/ 04/ 24	11:33:57	61	0.1	330	30.3	3300	3367	G	25.497329	84.95286	Normal	Good	Average	Poor
10/ 04/ 24	11:34:21	61	0.1	350	20.2	3500	3554	G	25.496162	84.952471	Normal	<4000	4001-5000	>5001
10/ 04/ 24	11:34:44	61	0.1	240	30.3	2400	2524	G	25.49539	84.951914	Normal			
10/ 04/ 24	11:35:08	61	0.1	290	20.2	2900	2992	G	25.49459	84.95159	Normal			
10/ 04/ 24	11:35:30	61	0.1	330	20.2	3300	3367	G	25.494034	84.95146	Normal			
10/ 04/ 24	11:35:52	61	0.1	270	30.3	2700	2805	G	25.493174	84.951139	Normal			
10/ 04/ 24	11:36:14	61	0.1	330	20.2	3300	3367	G	25.492348	84.951394	Curve			
10/ 04/ 24	11:36:37	61	0.1	300	20.2	3000	3086	G	25.491747	84.952219	Curve			
Total			1.28	3640	282.8	36400	37684		334.0000284	1104.38985				
Average						2800	2898.769							

Sany
10.4.24
P. P. Gangar

SP
10/4/24
GE



Name of Customer : Progressive Engicon Private Lin
 Name of Work/ Road : CHECHAUL - CHAK CHEAUL
 Lab Job number :
 Date : 10-04-2024
 Section No. : 60

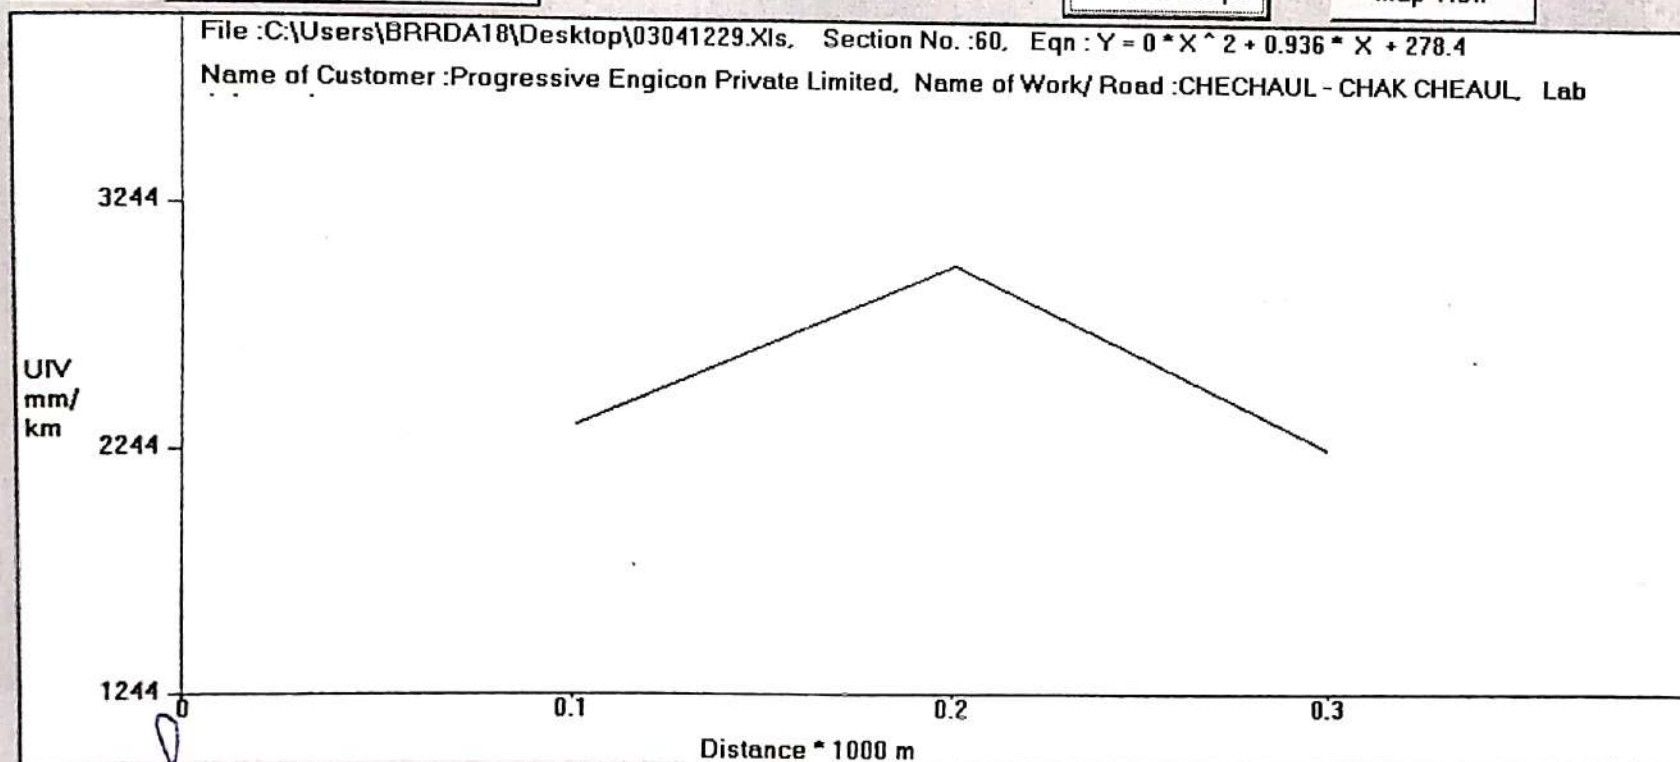
Test Date : 10-04-2024 Road Name : CHECHAUL - CHAK CHEAUL
 Machine No : 19206 Road Type : (R) RURAL ROAD
 Start S No : Side :
 Start E No : Interval
 Weather : UIV Range : 1244 To 4000 1000 mm/km
 Start Location : Dist Range : 0 To 0.4 0.1 * 1000 m
 End Location : Equation : $Y = 0 * X^2 + 0.936 * X + 278.4$

Print

Generate Report and Graph

Redraw Graph

Map View



10.4.24
 PT Engineer

10/4/24
 GG



Customer: Progressive Engicon Private Limited
 Name of Work/ Road: CHECHAUL - CHAK CHEAUL
 Lab Job number:
 Date: 10-04-2024
 Section No. 61

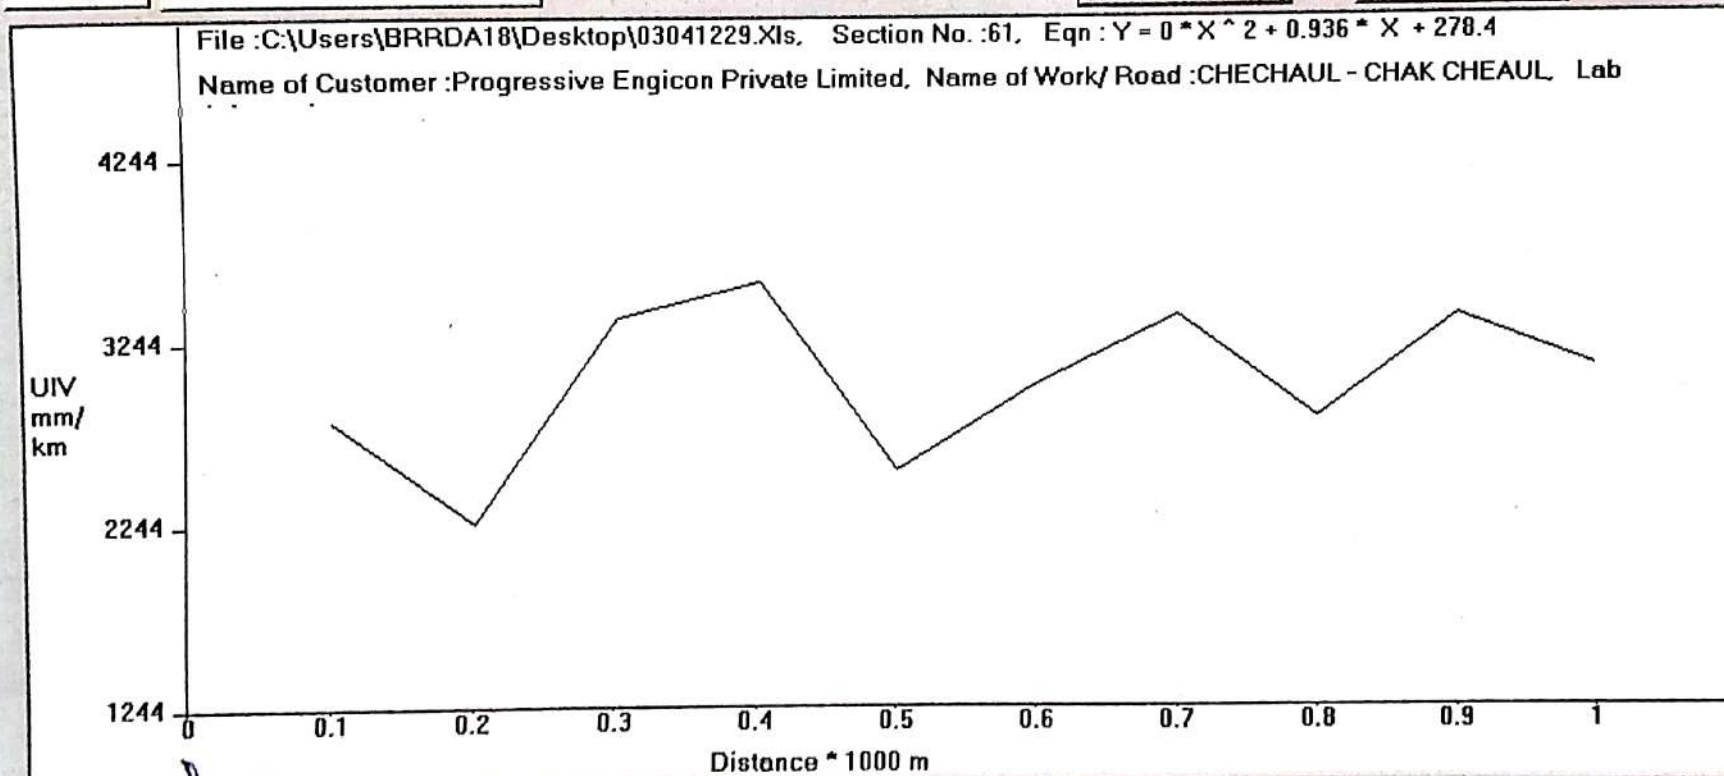
Test Date: 10-04-2024 Road Name: CHECHAUL - CHAK CHEAUL
 Machine No: 19206 Road Type: (R) RURAL ROAD
 Start S No: Side: Interval
 Start E No:
 Weather:
 UIV Range: 1244 To 5000 1000 mm/km
 Dist Range: 0 To 1.1 0.1 * 1000 m
 Start Location:
 End Location:
 Equation: $Y = 0 * X^2 + 0.936 * X + 278.4$

Print

Generate Report and Graph

Redraw Graph

Map View



10.4.24
 27 of manager.

10/4/24
 GG

N/W - CHECHAUL TO CHAK CHECHAUL

Schedule XLV Form No. 134.

Paliganj

DIVISION

Naubatpur

SUB-DIVISION

Progressive Engicon PVT LTD

Measurement Book

753

Ag No - 13 MBD/MR - 3054 New maint. policy 2018/23-24

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
2nd and final bill (for Repair work only)					
Name of work - Repair and five year maintenance of road from Checkaul to Chate Checkaul under MR-3054 New maint. Policy 2018.					
Name of Contractor - Progressive Engineers					
Attd. Dungs Ashram Gali Bailey road Sheikhpura Patna.					
Agreement no - 13 MBD/MR-3054 New maint. Policy 2018/2023-24					
Date of commencement - 15-03-2024					
Date of completion - 14-12-2024					
work done					
① Construction of Subgrade and earthen shoulders with approved material local upto 100m					
do do					
reporting					
$2 \times 24m \times 30.m \times 0.4m \times 0.3m = 14.40m^3$					
$2 \times 30m \times 30.m \times 0.4m \times 0.3m = 21.60$					
Qty = $36.00m^3$					
② Providing and erecting W metal beam crash barrier					
do do					
$1 \times 50m = 50.00m$					

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
<u>ABSTRACT OF COST</u>					
① Clearing & Grubbing of road land					
Qty vide T.M.B.P. - (16) 0.242 Hec					
@ 74926.08/Hec					18616.50
② Const ⁿ of Subgrade					
Qty vide T.M.B.P. - (16) 2 (10)					
= (399.36m ³ + 36.00m ³)					435.36m ³
@ 271.63/m ³					118257.50
③ Const ⁿ of G.S.B. course					
Qty vide T.M.B.P. - (16) 40.62m ³					
@ 2237.56/m ³					90890.50
④ Const ⁿ of W.B.M. course					
Qty vide T.M.B.P. - (16) 33.10m ³					
@ 4895.22/m ³					162032.50
⑤ Const ⁿ of W.B.M. course					
Qty vide T.M.B.P. - (16) 62.94m ³					
@ 4780.94/m ³					300912.50
⑥ P.V. Primer coat (SS-1)					
Qty vide T.M.B.P. - (16) 839.14m ²					
@ 57.05/m ²					47873.50
⑦ P.V. Tack coat (RS-1)					
Qty vide T.M.B.P. - (16) 2780.35m ²					
@ 19.42/m ²					53994.50
⑧ Paving of S.D.B.C.					
Qty vide T.M.B.P. - (16) 69.504m ³					
@ 13085.59/m ³					909501.50
⑨ P.V. P.L.C.					
Qty vide T.M.B.P. - (16) 11.214m ³					
@ 4318.61/m ³					48429.50
Continuation					
Grand Total					1750504.50

25.06.22

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(17) P/R road work done					
Qty side T.M.B.P. (17)		140.80m ²			
@ 886.50/m ²					1248192
(18) P/R road work done					
Qty side T.M.B.P. (17)		100.00m ²			
@ 995.39/m ²					99539
(19) P/R bridge Main					
Qty side T.M.B.P. (17)		03.14			
@ 11025.51/cu					330722
(20) P/R 300mm dia HP					
Qty side T.M.B.P. (17)		15.00			
@ 822.48/m					123372
Add. 18% GST					7,87,678
Add. 1% L. cen					43760
Add. S. fee side T.M.B.P. (18)					50,3252
P- (17)					1282
					RS 52,57,882
Less 0.05% below as per Govt. (17)					2,629
					RS 52,55,253
Less previous bill paid					(17) 49,54,398
					Payable RS 3,00,855

Continuation
