

कार्यपालक अभियंता का कार्यालय ग्रामीण कार्य विभाग, कार्य प्रमंडल, पालीगंज।

पत्रांक..... ९१३ हेतु पालीगंज / दिनांक 12/08/2024

प्रेषक,

ई० रवि शंकर कुमार
कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पालीगंज

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी -सह- सचिव
बिहार ग्रामीण पथ विकास अभिकरण,
ग्रामीण कार्य विभाग, पटना।

विषय:- शीर्ष MR 3054 Under Bihar Rural Road Maintenance Policy-2018 योजना अंतर्गत
आवंटन का अध्याचना के संबंध में।


महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष MR 3054 Under Bihar Rural Road Maintenance Policy-2018 योजना अंतर्गत पथों का अध्याचना का माँग विहित प्रपत्र में तैयार कर Signed Hard Copy of Recorded IRI के साथ अध्याचना हेतु भेजी जा रही है।

अतः अनुरोध है कि उक्त योजना का आवंटन उपलब्ध करने की कृपा की जाय, ताकि संवेदक का भुगतान हो सकें।

अनु०:- यथोक्त।

विश्वासभाजन


12/8/24


12/08/24

ई० रवि शंकर कुमार
कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, पालीगंज।


12-8-24

FORM GFR 19-A

(See Government of India's Decision (I) below Rule- 150
Form of Utilization Certificate up to the month- July 2024
New Maintenance Policy 2018 MR (3054)

PIU – R.W.D. Works Division Paliganj

SL. No.	Name of Scheme	Sanction No. & Date with	Amount Received (in Laes Rs.)	Particulars
1.	Construction of Rural Roads under New Maintenance Policy 2018 MR (3054)	Letter No. 89 & Date 31.07.2024	8396.75221	Certified that out of Rs 8396.75221 Lakhs received upto the years 23-24 in favour of Ex. Engineer, RWD Works Division, Paliganj a sum of Rs 8094.28045 lakhs has been utilized for the purpose of New Maintenance Policy 2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs 302.47176 lakhs remaining unutilized at the end of the period .
	Total		8396.75221	

2. Certified that I have satisfied may self that the conditions on which the grants in aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kinds of Checks exercised-

- Works have been supervised by Executive Engineer/ Superintending Engineer
- Periodical inspection has been conducted by Executive engineer/ Superintending Engineer
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer / Executive Engineer
- All other codal formalities have been observed.

3. Physical Progress achieved-

- Construction of Road Works
- Construction of C.D. Works

Gana
12/08/24
D.A.O.
RWD (w) Div. Paliganj

SM
12/8/24
Executive Engineer
Rural Work Department
Work Division Paliganj

SM
12/8/24
12.08.24



Requisition Format for Scheme Head-(3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Division : Paliganj

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of Road IRJ (in mm/Km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen content in Percentage	Previous Total Allotted Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount of (in Lakh)	Amount (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/PA/PAL/2 4/0002	NH-98 - KARASA	10100102207	6120 & 04.12.2023	1.48	70.582	65.11524	9.33236	13/MBD/MR-3054/2023-24 & 15.03.2024	14.12.2024	01.07.2024	2692.933	25mm SDBC	5%	62.59000	62.59000	2.44188	कमाल बाई नौवीं प्रमाणित रूप विनिर्देशों के अनुसार है यह सड़क का अधिकांश हिस्सा 10 मीटर का है।
2	RM/PA/PAL/2 4/0002	CHECHAUL - CHAK CHEAUL	10100102099	6120 & 04.12.2023	1.28	62.695	55.12721	10.10592	13/MBD/MR-3054/2023-24 & 15.03.2024	14.12.2024	22.05.2024	2898.769	25mm SDBC	5%	50.10625	49.54398	2.44628	
3	RM/PA/PAL/2 4/0002	Akwarpur - sawarchak (pradhanmantri gram sarak yojna) to Jampur - nauwatpur path bhava daryapur madhya	10100507020	6120 & 04.12.2023	0.77	37.578	27.08008	5.36573	13/MBD/MR-3054/2023-24 & 15.03.2024	14.12.2024	24.05.2024	2486.125	25mm SDBC	5%	25.82433	25.82433	1.17634	
4	RM/PA/PAL/2 4/0002	NAWAHI PWD - SOHRA MAHADALIT TOLA	10100102173	6120 & 04.12.2023	0.850	47.097	37.62229	6.65170	13/MBD/MR-3054/2023-24 & 15.03.2024	14.12.2024	05.07.2024	2951	25mm SDBC	5%	34.27004	34.27004	2.97296	
5	RM/PA/PAL/2 4/0002	Nagwan - Karai Main Road - Gadarpur Link Road	NEA220001585	6120 & 04.12.2023	1.525	67.165	54.78884	14.63012	13/MBD/MR-3054/2023-24 & 15.03.2024	14.12.2024	24.06.2024	2857.93700	25mm SDBC	5%	50.96659	50.96659	3.63440	
6	RM/PA/PAL/2 4/0002	Special repair of road from sadisopur road to Bihta basantchak via raunia mushari mahadalit tola	10100508057	6120 & 04.12.2023	1.025	56.507	40.92796	9.09094	13/MBD/MR-3054/2023-24 & 15.03.2024	14.12.2024	27.06.2024	2309.36300	25mm SDBC	5%	37.67246	37.67246	3.18605	

12/08/24
Divisonal Accounts Officer,
Rural Work Department
Work Division Paliganj

12/8/24
Executive Engineer
RWD Works Division, Paliganj

12-8-24
12-08-24

Name of The Road : Nagwan- Karai Main Road - Gadaipur Link Road

Length : 1.525 KM

Package No. : RM/PA/PAL/24/0002

Division Paliganj

Block : Naubatpur

Contractor Name : Progressive Engicon Private Limited

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event			
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			$Y = 0 * X^2 + 0.936 * X + 278.4$			
02/06/24	10:25:00	32	0.1	260	0	2600	2712	G	25.529944	84.971927	Normal	X = 3200		
02/06/24	10:25:22	32	0.1	230	30.3	2300	2431	G	25.530129	84.971026	Normal	Y = 3273		
02/06/24	10:25:52	32	0.1	290	30.3	2900	2992	G	25.530424	84.969833	Speed Breaker			
02/06/24	10:26:12	32	0.1	260	30.3	2600	2712	G	25.530548	84.969046	Normal			
02/06/24	10:26:31	32	0.1	280	30.3	2800	2899	G	25.530849	84.968025	Normal	(R) RURAL ROAD		
02/06/24	10:26:52	32	0.1	230	30.3	2300	2431	G	25.530808	84.967127	Normal	Good	Average	Poor
02/06/24	10:27:11	32	0.1	300	20.2	3000	3086	G	25.530376	84.966646	Curve	<4000	4001-5000	>5001
02/06/24	10:27:27	32	0.1	270	30.3	2700	2805	G	25.529433	84.96656	Normal			
02/06/24	10:27:51	32	0.1	280	30.3	2800	2899	G	25.529196	84.965934	Normal			
02/06/24	10:28:12	32	0.1	270	30.3	2700	2805	G	25.529328	84.964908	Normal			
02/06/24	10:28:12	32	0.1	260	30.3	2600	2712	G	25.529911	84.964434	Normal			
02/06/24	10:28:49	32	0.1	320	20.2	3200	3273	G	25.5304	84.96402	Curve			
02/06/24	10:29:10	32	0.1	280	30.3	2800	2899	G	25.530568	84.963002	Normal			
02/06/24	10:29:26	32	0.1	310	30.3	3100	3180	G	25.530884	84.962092	Normal			
02/06/24	10:29:55	32	0.1	250	30.3	2500	2618	G	25.531186	84.961105	Normal			
02/06/24	10:30:02	32	0.025	320	30.3	3200	3273	G	25.530903	84.960954	Normal			
Total			1.525	4410	434.3	44100	45727		408.484887	1359.456639	Normal			
Average						2756.25	2857.937							

Sany
 03.06.24
 ST Manager

03/06/2024
 OB

Sany
 03/06/24
 EE



Name of Customer : Progressive Engicon Private Lin
Name of Work/ Road : Nagwan- Karai Main Road - Ga
Lab Job number :
Date : 02-06-2024
Section No. : 32


Test Date : 02-06-2024 Road Name : Nagwan- Karai Main Road - Ga
Machine No : 19206 Road Type : (R) RURAL ROAD
Start S No : Side :
Start E No : Interval
Weather : UIV Range : 1431 To 4000 1000 mm/km
Start Location : Dist Range : 0 To 1.7 0.1 * 1000 m
End Location : Equation : $Y = 0 * X^2 + 0.936 * X + 278.4$

Print

Generate Report and Graph

Redraw Graph

Map View

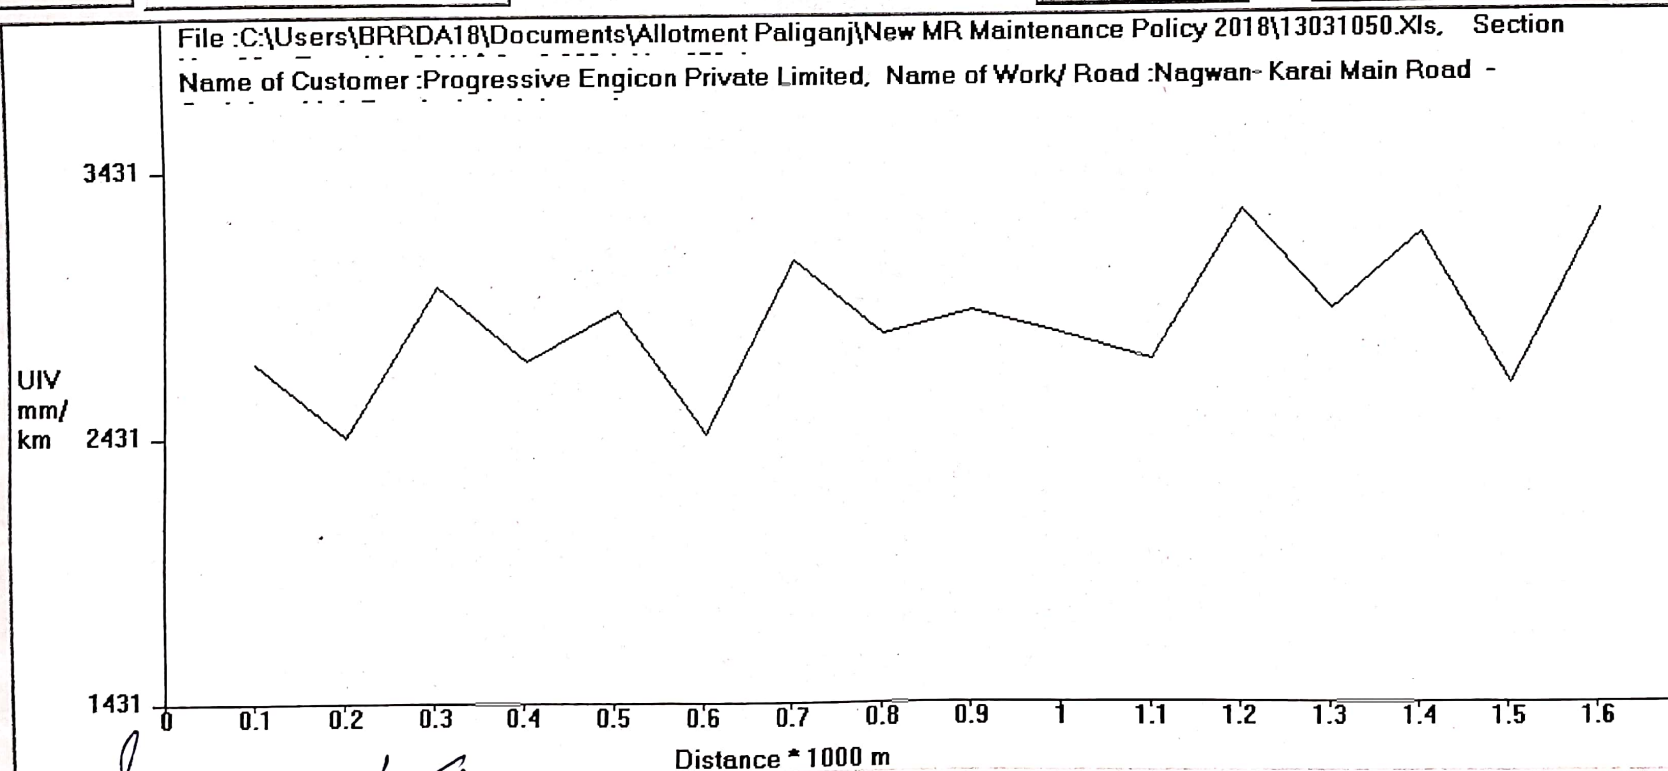

02/06/24
FT Manager
03/6/24
GE

03/6/24
GE



Schedule XLV-Form No. 134

N/W - Nagma Karai main Road to Godaichak
LINK ROAD

Paliganj

DIVISION

Naubatpur

SUB-DIVISION

Progressive Engicon PVT LTD

MEASUREMENT BOOK

751

Ag NO - 13 MBD/MR-3054 New maint policy 2018/23-24



Sch. XLV—Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
2nd and Final bill (for Repair work)					
Name of work - Repair and five year					
Maintenance of road from Nagma					
Karai main road to Godaichale					
link road under MR-3054 New main					
Policy 2018.					
Name of contractor - Progressive					
Engicon Pvt. Ltd. Durga Ashram					
Gali Bailey road Patna					
Agreement No - 13MB2/MR-3054 New					
maint. Policy 2018/2023-24					
Date of commencement - 15-03-2024					
Date of completion - 14-12-2024					
Date of entry - 24-06-2024					
work done					
① Construction of Subgrade					
and earthen shoulder with					
Approved accidental buildup					
to 100mm ch					
CH- 0 to 180m					
$2 \times 6.47 \times 30.00 \times 0.50 \times 0.30 = 55.08m^3$					
CH- 1320m to 1420m 137					
$2 \times 3.77 \times 30.00 \times 0.60 \times 0.30 = 32.40$					
$2 \times 1.47 \times 10.00 \times 0.60 \times 0.30 = 3.60$					
Total 91.08m ³					

Continuation

Sch. XLV—Form No. 134

Sch. XLV—Form No. 134					Contents of area
Particulars	Details of actual measurement				
	No.	L.	B.	D.	
ABSTRACT OF COST					
① clearing & grubbing road land -					
Qty side T.M.B.P. - (11)	0.105 Hec				
	@ 76926.08/Hec				234622
② Contn of Subgrade -					
Qty side T.M.B.P. - (11) 2 - (15)					
	(813.08m ³ + 91.08m ³)				
	= 604.08m ³ @ 271.63/m ³				16408620
③ Contn of G.S.B Gravel -					
Qty side T.M.B.P. - (11)	71.04m ³				
	@ 2310.88/m ³				16416520
④ P.V. W.S.M Gravel -					
Qty side T.M.B.P. - (11)	65.88m ³				
	@ 5063.11/m ³				33350720
⑤ P.V. W.S.M Gravel -					
Qty side T.M.B.P. - (12)	97.43m ³				
	@ 4928.61/m ³				48019420
⑥ P.V. Primer Coat (S.S.T) -					
Qty side T.M.B.P. - (12)	1299.0m ²				
	@ 57.05/m ²				7410820
⑦ P.V. Tack coat (R.S.T) -					
Qty side T.M.B.P. - (12)	4732.75m ²				
	@ 19.42/m ²				9191020
⑧ P.V. S.B.C -					
Qty side T.M.B.P. - (12)	118.316m ³				
	@ 13231.45/m ³				15654922
					28969240

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(18) P.V. road widening on RT.					
Qty side T.M.B.P. (18)		246.0m			
		QD 886.50/m ²			218079.20
(19) P.V. road widening in C.O. rd.					
Qty side T.M.B.P. (19)		54.0m			
		QD 995.39/m ²			53751.20
(20) P.V. road widening in main rd.					
Qty side T.M.B.P. (20)		83.4m			
		QD 11043.93/2000			33132.20
(21) Portico Masonry wall (1:3)					
Qty side T.M.B.P. (21)		1.296m			
		QD 6541.30/m ²			8478.20
(22) Plaster & puccin on (1:4)					

Qty side T.M.B.P. (17)		60.48m			
		QD 2000 191.91/m ²			11607.20
(23) Pataki plaster on wall					
Qty side T.M.B.P. (17)		60.48m			
		QD 139.16/m ²			8416.20
(24) P.V. road widening on HP					
Qty side T.M.B.P. (17)		15.0m			
		QD 816.84/m			12253.20
					45,44,882.20
Add. 18% GST					8,18,079.20
Add. 1% L.C. on					45,44,992.20
Add. S. Fee side T.M.B.P. (18)					54420.00
					54,62,832.20
Less 0.05% below as per Govt (100)					2,731.00
					54,60,099.20
Less previous bill payment up to 30					96,659.20
					Payable Rs. 5,63,440.00

Continuation

for 24/06/2024
RE
