

कार्यपालक अभियंता, का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल बिहारशरीफ

पत्रांक.....1528/2024 बिहारशरीफ, दिनांक.07.12.24

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ ।

सेवा में,

नोडल पदाधिकारी 3054
ग्रामीण कार्य विभाग, बिहार, पटना

विषय:-

नई अनुरक्षण नीति-2018 अन्तर्गत आवंटन उपलब्ध करने के संबंध में।


महाशय,

उपर्युक्त विषयक से संबंधित नई अनुरक्षण नीति-2018 अन्तर्गत इस प्रमंडल द्वारा कराये जा रहे पथों के निर्माण कार्य के लिये आवंटन उपलब्ध करने हेतु अधियाचना पत्र समर्पित की जा रही है।

अतः अनुरोध है कि पथ में कराये गये कार्यों के विरुद्ध भुगतान हेतु संलग्न सूची के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय ताकि संवेदक को भुगतान किया जा सके।

अनु०:- यथोक्त।

विश्वासभाजन


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ
11/12/24

(See Government of India's Decision (1) below Rule-150)
Form of Utilisation Certificate up to the month of 07.12.2024

(New Maintenance Policy 2018)

Year-2024-2025

PIU- BIHARSHARIF


Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in Rs. Lacs)	Amount Received (in Rs. Lacs)	Particulars
1	Construction of Rural Roads under New Maintenance Policy 2018	Itr-125 Dt-29.11.2024	7994.97272	Certified that out of Rs 7994.97272 received & balance during the years 2024-25 in favour of Ex. Engineer, R.W.D. Works Division Biharsharif, sum of Rs 7946.92552 has been utilized for the purpose of New Maintenance Policy 2018 scheme as given in the margin for which it was sanctioned and that the balance of Rs 48.04720 lacs remaining unutilized at the end of the period under 07.12.2024
	Total Rs.		7994.97272	

2 Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned
Kind of Checks exercised :-


- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction material have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant .
- All other codal formalities have been observed.

3 Physical Progress achieved:

- Construction of Road Works.
- Construction of CD works



Divisional Accounts Officer
Rwd, Works Division
Biharsharif



Executive Engineer
Rwd, Works Division
Biharsharif

7/12/24

Revision Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)
of Works Division :- Bihar Sharif

SI No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of ISI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Increase in Allotment	Remarks
					Length (in km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
	RM/N/A/B IH/24/000 6	Kayampur Makdampur to Ananpur	10200612021	1086 01 Mar 2024	1.350	68.10000	42.47226	7.13841	MBD- 03/2024-25 05/09/2024	04-06-2025	0	2143	25	5.02	0.00000	0.00000	39.77528	
	RM/N/A/B IH/24/000 6	Construction of road from barandi punha east side to jagandanpur village	10200613020	1086 01 Mar 2024	1.370	54.80400	29.80661	10.62461	MBD- 03/2024-25 05/09/2024	04-06-2025	0	2358	25	5.01	0.00000	0.00000	26.20525	
	RM/N/A/B IH/24/000 3	Soyba Alipur Road to Chistapur	10200613006	29 03 Jan 2024	0.650	54.84400	43.545	6.65535	MBD- 11/2023-24 02/03/2024	01-12-2024	0	2195	25	5.01	0.00000	0.00000	37.11952	
TOTAL																	103.10005	


Total = 103.10005

- 1 Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.
- 2 Up-to-date Physical Progress has been uploaded in MIS.


Divisional Accounts Officer
Rwd, works Division Bihar Sharif


Executive Engineer
Rwd, works Division Bihar Sharif
24/12/24

File : C:\Users\kkmm1\OneDrive\Desktop\Downloads\26110930.Xls, Section No. : 50, Eqn : $Y = 0 \cdot X^2 + 0.816 \cdot X$
 Name of Customer : M/S Bijay Construction, Name of Work/ Road : Kayanpur Makdumpur to Anantpur, Lab Job

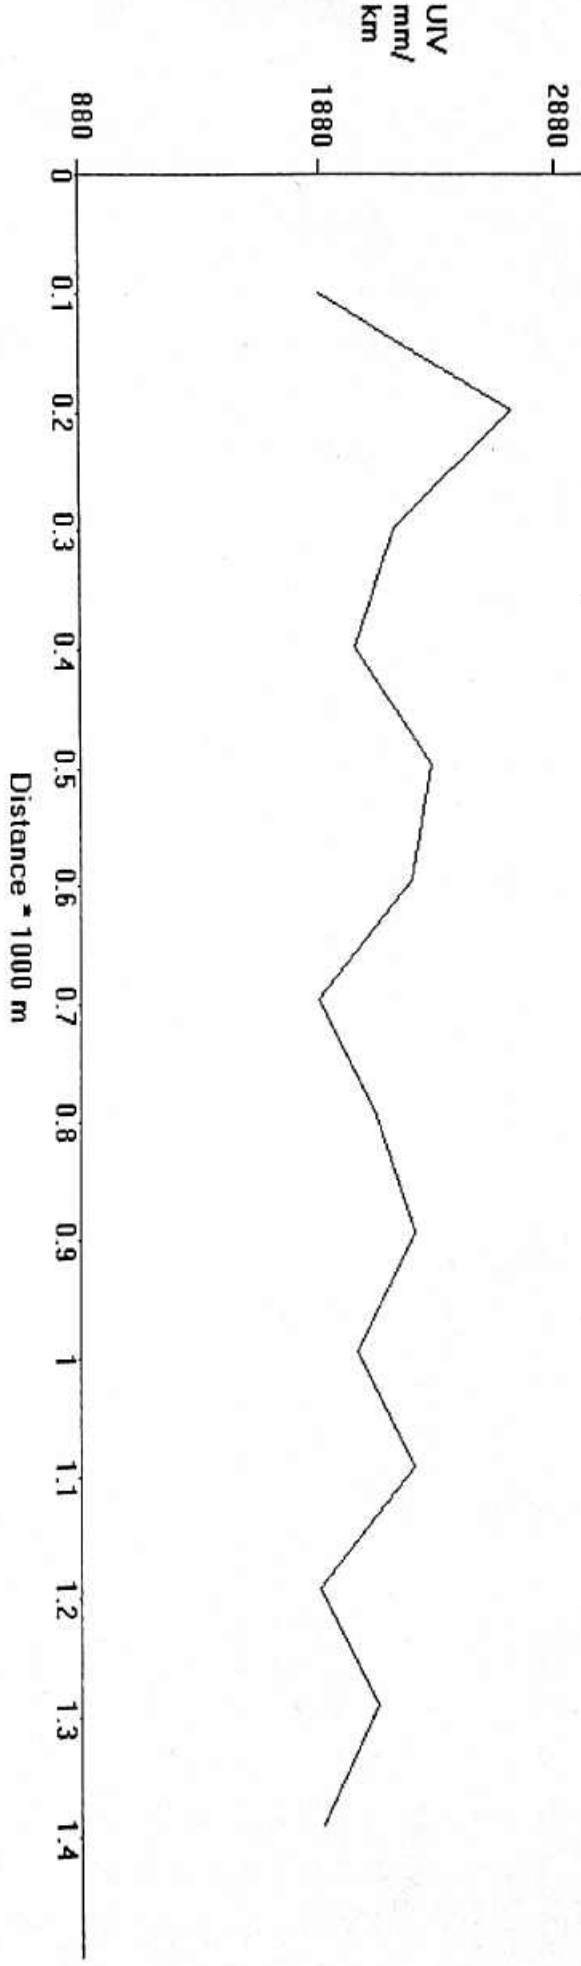

$\frac{1000}{0.816}$
 1224
 1224

$\frac{1000}{0.816}$
 1224
 1224

$\frac{1000}{0.816}$
 1224
 1224

HEAD-NEW MR
Road-Kayanpur Makdumpur to Anantpur
Con-M/S Bijay Constructions

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event			
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD						
26/11/24	7:47:32	50	0.1	200	0	2000	1880	G	25.254529	85.601291	Normal	$Y = 0 * X^2 + 0.816 * X + 249$		
26/11/24	7:48:8	50	0.1	300	10.1	3000	2696	G	25.254034	85.60102	Curve	$X = 2800$		
26/11/24	7:49:8	50	0.1	240	10.1	2400	2207	G	25.252919	85.600762	Normal	$Y = 2533$		
26/11/24	7:49:43	50	0.1	220	10.1	2200	2044	G	25.252166	85.600653	Normal			
26/11/24	7:50:18	50	0.1	260	10.1	2600	2370	G	25.250684	85.600501	Normal	(R) RURAL ROAD		
26/11/24	7:50:18	50	0.1	250	10.1	2500	2288	G	25.250008	85.600522	Normal	Good		
26/11/24	7:50:18	50	0.1	200	10.1	2000	1880	G	25.249824	85.601272	Normal	<4000		
26/11/24	7:50:53	50	0.1	230	10.1	2300	2125	G	25.250024	85.602665	Curve	Average		
26/11/24	7:50:53	50	0.1	250	10.1	2500	2288	G	25.250275	85.603047	Normal	4001-5000		
26/11/24	7:50:53	50	0.1	220	10.1	2200	2044	G	25.250391	85.60361	Normal	>5001		
26/11/24	7:51:29	50	0.1	250	10.1	2500	2288	G	25.250449	85.604224	Normal			
26/11/24	7:51:29	50	0.1	200	10.1	2000	1880	G	25.250543	85.60461	Curve			
26/11/24	7:51:29	50	0.1	230	10.1	2300	2125	G	25.250593	85.60555	Normal			
26/11/24	7:52:4	50	0.1	200	10.1	2000	1880	G	25.250743	85.606038	Normal			
						Total-	29995							
						IRI Value-	2143							

26/11/24
 26/11/24
 26/11/24

26/11/24
 26/11/24
 26/11/24

26/11/24
 26/11/24
 26/11/24

1st on A/c Bill

1.

Name of work -

Situation of work -

Agency by which work is executed -

Date of measurement -

No. and date of agreement.

(These four lines should be repeated at the commencement of the measurements relating to each work).

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of Work :- Kaganpur					
Makdumpur to Anantpur					
Name of Agency :- M/s Bijay					
Constructions					
Agreement No. :- MBD-03/2024-25					
Date of Commencement :- 05/09/2024					
Date of Completion :- 04/06/2025					

As per Record Entry Note Book No. - 37

MEASUREMENT

① Clearing and Grubbing Road land

----- do ----- do ----- e/i

2 X 10 X 30 X 1.00 = 600 m ²				
2 X 15 X 30 X 1.00 = 900 m ²				
2 X 5 X 30 X 1.00 = 300 m ²				
2 X 8 X 30 X 1.00 = 480 m ²				
2 X 7 X 30 X 1.00 = 420 m ²				
				2700 m ²
In Hectare - 2700/10,000 = 0.27 Ha				

Continuation

Sch.XLV-Form No. 134

Particulars	Details of actual measure				Contents of area
	No.	L.	B.	D.	
ABSTRACT OF COST					
(1/1) Clearing and grubbing Road Land					
----- do -----				e/i	
0.27 Ha VTMB P-01					
@ 76926.08 / Ha					Rs. 20770/-
(2/4) Construction of granular Sub-base by providing well graded material Gr. II					
----- do -----				e/i	
31.38 m ³ VTMB P-03					
@ 1491.28 / m ³					Rs. 46796/-
(3/5) Providing laying, spreading & compacting WBM Gr II					
----- do -----				e/i	
24.71 m ³ VTMB P-05					
@ 3159.21 / m ³					Rs. 78064/-
(4/6) Providing laying, spreading & compacting stone aggregate WBM Grade - III					
----- do -----				e/i	
67.48 m ³ VTMB P-07					
@ 3191.07 / m ³					Rs. 215333/-
Continuation					Rs. 360963/-

Sch.XLV-Form No. 134

Particulars	Details of actual measure				Contents of area
	No.	L.	B.	D.	
BF					360963/-
(5/7) Providing and applying Prime Coat (SS-1)					
--- do --- do ---				e/i	
899.73 m ² VTMB P-08					
@ 54.50 /m ²				Rs.	49035/-
(6/8) Providing and applying Tack Coat (RS-1) with Bitumen Emulsion					
--- do --- do ---				e/i	
2998.68 m ² VTMB P-08					
@ 18.69 /m ²				Rs.	56045/-
(7/9) Providing and laying Semi dense Bituminous Concrete					
--- do --- do ---				e/i	
74.96 m ³ VTMB P-09					
@ 12620.75 /m ³				Rs.	946051/-
(8/10) Construction of Dry lean Cement Concrete					
--- do --- do ---				e/i	
20.42 m ³ VTMB P-10					
@ 4567.19 /m ³				Rs.	93262/-
Continuation					Rs. 1505356/-

Continuation

Sch.XLV-Form No. 134

Particulars	Details of actual measure				Contents of area
	No.	L.	B.	D.	
BF					Rs 4151613/-
($\frac{12}{18}$) Providing and fixing 'Lono' of Project					
--- do --- do --- e/i					
2.00 Nos VTMB P-13					
@ 11508.79					Rs 23018/-
($\frac{13}{18}$) Providing and fixing Citizen information Board					
--- do --- do --- e/i					
2.00 Nos VTMB P-13					
@ 11508.79					Rs 23018/-
($\frac{14}{18}$) Providing and fixing Lono of Maintenance Board					
--- do --- do --- e/i					
1.00 Nos VTMB P-13					
@ 11508.79					Rs 11509/-
					Rs 4209158/-
Add Labour Cost @ 1% =					Rs 42092/-
Add GST @ 18% =					Rs 757648/-
Add Seigniorage fee @ 10% =					Rs 26585/-
					Rs 5035483/-
Less below @ 2.101% (-)					Rs 1057955/-
as per agreement					Rs 3977528/-

Continuation / 06/12/24
AE
