



कार्यपालक अभियंता का कार्यालय ग्रामीण कार्य विभाग, कार्य प्रमंडल, मढ़ौरा।

E-Mail – eerwd.marhaura@yahoo.com

पत्रांक:- 2208(अ.30) मढ़ौरा/दिनांक:- 10.12.24

प्रेषक:-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, मढ़ौरा।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण, बिहार, पटना।

विषय:- शीर्ष MR-3054 खोजनान्तर्गत बिहार ग्रामीण पथ नई अनुस्क्षण नीति-2018 के तहत स्वीकृत पथ में कराये गये कार्य का आवंटन मॉग के संबंध में।

प्रसंग:- भवदीय के पत्रांक:-113 अनु0, दिनांक:-10-01-2020

महाशय,

उपरोक्त विषयक प्रासंगिक पत्र के संबंध में कहना है कि इस कार्य प्रमंडल, अंतर्गत शीर्ष-3054 (MR-3054) अंतर्गत बिहार ग्रामीण पथ नई अनुस्क्षण नीति-2018 के तहत संवेदक गोर्बधनधारी इन्फ्राटेक प्रा0लि0 के द्वारा पथ में किये गये कार्य का अधियाचना उक्त प्रासंगिक पत्र द्वारा प्राप्त विहित प्रपत्र में भरकर आवंटन मॉग हेतु अधियाचना-पत्र सादर समर्पित की जा रही है।

अतः अनुरोध है कि अधियाचना प्रपत्र में दर्शाये गये पथवार राशि कॉलम सं0-18 के अनुरूप पथ में आवंटन उपलब्ध कराने की कृपा की जाय ताकि संबंधित संवेदक द्वारा पथ में कराये गये कार्य का भुगतान किया जा सकें।

अनु0-1) अधियाचना प्रपत्र।


2) 19 ए प्रपत्र।

3) BOMP Indicator Report संलग्न।

4) MB प्रति संलग्न।



विश्वासभाजन

H
10/12/24


10/12/24
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, मढ़ौरा।
10/12/24

FORM GER-19-A**(See Government of India'S Decision (I) below Rule -150)****Form of Utilization Certificate up to the Month of December-2024****PIU:- Executive Engineer RWD Works Division, Marhaura**

SL No	Name of Scheme	Sanction No & Date with Amount (in Lacs Rs.)	Amount Received (in lacs Rs.)	Particulars
1	Construction of Rural Roads under MR-3054 Rural Road Maintenance Policy-2018 (Ledger ID-7069)	सचिव ब्राडा के पत्रांक-125 we दिनांक-29-11-2024	11265.70862	Certified that out of Rs- 11265.70862 Lacs received during the Years, 2018-19 & 2019-20, 2020-21, 2021-22, 22-23, 23-24 & 2024-25 in favour of E.E., R.W.D. Works Division Marhaura Sum of Rs- 11209.05708 Lacs has been utilized for the Purpose of MR-3054 New Maint. Policy-2018 Scheme as given in the margin for Which it was Sanctioned and that the balance of Rs-56.65154 Lacs remaining unutilized at CFMS the end of the period under report.


**Sr. DAO****R.W.D. (W) Division Marhaura****Executive Engineer****R.W.D. (W) Division Marhaura**

Requisition Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of works Division:- Rural Work Department, Work Division, Mauhura.

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA) Total		Agreement Amount (In Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (In Lakh)	up-to-date expenditure as per MIS (In Lakh)	Requisition against work done. (In Lakh)	Remarks
					Length (in km.)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	BUNAMAR 2 (0001) MLN-23-34 Mauhura02	GAURA TEJPURWA PATH TO POKHAR TOLA AHIR TOLA TAN.	21J06M12024	Lt. No-6153 Date-05-12-2023	1.500	97.86000	79.15974	9.49817	09 MR-3054-24/ABID-2024-24 28-09-2024	27.06.2025		3091.38	N/A	N/A	0.00000	0.00000	69.36118	PCP Work Completed
Total:-															0.00000	0.00000	69.36118	

1. Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.
2. Up-to-date Physical Progress has been Uploaded in MIS.

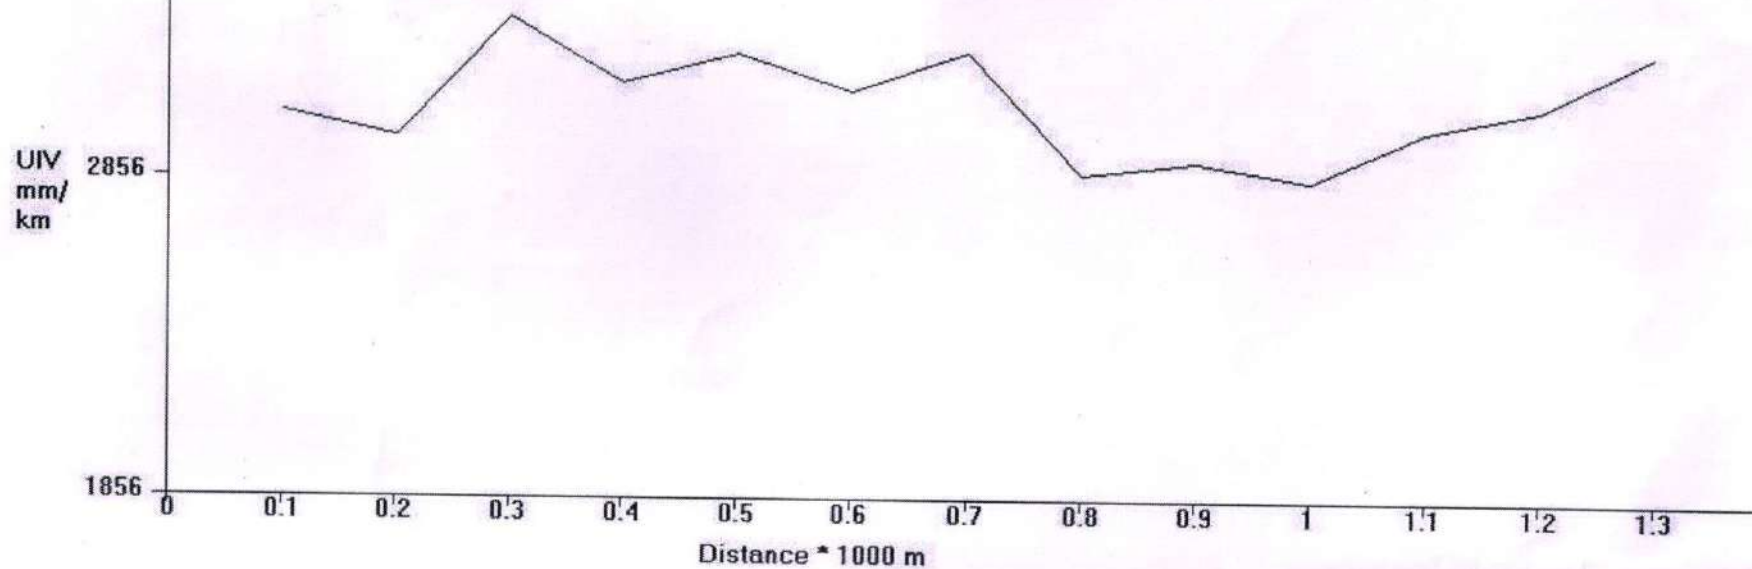

 Executive Engineer
 Rural Work Department
 Work Division, Mauhura

 10/12/24

 10/12/24

File : C:\Users\Admin\Desktop\125689.Xls, Section No. : 70, Eqn : $Y = 0 * X^2 + 0.816 * X + 249$

Name of Customer : Gobarhandhari Infratech Private Limited, Name of Work/ Road : Gaura Tejpurwa Path To Pokhari



Amor
09.12.24
A.E

Amil
10/12/24
EE
Executive Engineer
Rural Work Dept.
Works Division, Marhaura

Name of Customer :Goberdhandhari Infratech Private Limited

Name of Work/ Road :Gaura Tejpurwa Path To Pokhar Tola Ahir Tola Tak

Date	Time	Section	Length	Bumps	Speed	OR	IRI CATEGORY	Latitude	Longitude	Event
No.			in km	in mm	Rate	mm/km	mm/km	ROAD		
9/ 12/ 24	13: 11: 01	70	0.1	140	30.1	1400	3059 G	25.95201	84.79847	Normal
9/ 12/ 24	13:11:13	70	0.1	280	30.5	2800	2985 G	25.9524	84.79869	Normal
9/ 12/ 24	13:11:25	70	0.1	220	30.2	2200	3354 G	25.95283	84.79889	Normal
9/ 12/ 24	13:11:38	70	0.1	320	30.1	3200	3156 G	25.95333	84.79904	Curve
9/ 12/ 24	13: 11: 52	70	0.1	110	25.8	2500	3245 G	25.95368	84.79901	Normal
9/ 12/ 24	13: 12: 05	70	0.1	190	30.5	1900	3128 G	25.95403	84.79899	Normal
9/ 12/ 24	13:12:17	70	0.1	220	30.7	2200	3254 G	25.95423	84.79909	Curve
9/ 12/ 24	13:12:29	70	0.1	270	30.3	2700	2875 G	25.9546	84.79946	Normal
9/ 12/ 24	13: 12: 42	70	0.1	270	27.9	2700	2918 G	25.95526	84.7962	Curve
9/ 12/ 24	13: 12: 57	70	0.1	300	25.8	3000	2856 G	25.95552	84.79554	Normal
9/ 12/ 24	13:13:09	70	0.1	310	28.8	3100	3016 G	25.95577	84.79492	Normal
9/ 12/ 24	13: 25: 36	70	0.1	200	10.1	6667	3084 G	25.95605	84.79382	Curve
9/ 12/ 24	13: 26: 11	70	0.1	100	60.6	6667	3258 G	25.9563	84.79266	Normal
Length			1.3			Value IRI	3091.38			

$$Y = 0 * X^2 + 0.816 * X + 249$$

$$X = 6667$$

$$Y = 5689$$

(R) RURAL ROAD

Good Average Poor
 <4000 4001-5000 >5001

Damar
 09.12.24
 A.E

Pm P
 10/12/24
 EE
 Executive Engineer
 Rural Work Dept.
 Works Division, Marhaura

Lab Job number :386

Date :09/12/2024

Name of Customer :Goberdhandhari Infratech Private Limited

Name of Work/ Road :Gaura Tejpurwa Path To Pokhar Tola Ahir Tola Tak

Sr.no	Location of Corrected U.I test(in km) value(mm/km)	Road catagory
-------	---	---------------

1	0.1	3059 G
2	0.2	2985 G
3	0.3	3354 G
4	0.4	3156 G
5	0.5	3245 G
6	0.6	3128 G
7	0.7	3254 G
8	0.8	2875 G
9	0.9	2918 G
10	1	2856 G
11	1.1	3016 G
12	1.2	3084 G
13	1.3	3258 G

Damar
09.12.24
A.E

Amir
10/12/24
EE
Executive Engineer
Rural Work Dept.
Works Division, Marhaura

brausa Fey purwa patha to Poknas tola
Ahis tola tak.

Schedule XLV-Form No. 134

Executive Engineer

Rural Works Department

Works Division Mathura

DIVISION

Mathura

SUB-DIVISION

brobedhandhosi Infrastruch Pvt Ltd.

MEASUREMENT BOOK

1013

प्रमाणित किया जाता है कि इस मापीयुक्त
प्लान से टॉकल कुल 100 (एक सौ) रु
श्री. ए. लज्जा कुमार
सबो डिप्टी के माप से माप
माप है।


14/10/24
Executive Engineer
Rural Works Department
Works Division Marhaura
Mohammed
14/10/24

RWD(W) Division DIVISION
Marhaura.
Marhaura. SUB-DIVISION

MEASUREMENT BOOK

No. :

Name of Officer _____

Date of First Entry _____

Date of Last Entry _____

Name of Work :

Situation of Work

Agency by which work is executed :

Date of Measurement :

No. and date of agreement :

(These four lines should be repeated at the commencement of the measurements relating to each work.)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
1st an A/c Bill					
N/10 - Gauri Tejpurwar path to					
Pokhar toh Akir toh tak					
Agency - Gobardhandhari Const.					
Pvt. Ltd.					
Date of w.o - 28.09.2024					
Date of completion - 27.06.2025					
Date of measurement -					
(1) Clearing and grubbing					

2x 10x30.00 x 0.75 = 450m ²	
2x 10x30.00 x 0.75 = 450m ²	
2x 10x30.00 x 0.75 = 450m ²	
2x 10x30.00 x 0.75 = 450m ²	
2x 3x30.00 x 0.75 = 135m ²	
2x 1x10.00 x 0.75 = 15m ²	
	= 1950m ²
	= 0.195 hee.

(2) Box Cutting

2x 3x 30.00 x 0.225 x 0.175 = 7.07m ³	
2x 1 x 10.00 x 0.225 x 0.175 = 0.79m ³	
	= 7.88m ³ .

(3) G.S.B grading II

4 x 2.00 x 2.00 x 0.175 = 2.80m ³	
2x 3x 30.00 x 0.225 x 0.100 = 4.05m ³	
2x 1 x 10.00 x 0.225 x 0.100 = 0.45m ³	

Continuation

= 7.30m³As per Assg = 7.07m³.

2
Schedule XLV - Form No. 134

Particulars	Details of actual measurement			Contents of area
	No.	L	B	
(4) LBM (n) II				
4x	2.00	2.00	0.075	$= 1.20 \text{ m}^3$
6x	2.00	1.50	0.075	$= 1.35 \text{ m}^3$
1x	1.50	1.50	0.075	$= 0.17 \text{ m}^3$
				$= 2.72 \text{ m}^3$
				As per Agg = 2.16 m^3 .

(5) LBM (n) III				
4x	2.00	2.00	0.075	$= 1.20 \text{ m}^3$
6x	2.00	1.50	0.075	$= 1.35 \text{ m}^3$
1x	1.50	1.50	0.075	$= 0.17 \text{ m}^3$
1x	7.00	1.50	0.075	$= 0.79 \text{ m}^3$
1x	5.00	2.50	0.075	$= 0.94 \text{ m}^3$
7x	2.50	2.00	0.075	$= 2.63 \text{ m}^3$
1x	9.00	2.00	0.075	$= 1.35 \text{ m}^3$
2x3	30.00	0.225	0.075	$= 3.04 \text{ m}^3$

2x1	10.00	0.225	0.075	$= 0.33 \text{ m}^3$
				$= 11.80 \text{ m}^3$
				As per Agg = 11.23 m^3 .

(6) Dry lean Cement concrete.

1x	22.00	2.50	0.100	$= 5.50 \text{ m}^3$
1x	17.00	2.00	0.100	$= 3.40 \text{ m}^3$
1x	13.00	3.00	0.100	$= 3.90 \text{ m}^3$
1x	19.00	2.50	0.100	$= 4.75 \text{ m}^3$
1x	12.00	2.00	0.100	$= 2.40 \text{ m}^3$
1x	6.00	2.00	0.100	$= 1.20 \text{ m}^3$
				$= 21.15 \text{ m}^3$
				As per Agg = 19.32 m^3

Continuation

3
Schedule XLV - Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(A) Reinforced concrete Parapet					
1x10.00x9.75+3.75				x 0.125	= 8.13m ³
	2				
1x20.00x3.75				x 0.125	= 9.38m ³
4x30.00x3.75				x 0.125	= 56.25m ³
5x30.00x3.75				x 0.125	= 70.31m ³
5x30.00x3.75				x 0.125	= 70.31m ³
5x30.00x3.75				x 0.125	= 70.31m ³
3x30.00x3.75				x 0.125	= 42.19m ³
1x30.00x3.75+5.25+3.75				x 0.125	= 15.94m ³
1x5.00x2.75				x 0.125	= 2.34m ³
3x30.00x3.75				x 0.125	= 42.19m ³
1x25.00x3.75				x 0.125	= 11.72m ³
6x30.00x3.75				x 0.125	= 84.37m ³
1x15.00x7.25+3.75				x 0.125	= 2.56m ³
	2				

5x30.00x3.75				x 0.125	= 70.31m ³
4x30.00x3.75				x 0.125	= 28.13m ³
1x30.00x3.75				x 0.125	= 14.06m ³
1x15.00x3.75				x 0.125	= 7.03m ³
1x15.00x3.75+7.25				x 0.125	= 10.31m ³
	2				

= 615.84m³

As per Agg = 615.47m³

(B) Logo of Project = 02 Nos.

Signature
07.12.24
AK

Continuation

Abstract of cost

Schedule XLV—Form No. 134

Particulars	Details of actual measurement			Contents of area
	No.	L	B D	
(1) Clearing and grubbing 0.195 ha @ Rs 76,726.04/ha				Rs 15,000 = 00
(2) Box cutting 7.88 m ² @ Rs 104.01/m ²				- Rs 820 = 00
(3) C.S.B grading II 7.07 m ² @ Rs 2567.27/m ²				- Rs 18,165 = 00
(4) L.B.M (I - II) 2.16 m ² @ Rs 5707.44/m ²				- Rs 12,334 = 00
(5) W.B.M - III 11.23 m ² @ Rs 5201.09/m ²				- Rs 58,428 = 00
(6) Dry lean Cement concrete. 19.32 m ² @ Rs 5290.97/m ²				- Rs 1,02,222 = 00
(7) Paved cement concrete Pavement G.S. 47 m ² @ Rs 9310.76/m ²				- Rs 57,30,493 = 00
(8) Cost of Project 02 Nos. @ Rs 10941.61 each				Rs 21,883 = 00
Add 18% Crs. T				Rs 59,59,345 = 00
Add 1% L.C				Rs 10,72,682 = 00
Add S.Fee				Rs 59,593 = 00
				Rs 2,701 = 00
				Rs 70,94,321 = 00
less 2.23% below G.R.				Rs 1,58,203 = 00
				Rs 69,36,118 = 00
				C.P.
				M.P.
				09/12/24
				E.E.

Continuation
