

कार्यपालक अभियंता का कार्यालय ग्रामीण कार्य विभाग, कार्य प्रमंडल, छपरा-2

पत्रांक 341 (अ३)

छपरा/दिनांक 21.2.24

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, छपरा-2।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
बिहार ग्रामीण पथ विकास अभिकरण (ब्राडा),
बिहार, पटना।

विषय :- नई अनुरक्षण नीति-2018(HEAD-3054) योजना मद में आवंटन उपलब्ध कराने के संबंध में।


महाशय,

उपरोक्त विषय के संबंध में कहना है कि नई अनुरक्षण नीति-2018(HEAD-3054) योजना अंतर्गत 07 पथों में राशी का अधियाचना विहित प्रपत्र में तैयार कर BUMP INDICATOR का READING संलग्न कर आवश्यक कारवाई हेतु समर्पित की जाती है।

अतः अनुरोध है की पत्र के साथ संलग्न अधियाचना प्रपत्र में अंकित राशी उपलब्ध कराने की कृपा की जाय, ताकि संवेदक के विपत्र का भुगतान किया जा सकें।

अनु :- यथोक्त।

विश्वासभाजन


21/02/24
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, छपरा-2

FORM GFR 19-A

(See Government of India's Decision (1) below Rule-150)

Form of utilization Certificate up to month of FEB-2024

PIU: EXECUTIVE ENGINEER,RWD WORKS DIVISION,CHAPRA-2

S.No.	Name of Scheme	Sanction No.& Date with Amount (in Rs.lacs)	Amount Received (in Rs. lacs)	Particulars
1.	Construction of Rural Roads under New Maintenance Policy 2018	Letter No. 14 Dt. 06.02.2024	Allotment 7520.20011	Certified that out of Rs 7520.20011 lacs received till Date in favour of Ex.Engineer,RWD Works Division, Chapra-2 . A sum of Rs. 7,505.1107 Lacs has been utilized for the purpose of New Maintenance Policy 2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 15.08941 lacs remaining unutilized at the end of the period under Report.

M.P.
27/02/24
Executive Engineer
RWD Works Division
Chapra-2
27/2/24

Requisition Format for Scheme Head :- MR (3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Name of Division :- Rural Works Department, Works Division, Chapter-2

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in num/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in km)	Amount (in Lakh)	Initial Rectification with surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N-22-23 Chapter-2-08	Murapur Kali Sthan Se Paterna	31363189939	Lt. No. 1892 Dated 27.03.23	0.400	30.32500	29.16200	3.17995	07 MIBD/2023-24	03.05.24	BT Complete	2650.500	25.00	5%	20.39440	20.39440	8.74046	MIB No. 3570, Page No. 10 to 13
2	MR-N-22-23 Chapter-2-03	L031-T07 to Rampur (V.R-17)	31306302126	Lt. No. 2090 Dated 06.05.22	1.380	79.40000	64.82244	15.49130	03MIBD/2023-24	30.12.23	BT Complete	2756.280	25.00	5%	42.00000	42.00000	22.84462	MIB No. 3530, Page No. 37 to 43
3	MR-N-22-23 Chapter-2-03	Banpura - Tamarpura	31306302008	Lt. No. 2090 Dated 06.05.22	4.250	260.54000	160.18644	43.94730	01MIBD/2023-24	05.04.24	BT Complete	2846.550	25.00	5%	89.55973	89.55973	39.95203	MIB No. 3532, Page No. 27 to 32
4	MR-N-22-23 Chapter-2-03	Harpur Mukhampur P.M.G.S.V. Road To Upo Nadin Kahan ke Tola Pandey Tola Hote Huye Dhanesar Khas	31306312055	Lt. No. 2090 Dated 06.05.22	3.030	147.94000	84.23778	30.73120	01MIBD/2023-24	05.04.24	BT Complete	2795.610	25.00	5%	56.96931	56.96931	24.41543	MIB No. 3531, Page No. 27 to 33
5	MR-N-22-23 Chapter-2-03	Extra Mistrab P.M.G.S.V. Road to Urdu Middle School Tajpur Hote Huye Sunapur P.W.D. Road	31306313018	Lt. No. 2090 Dated 06.05.22	2.150	126.77000	80.23334	18.91185	01MIBD/2023-24	05.04.24	BT Complete	2697.360	25.00	5%	43.47853	43.47853	12.85653	MIB No. 3559, Page No. 21 to 25
6	MR-N-21-22 Chapter-2-01	Sasambha se usari ibard via Salampur	313631037232	Lt. No. 1099 Dated 31.03.21	6.300	216.95400	159.95869	54.73648	02MIBD/2023-24	19.12.23	BT Complete	2801.500	25.00	5%	111.94197	111.94197	47.97514	MIB No. 3560, Page No. 19 to 23
7	MR-N-21-22 Chapter-2-01	Adampur to Gambharia	313631037235	Lt. No. 1099 Dated 31.03.21	4.800	153.04700	110.88583	40.35055	02MIBD/2023-24	19.12.23	BT Complete	2836.200	25.00	5%	77.62008	77.62008	33.26575	

Divisional Account Officer
Rural Works Department,
Works Division, Chapter-2

[Signature]

Executive Engineer
Rural Works Department,
Works Division, Chapter-2

[Signature]

Cont. Name:- MUKESH SINGH

Road Name:-HARPUR MUKHUMPUR PMGSY ROAD TO UPTO NADIM RAHMAN KE TOLA PANDEY TOLA HOTE HUVE
DHAMASAR KHAS

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY	Latitude	Longitude	Event
29/12/23	12:14:13	53	0.1	250	0	2500	2970	ROAD	26.063453	84.611958	Normal
29/12/23	12:14:49	53	0.1	260	20.2	2600	3069	G	26.063453	84.611958	Normal
29/12/23	12:15:24	53	0.1	210	30.3	2600	2577	G	26.062645	84.612885	Normal
29/12/23	12:15:24	53	0.1	240	20.2	2400	2872	G	26.062141	84.613421	Normal
29/12/23	12:16:0	53	0.1	280	20.2	2800	3265	G	26.061591	84.614263	Normal
29/12/23	12:16:0	53	0.1	240	30.3	2400	2872	G	26.061041	84.615003	Normal
29/12/23	12:16:34	53	0.1	250	10.1	2500	2970	G	26.060445	84.615846	Normal
29/12/23	12:17:10	53	0.1	230	20.2	2300	2773	G	26.05914	84.61786	Normal
29/12/23	12:17:10	53	0.1	250	20.2	2500	2970	G	26.05898	84.618804	Normal
29/12/23	12:18:20	53	0.1	240	20.2	2400	2872	G	26.058728	84.619646	Normal
29/12/23	12:18:20	53	0.1	190	10.1	1900	2380	G	26.058682	84.62031	Normal
29/12/23	12:19:0	53	0.1	210	10.1	2100	2577	G	26.058453	84.621177	Normal
29/12/23	12:20:5	53	0.1	220	10.1	2200	2675	G	26.058865	84.621407	Normal
29/12/23	12:20:40	53	0.1	230	10.1	2300	2773	G	26.059173	84.621643	Normal
29/12/23	12:21:0	53	0.1	210	10.1	2100	2577	G	26.059	84.6222	Normal
29/12/23	12:21:0	53	0.1	200	10.1	2000	2478	G	26.058846	84.622278	Normal
29/12/23	12:21:16	53	0.1	270	10.1	2700	3167	G	26.058499	84.623466	Normal
29/12/23	12:21:16	53	0.1	250	10.1	2500	2970	G	26.058287	84.62411	Normal
29/12/23	12:22:0	53	0.1	230	20.2	2300	2773	G	26.057864	84.625499	Normal
29/12/23	12:22:0	53	0.1	250	20.2	2500	2970	G	26.057751	84.626607	Normal
29/12/23	12:22:26	53	0.1	240	20.2	2400	2872	G	26.057797	84.627041	Normal
29/12/23	12:22:26	53	0.1	190	10.1	1900	2380	G	26.057442	84.62759	Normal
29/12/23	12:23:0	53	0.1	190	10.1	1900	2380	G	26.057327	84.627883	Normal
29/12/23	12:23:0	53	0.1	210	10.1	2100	2577	G	26.05711	84.628343	Normal
29/12/23	12:23:2	53	0.1	220	10.1	2200	2675	G	26.056743	84.629223	Normal
29/12/23	12:23:2	53	0.1	250	10.1	2500	2970	G	26.056548	84.629835	Normal
29/12/23	12:23:37	53	0.1	230	20.2	2300	2773	G	26.056684	84.630626	Curve
29/12/23	12:24:0	53	0.1	250	20.2	2500	2970	G	26.056984	84.631915	Normal
29/12/23	12:24:12	53	0.1	240	20.2	2400	2872	G	26.056812	84.632374	Normal
29/12/23	12:24:12	53	0.03	240	20.2	2400	2872	G	26.056766	84.633025	Normal
29/12/23	12:24:12	53	0.03	240	20.2	2400	2872	G	26.056708	84.63374	Normal
29/12/23	12:24:12	53	0.03	240	20.2	2400	2872	G	26.056559	84.634327	Normal
		AVERAGE		2795.61							

$$V = 0.5 \times X^2 + 0.984 \times X + 510.7$$

$$X = 3300$$

$$V = 3757$$

$$(R) \text{ RURAL ROAD}$$

$$\text{Good}$$


$$\text{Average}$$

$$\text{Poor}$$

$$<4000$$

$$4001-5000$$

$$>5001$$

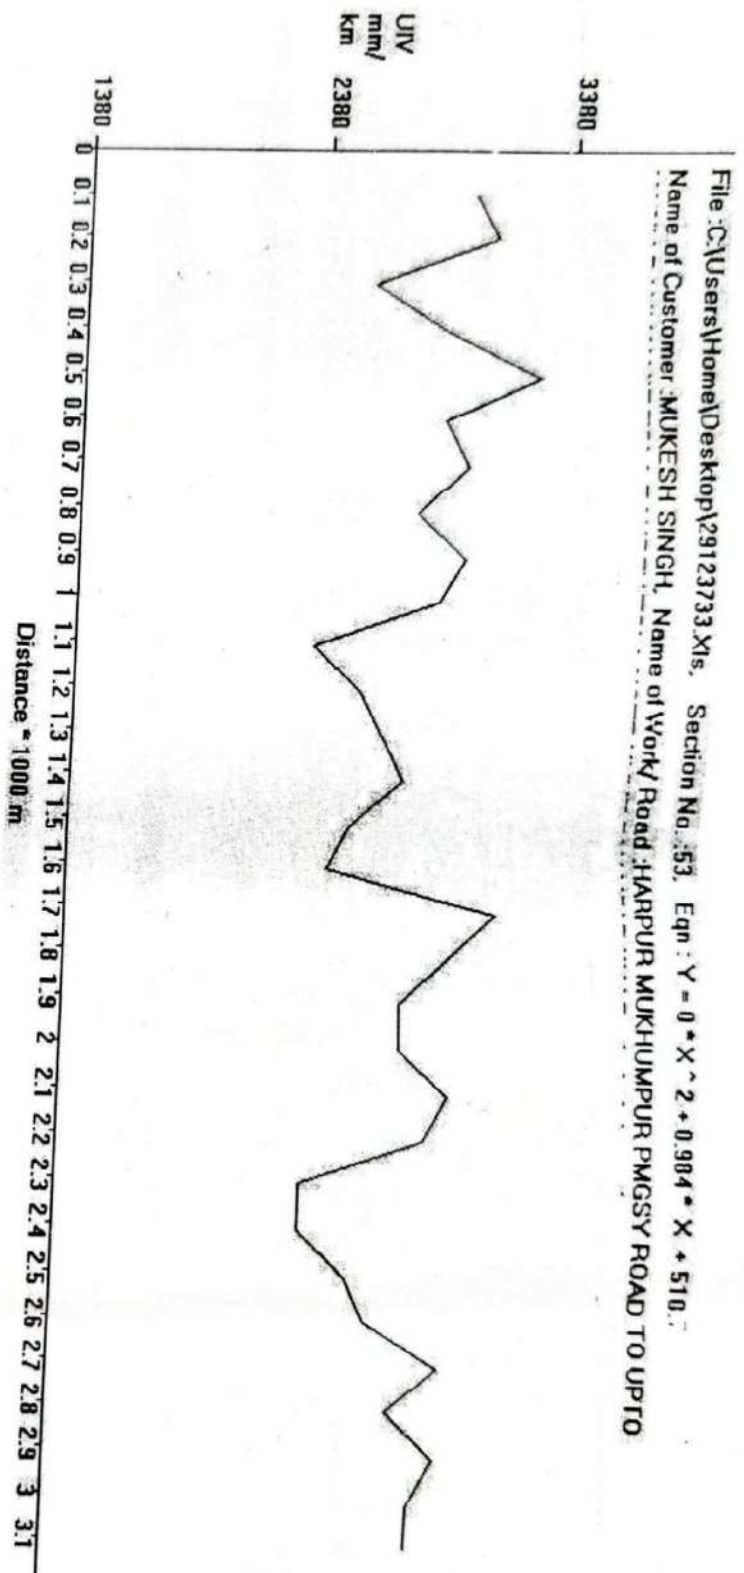

Mukesh Singh
29/11/23

Mukesh Singh
29/11/23

Mukesh Singh
29/11/23

MR-N/22.-23 Chabra-2/104
Schedule XLV-Form No. 134

3532

Harpur Mukhampur Pansy Road to upto
Nadim Rahman ke tola Pandey Tola Hote Hote
Dhamsan khas E.F.RUD-works **DIVISION**

Contractor - Sri Mukesh Singh **Chabra-2**

A.E. R.W.D. works - **SUB-DIVISION**

Agg-No - 01/MBD/23-24 **Lahladpur**

MEASUREMENT BOOK

=24.62-1. Below

3532

Sch.XLV-Form No. 134

Particulars	Details of actual measure				Contents of area
	No.	L.	B.	D.	
2nd and final bill of construction work.					
N/W -	Haripur Mukherampur PMGSY				
	Road to left Nadeem Rahman				
	Ko Tola Hote Huye Dhanisar				
	Kas.				
Name of Agency - Mukesh Singh					
Agreement No - 01MSA/2023-24					
Date of start - 20/2/23					
Date of completion - 15/03/24					
Date of Actual completion -					
Further Measurement					
Nil					
<i>Amal</i> 15/02/24 J.E. <i>P.K.</i> 15/2/24 A.E.					
Abstract of Cost					
(V94)	clearing of Grubbing Road				
	land including uprooting				
	wild vegetation etc				
	Qty UHB P. No - (18) -				
	0.6012 Hec @ 5976 = 133				
	35907 = 11ec				

Continuation

Sch.XLV-Form No. 134

Particulars	Details of actual measure				Contents of area
	No.	L.	B.	D.	
(2/75)	Construction of sub-grade and earthen shoulder etc.				
	Qty	UTMB	P.No.	(18)	
	1893.78	M ³	@		
	253 = 56	M ³			480187 = 20
(3/76)	Construction of C.B by P/V well graded material etc.				
	Qty	UTMB	P.No.		
	(18)	40.16	M ³	@	
	2665 = 24	M ³			107036 = 20
(4/77)	P/V laying & spreading WBH G-2 material etc.				
	Qty	UTMB	P.No.	(18)	
	34.11	M ³	@	5775 = 712	197007 = 20
(5/78)	P/V laying & spreading WBH G-3 material etc.				
	Qty	UTMB	Page No.	(18)	
	51.83	M ³	@	5322 = 582	275869 = 20
(6/79)	P/V and Applying primer coat (SS-1) on prepared surface etc.				
	Qty	UTMB			
	Page No.	(15)	- 691 = 07	M ²	
	@	59 = 512			41174 = 20

Continuation

Sch.XLV-Form No. 134

Particulars	Details of actual measure				Contents of area
	No.	L.	B.	D.	
(7/80) P/V and Applying Tack coat (RS-1) on prepared surface etc. Qty VMB P.No - (19) $691.07 \text{ m}^2 @ 20 = 13821.4$					14243=
(8/81) Road Patch work over WBM using HSS with Waste Plastic etc. Qty VMB P.No - (19) $691.07 \text{ m}^2 @$ $270 = 76 \frac{2}{3} \text{ m}^2$					187114=
(9/82) P/V and Applying Tack Coat (RS-1) on prepared surface etc. Qty VMB P.No - (19) $9262.50 \text{ m}^2 @$ $17 = 17 \frac{2}{3} \text{ m}^2$					159037=
(10/83) P/V and Laying SDBC on prepared surface etc. Qty VMB P.No - (20) $231.56 \text{ m}^3 @ 14733 = 8327$					3411766=
(11/84) Construction of D/L Sub-base over a prepared surface etc. Qty VMB P.No - (20) - 10.50 m^3 $@ 4505 = 42 \frac{2}{3} \text{ m}^3$					47307=

Continuation

Sch.XLV-Form No. 134

Particulars	Details of actual measure				Contents of area
	No.	L.	B.	D.	
(12/85)	Construction of Un-reinforced				
	PCC of M-30 grade do-do				
	all complete job. Qty				
	VTMB P.No. - (25) --				
	336.0 m ³ @ 877.4 = 672				2948289 =
(13/86)	RCC M-15 grade RM				
	stone etc. Qty VTMB				
	P.No. - (26) - 3.0 Nos				
	@ 2805 = 592 Nos				3417 =
(14/87)	RCC M-15 grade 20cm				
	stone etc. Qty VTMB				
	P.No. - (26) - 13.0 Nos				
	@ 785 = 54 Nos				10212 =
(15/88)	P/V and erecting direction				
	& Place etc. Qty VTMB				
	VTMB VTMB P.No. (20)				
	1.92 m ² @ 14808 = 512				28432 =
(16/89)	P/V and fixing of retro-reflectors in intermediary				
	Sign board etc. Qty				
	VTMB P.No. - (21) - 12.0 Nos				
	@ 4333 = 562 Nos				52003 =
(17/90)	600mm Circular etc.				
	Qty VTMB P.No. - (21) -				
	6.0 Nos @ 4273 = 25640				25640 =

Continuation

Sch.XLV-Form No. 134

Particulars	Details of actual measure				Contents of area
	No.	L.	B.	D.	
(18/91)	600mm x 450mm				
	Rectangular etc				
	Qty VMB P. No - (21)				
	6.0 Nos @	4129	52	$\frac{2}{No}$	$24777 = 00$
(19/92)	Rec M-15 grade				
	Boundary Pillar etc				
	Qty VMB P. No - (21)				
	96.0 Nos @	656	07	$\frac{2}{No}$	$62976 = 00$
(20/93)	Printing new letter				
	& figures of any				
	shade etc Qty VMB				
	Page No - (21) -				
	528 cm ht/letter @				
	0.61 $\frac{2}{cm}$ cm ht/letter				$322 = 00$
	etc-				
(21/94)	Planting of trees by				
	the road side 1m x 6mm				
	diameter etc - Qty				
	VMB P. No - (22) -				
	248.0 Nos @	1023	59	$\frac{2}{No}$	$263770 = 00$
(22/95)	P/V laying hot applied				
	thermo-plastic compound etc.				
	Qty VMB P. No - (22)				
	601.20 m ² @	323	44	$\frac{2}{m}$	$435232 = 00$

Continuation

Sch.XLV-Form No. 134

Particulars	Details of actual measure				Contents of area
	No.	L.	B.	D.	
(23/96) P/y and finding of typical Makes Informing High board etc. Qty VTM B P. No.					
(24) - 2 only @ 10676 = 132					213.52 = 00
(24/102) Brick Masonry 1cm (1:3) in parapet etc Qty VTM B P. No. (22)					
14.40 m ³ @ 5861 = 762					844.07 = 00
(25/103) Plastering with CM (1:4) on brickwork in Sub- Structure do-d all Complete					
Job- Qty VTM B P. No.					
(25) - 100.80 m ² @					
182 = 51 7/2					183.97 = 00
(26/104) Painting two coats including primer coat etc. Qty					
VTM B P. No. (23)					
100.80 m ² @ 114 = 732					115.65 = 00
					90,074420
Ad 18% for GST					1621340 = 00
Ad 1% for LC					9007420
SF					77740 = 00
					10798596 = 00
Less on for Amount 24.62% below					2658122 = 00
Less on previous bill VTM B P. No. (23)					8138474 = 00
					5676957 = 00
Continuation					24,91,543 = 00

Checked
15/02/24
JB

24/02/24
AE
