

कार्यपालक अभियंता का कार्यालय, ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मनिहारी (कटिहार)।



पत्रांक.....500.....अनु० मनिहारी,

दिनांक.....28.02.24.....

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल मनिहारी (कटिहार)।

सेवा में,

अपर —मुख्य—कार्यपालक —पदाधिकारी,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय :— MR (New-Maintenance Policy-2018) योजनान्तर्गत चल रहें कार्य का निधि की
अधियाचना के संबंध में।

महाशय

उपर्युक्त विषय के संबंध में कहना है कि ग्रामीण कार्य विभाग कार्य, कार्य प्रमंडल, मनिहारी
के अधीन MR (New-Maintenance Policy-2018) योजनान्तर्गत चल रहे कार्य का निधि उपलब्ध कराने
हेतु अधियाचना विहित प्रपत्र में तैयार कर आपके अग्रेतर कार्रवाई हेतु समर्पित की जाती है।

अनु:—यथोक्त।

विश्वासभाजन

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मनिहारी(कटिहार)।

23/02/24

RWD, Works Division, Manihari

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road maintenance Policy 2018 (Departmental Work)

Name of Division : Manihari

Sl No	Package no.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. Work order & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in percentage	Previous Total Allotted Amount (In Lac)	up to date expenditure as per MIS (In Lac)	Requisition Against work done (In lac)	Remarks
					Length (In Km)	Amount (in Lac)	Initial Rectification with Surface Renewal (in lac)	5 years Routine Maintenance (In lac)										
1	RM/KA/MAN/20/0003	Const. of road from Kumariapur Hat to Kalibari via Adiwasiola, Baigachhi upto Kusaha dhar under Manihari Block.	21105701002	10.02.2020	3.500	141.670	86.72	43.99235	44/MBD/2021-22 04.06.2021	03.06.2022	03.03.2023	2416.26	25	5.1%	81.72000	81.72000	4.96060	Completed
2	RM/KA/MAN/19/0004	Baghmara to Manihari	21105501008	24.06.2019	3.75	129.604	83.219	37.42156	35/MBD/2021-22 04.05.2021	03.05.2022	-	2385.12	25	5.1%	0.00000	0.00000	30.29082	Ongoing
Total															81.72000	81.72000	35.25142	


 23/02/24
 Divisional Accounts Officer
 RWD, Works Division, Manihari


 23/02/24
 Executive Engineer
 RWD, Works Division, Manihari

EXECUTIVE ENGINEER, WORK DEPARTMENT , WORKS DIVISION, MANIHARI

FORM GER - 19 - A

(See Government of India's Decision (i) below Rule - 150)

Form of Utilization Certificate up to month of Feb-2024

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (In Lacs)		Total Amount Received (In Lacs)	Particulars	Balance Amount (in Lakh) Bank+ CFMS
1	Construction of Rural Road under MR (New-Maintenance Policy-2018)	Letter No.63 we. Dt- 13.04.2023	413.75256	2981.65471	Certified that out of Rs. 2981.65471 lakh through CFMS of grants in aid sanctioned during the years in favour of Engineer incharge , R.W.D, Works Division, Manihari, Sum of Rs. 2866.00936 Lacs has been utilized for the purpose New-Maintenance Policy-2018 New Rural Roads & Bridge Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 115.64535 Lacs remaining unutilized at the end of the period under.	115.64535
		Total	413.75256	2981.65471		115.64535
Certified that I have satisfied myself that the condition on which the grants in aid sanctioned have been duly fulfilled / are being fulfilled and that I have Exercised the following Checks to see that the money was actually utilized for the purpose for which it was sanctioned .						
2	i	Works have been supervised by Executive Engineer / Superintending Engineer.				
	ii	Periodical inspection has been conducted by A.E. / Executive Engineer / Superintending Engineer.				
	iii	Construction materials have been tested.				
	iv	Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer / Executive Engineer.				
	v	All other Codal formalities have been observed.				

CEP
23/02/24
D.A.O.

Rural works Department
Works Division Manihari

A 23/2/24

Executive Engineer
Rural works Department
Works Division Manihari

Road Name:- Baghmara to Manihari

Name of Contractor :- Anil Kumar Garg

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
18/12/23	16:09:12	84	0.1	230	0	2300	2254	G	25.366863	87.61858	Normal
18/12/23	16:09:19	84	0.1	240	10.1	2400	2358	G	25.365816	87.618699	culvert
18/12/23	16:09:26	84	0.1	270	0	2700	2694	G	25.364871	87.618648	culvert
18/12/23	16:09:33	84	0.1	250	10.1	2500	2465	G	25.364544	87.618446	Normal
18/12/23	16:10:22	84	0.1	230	10.1	2300	2257	G	25.364292	87.619039	Normal
18/12/23	16:10:29	84	0.1	290	10.1	2900	2890	G	25.364203	87.618845	Normal
18/12/23	16:10:36	84	0.1	220	10.1	2200	2156	G	25.362778	87.617979	Normal
18/12/23	16:10:43	84	0.1	220	10.1	2200	2236	G	25.362594	87.617669	Normal
18/12/23	16:10:50	84	0.1	260	10.1	2600	2645	G	25.361101	87.617655	Normal
18/12/23	16:10:57	84	0.1	260	10.1	2600	2592	G	25.360083	87.617571	Normal
18/12/23	16:11:04	84	0.1	220	10.1	2200	2213	G	25.359347	87.616261	Normal
18/12/23	16:11:11	84	0.1	240	10.1	2400	2418	G	25.358295	87.616584	Normal
18/12/23	16:12:23	84	0.1	240	10.1	2400	2367	G	25.358056	87.616235	Normal
18/12/23	16:11:43	84	0.1	210	10.1	2100	2142	G	25.355102	87.617905	Normal
18/12/23	16:11:57	84	0.1	220	10.1	2200	2243	G	25.354949	87.618532	Normal
18/12/23	16:12:25	84	0.1	220	10.1	2200	2232	G	25.353485	87.615165	Normal
AVERAGE							2385.12				

$$Y = 0 * X^2 + 0.989 * X + 13.58$$

$$X = 2300$$

$$Y = 2272$$

Report by
20/12/23
AE

16/12/23


Name of Customer : Anil Kumar Garg
 Name of Work/ Road : Baghmara To Manihari
 Lab Job number : 84
 Date : 18-12-2023
 Section No. : 84

Test Date : 18-12-2023 Road Name : Baghmara To Manihari
 Machine No : 404 Road Type : (A) ASPHALTIC
 Start S No : Side : Interval
 Start E No :
 Weather : UIV Range : 1142 To 4000 1000 mm/km
 Start Location : Dist Range : 0 To 1.7 0.1 * 1000 m
 End Location : Equation : $Y = 0 * X^2 + 0.989 * X + 13.58$

Print Generate Report and Graph

Redraw Graph

Map View

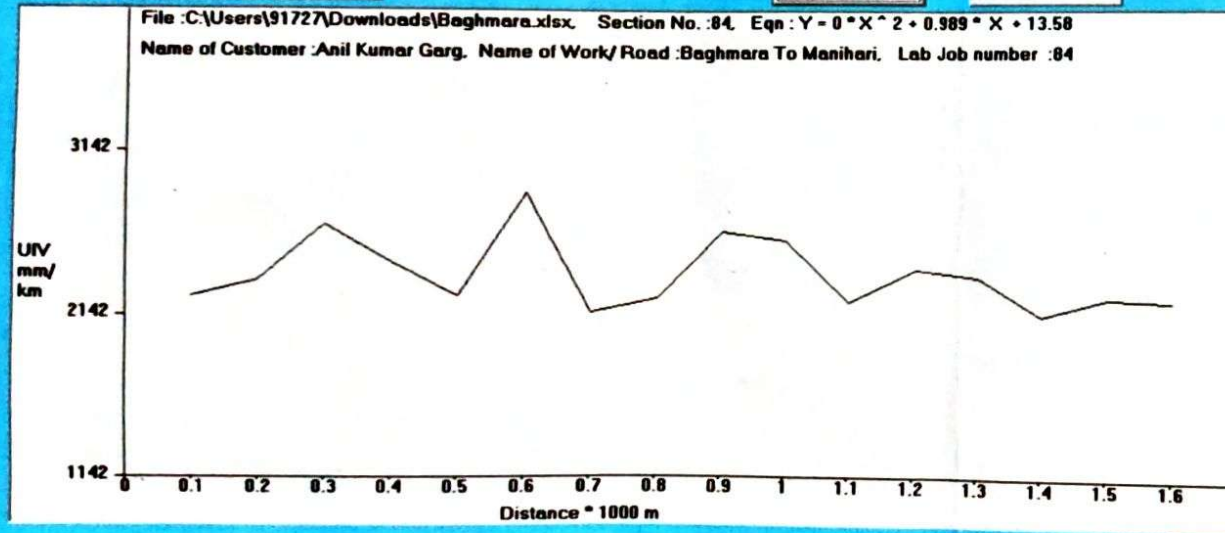

By 21
20/12-23
or

Asmita
20/12/23
AE

20/12/23

MIR 3054.

Manikari

Schedule XLV-Form No. 134

MIR 3054 maint. OF Road From Baghmar.
to manikari

Agreement no. 35/MBD/2024-22

DIVISION

Agreement Value - 2,40,55,755.00

SUB-DIVISION

MEASUREMENT BOOK

Anil Kumar Chary.

643
4/5/21

Assumed at cost

5

Sch. XLV - Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
1/ Clearing & grading road					
land wide TMS from 1 =					
0.33 Hrs @ Rs 49496.20/Hrs					Rs 16,334.00
2/ Const of G.S.O wide TMS					
Rs 1 = 41.02 m @ Rs 1985.00/m					Rs 81,428.00
3/ Prov. laying, Spreading WBM Gr-2					
Wide TMS from 2 = 76.09 m ²					
@ Rs 3498.16/m ²					Rs 1,26,249.00
4/ Prov. laying, Spreading					
WBM Gr-2 wide TMS from					
2 = 54.23 m ² @ Rs 3247.67/m ²					Rs 1,76,121.00
5/ Prov. f. of laying Prime coat					
wide TMS from 2 = 727.07 m ²					
@ Rs 42.17/m ²					Rs 30,492.00
6/ Prov. laying f. M.S.S. wide					
TMS from 3 = 1473.85 m ²					
@ Rs 187.42/m ²					Rs 2,76,244.00
7/ Prov. and applying tack coat					
Wide TMS from 3 = 7661.25 m ²					
@ Rs 14.29/m ²					Rs 1,09,479.00
8/ Prov. f. laying S.D.S.C. wide					
TMS from 4 = 155.84 m ²					
@ Rs 9384.86/m ²					Rs 1,46,256.00
9/ Prov. f. fixing kerb stone					
TMS from 4 = 3 nos @ Rs					
2208.37/each					Rs 6,625.00

Continuation

(Total Rs 2,87,000.00)

Sch. XLV—Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
$\frac{10}{4}$ Prov. & fixy run area					
side TMA pgs 4: 8 m. EB					
603.36/Ea				L	4827.00
$\frac{11}{12}$ Prov. & fixy black identification					
& direction board side TMA					
pgs 1.92 at EB 12.312 31/12					23640.00
$\frac{12}{13}$ Prov. & fixy irregular					
board side TMA pgs 4:					
12 m. EB 7625.00/Ea				L	43500.00
$\frac{13}{14}$ Prov. & fixy circular					
side TMA pgs 4: 6 m. EB					
2724.35/Ea				L	22346.00
$\frac{14}{15}$ Prov. & fixy rectangle					
board side TMA pgs 4:					
8 m. EB 3595.23/Ea				L	28762.00
$\frac{15}{16}$ Prov. & fixy octagonal					
side TMA pgs 4: 1 m. EB					
7588.02/Ea				L	7588.00
$\frac{16}{17}$ Prov. & fixy road marking					
side TMA pgs 4: 330.00 m. EB					
Ls 735.40/L				L	242682.00
$\frac{17}{18}$ Prov. & fixy pedestrian					
crossing side TMA pgs 4:					
6 m. EB 735.40/L				L	4412.00
$\frac{18}{19}$ Prov. & fixy margin					
board side TMA pgs 4: 2 m. EB					

Continuation

Sch. XLV—Form No. 134

7

1/26 25,64,764 ~

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
9225.26/ea					18657 ~
Total B					2681945 ~
Add 12x GSC B					321833 ~
Add 1x (Cus B					26819 ~
Total B					30,30,597 ~
less 0.05% as per Agreement Bx					1515 ~
Total B					30,29,082 ~
Accepted by					
20/12/23					
RE					
Accepted					
20/12/23					
AE					
