

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, बारसोई (कटिहार)

Mob. No- 8986915775

E-Mail Id :- rwd.barsoi@gmail.com

पत्रांक 1343 /

बारसोई, दिनांक 04/07/24 /

प्रेषक:-

ई० विश्वबन्धु राजीव रंजन
कार्यपालक अभियंता

सेवा में,

अपर मुख्य कार्यपालक पदाधिकार-सह-सचिव,
ग्रामीण कार्य विभाग, ब्राडा बिहार, पटना।

विषय :

शीर्ष 3054 अंतर्गत बिहार ग्रामीण पथ अनुरक्षण नीति-2018 के तहत स्वीकृत कार्यों का
आवंटन उपलब्ध कराने के सम्बन्ध में।

प्रसंग:-

भवदीय का पत्रांक 4843 दिनांक 06.12.2021


महाशय,


उपर्युक्त विषयक एवं प्रासंगिक पत्र के आलोक में ग्रामीण कार्य विभाग, कार्य प्रमंडल,
बारसोई, कटिहार के अधीन शीर्ष 3054 अंतर्गत बिहार ग्रामीण पथ अनुरक्षण नीति-2018 के तहत
स्वीकृत कार्यों में निधि उपलब्ध कराने हेतु अधियाचना विहित प्रपत्र में तैयार कर आपके अग्रेतर
कार्रवाई हेतु समर्पित किया जाता है।

अतः आप से अनुरोध है कि आवंटन शीघ्र उपलब्ध कराने की कृपा की जाय।

अनु०- यथोक्त।

विश्वास भाजन


कार्यपालक अभियंता
ग्रामीण कार्य विभाग,

कार्य प्रमंडल, बारसोई, कटिहार


29/6/24

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, बारसोई (कटिहार)

Mob. No- 8986915775

E-Mail Id :- rwd.barsoi@gmail.com

पत्रांक /

बारसोई, दिनांक..... /

प्रेषक:-

ई० विश्वबंधु राजीव रंजन
कार्यपालक अभियंता

सेवा में,

अपर मुख्य कार्यपालक पदाधिकार-सह-सचिव,
ग्रामीण कार्य विभाग, ब्राडा बिहार, पटना।

विषय : शीर्ष 3054 अंतर्गत बिहार ग्रामीण पथ अनुरक्षण नीति-2018 के तहत स्वीकृत कार्यों का आवंटन उपलब्ध कराने के सम्बन्ध में।

प्रसंग:- भवदीय का पत्रांक 4843 दिनांक 06.12.2021

महाशय,

उपर्युक्त विषयक एवं प्रासंगिक पत्र के आलोक में ग्रामीण कार्य विभाग, कार्य प्रमंडल, बारसोई, कटिहार के अधीन शीर्ष 3054 अंतर्गत बिहार ग्रामीण पथ अनुरक्षण नीति-2018 के तहत स्वीकृत कार्यों में निधि उपलब्ध कराने हेतु अधियाचना विहित प्रपत्र में तैयार कर आपके अग्रेतर कार्रवाई हेतु समर्पित किया जाता है।

अतः आप से अनुरोध है कि आवंटन शीघ्र उपलब्ध कराने की कृपा की जाय।

अनु०- यथोक्त।

विश्वास भाजन

६१
कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बारसोई, कटिहार

ज्ञापक 1343 दिनांक 04/07/24

प्रतिलिपि - नोडल पदाधिकारी, 3054 MR, ग्रामीण कार्य विभाग, बिहार पटना को सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।


कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बारसोई, कटिहार
29.6

Rural Works Department, Works Division, Barsoi, Katihar.
MIR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Initial Rectification and Surface Renewal)

Name of Division :- Barsoi (Katihar)

Name of Division - Barsoi (Kailash)																				
Sl No	Packaging No	Name Of Road	Project ID as per MIS	Administrative Approval (AA) Letter No / Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen content in Percentage	Previous Tola Allotted Amount (In Lkh)	up-to-date expenditure as per MIS (In Lakh)	Total Value of Measurement (In Lakh)	Requisition against work done (In Lakh)	Remarks	
					Length of (In Km)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Year Routine Maintenance (In Lakh)												
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	
		L038 T05 Kalyangawn To Gora Salempur	21105602091	1941 / 29.03.2023	2.497	155.45600	115.36955	26.9684	22 MBD /2023-24	Completed	Completed	2907.40	25mm	5.1%	41.07022	41.07022	115.25918	74.18896		
		Bakhota Swash Kendra To Manjhauli Hanuman Chowk Via Kala Pahar	21105612005	1942 / 29.03.2023	1.833	130.64800	97.24055	23.75346		Completed	Completed	2792.32	25mm	5.1%	40.21019	40.21019	97.15377	56.94358		
		Kuraota To NH 31 Via Bagdogra Kathalbari	21105612009	1942 / 29.03.2023	2.39	125.81400	87.90137	30.09905		12.07.24	Completed	Completed	2685.29	25mm	5.1%	57.50247	57.50247	87.43392	29.93145	
		Ambika Das Mill To Balraipur Dakshin Tola Digba Tola	21105612008	1942 / 29.03.2023	2.015	123.37800	90.73526	21.68856		Completed	Completed	Completed	2788.76	25mm	5.1%	32.73325	32.73225	90.72586	57.99361	
				Total :-	8.735	535.29600	391.24673	102.50947							171.51513	171.51513	390.57273	219.05760		
MR-N-23-24 BARSOI-02																				


 Executive Engineer
 R.W.D. Works Division
 Barsoi, Katihar
 29/6/23

FROM GFR 19 - A

**(See Government of India's Decision (I) Below Rule - 150)
Form of Utilisation Certificate**

Sl No	Name of Scheme	Sanctioned No Date with Amount (in Lakh Rs.)	Amount Received (in Lakh Rs.)	Particulars
1	2	4	5	6
1	MR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Year-2021-22, 2022-23 & 2023-24)	MR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Year- 2021-22, 2022-23 & 2023-24) Lt. No. 32 Dt- 28.05.2021 Lt. No. 40 Dt- 14.06.2021 Lt. No. 05 Dt- 25.01.2022 Lt. No. 10 Dt- 21.02.2022 Lt. No. 49 Dt- 27.04.2022 Lt. No. 22 Dt- 08.08.2022 Lt. No. 12 Dt- 03.02.2023 Lt. No. 35 Dt- 14.03.2023 Lt. No. 42 Dt- 20.03.2023 Lt. No. 72 Dt- 10.05.2023 Lt. No. 78 Dt- 24.05.2023 Lt. No. 84 Dt- 08.06.2023 Lt. No. 96 Dt- 07.07.2023 Lt. No. 106 Dt- 02.08.2023 Lt. No. 113 Dt- 14.08.2023 Lt. No. 136 Dt- 10.10.2023 Lt. No. 140 Dt- 16.10.2023 Lt. No. 144 Dt- 20.10.2023 Lt. No. 152 Dt- 16.11.2023 Lt. No. 14 Dt- 06.02.2024 Lt. No. 31 Dt- 09.03.2024 Lt. No. 37 Dt- 15.03.2024 Lt. No. 40 Dt- 18.03.2024 Lt. No. 47 Dt- 25.03.2024 Lt. No. 72 Dt- 29.05.2024 Lt. No. 74 Dt- 03.06.2024	4344.31204	Certified that out of Rs.- 4344.31204 Lakh of grants in aid sanctioned during the Years 2021-22, 2022-23 & 2023-24 In Favour of Executive Engineer, Rural Works Department, Works Division, Barsoi sum of Rs.- 4190.06724 Lakh has been utilized for the purpose of MR(3054) under Bihar Rural Road Maintenance Policy- 2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs.- 154.24480 Lakh remaining unutilized at the end of the period under report.purpose.
	Total -		4344.31204	

- 2 Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose fo

Kind of Checks Exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test checks conducted by the Assistant Engineer/ Executive Engineer.
- All other codal formatities have been observed.

3 **Physical Progress achieved :-**

- Construction of Road Works.
- Construction of CD. Works.

15
29/6/24


Executive Engineer
Rural Works Department
Works Division, Barsoi, Katihar

Schedule XLV-Form No. 134

Kirauwa to NH31 Tak via Bagdogra
Kathalbari

MR

Bargur

DIVISION

Balrampur

SUB-DIVISION

MEASUREMENT BOOK

2084

Krishnaipali Construction Pvt. Ltd.

Agreement No - 22/94/23-24

15

Sch. XLV—Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of work:- Repair of					
Road from Kiraura					
to NH-31 via					
Bagdogra Katla/Bari.					
Agency:- Krishnapali const ⁿ					
Pvt. Ltd.					
satyadeo singh,					
chakrapuram					
[chulai chak] Rupsapur					
Danapur, patna					
801105					
Agreement No:- 27 MBD-2023-24					

(Under MR 3054)

Date of commencement:- 13-10-23

Date of completion:- 12-7-24

Date of Actual completion:- 10-6-24

Record entry

10> Providing and fixing
of typical MMSY
informational sign
board - with logo as
per Mord Sp.

02 NOS

12> constⁿ of un-reinforced
plain cement concrete

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
vide - Page - 15, Item - $\frac{1}{28}$					
Qty. = 02 NOS					
Total Qty. = 04 NOS					
@ Rs. 13752.39/each					- Rs. 55010 = Rs.
$\frac{24}{29}$ > plastering with cement mortar - on brick work					
vide - p-19, Item = $\frac{12}{29}$					
Qty. = 80.64 m ²					
@ Rs. 241.07 /m ² - Rs. = 19440 = Rs.					
$\frac{28}{30}$ > painting two coats on new concrete surface					
vide - Page - 19, Item = $\frac{1}{30}$					
Qty. = 80.64 m ²					
@ Rs. 137.87 /m ² - Rs. = 11118 = Rs.					
					Rs. = 8112635 = Rs.
Add GST @ 18% (+) Rs. = 1460274 = Rs.					
Add L.C.E.S. @ 01% (+) Rs. = 81126 = Rs.					
Add sig. fee @ 10% (+) Rs. = 60845 = Rs.					
vide p-20					Rs. = 9714880 = Rs.
less 10% below (-) Rs. = 971488 = Rs.					
					Rs. = 8743392 = Rs.
less previous paid amt (-) Rs. = 5750247 = Rs.					
					Rs. = 2993145 = Rs.

Attested
 Executive Engineer
 Rural Works Department
 Works Division, Bikaner
 10/6/24

Continuation

Lab Job number :24

Date :25-01-2024

Name of Customer :Krishnapali Construction Pvt. Ltd.

Name of Work/ Road :Kiraure To NH-31 Via Bagdogara Kathalbari

Sr.no	Location of test (in km)	Corrected U.I value (mm/km)	Road catagory
1	0.100	2593	G
2	0.200	2690	G
3	0.300	2497	G
4	0.400	2593	G
5	0.500	2303	G
6	0.600	2593	G
7	0.700	2787	G
8	0.800	2012	G
9	0.900	3175	G
10	1.000	3078	G
11	1.100	3175	G
12	1.200	2593	G
13	1.300	2884	G
14	1.400	2690	G
15	1.500	2884	G
16	1.600	2497	G
17	1.700	2593	G
18	1.800	2690	G
19	1.900	2593	G
20	2.000	2981	G
21	2.100	2787	G
22	2.200	2400	G
23	2.300	2593	G
24	2.400	2766	G
Average IRI value		2685.29	

25/01/2024
J.E

Under review
25.1.24

Executive Engineer
Rural Works Department
Works Division, Barsoi

Lab Job number :24
Date :25-01-2024

Name of Customer :Krishnapali Construction Pvt. Ltd.

Name of Work/ Road :Kiraure To NH-31 Via Bagdogara Kathalbari

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
25/1/24	17:1:15	24	0.1	260	0	2600	2593	G	25.85604	87.83267	Curve
25/1/24	17:1:48	24	0.1	270	20.2	2700	2690	G	25.85568	87.83183	Normal
25/1/24	17:2:13	24	0.1	250	20.2	2500	2497	G	25.85528	87.83089	Normal
25/1/24	17:2:45	24	0.1	260	10.1	2600	2593	G	25.85525	87.83002	Curve
25/1/24	17:3:10	24	0.1	230	20.2	2300	2303	G	25.85524	87.82920	Curve
25/1/24	17:3:42	24	0.1	260	20.2	2600	2593	G	25.85585	87.82865	Speed Breaker
25/1/24	17:3:59	24	0.1	280	20.2	2800	2787	G	25.85631	87.82792	Curve
25/1/24	17:4:24	24	0.1	200	30.3	2000	2012	G	25.85617	87.82688	Normal
25/1/24	17:4:47	24	0.1	320	30.3	3200	3175	G	25.85622	87.82595	Normal
25/1/24	17:5:12	24	0.1	310	30.3	3100	3078	G	25.85648	87.82525	Normal
25/1/24	17:5:42	24	0.1	320	30.3	3200	3175	G	25.85687	87.82441	Normal
25/1/24	17:5:58	24	0.1	260	10.1	2600	2593	G	25.85749	87.82377	Speed Breaker
25/1/24	17:6:23	24	0.1	290	20.2	2900	2884	G	25.85734	87.82294	Curve
25/1/24	17:6:53	24	0.1	270	20.2	2700	2690	G	25.85675	87.82233	Normal
25/1/24	17:7:13	24	0.1	290	10.1	2900	2884	G	25.85671	87.82128	Curve
25/1/24	17:7:50	24	0.1	250	10.1	2500	2497	G	25.85661	87.82025	Normal
25/1/24	17:8:15	24	0.1	260	20.2	2600	2593	G	25.85650	87.81924	Normal
25/1/24	17:8:44	24	0.1	270	20.2	2700	2690	G	25.85580	87.81900	Curve
25/1/24	17:9:14	24	0.1	260	10.1	2600	2593	G	25.85489	87.81867	Normal
25/1/24	17:9:46	24	0.1	300	20.2	3000	2981	G	25.85393	87.81841	Normal
25/1/24	17:10:8	24	0.1	280	20.2	2800	2787	G	25.85341	87.81789	Curve
25/1/24	17:10:45	24	0.1	240	10.1	2400	2400	G	25.85310	87.81706	Curve
25/1/24	17:11:10	24	0.1	260	20.2	2600	2593	G	25.85350	87.81615	Normal
25/1/24	17:11:47	24	0.09	250	10.1	2778	2766	G	25.85371	87.81507	Normal

$$Y = 0 * X^2 + 0.969 * X + 74.60$$

$$X = 2778$$

$$Y = 2766$$

(R) RURAL ROAD

Good <4000
Average 4001-5000
Poor >5001

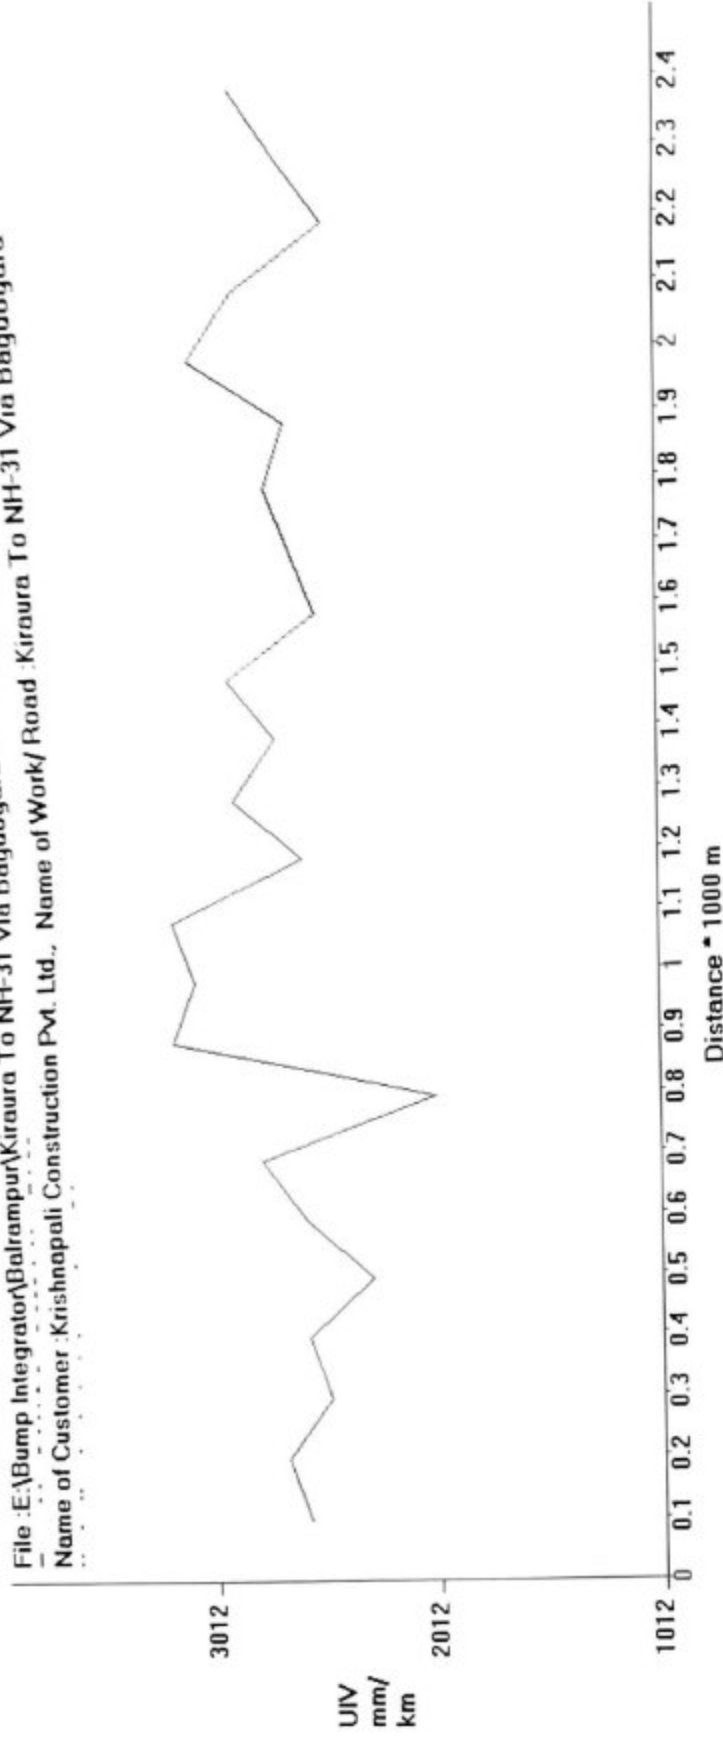
2/Jan-25
25/01/24
J.E

Chandra Kumar
25/1/2024

[Signature]
Executive Engineer
Rural Works Department
Works Division, Barsoi

File : E:\Bump Integrator\Balrampur\Kiraure To NH-31 Via Bagdogara Kathalbar\25011714.xls, Section No. 24.

Name of Customer : Krishnapali Construction Pvt. Ltd., Name of Work/Road : Kiraure To NH-31 Via Bagdogara



[Signature]
Executive Engineer
Rural Works Department
Works Division, Barsoi

[Signature]
25/1/24

[Signature]
29/01/24
J.E
