

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग
कार्य प्रमंडल, सोनपुर

Mob No :- 8986915436

E.Mail :- eerwdsonpur@gmail.com

पत्रांक 1424/3170
प्रेषक,

सोनपुर, दिनांक..... 24/12/24

ई0 अशोक कुमार
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर।

सेवा में,

नोडल पदाधिकारी (3054),
ग्रामीण कार्य विभाग
बिहार, पटना।

विषय:- बिहार ग्रामीण पथ अनुरक्षण नीति-2018 के तहत स्वीकृत योजना में
आवंटन उपलब्ध कराने के संबंध में।


महाशय,

उपर्युक्त विषयक ग्रामीण कार्य विभाग कार्य प्रमंडल सोनपुर के अंतर्गत बिहार ग्रामीण पथ अनुरक्षण नीति-2018 के तहत स्वीकृत योजना के क्रियान्वयन हेतु आवंटन की मांग विहित प्रपत्र में तैयार कर भेजी जा रही है। उक्त पथ का स्वीकृत कुल लम्बाई 3.725 कि०मी० है, जिसमें से 2.600 कि०मी० पथ का नवीकरण कार्य पूर्ण करा दिया गया है। शेष लम्बाई 1.125 कि०मी० का कार्य स्थानीय ग्रामीणों के द्वारा कार्य में बाधा उत्पन्न किया जा रहा है। इसलिए इस पथ के 2.600 कि०मी० पथांश के सतह नवीकरण का किए गए कार्य का ही Bump Indicator का रिपोर्ट संलग्न है।

अतः अनुरोध है कि उपर्युक्त योजना में स्वीकृत लंबाई 3.725 कि०मी० के विरुद्ध 2.600 कि०मी० के लिए आवंटन उपलब्ध कराने की कृपा की जाये।

अनु०:-उपयोगिता प्रमाण-पत्र।

विश्वासभाजन


कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर
24/12/24


FORM GER 19-A

(See Government of India's Decision (I) below Rule-150
Form of Utilization Certificate up to the month of **July-2024**


PIU:- E.E.,R.W.D. Works Division Sonapur.

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in lacs Rs.)	Amount Received (in lac Rs.)	Particulars
1	2	3	4	5
1	Construction of Rural Roads under New Maintenance Policy-18		8793.49618	Certified that out of Rs 8793.49618 lakh received during the years 2020-21 to 2023-24 in favour of E.E.R.W.D. works division Sonapur a sum of Rs 8793.44011 Lakh has been utilized for the purpose of New Maintenance Policy-18 Scheme as given in the margin for which it was sanctioned and that the balance of Rs 0.05607 Lakh remaining unutilized at the end of the period under report.

Certified that I have satisfied that the condition of which the grants-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually for the purpose for which it was sanctioned.


24/07/24
D.A.O-I

R.W.D. Works Division Sonpur.


24/07/24
EXECUTIVE ENGINEER
R.W.D. Works Division Sonpur.

Requisition Formate for Scheme Head - MR-3054 Under Bihar Rural Road Maintenance Policy 2018 (In Rectification and surface Renewal)

Division Name:- Rural Works Department, Works Division- Sonpur

Sl.No	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lac)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in Km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content In %	Previous Total Allotted Amount (In Lac)	Upto date expenditure as per MIS (In Lac)	Requisition against Work Done (In Lac)	Remarks
					Length (in Km.)	Amount (In Lac)	Initial Rectification on with Surface Renewal (In Lac)	5 Years Routine Maintenance (In Lac)										
1	RM/SA/SON/23/0009	Ishuapur Se Nawalpur Kameshwar Rai Ke ghar se Dafali tola hote hue kushwaha Tola Guputasthan tak	313641899384	1797 20.03.23	3.725	276.127	191.35102	39.15530	07/SBD/2023-24	13.06.2024	-	2784	25	5.03	0.000	0.000	94.99870	
TOTAL																		94.99870

Asst. Engineer
D.A.O-I

R.W.D Works Div- Sonpur


Executive Engineer
R.W.D Works Div- Sonpur
24/3/24

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर

का0आ0सं0.....1424.....सोनपुर, दिनांक.....14/7/24.....

कार्यालय आदेश

प्रमाणित किया जाता है कि बिहार ग्रामीण पथ अनुरक्षण निती-2018 योजनान्तर्गत Ishuapur Se Nawalpur Kameshwar Rai Ke ghar se Dafali tola hote hue kushwaha Tola Guputasthan tak (Project ID- 313641899384) का कार्य गुणवत्ता एवं विशिष्टियों के अनुरूप पूर्ण कराया गया है। पथ के मापीपुस्त की जाँच मेरे द्वारा 25 प्रतिशत एवं सहायक अभियंता के द्वारा 50 प्रतिशत एवं कनीय अभियंता के द्वारा शत प्रतिशत किया गया है।


23/07/24

कनीय अभियंता
ग्रामीण कार्य विभाग
कार्य प्रशाखा दिघवारा


23/07/24

सहायक अभियंता
ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल दिघवारा



कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर
23/07/24

Lab Job number :

Date :08-Jun-24

Name of Customer :ABHAY CONSTRUCTION

Name of Work/ Road :Ishuapur Se Nawalpur Kameshwar Rai Ke Ghar Se Dafali Tola Hote Hue
Kushwaha Tola Gupta Asthan Tak

Sr.no	Location of test(in km)	Corrected U.I value(mm/km)			Road catagory
9	0.1			3204	G
10	0.2			3304	G
11	0.3			3502	G
12	0.4			3214	G
13	0.5			2847	G
14	0.6			3203	G
15	0.7			2601	G
16	0.8			2847	G
17	0.9			3303	G
18	1			3014	G
19	1.1			3240	G
20	1.2			3303	G
21	1.3			3002	G
22	1.4			2615	G
23	1.5			2904	G
24	1.6			2402	G
25	1.7			3184	G
26	1.8			2991	G
27	1.9			2702	G
28	2			3202	G
29	2.1			2285	G

[Signature]
8/6/24
J.E

[Signature]
18/6/24
R.E.

[Signature]
24/07/24
Executive Engineer
R.W.D. Works Division Sonapur

Lab Job number :
Date :08-Jun-24

Name of Customer :ABHAY CONSTRUCTION

Name of Work/ Road :Ishuapur Se Nawalpur Kameshwar Rai Ke Ghar Se Dafali Tola Hote Hue
Kushwaha Tola Gupta Asthan Tak

Sr.no	Location of test(in km)	Corrected U.I value(mm/km)			Road catagory
				2896	G
30	0.1			3302	G
31	0.2			2498	G
32	0.3			2874	G
33	0.4			2347	G
34	0.5				

[Signature]
8/6/24
J.E

[Signature]
18/06/24
A.E.

[Signature]
Executive Engineer
R.W.D. Works Division Sonapur

File : F:\DESKTOP ALL FILE\SCAN FILE of TENDER DOCUMENT\ABHAY CONSTRUCTION\30 MR-N22-23

Name of Customer : ABHAY CONSTRUCTION. Name of Work/ Road : Ishuapur Se Nawalpur Kameshwar Rai Ke Ghar

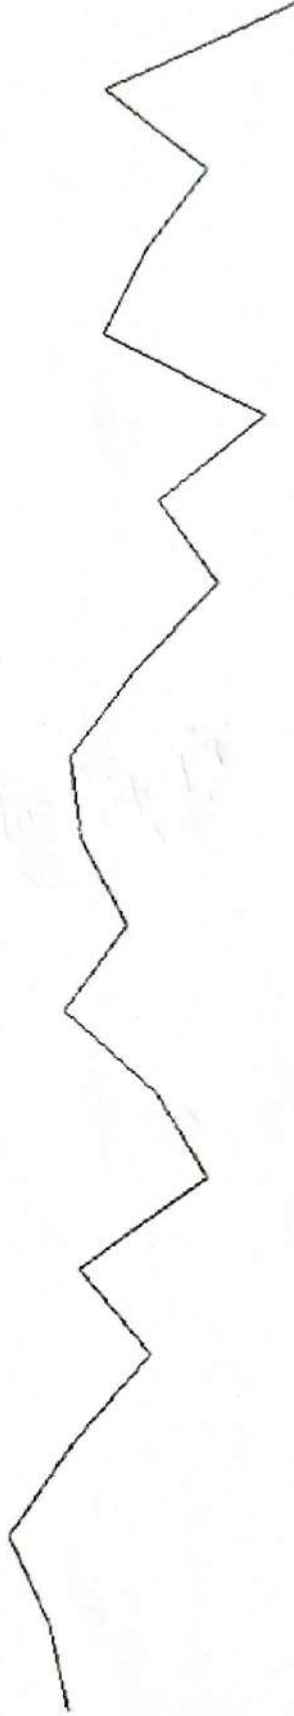
4285

3285

2285

1285

UIV
mm/
km



Distance * 1000 m

[Signature]
8/6/24

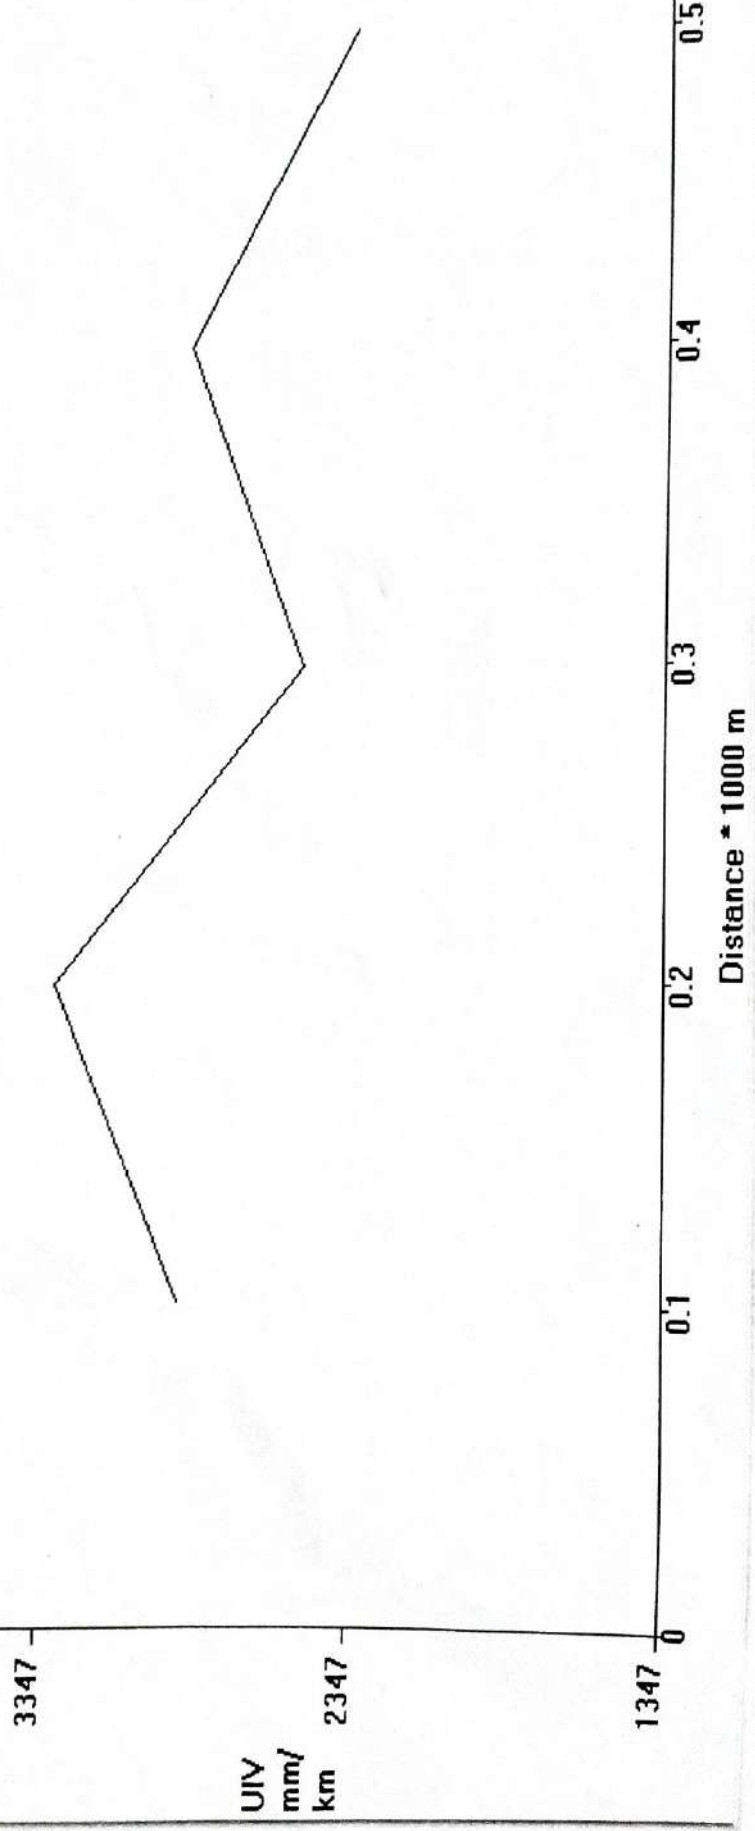
[Signature]
8/6/24
J.E

[Signature]
21/01/24

Executive Engineer
R.W.D. Works Division Sonapur

File : F:\DESKTOP ALL FILE\SCAN FILE of TENDER DOCUMENT\ABHAY CONSTRUCTION\30 MR-N22-23

Name of Customer : ABHAY CONSTRUCTION, Name of Work/ Road : Ishuapur Se Nawalpur Kameshwar Rai Ke Ghar



Signature
8/6/24
J.E

Signature
8/6/24
A.E

Signature

Executive Engineer
A.M.D. Works Division Sonapur

W on A/c Bill

1.

Name of work -

Situation of work -

Agency by which work is executed -

Date of measurement -

No. and date of agreement.

(These four lines should be repeated at the commencement of the measurements relating to each work).

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
N/W - Ishapur Se Nauwalpur					
Kamethwar Rai ke Ghar Se					
Dafali Tola hote hui Kuthuaha					
Tola Gupta sthan Tak.					
Agency:- Abhay Construction.					
Agst. No - 07MBD/2023-24					
DOS - 14/9/23					
DOC - 13/06/24					
Date of entry - 15/03/24					

① Clearing and grubbing - etc					
2x20x30m	x	1.0m	=	1200m ²	
2x20x30m	x	1.0m	=	1200m ²	
2x20x30m	x	1.0m	=	1200m ²	
2x20x30m	x	1.0m	=	1200m ²	
Total =				4800m ²	
Hence				$\frac{4800m^2}{10000}$	= 0.48 Ha.

② Construction of Subgrade and earthen shoulder - etc					
2x20x30m	x	0.75x0.30	=	270m ³	
2x20x30m	x	0.80x0.30	=	288m ³	
2x20x30m	x	0.55x0.30	=	198m ³	
2x20x30m	x	0.70x0.30	=	252m ³	
Continuation				Total =	1008m ³

Sch. XLV-Form No. 134

Particulars	Details of actual measure				Contents of area
	No.	L.	B.	D.	

$$B.F = R 5752686 = 00$$

(20/6) P/A of Tank Cont - etc.

$$Q = 7500 m^3$$

$$@ R 17.12 / Per m^3 = R 128400 = 00$$

(21/10) P/L of SDBL 25 mm th.

$$Q = 187.50 m^3$$

$$@ R 15581.91 / Per m^3 = R 2921608 = 00$$

$$Total = R 8802694 = 00$$

$$Add 18\% GST = R 1584485 = 00$$

$$Add 1\% L.C. = R 88027 = 00$$

$$Add S. Fee vide = R 80205 = 00$$

$$P. J. No. 20 Total = R 10555411 = 00$$

Let 10% below as per

Agst

$$= R 10555411 = 00$$

$$Net = R 9499870 = 00$$

19/01/24
J.E.

19/01/24
A.C.

Continuation
