

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, बारसोई (कटिहार)

Mob. No- 8986915775

E-Mail Id :- rwd.barsoi@gmail.com

पत्रांक 462 /

बारसोई, दिनांक 29/02/24 /

प्रेषक:-

ई० विश्वबन्धु राजीव रंजन
कार्यपालक अभियंता०

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी
BRRDA, 3rd Floor भूमि विकास बैंक भवन,
बिहार, पटना।

विषय : शीर्ष 3054 अंतर्गत बिहार ग्रामीण पथ अनुरक्षण नीति-2018 के तहत स्वीकृत कार्यों का आवंटन उपलब्ध कराने के सम्बन्ध में।

प्रसंग:- भवदीय का पत्रांक 4843 दिनांक 06.12.2021


महाशय,

उपर्युक्त विषयक एवं प्रासंगिक पत्र के आलोक में ग्रामीण कार्य विभाग, कार्य प्रमंडल, बारसोई, कटिहार के अधीन शीर्ष 3054 अंतर्गत बिहार ग्रामीण पथ अनुरक्षण नीति-2018 के तहत स्वीकृत कार्यों में निधि उपलब्ध कराने हेतु अधियाचना विहित प्रपत्र में तैयार कर आपके अग्रेतर कार्रवाई हेतु समर्पित किया जाता है।

अतः आप से अनुरोध है कि आवंटन शीघ्र उपलब्ध कराने की कृपा की जाय।


अनु०- यथोक्त।

विश्वास भाजन

 29/02/24

कार्यपालक अभियंता

ग्रामीण कार्य विभाग,

कार्य प्रमंडल, बारसोई, कटिहार


कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, बारसोई (कटिहार)

Mob. No- 8986915775

E-Mail Id :- rwd.barsoi@gmail.com

पत्रांक /

बारसोई, दिनांक..... /

प्रेषक:-

ई० विश्वबन्धु राजीव रंजन
कार्यपालक अभियंता०

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी
BRRDA, 3rd Floor भूमि विकास बैंक भवन,
बिहार, पटना।

विषय : शीर्ष 3054 अंतर्गत बिहार ग्रामीण पथ अनुरक्षण नीति-2018 के तहत स्वीकृत कार्यों का
आवंटन उपलब्ध कराने के सम्बन्ध में।

प्रसंग:- भवदीय का पत्रांक 4843 दिनांक 06.12.2021

महाशय,

उपर्युक्त विषयक एवं प्रासंगिक पत्र के आलोक में ग्रामीण कार्य विभाग, कार्य प्रमंडल,
बारसोई, कटिहार के अधीन शीर्ष 3054 अंतर्गत बिहार ग्रामीण पथ अनुरक्षण नीति-2018 के तहत
स्वीकृत कार्यों में निधि उपलब्ध कराने हेतु अध्याचना विहित प्रपत्र में तैयार कर आपके अग्रेतर
कार्रवाई हेतु समर्पित किया जाता है।

अतः आप से अनुरोध है कि आवंटन शीघ्र उपलब्ध कराने की कृपा की जाय।

अनु०- यथोक्त।

विश्वास भाजन

30-

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बारसोई, कटिहार

ज्ञापांक 462 दिनांक 29/02/24

प्रतिलिपि - नोडल पदाधिकारी, 3054 MR, ग्रामीण कार्य विभाग, बिहार पटना को सूचनार्थ एवं
आवश्यक कार्रवाई हेतु समर्पित।

29/02/24

कार्यपालक अभियंता

ग्रामीण कार्य विभाग,

कार्य प्रमंडल, बारसोई, कटिहार

29/02/24

Rural Works Department, Works Division, Barsoi, Katihar.
MR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Initial Rectification and Surface Renewal)

NIR(3054) under Bihar Rural Road Maintenance Policy																														
Name of Division :- Barsoi (Katihar)																														
Sl No	Project ID as per MIS	Name Of Road	Administrative Approval (AA) Letter No / Date	Length of (In KM)	Amount of (In Lakh)	Rectification with Surface Renewal (In Lakh)	5 Year Routine Maintenance (In Lakh)	Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen content in Percentage	Previous Total Allocated Amount (In Lkh)	up-to-date expenditure as per MIS (In Lakh)	Total Value of Measurement (In Lakh)	Requisition against work done (In Lakh)	Remarks												
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20											
1	NIR-N/22-23 BARSOI /13	L.025-T02 To Kandarpaili (VR25)	455 / 04.07.2022	1.066	61.74800	35.20532	14.26921	02 MBD /2023-24		04.01.24	2622.91	25mm	5.1%	0.00	0.00	0.00	0.00	0.00												
																				05.01.24	04.01.24	2779.08	25mm	5.1%	0.00	0.00	0.00	0.00	38.15960	38.15960
2	NIR-N/22-23 Barsoi/18	Kadiwa Chowk To Ghoshala Gaon Via Nungaha Tola Tegachhya Tak.	1447 De- 28.02.2023	4.374	308.54600	218.42522	62.65684	24 MBD/2023-24	16.07.24	On Going	2895.41	25mm	5.1%	72.16428	72.16428	170.88439	98.72011													
3	MR-N/22-23 BARSOI/06	Fatehpur To Manikpur	2011 / 02.05.2022	5.705	320.51400	244.66939	63.22869	32 MBD/2023-23	19.12.23	On Going	2113.03	25mm	5.1%	82.47911	82.47911	117.82731	35.34820	10.02132												
		Lachor Chouk to Bhuri Gaon Via Adivasi Tola Hasandpur Shersahi.		2.840	145.71800	102.07425	25.39224			On Going	2935.45	25mm	5.1%	23.38307	23.38307	33.40439	10.02132													
		Total :-		16.179	958.13100	667.46969	188.31755							178.02646	178.02646	360.27569	182.24923													

29/12/24
 Executive Engineer
 R W D, Works Division
 Barsoi-Katihar

FROM GFR 19 - A

(See Government of India's Decision (I) Below Rule - 150)

Form of Utilisation Certificate

Sl. No.	Name of Scheme	Sanctioned No Date with Amount (in Lacs Rs.)	Amount Received (in Lacs Rs.)	Particulars
1	2	4	5	6
1	MR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Year-2021-22, 2022-23 & 2023-24)	MR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Year- 2021-22, 2022-23 & 2023-24) Lt. No. 32 Dt- 28.05.2021 Lt. No. 40 Dt- 14.06.2021 Lt. No. 05 Dt- 25.01.2022 Lt. No. 10 Dt- 21.02.2022 Lt. No. 49 Dt- 27.04.2022 Lt. No. 22 Dt- 08.08.2022 Lt. No. 12 Dt- 03.02.2023 Lt. No. 35 Dt- 14.03.2023 Lt. No. 42 Dt- 20.03.2023 Lt. No. 72 Dt- 10.05.2023 Lt. No. 78 Dt- 24.05.2023 Lt. No. 84 Dt- 08.06.2023 Lt. No. 96 Dt- 07.07.2023 Lt. No. 106 Dt- 02.08.2023 Lt. No. 113 Dt- 14.08.2023 Lt. No. 136 Dt- 10.10.2023 Lt. No. 140 Dt- 16.10.2023 Lt. No. 144 Dt- 20.10.2023 Lt. No. 152 Dt- 16.11.2023	238.50541 2993.07433	Certified that out of Rs.- 3231.57974 Lakh of grants in aid sanctioned during the Years 2021-22, 2022-23 & 2023-24 In Favour of Executive Engineer, Rural Works Department, Works Division, Barsoi sum of Rs.- 3224.23764 Lakh has been utilized for the purpose of MR(3054) under Bihar Rural Road Maintenance Policy- 2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs.- 7.34210 Lakh remaining unutilized at the end of the period under report.purpose.
	Total -		3231.57974	

- 2 Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose fo

Kind of Checks Exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test checks conducted by the Assistant Engineer/ Executive Engineer.
- All other codal formalities have been observed.

3 Physical Progress achieved :-

- Construction of Road Works.
- Construction of CD. Works.

K
29/2/24

[Signature]
29/02/24
Executive Engineer
Rural Works Department
Works Division, Barsoi, Katihar
29.2.24

MAHAVIR CONSTRUCTION

Abdul Rajjak

M/R

DAHAKHORA

SUB-DIVISION

MEASUREMENT BOOK

BARSOI

DIVISION

Schedule XLV Form No. 134.
BIHAR P.W.D.

MBN-1119

REO Road Borei Chowk to Kusaba Santhali

SANTOLI TO DAHAKHORA (CH) TO BARSOI

MUSLIMCHOWK TO DAKSHIN TOLA VIA

1st and Final bill

Abstract of Cost

Sch. XLV - Form No. 134

10

Particulars	Details of actual measurement				Content or area
	No.	L.	B.	D.	
N/W:- Const. & Maint. of road from RPO Road Barichowk to Kushwa Mahasaha Santhali					
Agency:- Abdul Rajjak Kumhari, Katihar					
Aggr. No:- 02 MBD 2022-24					
Suppl. Aggr. No:- 62 MBD 2023-24					
D.O.S:- 06-04-2023					
D.O.C:- 05-01-2024					
A.D.O.C:- 04-01-2024					
1/55 > Clearing and grubbing the road land Qty-wide TMB page-1					0.20 Hct
@ Rs- 62032.43/Hct					Rs- 12406.48

2/57 > Construction of Subgrade and earthen shoulder					
Qty-wide TMB page-1					606.15 m ³
@ Rs- 254.50/m ³					Rs- 154265

3/56 > Excavation for roadway in Soil using manual means -					
Qty-wide TMB page-2					32.81 m ³
@ Rs- 99.78/m ³					Rs- 3274.1

4/58 > Construction of granular sub-base					
Qty-wide TMB page-2					74.75 m ³
@ Rs- 2369.96/m ³					Rs- 17700.9

5. P/L SIC Stone 100. of Specific

18
72

Plastering with C.M (1:4) in
Substructure

Qty-wide TMB

Page-8

60.48 m²

@ Rs-224.81/m²

Rs-13605.00

19
73

Painting two coats including
primer coat

Qty wide TMB

Page-9

60.48 m²

@ Rs-115.79/m²

Rs-7003.00

20
74

Planting of trees by the

road side

Qty-wide TMB

Page-9

45.00 nos

@ Rs-114.62/no

Rs-5015.80

21
75

PIF of typical Informative
Sign board with logo and
Maintenance board

Qty-wide TMB

Page-9

3.00 nos

@ Rs-11835.11/no

Rs-35505.33

3890287.00

Total - Rs-3890287.00

Add 1% cess - Rs-38903.00

Add 12% GST - Rs-300259.00

Add 10% S.F - Rs-11152.00

C.D → Total Rs-4640594.00

Continuation

Particulars	Details of actual measurement				Contents or area
	No.	L.	B.	D.	
B. P					Rs. 4640594.00
1 egg - 18.77% below					(-) Rs. 824634.00
Total					Rs. 3815960.00

Attested

Amrinder Singh
29/12/24

29/12/24
Executive Engineer
Rural Works Department
Works Division, Barsoi

Material statement

1) S/W - 606.15 m ³					
@ Rs. 23.00/m ³					Rs. 2003200
2) 26.5 mm to 9.5 mm - 33.64 m ³					
@ Rs. 657.85/m ³					Rs. 2213000
3) 9.5 mm to 2.36 mm - 32.32 m ³					
@ Rs. 514.58/m ³					Rs. 1230900
4) Below 2.36 mm - 38.12 m ³					
@ Rs. 141.85/m ³					Rs. 540700
5) 53 mm to 22.4 mm - 61.60 m ³					
					Rs. 3150500
6) 11.2 mm - 12.22 m ³					
@ Rs. 237.73/m ³					Rs. 486000

Lab Job number :61

Date :02-01-2024

Name of Customer :Abdul Rajjak

Name of Work/ Road :REO Road Bari Chowk o Kushaha Santhali

Sr.no	Location of test (in km)	Corrected U.I value (mm/km)	Road catagory
1	0.100	2787	G
2	0.200	2593	G
3	0.300	2303	G
4	0.400	2690	G
5	0.500	2497	G
6	0.600	2884	G
7	0.700	2497	G
8	0.800	2884	G
9	0.900	3078	G
10	1.000	3166	G
Average IRI Value		2737.90	

eh
02/01/2024
x

Chandran 12/01/2024
Aty 21/1/2024

[Signature]
Executive Engineer
Rural Works Department
Works Division, Barsoi

Lab Job number :61
Date :02-01-2024

Name of Customer :Abdul Rajjak

Name of Work/ Road :REO Road Bari Chowk o Kushaha Santhali

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY	Latitude	Longitude	Event
2/1/24	9:16:0	61	0.1	280	10.1	2800	2787	ROAD	25.55104	87.66843	Normal
2/1/24	9:16:45	61	0.1	260	10.1	2600	2593	G	25.55228	87.66828	Curve
2/1/24	9:17:10	61	0.1	230	20.2	2300	2303	G	25.55247	87.66948	Normal
2/1/24	9:17:42	61	0.1	270	20.2	2700	2690	G	25.55255	87.67052	Normal
2/1/24	9:18:15	61	0.1	250	20.2	2500	2497	G	25.55265	87.67150	Normal
2/1/24	9:18:51	61	0.1	290	20.2	2900	2884	G	25.55276	87.67251	Culvert
2/1/24	9:19:20	61	0.1	250	20.2	2500	2497	G	25.55280	87.67345	Normal
2/1/24	9:19:53	61	0.1	290	10.1	2900	2884	G	25.55287	87.67448	Normal
2/1/24	9:20:23	61	0.1	310	10.1	3100	3078	G	25.55293	87.67540	Normal
2/1/24	9:20:58	61	0.094	300	10.1	3191	3166	G	25.55302	87.67621	Normal

$$Y = 0 * X^2 + 0.969 * X + 74.60$$

$$X = 2891$$

$$Y = 2766$$

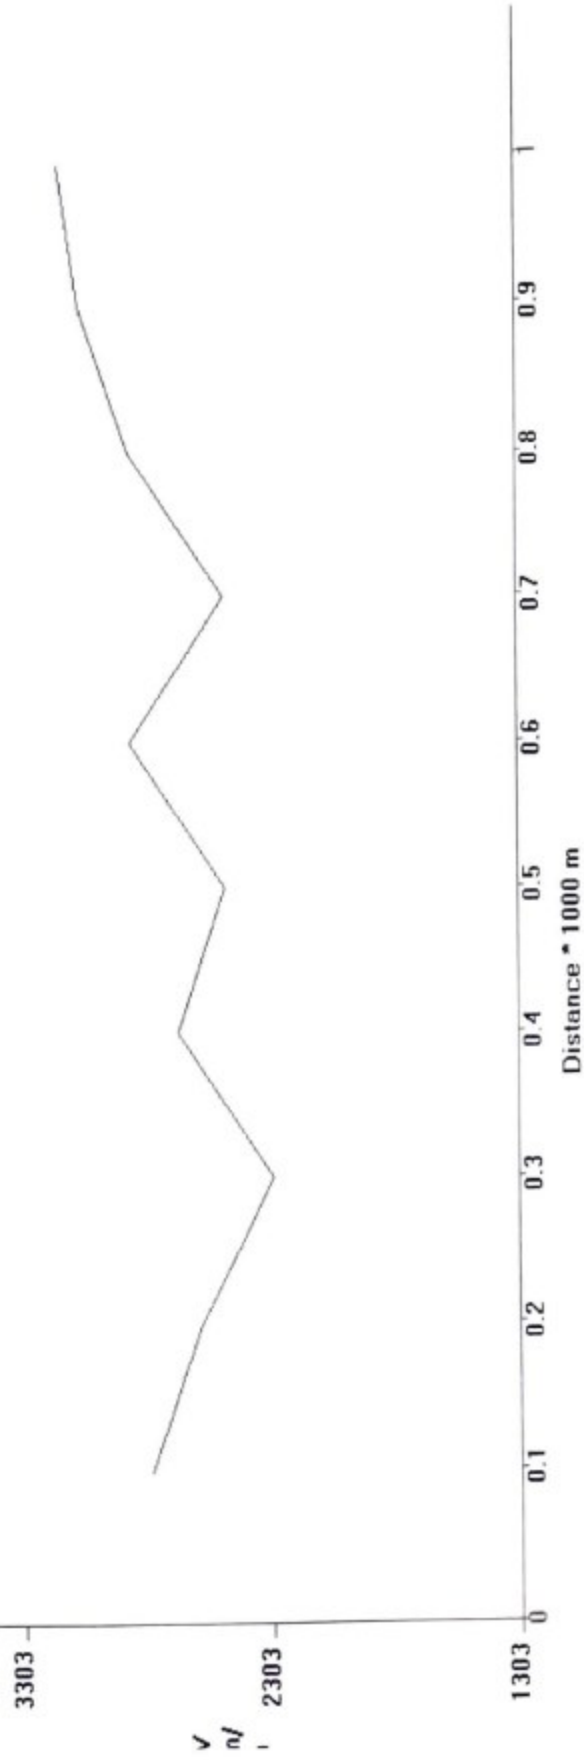
(R) RURAL ROAD

Good <4000
Average 4001-5000
Poor >5001

Handwritten signature and date: 21/1/2024

Handwritten signature: *Dr. J. S. Sanyal*
Executive Engineer
Rural Works Department
Works Division, Barsoi

File : E:\Bump Integrator\Dandkhora\REO Road Bari Chowk o Kushaha Santhali\02010922.Xls, Section No. :61,
 Name of Customer : Abdul Rajjak, Name of Work/ Road : REO Road Bari Chowk o Kushaha Santhali, Lab Job



Handwritten signature: *Chandran Prasad*
 Date: 21/1/2024

Handwritten signature: *Abdul Rajjak*
 Executive Engineer
 Rural Works Department
 Works Division, Barsoi
