

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल- डुमरांव।

पत्रांक:- 285 / डुमरांव

दिनांक:- 07-03-2024

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, डुमरांव।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास अभिकरण,
बुद्ध मार्ग, पटना

विषय :- शीर्ष 3054 (बिहार ग्रामीण पथ अनुरक्षण निति-2018) योजनान्तर्गत राशि की अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष 3054 मरम्मति (बिहार ग्रामीण पथ अनुरक्षण निति-2018) अन्तर्गत कराये गये कार्यों के भुगतान हेतु राशि की आवश्यकता है जिसे अधियाचना प्रपत्र के साथ संलग्न कर भेजा जा रहा है।

अतः श्रीगान से अनुरोध है कि संलग्न विवरणी के अनुसार आवंटन उपलब्ध कराने की कृपा की जाए, ताकि संवेदक द्वारा कराये गये कार्य का भुगतान किया जा सके।

अनु०:- यथोक्त।

विश्वासभाजन

[Signature]
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल डुमरांव
[Signature]
07/03/2024

FORM GFR 19-A
(SEE Government of India's Decision (I) below Rule-150)
Form of Utilisation Certificate upto the month of 06.03.2024

New Maintenance Policy 2018 Through CFMS

PIU:- RWD(WD), Dumraon

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in Rs. Lacs)	Amount Received (in Rs. Lacs)	Particulars
1	Construction of Rural Roads under New Maintenance Policy 2018	Letter No:- 14 date- 06.02.2024	2709.65834	Certified that out of Rs.2709.65834 lacs received during the years in favour of Ex. Engineer, RWD (W), Div.- Dumraon, Bihar, a sum of Rs 2706.17581 lacs has been utilized for the purpose of MMGSY NDB Schemes as given in the margin for which it was sanctioned and that the balance of Rs.03.48253 lacs remaining unutilized at the end of the period under.
Total -				

2 Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised :-

- Works have been supervised by Executive Engineer/ Supertending Engineer.
- Periodical inspection has been conducted by Executive Engineer/ Supertending Engineer.
- Construction materials have been tested
- Measurements have been recorded in the MBs and test check conducted by the Assistant.
- All other codal formalities have been observed.

3 Physical Progress achieved :-

- Construction of Road works
- Construction of CD works

At inda
7/03/24

07/03/2024
Executive Engineer
R.W.D. (w) Div. Dumraon
07/03/2024

Requisition Format for Scheme Head - M/R (3054) Under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)
Name of Works Division :- RWD, Works Division, Dumraon.

Sl. No	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No/ Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Amount Allotted (In Lakh)	up-to-date expenditure as per MIS (In Lakh)	Requisition against work done (In Lakh)	Remarks
					Length (in KM)	Amount (in Lakh)	Initial Rectification With Surface Renewal (In Lakh)	5 Year Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
		Brahmpur Raghunathpur To Babu Dera Hote Raghunathpur Railway Crossing Tak	10402013002	1941/29.03.2023	2.100	122.68	79.16800	20.89695	09/MIBD/2023-24(09.09.2023)	06-Aug-24	Ongoing	2928	25.00	5.02	0.00000	0.00000	67.81241	
		L028-Brahmpur Bagan Road to Kant village (L028)	10402002065	1941/29.03.2023	2.000	142.49	97.86318	19.14410	09/MIBD/2023-24(09.09.2023)	06-Aug-24	Ongoing	3005	25.00	5.02	0.00000	0.00000	92.70624	
		SUNDAR TOLA - DHASI	10402002076	1941/29.03.2023	2.548	141.17	94.33127	28.20280	09/MIBD/2023-24(09.09.2023)	06-Aug-24	Ongoing	3419	25.00	5.02	0.00000	0.00000	67.98925	
		Saphi - Balua - Simra - Ghaighai Road	NEA22000715	1941/29.03.2023	2.600	161.12	111.70373	22.93140	09/MIBD/2023-24(09.09.2023)	06-Aug-24	Ongoing	2987	25.00	5.02	0.00000	0.00000	88.09006	
4	M/23/00066																316.59796	

1 Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.
2 Up-to-date Physical Progress has been Uploaded in MIS.

Handwritten signature
7/13/24

Handwritten signature
09/10/2024
Executive Engineer
RWD, Works Division,
Dumraon.

Road Name-L028-Brahmpur Bagan road to Kant village (L028), Contractor Name-Alok Kumar Singh

Project ID-10402002065


Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event	
6/3/24	15:14:17	74	0.1	410	20.2	4100	3782	G	25.58019	84.30271	Speed Breaker	$Y = 0. * X ^ 2 + 0.840 * X + 339.0$
6/3/24	15:14:17	74	0.1	290	30.3	2900	2774	G	25.58034	84.30369	Normal	$Y = 2858$
6/3/24	15:15:0	74	0.1	420	30.3	4200	3866	G	25.58041	84.30473	Normal	
6/3/24	15:15:0	74	0.1	300	40.4	3000	2858	G	25.58057	84.30572	Normal	
6/3/24	15:15:0	74	0.1	260	50.5	2600	2522	G	25.58069	84.30665	Normal	(R) RURAL ROAD
6/3/24	15:15:28	74	0.1	320	20.2	3200	3026	G	25.58107	84.30744	Curve	Good
6/3/24	15:15:28	74	0.1	270	30.3	2700	2606	G	25.58109	84.308	Normal	<4000
6/3/24	15:15:28	74	0.1	410	20.2	4100	3782	G	25.58142	84.30928	Curve	Average
6/3/24	15:16:3	74	0.1	270	40.4	2700	2606	G	25.58165	84.31025	Normal	Poor
6/3/24	15:16:3	74	0.1	420	30.3	4200	3866	G	25.58181	84.31125	Culvert	
6/3/24	15:16:3	74	0.1	280	40.4	2800	2690	G	25.58188	84.31231	Curve	
6/3/24	15:16:3	74	0.1	270	30.3	2700	2606	G	25.58178	84.31328	Normal	
6/3/24	15:16:3	74	0.1	260	40.4	2600	2522	G	25.58175	84.31429	Normal	
6/3/24	15:16:38	74	0.1	290	30.3	2900	2774	G	25.58163	84.31532	Normal	
6/3/24	15:17:0	74	0.1	190	20.2	1900	1934	G	25.58171	84.31636	Normal	
6/3/24	15:17:14	74	0.1	260	10.1	2600	2522	G	25.58218	84.31699	Curve	
6/3/24	15:17:49	74	0.1	300	20.2	3000	2858	G	25.58211	84.31798	Normal	
6/3/24	15:18:0	74	0.1	420	20.2	4200	3866	G	25.58218	84.31902	Normal	
6/3/24	15:18:24	74	0.1	410	20.2	4100	3782	G	25.58243	84.31998	Speed Breaker	
6/3/24	15:18:24	74	0.1	300	20.2	3000	2858	G	25.58294	84.32014	Normal	
Total IRI							60100					
Average IRI							3005					

Shakun
07/03/24
J-E

67/103/2024
AF

67/103/2024

File : E:\74\L028-Brahmpur Bagan road to Kant village (L028).xlsx Section No. : 74, Eqn : $Y = 0. * X^2 + 0.840 * X +$
 Name of Customer : Alok Kumar Singh, Name of Work/ Road : L028-Brahmpur Bagan road to Kant village (L028), Lab

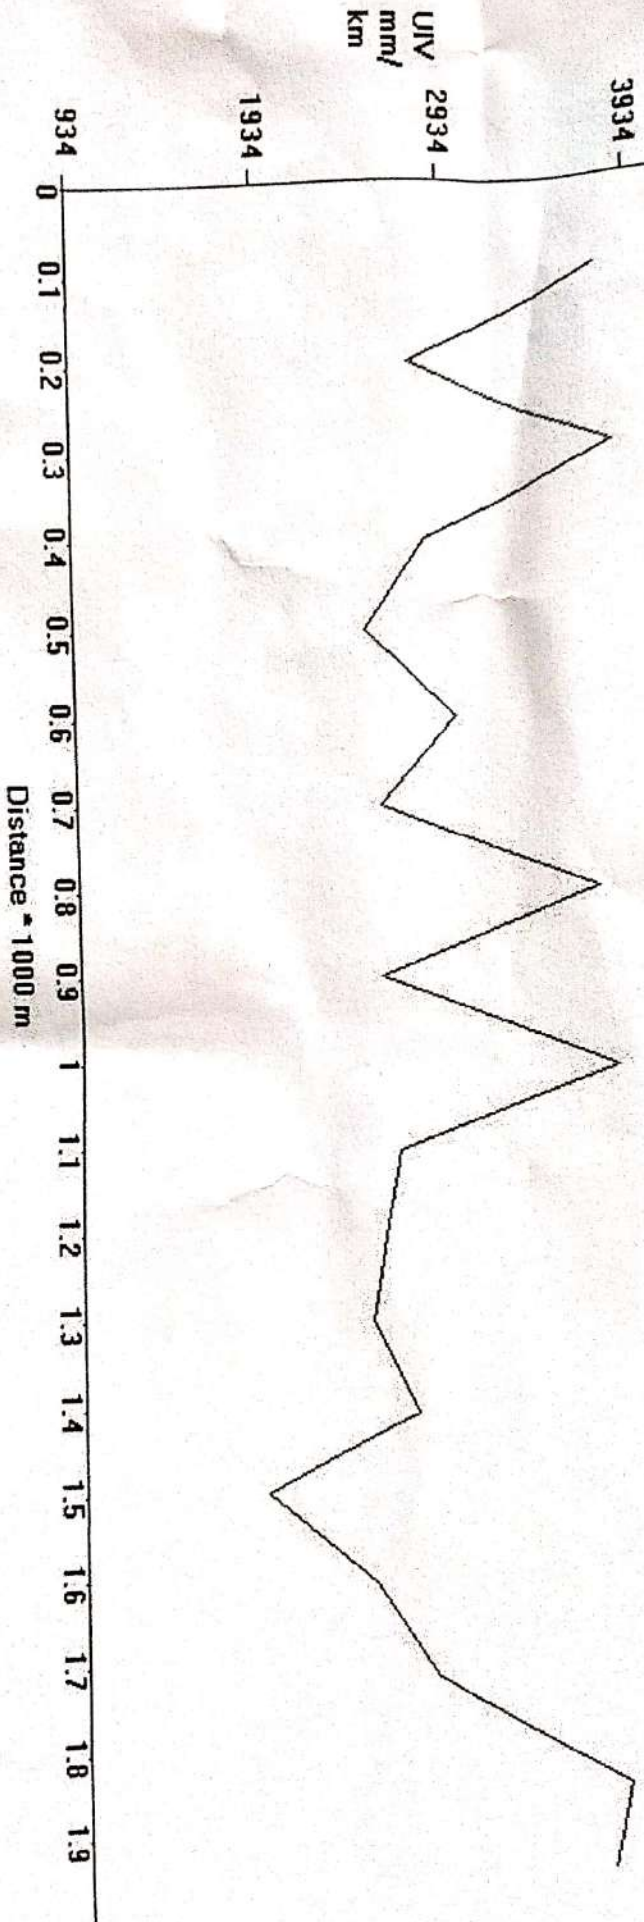

Shaf Kumar
 07/03/24
 J-E

H
 07/03/24
 DE

9/03/24
 DE

Schedule XLV-Form No. 134

प्राप्त (ग्र) चयन के लिए अतिरिक्त Length - 2 K.M

Start - 9/9/23

New Maint. Policy - 2018 (MIR-3054)

Comp - 8/6/24

अधिकारी

DIVISION

अधिकारी

SUB-DIVISION

Agre No - 09.MBD/23-24

MEASUREMENT BOOK

1254

अतिरिक्त अतिरिक्त के लिए

1.

Name of work -

Situation of work -

Agency by which work is executed -

Date of measurement -

No. and date of agreement.

(These four lines should be repeated at the commencement of the measurements relating to each work).

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
H/W:- Maint. of road from					
L028 Brahmapur Bageroad to					
Kant under H.M.P.					
H/A:- SRI - ALOK Kumar Singh.					
A/HO:- 09 HBD/2023-2024					
Date of start:- 09-09-2023					
Date of completion:- 08-06-2024					
Date of Measurement:-					
Details of work -					

Item NO (1) - Clearing and					
grading road (all)					
$2 \times 20 \times 30.00 \times 1.00 (AV) =$					$1200.00 M^2$
$2 \times 20 \times 30.00 \times 1.00 (AV) =$					$1200.00 M^2$
$2 \times 20 \times 30.00 \times 1.00 (AV) =$					$1200.00 M^2$
$2 \times 6 \times 30.00 \times 1.00 (AV) =$					$360.00 M^2$
$2 \times 1 \times 20.00 \times 1.00 (AV) =$					$40.00 M^2$
					$4000.00 M^2$
					or 0.40 Ha

Item NO (2) - Cost of subgrade					
and earthen shoulder					
$2 \times 25 \times 30.00 \times 1.250 \times 0.30 =$					$562.50 M^3$
$2 \times 25 \times 30.00 \times 1.250 \times 0.30 =$					$562.50 M^3$
$2 \times 16 \times 30.00 \times 1.250 \times 0.30 =$					$360.00 M^3$
$2 \times 1 \times 20.00 \times 1.250 \times 0.30 =$					$15.00 M^3$
Continuation					
					$1500.00 M^3$

ABSTRACT of COST

Sch.XLV-Form No. 134

Particulars	Details of actual measure				Contents of area
	No.	L.	B.	D.	
Item No (1):- Clearing and grubbing road land and					
Qty vide T.M.B P _{No} ① ie					
0.40 Ha @ Rs 72697.96/Ha					Rs 29079 =
Item No (2):- Cost of subgrade and earthen shoulders					
Qty vide T.M.B P _{No} ① ie					
1500.00 m ³ @ Rs 264.23/m ³					Rs 396345 =
Item No (3):- Cost of G.S.B as per 7 1/2 clause 401					
Qty vide T.M.B P _{No} ② ie					
145.60 m ³ @ Rs 3299.90/m ³					Rs 480470 =
Item No (4):- Providing laying and compacting N.B. mgs-2					
Qty vide T.M.B P _{No} ③ ie					
139.93 m ³ @ Rs 5745.40/m ³					Rs 803954 =
Item No (5):- Providing laying and compacting N.B. mgs-3					
Qty vide T.M.B P _{No} ③ ie					
167.82 m ³ @ Rs 5491.34/m ³					Rs 921596 =
Item No (6):- Providing and applying primer coat					
Qty vide T.M.B P _{No} ③ ie					
2237.60 m ² @ Rs 60.40/m ²					Rs 135151 =
Item No (7):- Providing laying					
8 rolling m.s.s					

Continuation

Rs 2766595 =

(C.O)

(P.T.O)



Sch.XLV-Form No. 134

Particulars	Details of actual measure				Contents of area
	No.	L.	B.	D.	
				B/E	Rs 8140202 =
(i) 08 Nos @ Rs 5055.95/No					Rs 40448 =
(ii) 04 Nos @ Rs 5371.35/No					Rs 21485 =
(iii) 06 Nos @ Rs 5180.70/No					Rs 31084 =
(iv) 02 Nos @ Rs 11076.35/No					Rs 22153 =
Step No (13) :- Road Marking					
in B.T Position					
Qty vide T.M.B P/No 610					
328.00 M ² @ Rs 886.39/M ²					Rs 290736
Step No (14) :- Road Marking					
C.C Position					
Qty vide T.M.B P/No 610					
80.00 M ² @ Rs 991.23/M ²					Rs 79298 =
Step No (15) :- Providing and					
fixing Project board					
Qty vide T.M.B P/No 610					
02 Nos @ Rs 15319.67/No					Rs 30639 =
					Rs 8652045 =
Add 1% Labourers cess (+) Rs 86560 =					
Add 18% G.S.T (+) Rs 1558088 =					
					Rs 10300693 =
Less 10% below Agg cost (-) Rs 1030069 =					
					Rs 9270624 =
07/03/24 PK (b) of 100000 07/03/24 J-E					

Continuation
