

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल- डुमरांव।

पत्रांक:- 502, डुमरांव /

दिनांक:- 02/05/2024

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, डुमरांव ।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास अभिकरण,
बुद्ध मार्ग, पटना

विषय :- शीर्ष 3054 (बिहार ग्रामीण पथ अनुरक्षण निति-2018) योजनान्तर्गत राशि की अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि शीर्ष 3054 मरम्मत (बिहार ग्रामीण पथ अनुरक्षण निति-2018) अन्तर्गत कराये गये कार्यों के भुगतान हेतु राशि की आवश्यकता है जिसे अधियाचना प्रपत्र के साथ संलग्न कर भेजा जा रहा है।

अतः श्रीमान से अनुरोध है कि संलग्न विवरणी के अनुसार आवंटन उपलब्ध कराने की कृपा की जाए, ताकि संवेदक द्वारा कराये गये कार्य का भुगतान किया जा सके।

अनु०:- यथोक्त।

विश्वासभाजन

Gopal
02/05/2024

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल डुमरांव

02/05/2024

25/5/24

FORM GFR 19-A
(SEE Government of India's Decision (I) below Rule-150)
Form of Utilisation Certificate upto the month of 02.05.2024

New Maintenance Policy 2018 Through CFMS

PIU:- RWD(WD), Dumraon

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in Rs. Lacs)	Amount Received (in Rs. Lacs)	Particulars
1	Construction of Rural Roads under New Maintenance Policy 2018	Letter No:- 40 date- 18.03.2024	3248.45509	Certified that out of Rs.3248.45509 lacs received during the years in favour of Ex. Engineer, RWD (W), Div.- Dumraon, Bihar, a sum of Rs 3244.97256 lacs has been utilized for the purpose of MMGSY NDB Schemes as given in the margin for which it was sanctioned and that the balance of Rs.3.48253 lacs remaining unutilized at the end of the period under.
Total -				

- 2 Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised :-

- Works have been supervised by Executive Engineer/ Supertending Engineer.
- Periodical inspection has been conducted by Executive Engineer/ Supertending Engineer.
- Construction materials have been tested
- Measurements have been recorded in the MBs and test check conducted by the Assistant.
- All other codal formalities have been observed.

3 Physical Progress achieved :-

- Construction of Road works
- Construction of CD works

Atk
21/5/24

Gopal
10/05/2024
Executive Engineer
R.W.D. (w) Div. Dumraon
Chitra
02/05/2024

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- RWD, Works Division, Dumraon.

Sl. NO	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No/ Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (In Lakh)	up-to-date Expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in KM)	Amount (in Lakh)	Initial Rectification With : Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/BU/D UM/19/0003	NH 84 DEOKULI SCHOOL - KOTHA	10401902052	201402.07.2019	1.600	47.27	29.59500	12.69504	13/MIBD/2019-20(10.12.2019)	09.09.2020	completed (01.10.2020)	3034	25.00	5.00	28.54667	28.54667	1.04714	
																	1.04714	

1 Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.
2 Up-to-date Physical Progress has been Uploaded in MIS.

21/5/20

20/5/2024
Executive Engineer,
RWD, Works Division,
Dumraon.

Name of Road :- NH -84 DEVKULI SCHOOL TO KOTHIVA . (MACHINE - BUXAR)

Date	Time	Section	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY Road	Latitude	Longitude	Event
		No.									
21/9/21	11:32:45	34	0.1	290	0	2900	2970	G	25.622093	84.325773	Normal
21/9/21	11:33:0	34	0.1	330	30.2	3300	3364	G	25.62188	84.324882	Normal
21/9/21	11:33:12	34	0.1	270	32.5	2700	2794	G	25.621745	84.324325	Normal
21/9/21	11:33:26	34	0.1	250	33.2	2500	2593	G	25.62167	84.32404	Normal
21/9/21	11:33:50	34	0.1	250	30.5	2500	2577	G	25.621048	84.323332	Normal
21/9/21	11:33:59	34	0.1	280	32.5	2800	2874	G	25.620553	84.322693	Normal
21/9/21	11:34:12	34	0.1	300	33.2	3000	3069	G	25.619695	84.322928	Curve
21/9/21	11:34:24	34	0.1	300	31.5	3000	3070	G	25.619197	84.322473	Normal
21/9/21	11:34:42	34	0.1	270	30.5	2700	2773	G	25.61825	84.322625	Normal
21/9/21	11:34:59	34	0.1	280	30.3	2800	2872	G	25.617292	84.322642	Normal
21/9/21	11:35:12	34	0.1	330	32.5	3300	3364	G	25.61642	84.322575	Normal
21/9/21	11:35:26	34	0.1	300	30.3	3000	3069	G	25.615475	84.322508	Normal
21/9/21	11:35:42	34	0.1	330	31.5	3300	3364	G	25.614702	84.322205	Curve
21/9/21	11:35:58	34	0.1	310	32.5	3100	3167	G	25.613878	84.322087	Normal
21/9/21	11:36:21	34	0.1	340	30.2	3400	3462	G	25.613057	84.32182	Normal
21/9/21	11:36:48	34	0.1	310	32.5	3100	3167	G	25.612242	84.321648	Normal
CUMULATIVE							48549				
AVERAGE IRI							3034				

22/9/21
JF

22/9/2021


Name of Customer : JAWAHAR LAL YADAV
 Name of Work/ Road : NH-04 Deokuli School to Kothia
 Lab Job number :
 Date : 9/21/2021
 Section No. : 34

Test Date : 9/21/2021 Road Name : NH-04 Deokuli School to Kothia
 Machine No : 312 Road Type : (F) RURAL ROAD
 Start S No : Side : Interval
 Start E No :
 Weather : UIV Range : 1577 To 4000 1000 mm/km
 Start Location : NH-04 Deokuli Dist Range : 0 To 1.7 0.1 * 1000 m
 End Location : Kothia Equation : $Y = 0 * X^2 + 1.047 * X - 63.36$

Print Generate Report and Graph

Redraw Graph

Map View

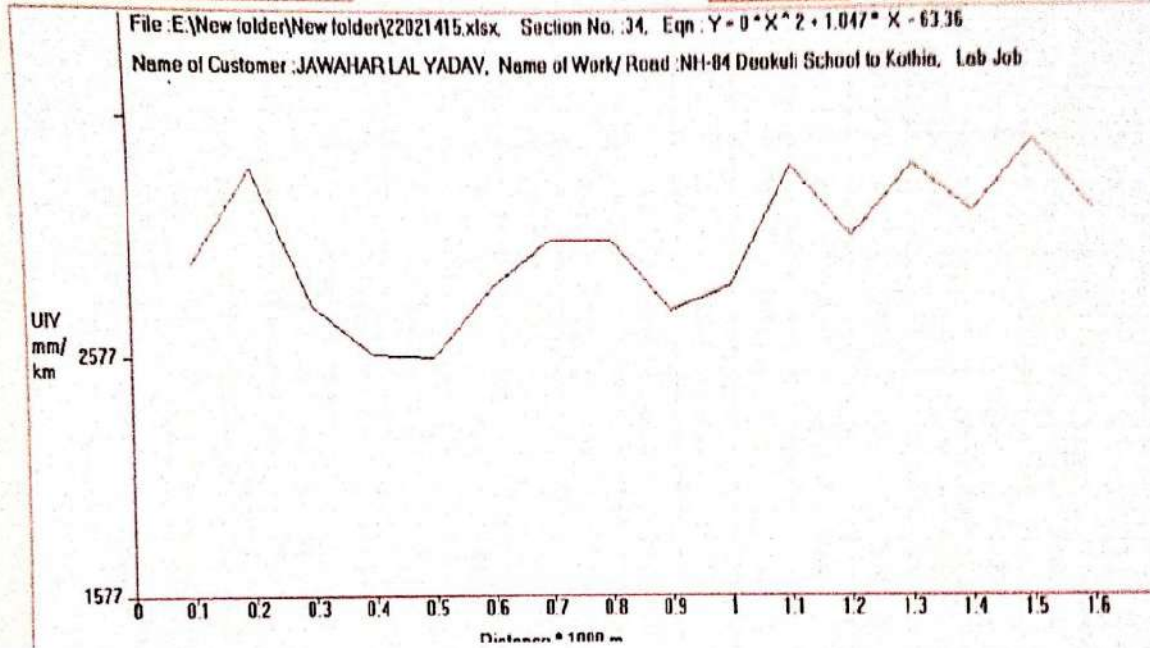

Akshar
 22/09/21
 JE

Gopal
 19/09/2021

2114 M. R. (3054) - प्रत्येक - अलग
पुस्तक नाम - NH-84 देवकुली विद्यालय
कोटियाल एवं पु. विद्यालय का
Schedule XLY-Form No. 134
देवकुली नाम - श्री गजानंद लाल भार्गव
देवकुली नाम - श्री रानी -
DIVISION

कार्य प्रगति की तिथि

कार्य प्रगति की तिथि - SUB-DIVISION

13 MB of 19-20 M. R. No- 1136

Measurement Book

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of work - Construction					
(M.R.) of road from					
NH 84 Deokuli school to Kothia					
Name of Agency - Sri Jawahar Lal					
Yadav, Vihar - Patna					
P.O. - Agas Sander Behra					
Dt. - Bhogapur, Bihar					
Agreement No. - 13 MBD of 2019-20					
Date of start of work - 10-12-2019					
Date of completion of work - 09-09-20					
Date of measurement - 08-09-20					

measurement					
1/24. Planting of trees					
by road side —					64 nos
2/27. Brick masonry work					
in cement mortar —					
2x2x6.00x0.40x0.60m =					5.76 m ³
3/28. Plastering with cement					
mortar —					
Side face 2x4.00x6.00x0.60m =					28.80 m ²
Top 2x2x6.00x0.40m =					9.60 "
Front face 2x4.00x0.40x0.60m =					1.92 "
					40.32 m ²
4/29. Painting two coats					

Continuation

[illegible]

Material consumption			
1. Earth work	—	1179.0 m ³	
2. G.S.B.	—	22.50 m ³	
Coarse sand	—	14.90 m ³	
3. W.B.M.	—		
Patch repairs	—	58.58 m ³	
Screening material	—	13.175 m ³	
			71.755 m ³
4. Bitumin Emulsion SS-1	—	0.3415 m.T.	
Bitumin Emulsion RS-1	—	3.4671 m.T.	
Bitumin S-90	—	18.1800 m.T.	
	—	11.5140 m.T.	
Chips	—	216.64 m ³	
	—	12.4411 m.T.	
	—	19.1071 m.T.	

Continuation
