

कार्यपालक अभियंता, का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल बिहारशरीफ

पत्रांक 1439/2024 बिहारशरीफ, दिनांक 15/11/2024

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ ।

सेवा में,

नोडल पदाधिकारी 3054
ग्रामीण कार्य विभाग, बिहार, पटना

विषय:- नई अनुरक्षण नीति-2018 अन्तर्गत आवंटन उपलब्ध करने के संबंध में।

महोदय,

उपर्युक्त विषयक से संबंधित नई अनुरक्षण नीति-2018 अन्तर्गत इस प्रमंडल द्वारा कराये जा रहे पथों के निर्माण कार्य के लिये आवंटन उपलब्ध करने हेतु अध्यादेश पत्र समर्पित की जा रही है।

अतः अनुरोध है कि पथ में कराये गये कार्यों के विस्तृत भुगतान हेतु संलग्न सूची के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय ताकि संवेदक को भुगतान किया जा सके।

अनु:- यथावत।

विश्वात्मनाजन

15/11/24
AM

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ

15/11/24

(See Government of India's Decision (I) below Rule-150)
Form of Utilisation Certificate up to the month of 15.11.2024
(New Maintenance Policy 2018)

PIU- BIHARSHARIF

Year-2024-2025

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in Rs. Lacs)	Amount Received (in Rs. Lacs)	Particulars
1	Construction of Rural Roads under New Maintenance Policy 2018	Itr-92 Dt-16.08.2024	6831.62977	Certified that out of Rs 6831.62977 received & balance during the years 2024-25 in favour of Ex. Engineer, R.W.D. Works Division Biharsharif, sum of Rs 6821.32419 has been utilized for the purpose of New Maintenance Policy 2018 scheme as given in the margin for which it was sanctioned and that the balance of Rs 10.30558 lacs remaining unutilized at the end of the period under 15.11.2024
	Total Rs.		6831.62977	

2 Certified that I have satisfied myself that the conditions on which the grants-in- aid was sanctioned
Kind of Checks exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
 - Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
 - Construction material have been tested.
 - Measurements have been recorded in the MBs and test check conducted by the Assistant .
 - All other codal formalities have been observed.
- 3 Physical Progress achieved:
- Construction of Road Works.
 - Construction of CD works


Divisional Accounts Officer
Rwd, Works Division
Biharsharif


Executive Engineer
Rwd, Works Division
Biharsharif
15/11/24

Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)
Works Division :- Bihar Sharif

Sl No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Increase in Allotment	Remarks
					Length (in km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/NA/B IH/24/000 4	Bena- Saksohra Path To Bishampur	10200612001	6120 04 Dec 2023	0.530	35.21600	28.98109	2.18172	MBD- 01/2024-25 27.08.2024	26-05-2025	0	2664	25	5.01	24.80535	24.80535	3.73252	
2	RM/NA/B IH/24/000 4	NH-82 Gorabartar Road to Jama Masjid Tola	10200612024	6120 04 Dec 2023	0.550	22.56800	13.13257	5.78817	MBD- 01/2024-25 27.08.2024	26-05-2025	0	2642	25	5.02	0	0	10.10777	
3	RM/NA/B IH/24/000 4	Construction of road from Nh-82 pachetam road to pachetam (test proton) via pachetan	10200612025	6120 04 Dec 2023	1.700	74.64100	45.49869	17.56132	MBD- 01/2024-25 27.08.2024	26-05-2025	0	2158	25	5.00	0	0	43.87799	
4	RM/NA/B IH/24/000 5	LO3S-LO29A To Palani (VR21)	10200602045	6120 04 Dec 2023	1.000	45.30900	28.04151	10.36195	MBD- 02/2024-25 05.09.2024	04.06.2025	0	2166	25	5.01	0	0	27.63042	
TOTAL																	85.34870	

Total = 85.34870

- 1 Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.
- 2 Up-to-date Physical Progress has been uploaded in MIS.


Divisional Accounts Officer
 Rwd, works Division Bihar Sharif

MS
 15/11/24

Executive Engineer
 Rwd, works Division Bihar Sharif

MS
 15/11/24

File : C:\Users\kkmml\OneDrive\Desktop\Downloads\12100910.xls. Section No. : 36. Eqn : $Y = 0.0 \cdot X^2 + 0.816 \cdot X$
Name of Customer : Deepak Kumar. Name of Work/ Road : Benar Saksobra path se Bishunpur. Lab Job number :

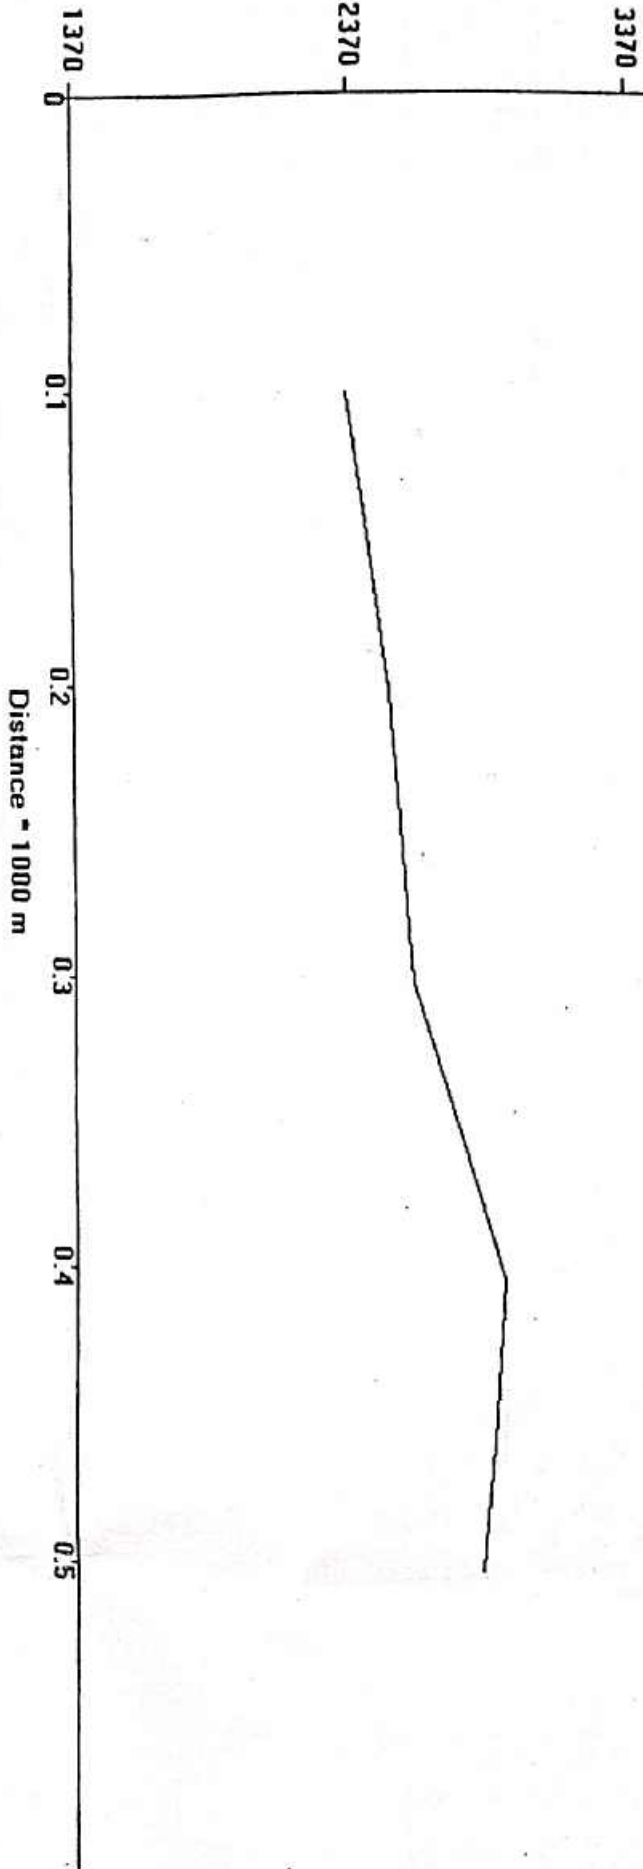

14/10/24
HSH

Paul
14/10/24
TS

14/10/24
Bishunpur

14/10/24
Bishunpur

Head-NEW MR
Road-Benar Saksohra road se Bishunpur
Con-Deepak Kumar

date	Time	Section No.	Length In km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event	$Y = 0 \cdot X^2 + 0.816 \cdot X + 249$		
12/10/24	8:29:9	36	0.1	260	0	2600	2370	G	25.329977	85.691821	Normal	X = 3200		
12/10/24	8:29:45	36	0.1	280	20.2	2800	2533	G	25.330457	85.691944	Normal	Y = 2860		
12/10/24	8:30:0	36	0.1	290	20.2	2900	2615	G	25.330802	85.692227	Normal			
12/10/24	8:30:0	36	0.1	330	20.2	3300	2941	G	25.331358	85.692681	Normal			
12/10/24	8:30:20	36	0.1	320	10.1	3200	2860	G	25.331953	85.693050	Normal	(R) RURAL ROAD		
						Total-	13319					Good	Average	Poor
						IRI Value-	2664					<4000	4001-5000	>5001

14/10/24
14/10/24

14/10/24
14/10/24

14/10/24
14/10/24

① construction of subgrade & earthen shoulder			
- - - do - - - do - - - el			
<u>For BT Portion</u>			
	$2 \times 17 \times 1.0 \times 0.30 =$	10.2 m^3	
	$2 \times 25 \times 1.0 \times 0.30 =$	15.0 m^3	
	$2 \times 40 \times 1.0 \times 0.30 =$	24 m^3	
	$2 \times 13 \times 1.0 \times 0.30 =$	7.8 m^3	
		<u>57 m^3</u>	
<u>Sur P.C.C Portion</u>			
	$1 \times 20 \times 0.70 \times 0.30 =$	4.2 m^3	
	$1 \times 23 \times 0.70 \times 0.30 =$	4.83 m^3	
	$2 \times 15 \times 0.70 \times 0.30 =$	6.3 m^3	
	$1 \times 27 \times 0.70 \times 0.30 =$	5.67 m^3	

Continuation

Sch.XLV-Form No. 134

Particulars	Details of actual measure				Contents of area
	No.	L.	B.	D.	
④ Plv lining Logo of maintenance board					
--- do --- do --- el					
1x1.00 No =					1.00 No.
⑧ Planting of trees by road side.					
--- do --- do --- el					
10x1.00 No =					10.00 No.

30/10/24
NE

ABSTRACT OF COST

① clearing and grubbing of road land	
--- do --- do --- el	
0.106 HA NTMB — P-01	
② Rs 76926.08/HA — Rs= 8154/-	
② Plv laying and spreading WSB W-11	
--- do --- do --- el	
30.96 m ³ NTMB — P-02	
③ 1509.81/m ³ — Rs= 46787/-	
③ Plv laying and compacting WBM-II	
--- do --- do --- el	
20.48 m ³ NTMB — P-03	
④ 3252.11/m ³ — Rs= 66603/-	

Continuation

Sch.XLV-Form No. 134

Particulars	Details of actual measure				Contents of area
	No.	L.	B.	D.	
④ P/v laying, spreading and compaction					
W 8 m W 8 m III					
— do — do — e/i					
9.99 m ³ NTMB					P-04
② 8227.98/m ³					R _s = 29987/-
⑤ construction of dry lean cement concrete					
— do — do — e/i					
2.02 m ³ NTMB					P-05
② 4928.44/m ³					R _s = 9955/-
⑥ construction of Panel concrete					
Pavement (M 30)					
— do — do — e/i					
202.58 m ³ NTMB					P-06
② 3046.33/m ³					R _s = 1841652/-
⑦ construction of subgrade & earthen shoulder					
— do — do — e/i					
NTMB					P-07 & P-08
89.64 m ³ @ 264.51/m ³					R _s = 23710/-
+ 114.06 m ³ @ 264.51/m ³					R _s = 30170/-
					R _s = 53880/-
⑧ P/v fixing R.C.C M15 KM Stone					
— do — do — e/i					
NTMB					P-07
1.0000 @ R _s 2814.42					R _s = 2814

Continuation

Sch.XLV-Form No. 134

Particulars	Details of actual measure				Contents of area
	No.	L.	B.	D.	
⑨ P/v Fixing R.C.C M/S 200mm Stone					
— do — do — e/i					
VTMB — P — 08					
2.00 No @ Rs 805.15 — Rs = 1610/-					
⑩ P/v Fixing Retro-reflectonised 600mm equilateral triangle					
— do — do — e/i					
VTMB — P — 08					
2.00 No @ Rs 4432.44 — Rs = 8868/-					
⑪ P/v Fixing retro-reflectonised circular sign					
— do — do — e/i					
VTMB — P — 08					
1.00 No @ Rs 4276.71 — Rs = 4276/-					
⑫ P/v Fixing Retro-reflectonised rectangular sign					
— do — do — e/i					
VTMB — P — 08					
1.00 No @ 4132.22 — Rs = 4132/-					
⑬ P/v Fixing Logo of Project Board					
— do — do — e/i					
VTMB — P-08 & P-17					
1.00 No @ 11572.86 — Rs = 11572					
+ 1.00 No @ 11572.86 — Rs = 11572					
					Rs = 23144/-

Continuation

Sch.XLV-Form No. 134

Particulars	Details of actual measure				Contents of area
	No.	L.	B.	D.	
(14) P/v fixing of citizen information Board	---	do	do	---	e/d
		VTMB	P	08	
	1.00 No	@ Rs 11572.86			Rs = 11572/-
(15) P/v fixing of Logo of Maintenance Board	---	do	do	---	e/d
		VTMB	P-09 & P-18		
	1.00 No	@ Rs 11572.86			Rs = 11572/-
	+ 1.00 No	@ Rs 11572.86			Rs = 11572/-
					Rs = 23144
(16) P/v & laying Prime coat (SS-1) 415-11	---	do	do	---	e/d
		VTMB	P	16	
	76.24 @	57.17/m ²			Rs = 4358/-
(17) P/v and applying tack coat with bitumen emulsion	---	do	do	---	e/d
		VTMB	P	17	
	378.75 m ²				
	@ 19.60/m ²				Rs = 7423/-
(18) P/v & laying semi-dense bitumen	---	do	do	---	e/d
		VTMB	P	17	
	9.47 m ³				
	@ 13350.07/m ³				Rs = 126425/-

Continuation

Continuation

BF	Rs = 2332026/-
Add labour cost @ 1% =	23320/-
Add wst @ 18% — Rs =	430564/-
Add Seigniorage — Rs =	8419/-
	Rs = 2854929/-
Less below 0.04% = Rs =	-1192
	Rs = 2853787/-
Less Previous Bill = Rs =	2480535/-
	2485155/-
	Rs = 368692/-
	373252 =

Which
30/10/21
AE

Continuation
