

कार्यपालक अभियंता, का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल बिहारशरीफ

पत्रांक...1439379/ बिहारशरीफ, दिनांक...15/11/2024

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ ।

सेवा में,

नोडल पदाधिकारी 3054
ग्रामीण कार्य विभाग, बिहार, पटना

विषय:- नई अनुरक्षण नीति-2018 अन्तर्गत आवंटन उपलब्ध करने के संबंध में।
महाशय,

उपर्युक्त विषयक से संबंधित नई अनुरक्षण नीति-2018 अन्तर्गत इस प्रमंडल द्वारा कराये जा रहे पथों के निर्माण कार्य के लिये आवंटन उपलब्ध करने हेतु अध्याचना पत्र समर्पित की जा रही है।

अतः अनुरोध है कि पथ में कराये गये कार्यों के विरुद्ध भुगतान हेतु संलग्न सूची के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय ताकि संवेदक को भुगतान किया जा सके।

अनु०:- यथोक्त।

5004
15/11/24
AS

विश्वासभाजन


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ
15/11/24

(See Government of India's Decision (I) below Rule-150)
Form of Utilisation Certificate up to the month of 15.11.2024

(New Maintenance Policy 2018)

PIU- BIHARSHARIF

Year-2024-2025

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in Rs. Lacs)	Amount Received (in Rs. Lacs)	Particulars
1	Construction of Rural Roads under New Maintenance Policy 2018	Itr-92 Dt-16.08.2024	6831.62977	Certified that out of Rs 6831.62977 received & balance during the years 2024-25 in favour of Ex. Engineer, R.W.D. Works Division Biharsharif, sum of Rs 6821.32419 has been utilized for the purpose of New Maintenance Policy 2018 scheme as given in the margin for which it was sanctioned and that the balance of Rs 10.30558 lacs remaining unutilized at the end of the period under 15.11.2024
	Total Rs.		6831.62977	

2 Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned
Kind of Checks exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction material have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant.
- All other codal formalities have been observed.

3 Physical Progress achieved:

- Construction of Road Works.
- Construction of CD works


15/11/24

Divisional Accounts Officer
Rwd, Works Division
Biharsharif


15/11/24
Executive Engineer
Rwd, Works Division
Biharsharif
15/11/24

Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)
Works Division :- Bihar Sharif

Sl No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Amount Allotted (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Increase in Allotment	Remarks
					Length (in km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/NAB IH24/000 4	Berua-Saksolra Path To Bishampur	10200612001	6120 04 Dec 2023	0.530	35.21600	28.98109	2.18172	MBD- 01/2024-25 27.08.2024	26-05-2025	0	2664	25	5.01	24.80535	24.80535	3.73252	
2	RM/NAB IH24/000 4	NH-82 Gorbahatar Road to Jama Masjid Tola	10200612024	6120 04 Dec 2023	0.550	22.56800	13.13257	5.78817	MBD- 01/2024-25 27.08.2024	26-05-2025	0	2642	25	5.02	0	0	10.10777	
3	RM/NAB IH24/000 4	Construction of road from Nh-82 pachetam road to pachetandih (rest proton) via pachetan	10200612025	6120 04 Dec 2023	1.700	74.64100	45.49869	17.56132	MBD- 01/2024-25 27.08.2024	26-05-2025	0	2158	25	5.00	0	0	43.87799	
4	RM/NAB IH24/000 5	LO35-L029A To Palani (VR21)	10200602045	6120 04 Dec 2023	1.000	45.30900	28.04151	10.36195	MBD- 02/2024-25 05.09.2024	04.06.2025	0	2166	25	5.01	0	0	27.63042	
TOTAL																	85.34870	

Total = 85.34870


- Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.
- Up-to-date Physical Progress has been uploaded in MIS.

Divisional Accounts Officer
 Rwd, works Division Bihar Sharif

MS
15/11/24

Executive Engineer
 Rwd, works Division Bihar Sharif
15/11/24

File : C:\Users\kkmm\OneDrive\Desktop\Downloads\10110930.Xls. Section No.: 66, Eqn : $Y = 0 \cdot X^2 + 0.816 \cdot X$
 Name of Customer : Deepak Kumar, Name of Work/ Road : Con. of road from NH-82 pachelam road to pachelamdihi

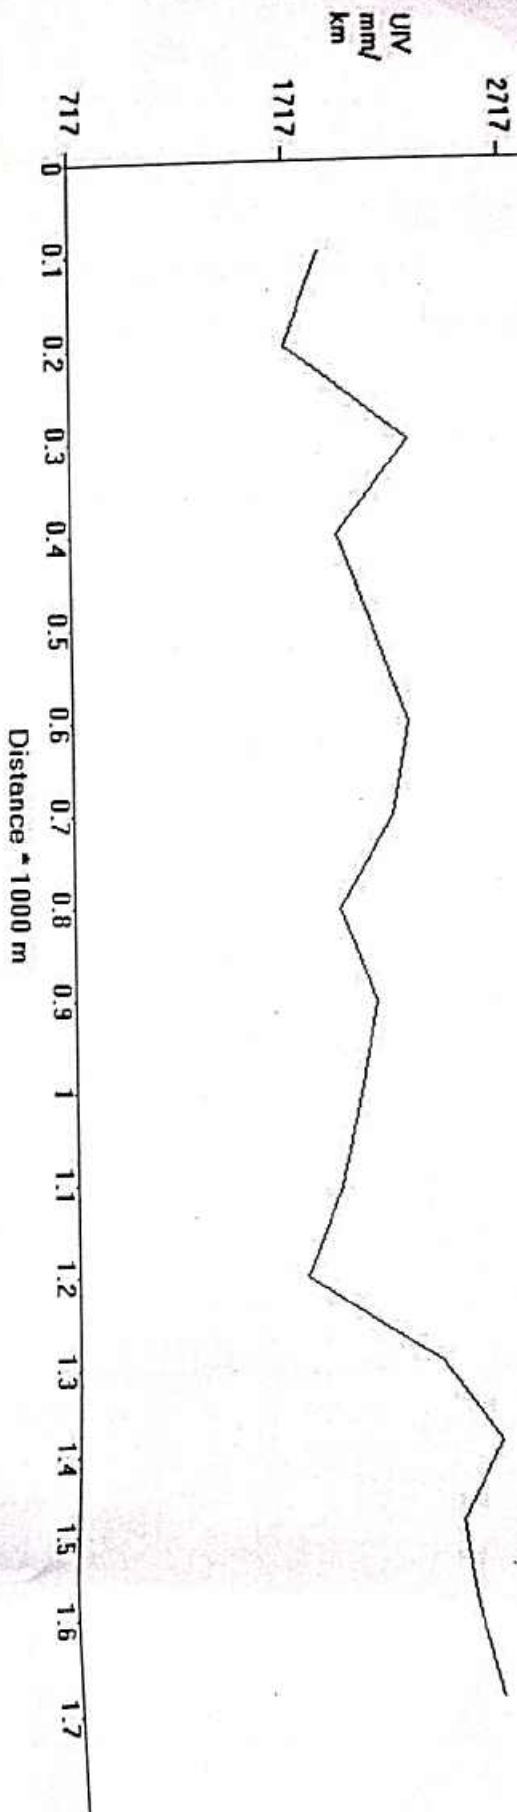

12/11/24
 Atm

12/11/24
 DE

12/11/24
 DE

Head-NEW MR
Road-Construction of road from NH-82 pachetam road to pachetandih (rest protion) via pachetam
Con-Deepak Kumar

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event	$Y = 0 * X^2 + 0.816 * X + 249$
10/11/24	8:43:16	66	0.1	200	0	2000	1880	G	25.234462	85.613836	Normal	X = 2600
10/11/24	8:44:0	66	0.1	180	10.1	1800	1717	G	25.234742	85.614038	Normal	Y = 2370
10/11/24	8:44:25	66	0.1	250	10.1	2500	2288	G	25.235105	85.614114	Normal	
10/11/24	8:44:25	66	0.1	210	20.2	2100	1962	G	25.236041	85.613923	Curve	
10/11/24	8:44:25	66	0.1	230	10.1	2300	2125	G	25.236584	85.613481	Normal	(R) RURAL ROAD
10/11/24	8:45:1	66	0.1	250	20.2	2500	2288	G	25.237302	85.613427	Normal	Good
10/11/24	8:45:1	66	0.1	240	20.2	2400	2207	G	25.238531	85.613521	Curve	<4000
10/11/24	8:45:1	66	0.1	210	20.2	2100	1962	G	25.240031	85.623581	Curve	Average
10/11/24	8:45:36	66	0.1	230	20.2	2300	2125	G	25.240546	85.613771	Normal	
10/11/24	8:46:0	66	0.1	220	20.2	2200	2044	G	25.241012	85.613848	Normal	
10/11/24	8:46:11	66	0.1	210	20.2	2100	1962	G	25.242231	85.614142	Normal	
10/11/24	8:46:47	66	0.1	190	10.1	1900	1799	G	25.243029	85.614317	Normal	
10/11/24	8:48:0	66	0.1	270	10.1	2700	2452	G	25.244314	85.614407	Normal	
10/11/24	8:49:43	66	0.1	310	10.1	3100	2778	G	25.244177	85.615546	Normal	
10/11/24	8:51:0	66	0.1	290	10.1	2900	2615	G	25.244177	85.615546	Normal	
10/11/24	8:51:29	66	0.1	300	10.1	3000	2696	G	25.243789	85.617078	Speed Breaker	
10/11/24	8:52:4	66	0.1	310	10.1	3100	2778	G	25.243204	85.616952	Normal	
						Total-	37678					
						IRI Value-	2158					

12/11/24
 12/11/24

12/11/24

13/11/24

1.
Name of work -
Situation of work -
Agency by which work is executed -
Date of measurement -
No. and date of agreement.

(These four lines should be repeated at the commencement of the measurements relating to each work).

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
1st original Bill					
Name of work:-	Construction of Road				
	From NH-82 Pachetam Road To				
	Pachetandih (Rest Portion) via				
	Pachetan				
Agency:-	Deepak Kumar				
Agreement No.:-	MBD 01/2024-25				
Date of commencement:-	27-08-2024				
Date of completion:-	05-11-2024				

MEASUREMENT				
1) Clearing and Grubbing Road land				
---	do	---	do	---
				e/i
	2	1435	1.00	= 2870m ²
	1	25	1.00	= 25m ²
	2	240	1.00	= 480m ²
				3375m ²
	In HA, 3375/10000 = 0.3375HA			
2) Providing laying, Spreading & compacting GSB-II (Patchwork)				
---	do	---	do	---
				e/i
	5	1.8	0.4	0.175 = 0.63m ³
	9	2.0	0.5	0.150 = 1.35m ³
				1.98m ³

Continued

Continuation

⑮ Providing and fixing
'Logo' of maintenance board
- - - do - - - do - - - c/i

$$Q + y = 100 \text{ Noz}$$
$$= 1.00 \text{ N}$$

14/1/24
AF

ABSTRACT OF COST

D) Clearing and grubbing Road land

-	- do	-	- do	-	- ei ^v
---	------	---	------	---	-------------------

0.3375 HA VT MB P — (01)

@R876926-08/HA	R325962/-
----------------	-----------

② Providing laying, spreadings

Compacting	GISB-II
------------	---------

- - - do - - - do - - e/i

77.81m³ VTmB P — 03

@ Rs 1427.12/m³ — Rs 111044/-

Continuation

Rs 137006/-

Sch. XLV-Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
BF					Rs 137006/-
③ Providing, laying, spreading and compacting WBM Gr-II					
--- do ---				e/i	
53.35m ³ VTMB P				⑥	
@ 3032.67/m ³					Rs 161793/-
④ Providing, laying, spreading and compacting WBM Gr-III					
--- do ---				e/i	
82.82m ³ VTMB P				⑧	
@ 3061.86/m ³					Rs 253583/-
⑤ Providing and applying Primer Coat with Bitumen Emulsion (SSS)					
--- do ---				e/i	
1104.27m ² VTMB P				⑨	
@ 57.15/m ²					Rs 63109/-
⑥ Providing and applying Tack Coat with Bitumen Emulsion (RS)					
--- do ---				e/p	
6429.73m ² VTMB P				⑩	
@ Rs 19.60/m ²					Rs 126023/-
					Rs 741514/-

Continuation

Sch. XLV-Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
	BF				Rs 741514/-
⑦ Providing and laying semi-Dense Bituminous concrete					
---	do	---	do	---	e/i
160.75 m ³	VTMB P				⑩
@ 13020.18/m ³					Rs 2092994/-
					Rs 2099527/-
⑧ Construction of subgrade and Earthen shoulder					
---	do	---	do	---	e/i
796.79 m ³	VTMB P				⑪
@ 26451/m ³					Rs 263661/-
⑨ Reinforced Cement Concrete					
M15 KM stone					
---	do	---	do	---	e/i
3.00 NOS	VTMB P				⑪
@ 2765.06/NOS					Rs 8295/-
⑩ Reinforced Cement concrete					
M15 200 mm stone					
---	do	---	do	---	e/i
7.00 NOS	VTMB P				⑪
@ 796.38/NOS					Rs 5575/-
					Rs 3112039/-

Continuation

Sch. XLV-Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
	BF				Rs 3112039/-
① Providing and fixing of Retro-Reflectorised 600mm Equilateral triangle					
--- do --- do --- e/i					
13.00 Nos VTMB P				⑫	
@ 4411.34					Rs 57347/-
② Providing and fixing of Retro-Reflectorised 600mm Circular					
--- do --- do --- e/i					
2.00 Nos VTMB P				⑫	
@ 4253.46					Rs 8507/-
③ Providing and fixing of Retro-Reflectorised 600mm x 450mm rectangular					
--- do --- do --- e/i					
3.00 Nos VTMB P				⑫	
@ 4109.13					Rs 12327/-
④ Providing and laying of hot applied Thermoplastic Compound Road Marking					
--- do --- do --- e/i					
340 m ² VTMB P				⑬	
Continuation					Rs 3190220/-

Sch. XLV-Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
B.F.					Rs 3190220/-
@ 886.5/m ²					Rs 301410/-
(15) Planting of trees by the road side					
do do do					
800 NOS VTMB P (13)					
@ 1305.10					Rs 104408/-
(6) Providing and fixing 'Logo' of Project					
do do do					
2.00 NOS VTMB P (13)					
@ 11526.67					Rs 23053/-
(17) Providing and fixing citizen Information Board					
do do do					
2.00 NOS VTMB P (13)					
@ 11526.67					Rs 23053/-
(8) Providing and fixing 'Logo' of maintenance board					
do do do					
1.00 NOS VTMB P (14)					
@ 11526.67					Rs 11526/-
Continuation					Rs 3653670/-

24/11/27
A/E

- ① $E/w = 996.79 \text{ m}^3$
- ② $\text{GSB-II (Stone metal)} = 56.02 \text{ m}^3$
- ③ $\text{Local sand} = 37.35 \text{ m}^3$
- ④ $\text{WBM Gr-II (Metal)} = 64.55 \text{ m}^3$
- ⑤ $\text{Screening} = 14.70 \text{ m}^3$
- ⑥ $\text{WBM Gr-III (metal)} = 100.21 \text{ m}^3$
- ⑦ $\text{Screening} = 19.87 \text{ m}^3$
- ⑧ $\text{Emulsion (SSI)} = 0.939 \text{ MT}$
- ⑨ $\text{Emulsion (RSI)} = 1.929 \text{ MT}$
- ⑩ $\text{SDBC} = 17.683 \text{ MT}$
- ⑪ $\text{Waste Plastic (7\%)} = 1.237 \text{ MT}$
- ⑫ $\text{Stone chips} = 229.87 \text{ m}^3$

Dinar
14/11/22
AE
