

**कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल छपरा 2**

पत्रांक 1502अनु०

छपरा/दिनांक 12/11/2024

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, छपरा-2

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
बिहार ग्रामीण पथ विकास अभिकरण (ब्राड),
बिहार, पटना।

विषय:- नई अनुरक्षण नीति 2018 (Head - 3054) योजना मद में आवंटन उपलब्ध कराने के संबंध में।


महाशय,

उपर्युक्त विषय के संबंध में कहना है कि नई अनुरक्षण नीति 2018 (Head - 3054) योजना अंतर्गत 06 (छः) पथों में राशि का अधियाचना विहित प्रपत्र में तैयार कर मापपुस्त की छायाप्रति एवं Bump Indicator का Reading संलग्न कर आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अतः अनुरोध है कि पत्र के साथ संलग्न अधियाचना प्रपत्र में अंकित राशि उपलब्ध कराने की कृपा की जाय ताकि संवेदक के विपत्र का भुगतान किया जा सके।

अनु०:- यथोक्त।

विश्वासभाजन



कार्यपालक अभियंता,

ग्रामीण कार्य विभाग,

कार्य प्रमंडल, छपरा-2



Name of Division :- Rural Works Department, Works Division, Chapra-2

Requisition Format for Scheme Head :- MR (3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of RI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition work done against (in Lakh)	Remarks
					Length (in km)	Amount (in Lakh)	Initial Rectification with surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/23-24 Chapra-2/07	Chetan Chapra Arwa PMGSY Road to Kaval Chapra	31306312006	Lt. No. 6115 Dated 04.12.23	1.210	54.56000	37.07260	10.74850	02 MBD/2024-25	25.04.25	BT Complete	2834.000	25.00	5%	36.50000	36.48650	0.55772	
2	MR-N/23-24 Chapra-2/07	Bashi Bhakhura Bhatti PMGSY Upto Rajua More to Kamta New Tola Dhobwal Bazar.	31306312018	Lt. No. 6115 Dated 04.12.23	1.400	53.82000	32.31335	12.41109	02 MBD/2024-25	25.04.25	BT Complete	2852.200	25.00	5%	31.50000	31.50000	0.81219	
3	MR-N/23-24 Chapra-2/07	Ekma Mashtakhi Road to Upto Sisi Harijan Tola.	31306313029	Lt. No. 6115 Dated 04.12.23	0.850	56.93200	43.38330	6.63685	02 MBD/2024-25	25.04.25	BT Complete	2959.110	25.00	5%	42.50000	42.50000	0.88330	
4	MR-N/23-24 Chapra-2/07	Chetan Chapra to Harpur	31306302026	Lt. No. 6115 Dated 04.12.23	1.000	51.97300	37.72321	7.87375	02 MBD/2024-25 & Date 26.07.2024	25.04.25	BT Complete	2734.000	25.00	5%	36.00000	36.00000	1.72286	
5	MR-N/23-24 Chapra-2/11	PWD (Sikariya Paganbarpur) Road to Upto Lahadpur Chamar Tola.	31306313017	Lt. No. 6115 Dated 04.12.23	1.050	66.45000	40.41750	6.24350	04 MBD/2024-25 & Date 08.06.2024	05.05.25	BT Complete	2648.27	25.00	5%	39.00000	39.00000	1.41750	
6	MR-N/23-24 Chapra-2/11	Mirzapur Bhawal Pokhra to Mirzapur Khns.	31306312014	Lt. No. 6115 Dated 04.12.23	1.000	62.49300	38.40711	5.76015	04 MBD/2024-25 & Date 08.06.2024	05.05.25	BT Complete	2645.60	25.00	5%	37.00000	37.00000	1.40711	

Divisional Account Officer
Rural Works Department,
Works Division, Chapra-2

Executive Engineer
Rural Works Department,
Works Division, Chapra-2

FORM GER 19-A

(See Government of India's Decision (I) below Rule-150)

Form of Utilization Certificate up to the Month of November 2024

PIU:- E.E.,R.W.D. Works Division , Chapra- 2

Sl. No	Name of Scheme	Sanction No. & Date with Amount (in Lac Rs.)	Amount Received (in lac Rs.)	Particulars
1	2	3	4	5
1	Construction of Rural Roads under New Maintenance Policy 2018	Letter No. 118 (WE) Dt. 06.11.2024	Allotment 10194.94324 Lacs	Certified that out of Rs. 10194.94324 Lacs received during the years 2019-20 to 2024-25 and in favour of EE., R.W.D Works Division 2, Chapra a sum of Rs. 10075.15579 Lacs has been utilised And Rs. 30.99714 Surrender for the purpose of New Maintenance Policy 2018 Scheme as given in the margin for which it was sanctioned and that the balance of Rs. 88.79031 lacs remaining unutilised at the end of the period under report.

Adinda
12/11/24
Divisional Account Officer
R.W.D., Works Division, Chapra-2

Pratibha
12/11/24
Executive Engineer
R.W.D, Works Division, Chapra-2

MR-3054

MBNO-3646

Schedule XLV-Form No. 134

Mirzapur Bhawal Pukhra to

DIVISION

Mirzapur Khaz.

SUB-DIVISION

Palak Infote / Ry. 4. 4d.

Measurement Book

"Lahlabur"

2nd And final bill

16

Sch. XLV-Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of work - Mirzapur Bahawal					
Pokhara to Mirzapur Khas.					
Agency - Dalak Infratel Pvt. Ltd.					
Agreement no - 04/MBD/24-25					
Date of start - 06-08-2024					
Date of completion - 05-05-2025					

Date of measurement:					
① Printing new letter and figures of any shade with — E/t.					
= 176 Per Cm					
② Plastering with cement mortar (24) on brick work in sub-structure — E/t					
4.00 x 6.00 x 0.60				= 14.400 m ²	
2.00 x 6.00 x 0.40				= 4.800 m ²	
4.00 x 0.40 x 0.60				= 0.960 m ²	
				= 20.160 m ²	

Continuation

ABSTRACT of COST.

18

Sch. XLV-Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
① Printing new letter and figure of any shade — e/t.					
Qty. vide TMB P. (16)					
i. no. ① 126 Per cm					
@ Rs 0.77 Per cm per letter = 136 = 00					
② Plastering with cement mortar (1:4) on brick work in sub grade structure — e/t.					
Qty vide TMB P. (16)					
i. no. ② 20.16 m ²					
@ Rs 225 = 19/m ²					Rs 4540 = 00
③ Painting two coats including primer coat — e/t.					
Qty vide TMB P. (17)					
i. no. ③ 20.16 m ²					
@ Rs 137 = 55/m ²					Rs 2773 = 00
④ Clearing & grubbing road land (by manual means) —					
Qty vide TMB P. (9)					
i. no. ④ = 0.20 Ha					
@ Rs 76926 = 08/Ha					Rs 15385 = 00
					40 Rs 22834 = 00

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
6/2 Const. of subgrade & earthen shoulder — Qty wide TMB P-9 i.no ② = 450.00 m ³ @ Rs 263=24/m ³ Rs 118458=00					
6/3 Const. of granular sub base by providing — Qty wide TMB P-9 i.no ③ = 19.93 m ³ @ Rs 2833=65/m ³ Rs 56475=00					
7/4 P/L spreading & compacting — Qty wide TMB P-9 i.no ④ = 21.42 m ³ @ Rs 6045=77/m ³ Rs 129802=00					
8/5 P/L spreading & compacting stone aggregate — WBM gr ³ Qty wide TMB P-9 i.no ⑤ = 34.92 m ³ @ Rs 5654=86/m ³ Rs 297461=00 C/o Pr 525020=00					

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
9/6 P/A Primer coat with bitumen emulsion (SS-1) Qty wide TMB P. (10) i. no. (6) 2465.60 m ² @ Rs 52.26/m ² Rs 26660 = 00					
10/7 P/A tack coat with bitumen emulsion (RS-1)- Qty wide TMB P. (10) i. no. (7) 1875.00 m ² @ Rs 16.44/m ² Rs 30825 = 00					
11/8 p/l semi dense bituminous concrete — Qty wide TMB P. (10) i. no. (8) 46.88 m ³ @ Rs 15162 = 25/m ³ Rs 710805 = 00					
12/9 Const of dry lean cement concrete. — Qty wide TMB P. (10) i. no. (9) 28.34 m ³ @ Rs 4965 = 22/m ³ Rs 140714 = 00					
13/10 const. of unreinforced plain cement panel — Qty wide TMB P. (10)					

Continuation

C/o R 1424024 = 00

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
i. no. (10) = 234.88 m ³					
@ Rs 9655 = 90/m ³					Rs 226350 = 00
(14/11) Km stone					
Qty vide TMB P-11					
i. no. (11) = 1 nos					
@ Rs 3219 = 82/nos					Rs 3220 = 00
(15/12) 200mm stone					
Qty vide TMB P-11					
i. no. (12) = 5 nos.					
@ Rs 876 = 97/nos					Rs 4385 = 00
(16/13) Refrerectioned					
dinn and place indistinct					
Qty vide TMB P-11					
i. no. (13) = 2.92 m ²					
@ Rs 15240 = 99/m ²					Rs 29263 = 00
(17/16) 600mm x 450mm					
rectangular					
Qty vide TMB P-11					
i. no. (16) = 4 nos					
@ Rs. 4318 = 64/nos					Rs 17275 = 00
(18/17) R.C.C m.s grade					
boundary pillars					
Qty vide TMB P-11					
i. no. (17) = 20 nos					
@ Rs. 824 = 88/nos					Rs 16498 = 00

Continuation

C/o M-2767825 = 00

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(19/14) 600 mm equilateral and triangle —					
Qty. vide TMB P-(12)					
i.no. (14) = 6 nos					
@ Rs 4620 = 86/nos					Rs 27725=00
(20/15) 600 mm circular —					
Qty. vide TMB P-(12)					
i.no. (15) = 4 nos					
@ Rs 4463 = ¹⁷ 17/nos					Rs 17852=00
(21/19) Planting of trees by the road side —					
Qty vide TMB P-(12)					
i.no. (19) = 50 nos					
@ Rs 1305 = 10/nos					Rs 65255=00
(22/20) p/l of hot applied thermoplastic compound —					
Qty. vide TMB P-(12)					
i.no. (20) = 200.00 m ²					
@ Rs 886 = 50/m ²					Rs 177300=00
(23/21) P/F of typical mmgsy informatory sign —					
Qty. vide TMB P-(12)					
i.no. (21) = 4 nos					
@ Rs 11833 = 20/nos					Rs 47332=00


Continuation

C/o Rs 4103289=00

C/o limit Rs 4103288=00

[illegible]

File : E:\chakra-2\sept 24\bump\palak infratel_guddu singh.xls, Section No. : 15, Egn :
Name of Customer : PALAK INFRA TEL PVT. LTD., Name of Work/ Road : MIRZAPUR BHAWAL POKHRA TO

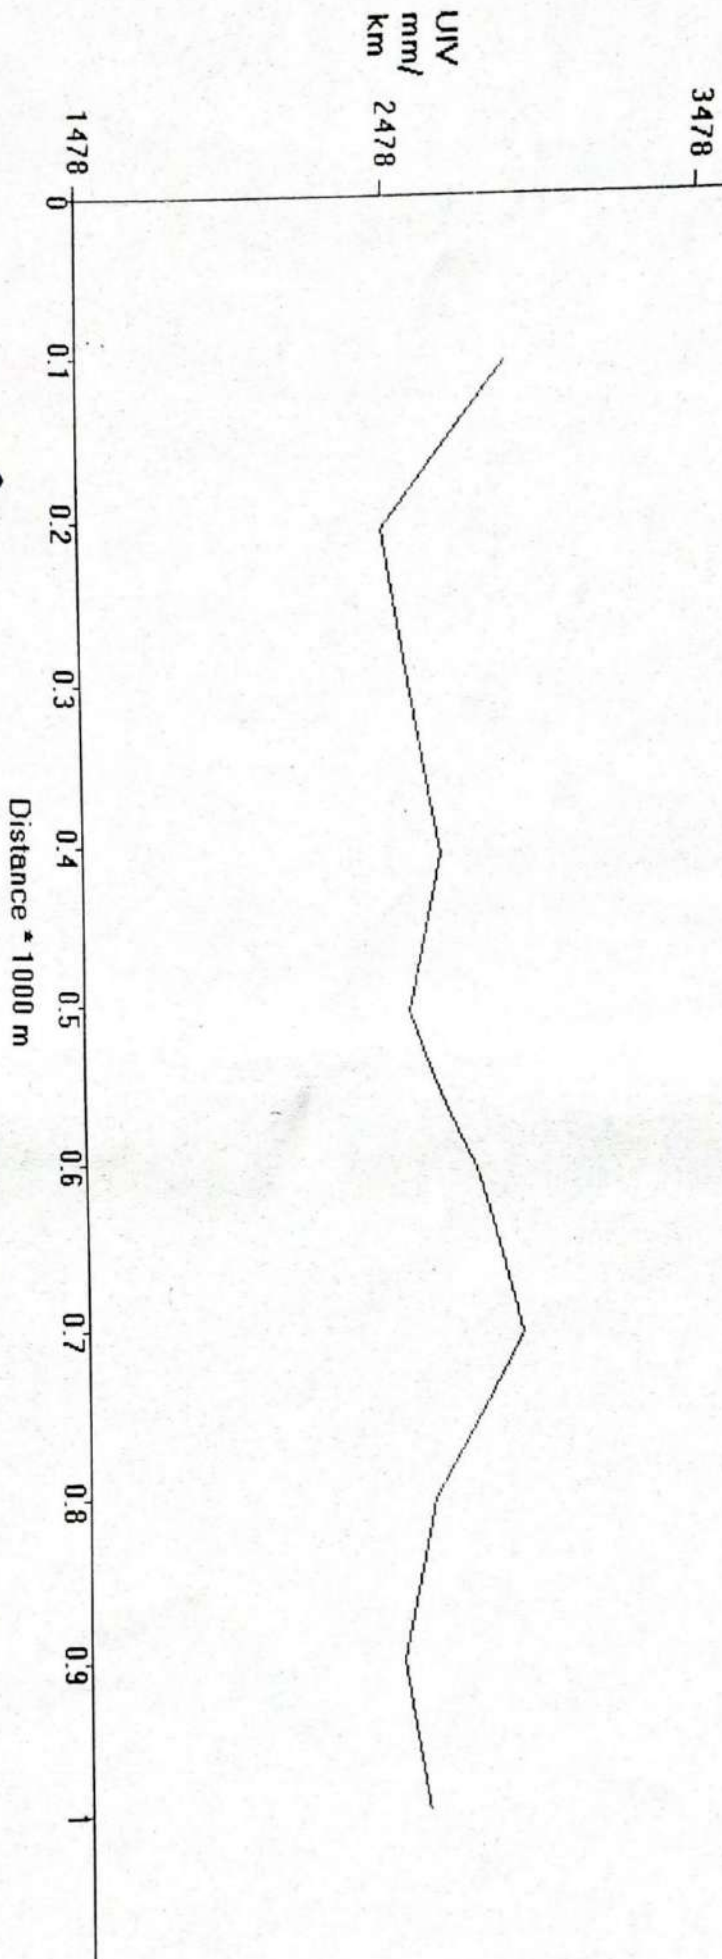

Jagvir
01.10.24
S.E


11/10/24
S.E


01/10/24
S.E

Cont. Name:- Palak Infratel Private Limited
Road Name:-Mirzapur Bhawal Pokhara To Mirzapur Khas

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event	X = 0	Y = 510	(R) RURAL ROAD	Good <4000	Average 4001-5000	Poor >5001
28/9/24	7:20:24	15	0.1	240	10.1	2400	2872 G		26.025223	84.644927	Normal						
28/9/24	7:21:0	15	0.1	200	10.1	2000	2478 G		26.025351	84.646411	Normal						
28/9/24	7:21:0	15	0.1	210	10.1	2100	2577 G		26.025639	84.647068	Normal						
28/9/24	7:21:35	15	0.1	220	10.1	2200	2675 G		26.025822	84.648174	Normal						
28/9/24	7:22:0	15	0.1	210	10.1	2100	2577 G		26.025892	84.648139	Normal						
28/9/24	7:22:10	15	0.1	230	10.1	2300	2773 G		26.026316	84.649172	Normal						
28/9/24	7:23:0	15	0.1	240	10.1	2400	2872 G		26.026745	84.649824	Normal						
28/9/24	7:23:21	15	0.1	210	10.1	2100	2577 G		26.027046	84.650191	Normal						
28/9/24	7:24:0	15	0.1	180	10.1	2000	2478 G		26.027375	84.651214	Normal						
28/9/24	7:25:29	15	0.1	210	10.1	2100	2577 G		26.028015	84.651519	Normal						
AVERAGE								2645.60									

Jaquib
01.10.24
11/10/24
AE
Mirza
01.10.24
EC
