

कार्यपालक अभियंता, का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल बिहारशरीफ

पत्रांक...1116 3054/ बिहारशरीफ, दिनांक 23-09-2024

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ ।

सेवा में,

नोडल पदाधिकारी 3054
ग्रामीण कार्य विभाग, बिहार, पटना

विषय:- नई अनुरक्षण नीति-2018 अन्तर्गत आवंटन उपलब्ध करने के संबंध में।
महाशय,

उपर्युक्त विषयक से संबंधित नई अनुरक्षण नीति-2018 अन्तर्गत इस प्रमंडल द्वारा कराये जा रहे पथों के निर्माण कार्य के लिये आवंटन उपलब्ध करने हेतु अध्याचणा पत्र समर्पित की जा रही है।

अतः अनुरोध है कि पथ में कराये गये कार्यों के विरुद्ध भुगतान हेतु संलग्न सूची के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय ताकि संवेदक को भुगतान किया जा सके।

अनु०:- यथोक्त।

विश्वासभाजन


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बिहारशरीफ
23/9/24

(See Government of India's Decision (1) below Rule-150)
Form of Utilisation Certificate up to the month of 23.09.2024

(New Maintenance Policy 2018)

PIU- BIHARSHARIF

Year-2024-2025


Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in Rs. Lacs)	Amount Received (in Rs. Lacs)	Particulars
1	Construction of Rural Roads under New Maintenance Policy 2018	Itr-92 Dt-16.08.2024	6831.62977	Certified that out of Rs 6831.62977 received & balance during the years 2024-25 in favour of Ex. Engineer, R.W.D. Works Division Biharsharif, sum of Rs 6821.32419 has been utilized for the purpose of New Maintenance Policy 2018 scheme as given in the margin for which it was sanctioned and that the balance of Rs 10.30558 lacs remaining unutilized at the end of the period under 23.09.2024
	Total Rs.		6831.62977	

2 Certified that I have satisfied myself that the conditions on which the grants-in- aid was sanctioned
Kind of Checks exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction material have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant .
- All other codal formalities have been observed.

3 Physical Progress achieved:

- Construction of Road Works.
- Construction of CD works


23/9/24
Divisional Accounts Officer
Rwd, Works Division
Biharsharif


23/9/24
Executive Engineer
Rwd, Works Division
Biharsharif
23/9/24

aquisition Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)
Name of Works Division :-Bihar Sharif

Sl No	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	up-to-date expenditure as per MIS (in Lakh)	Increase in Abatement	Remarks
					Length (in km)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
		Sare- Naawan Path, Chakdin More To Village Chakdin	10200612008	6120 04 Dec 2023	0.620	36.90200	29.35869	3.08289	MBD- 01/2024-25 8/27/2024	26-05-2025	0	2316	25	5.01	0	0	22.64440	
2	4	RM/N/A/B IH24/000 NH 82, Jirain- Onda Path To Molna Bigha	10200612006	6120 04 Dec 2023	1.070	78.091000	66.91105	4.63164	MBD- 01/2024-25 8/27/2024	26-05-2025	0	2517	25	5.2	0	0	58.30654	
3	3	RM/N/A/B IH23/001 chikpur path se Dhogyakol more se kabhauti farida lak sadak nirman kanya	10200604108	1447 28.02.24	1.00	69.239000	51.92583	12.41784	MBD- 05/2023-24 10.7.23	09.04.2024	0	2142	25	5.01	0	0	45.13543	
TOTAL																	126.08637	

Total = 126.08637


- 1 Signed Hard Copy and Soft Copy (in Excel) of recorded IRI is enclosed.
- 2 Up-to-date Physical Progress has been uploaded in MIS.

Divisional Accounts Officer
 Rwd,works Division Biharsharif

[Signature]
 23/9/24

Executive Engineer
 Rwd,works Division Biharsharif
[Signature]
 23/9/24

File : C:\Users\kkm1\OneDrive\Downloads\16090809.Xls, Section No. : 77, Eqn : $Y = 0 * X^2 + 0.816 * X$
 Name of Customer : Deepak Kumar, Name of Work/ Road : NH 82, Jirain-Onda Path To Molina Bigha, Lab Job

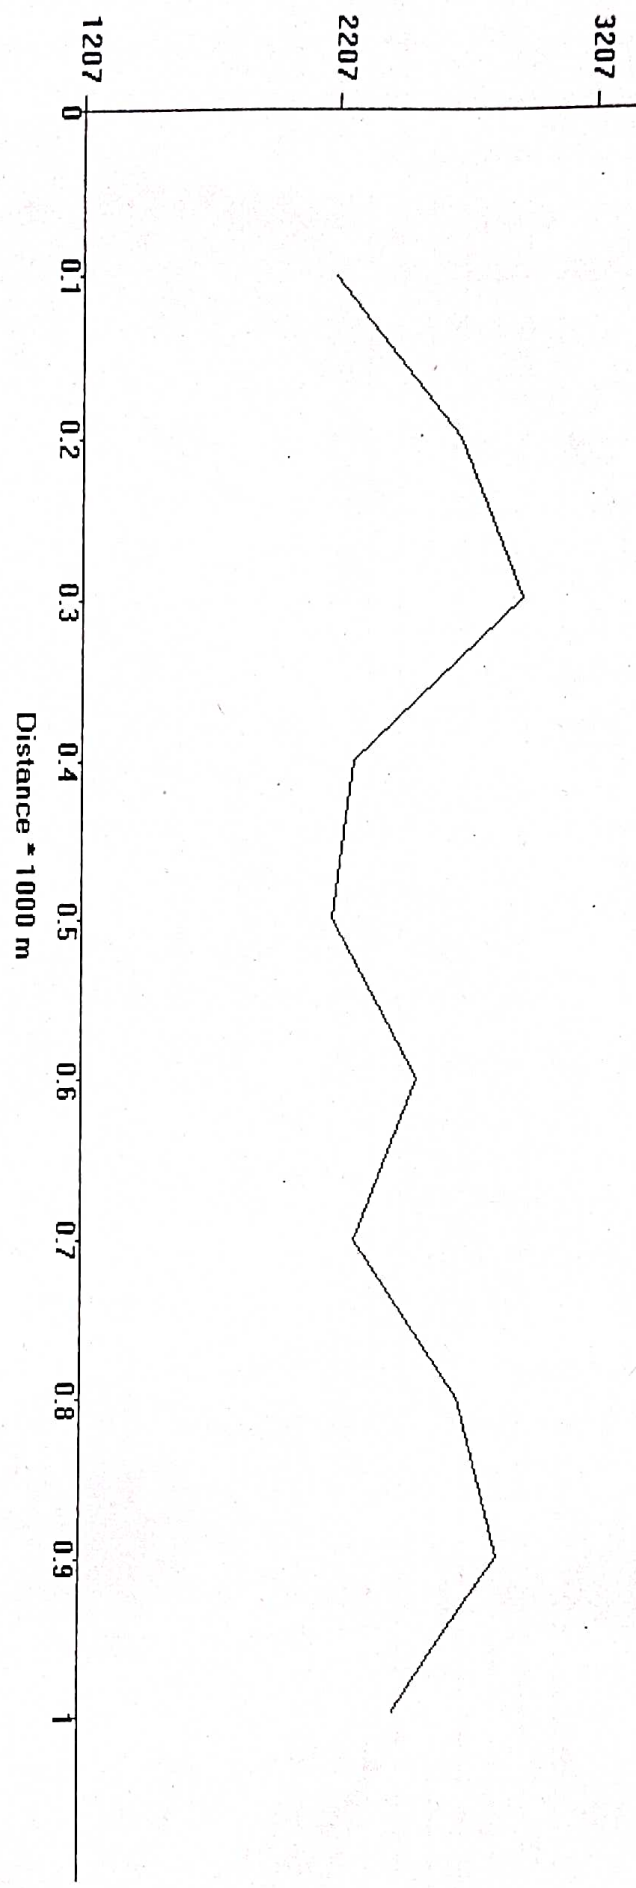

~~Signature~~
 12/6/23
 11/11/23
 11/11/23

~~Signature~~
 12/6/23
 11/11/23

CS
 12/6/23
 11/11/23

Head-NEW MR
Road-NH 82, Jirain-Onda Path To Molina Bigha
Contractor-Deepak Kumar

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY	Latitude	Longitude	Event	$Y = 0 * X^2 + 0.816 * X + 249$		
16/9/24	1:34:0	77	0.1	240	0	2400	2207	ROAD	25.235464	85.652568	Normal	X = 2700		
16/9/24	1:34:35	77	0.1	300	10.1	3000	2696	G	25.234176	85.653249	Curve	Y = 2452		
16/9/24	1:34:35	77	0.1	330	10.1	3300	2941	G	25.233173	85.652388	Normal			
16/9/24	1:35:10	77	0.1	250	10.1	2500	2288	G	25.23314	85.651537	Curve			
16/9/24	1:35:10	77	0.1	240	20.2	2400	2207	G	25.232845	85.650635	Normal	[R] RURAL ROAD		
16/9/24	1:35:46	77	0.1	280	10.1	2800	2533	G	25.23332	85.649649	Curve	Good	Average	Poor
16/9/24	1:36:0	77	0.1	250	10.1	2500	2288	G	25.233311	85.648417	Normal	<4000	4001-5000	>5001
16/9/24	1:36:21	77	0.1	300	20.2	3000	2696	G	25.233449	85.648109	Normal			
16/9/24	1:36:21	77	0.1	320	10.1	3200	2860	G	25.233967	85.648214	Curve			
16/9/24	1:37:0	77	0.1	270	10.1	2700	2452	G	25.234077	85.648081	Normal			
						Total-	25168							
						IRI Value-	2517							

Signature
16/9/24
1:37:0

Signature
17/9/24
#4

Signature
17/9/24

Name of Work—
 Situation of Work—
 Agency by which work is executed—
 Date of Measurement—
 No. and date of agreement

(These four lines should be repeated at the commencement of the measurement relating to each work)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
1st	On	A/c	bill		
Name of Work:-	NH 82 Jirain Onda				
Path, Chakdin	More To Molna Bishe				
Agency :-	Dec Pak Kumar				
Agreement No. :-	MBD - 01/2024-25				
Date of Commencement :-	27-08-2024				
Date of Completion :-	26-05-2025				

MEASUREMENT

① Clearing and Grubbing Road Land					
----- do ----- do -----					
	2	10	30.00	1.00	= 600m ²
	2	10	30.00	1.00	= 600m ²
	2	10	30.00	1.00	= 600m ²
	2	1	27.00	1.00	= 54 m ²
	Total Quantity = 1854 m ²				
	In HA, 1854/10000 = 0.1854 HA				
② Dismantling of Existing RCC					
----- do ----- do -----					
	1	8	3.75	0.18	= 5.40 m ³
	1	5	3.75	0.18	= 3.37 m ³
	1	12	3.75	0.18	= 8.10 m ³
	16.87 m ³				

M. Jyoti
 21/09/24
 T.S

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
ABSTRACT OF COST					
① Clearing and Grubbing of Road land					
----- do -----					epi
0.1854 HA VTMB P — 01					
@ Rs 76926.08/HA Rs = 14262.7/-					
② Dismantling of existing P.C.C					
----- do -----					epi
1139.57m ² VTMB P — 02					
@ Rs 68718 /m ² Rs = 95810.00/-					
③ P/v laying and compacting of WBM-III					
----- do -----					epi
51.46 m ³ VTMB P — 03					
@ 302494 /m ³ Rs 155663/-					
④ Construction of Paved concrete Pavement (M ₃₀)					
----- do -----					epi
452.44m ³ VTMB P — 05					
@ 8788.57/m ³ Rs 3976301.00/-					
⑤ Construction of Subgrade & Earthen Shoulder					
----- do -----					epi
117.18m ³ VTMB P — 06					
@ 264.51/m ³ Rs 30995.00/-					
					Rs 4273131.00/-

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
B.F.					Rs 4273131.00
⑥ P/v fixing R.C.C Mis km stone					
do do do					e/i
VTMB					P-06
1.00 NO @ Rs 2755.57					Rs 2755.57/-
⑦ P/v fixing R.C.C Mis 200m stone					
do do do					e/i
VTMB					P-06
3.00 NO @ Rs 795.40					Rs 2386.00/-
⑧ P/v fixing Retro-Reflectorised 600mm Equilateral triangle					
do do do					e/i
VTMB					P-06
5.00 NO @ 4408.78					Rs 22044/-
⑨ P/v fixing RetroReflectorised 600mm Circular					
do do do					e/i
VTMB					P-06
1.00 NO @ 4251.09					Rs 4251.09/-
⑩ P/v Road Marking with hot applied Thermoplastic compound					
do do do					e/i
185.4m ² VTMB					P-07
@ 1005.95/m ²					Rs 186503/-
					Rs 4491075.00/-

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
	BF				Rs 4491075/-
(1) construction of CD work (Irrigation conduit)					300mm
--- do --- do ---					e/i
(1 No.) 7.50m VTMB			P	07	
@ 7577.70					Rs 757770/-
(12) P/V Fixing Logo maintenance work					
--- do --- do ---					e/i
1 No. VTMB			P	07	
@ 11521.53					Rs 11521.53/-
(13) P/V Fixing of Citizen Information Board					
--- do --- do ---					e/i
1 No. VTMB			P	07	
@ 11521.53					Rs 11521.53/-
					Rs 452169500/-
Add Labour cost @ 1%					Rs 45217.00/-
Add GST @ 18%					Rs 813905.00/-
Add Selgnorage @ 10%					Rs 452170.00/-
					Rs 5832987.00/-
Less below 0.04% as per agm.					Rs 2333.00/-
					Rs 5830654.00/-
