

कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, बारसोई (कटिहार)

पत्रांक 746 अ/४०

बारसोई, दिनांक 15/04/2025

प्रेषक:-

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बारसोई, कटिहार

सेवा में,

अपर मुख्य कार्यपालक पदाधिकार-सह-सचिव,
ग्रामीण कार्य विभाग, ब्राडा बिहार, पटना।

विषय : शीर्ष 3054 अंतर्गत बिहार ग्रामीण पथ अनुरक्षण नीति-2018 के तहत स्वीकृत कार्यों का आवंटन उपलब्ध कराने के सम्बन्ध में।

प्रसंग:- भवदीय का पत्रांक 4843 दिनांक 06.12.2021

महाशय,

उपर्युक्त विषयक एवं प्रासंगिक पत्र के आलोक में ग्रामीण कार्य विभाग, कार्य प्रमंडल, बारसोई, कटिहार के अधीन शीर्ष 3054 अंतर्गत बिहार ग्रामीण पथ अनुरक्षण नीति-2018 के तहत स्वीकृत कार्यों में निधि उपलब्ध कराने हेतु अध्याचना विहित प्रपत्र में तैयार कर आपके अग्रेतर कार्रवाई हेतु समर्पित किया जाता है।

अतः आप से अनुरोध है कि आवंटन शीघ्र उपलब्ध कराने की कृपा की जाय।

अनु०- यथोक्त।

विश्वास भाजन

६०४

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, बारसोई, कटिहार

ज्ञापांक 746 दिनांक 15/04/2025

प्रतिलिपि - नोडल पदाधिकारी, 3054 MR, ग्रामीण कार्य विभाग, बिहार पटना को सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,

कार्य प्रमंडल, बारसोई, कटिहार
15.4.25

FROM GFR 19 - A(See Government of India's Decision (I) Below Rule - 150)
Form of Utilisation Certificate

Sl. No.	Name of Scheme	Sanctioned No Date with Amount (in Lakh Rs.)	Amount Received (in Lakh Rs.)	Particulars
1	2	4	5	6
1	MR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Year-2021-22, 2022-23, 2023-24, 2024-25)	MR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Year- 2021-22, 2022-23 & 2023-24) Lt. No. 32 Dt- 28.05.2021 Lt. No. 40 Dt- 14.06.2021 Lt. No. 05 Dt- 25.01.2022 Lt. No. 10 Dt- 21.02.2022 Lt. No. 49 Dt- 27.04.2022 Lt. No. 22 Dt- 08.08.2022 Lt. No. 12 Dt- 03.02.2023 Lt. No. 35 Dt- 14.03.2023 Lt. No. 42 Dt- 20.03.2023 Lt. No. 72 Dt- 10.05.2023 Lt. No. 78 Dt- 24.05.2023 Lt. No. 84 Dt- 08.06.2023 Lt. No. 96 Dt- 07.07.2023 Lt. No. 106 Dt- 02.08.2023 Lt. No. 113 Dt- 14.08.2023 Lt. No. 136 Dt- 10.10.2023 Lt. No. 140 Dt- 16.10.2023 Lt. No. 144 Dt- 20.10.2023 Lt. No. 152 Dt- 16.11.2023 Lt. No. 14 Dt- 06.02.2024 Lt. No. 31 Dt- 09.03.2024 Lt. No. 37 Dt- 15.03.2024 Lt. No. 40 Dt- 18.03.2024 Lt. No. 47 Dt- 25.03.2024 Lt. No. 72 Dt- 29.05.2024 Lt. No. 74 Dt- 03.06.2024 Lt. No. 29 Dt- 30.03.2025	6205.39473	Certified that out of Rs.- 6205.39473 Lakh of grants in aid sanctioned during the Years 2021-22, 2022-23, 2023-24 & 2024-25 In Favour of Executive Engineer, Rural Works Department, Works Division, Barsoi sum of Rs.- 6050.57249 Lakh has been utilized for the purpose of MR(3054) under Bihar Rural Road Maintenance Policy- 2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs.- 154.82224 Lakh remain balance vide departmental Letter No. 29 dt. 30.03.2025.
	Total -		6205.39473	

- 2 Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose fo

Kind of Checks Exercised :-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test checks conducted by the Assistant Engineer/ Executive Engineer.
- All other codal formatities have been observed.

3 Physical Progress achieved :-

- Construction of Road Works.
- Construction of CD. Works.

[Signature]
Executive Engineer
Rural Works Department
Works Division, Barsoi, Katihar
8/5/25

Rural Works Department, Works Division, Barsoi, Katihar.
MR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Initial Rectification and Surface Renewal)

MR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Initial Requisition and Contract award)																			
Name of Division :- Barsoi (Katihar)																			
Sl. No.	Package No.	Name Of Road	Project ID as per MIS	Administrative Approval (AA) Letter No./ Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen content in Percentage	Previous Total Allocated Amount (In Lakh)	up-to-date expenditure as per MIS (in Lakh)	Total Value of Measurement (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length of (in KM)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Year Routine Maintenance (In Lakh)											
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20
1	RM/KA/BAR/24/0003	032-RATAPORCHAR TO DHACHINA (VR32)	21105602086	6120 / 04.12.2023	3.800	204.947	117.21351	36.51944	21 MRD /2024-25 dated 06.11.2024	05-08-2025	02-04-2025	2793.05	25mm	5.1%	0.00000	0.00000	116.65298	116.65298	Surface Completed
2	RM/KA/BAR/24/0003	LD46-PAULI TO DHACHINA (VR46)	21105602095		1.752	98.386	58.44144	15.32674		05-08-2025	02-04-2025	2775.72	25mm	5.1%	0.00000	0.00000	58.38863	58.38863	Surface Completed
			Total :-		5.552	303.333	175.655	51.846							0.000	0.000	175.04161	175.04161	

[Signature]
 Executive Engineer
 R.W.D. Works Division
 Barsoi, Katihar

Name of Road: L032-RATAPOKHAR TO DHACHNA (VR32)
 Name of Agency: M/S A B C L Construction
 Length: 3.8 km

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
02/04/25	15:41:7	33	0.1	240	0	2400	2504	G	25.656362	87.961449	Normal
02/04/25	15:43:2	33	0.1	330	10.1	3300	3402	G	25.654872	87.964848	Normal
02/04/25	15:43:38	33	0.1	310	10.1	3100	3203	G	25.655003	87.963568	Normal
02/04/25	15:44:11	33	0.1	230	10.1	2300	2402	G	25.655466	87.962454	Normal
02/04/25	15:44:45	33	0.1	310	10.1	3100	3203	G	25.654871	87.964957	Normal
02/04/25	15:46:24	33	0.1	340	10.1	3400	3502	G	25.655558	87.96358	Normal
02/04/25	15:46:58	33	0.1	220	10.1	2200	2303	G	25.656166	87.96234	Normal
02/04/25	15:47:9	33	0.1	240	20.2	2400	2502	G	25.65688	87.960437	Normal
02/04/25	15:47:35	33	0.1	310	20.2	3100	3202	G	25.65739	87.96011	Normal
02/04/25	15:48:10	33	0.1	290	10.1	2900	3003	G	25.657467	87.960033	Curve
02/04/25	15:48:41	33	0.1	220	10.1	2200	2303	G	25.659293	87.960292	Normal
02/04/25	15:49:5	33	0.1	310	10.1	3100	3203	G	25.659314	87.960289	Normal
02/04/25	15:49:21	33	0.1	260	10.1	2600	2703	G	25.660587	87.959907	Normal
02/04/25	15:50:0	33	0.1	310	10.1	3100	3203	G	25.660883	87.959644	Normal
02/04/25	15:50:29	33	0.1	230	10.1	2300	2402	G	25.663199	87.957642	Normal
02/04/25	15:50:58	33	0.1	290	10.1	2900	3003	G	25.665695	87.955005	Normal
02/04/25	15:51:17	33	0.1	240	10.1	2400	2502	G	25.667901	87.954722	Curve
02/04/25	15:51:42	33	0.1	320	10.1	3200	3303	G	25.655571	87.96368	Normal
02/04/25	15:52:7	33	0.1	240	10.1	2400	2502	G	25.668532	87.954549	Normal
02/04/25	15:52:37	33	0.1	210	10.1	2113	2218	G	25.668859	87.953616	Normal
02/04/25	15:53:8	33	0.1	220	10.1	2200	2303	G	25.66863	87.95096	Normal
02/04/25	15:53:38	33	0.1	240	20.2	2400	2502	G	25.667214	87.948197	Normal
02/04/25	15:54:12	33	0.1	310	20.2	3100	3202	G	25.665443	87.94766	Normal
02/04/25	15:54:35	33	0.1	290	10.1	2900	3003	G	25.66477	87.947513	Normal
02/04/25	15:54:58	33	0.1	220	10.1	2200	2303	G	25.667325	87.948227	Normal
02/04/25	15:55:24	33	0.1	310	10.1	3100	3203	G	25.665898	87.947525	Normal
02/04/25	15:55:54	33	0.1	260	10.1	2600	2703	G	25.666205	87.947801	Normal
02/04/25	15:56:39	33	0.1	310	10.1	3100	3203	G	25.66729	87.94822	Normal
02/04/25	15:56:13	33	0.1	230	10.1	2300	2402	G	25.667365	87.948288	Normal
02/04/25	15:56:44	33	0.1	290	10.1	2900	3003	G	25.667488	87.948309	Normal
02/04/25	15:57:4	33	0.1	240	10.1	2400	2502	G	25.667614	87.948458	Normal
02/04/25	15:57:35	33	0.1	220	10.1	2200	2303	G	25.668662	87.941047	Normal
02/04/25	15:58:45	33	0.1	240	20.2	2400	2502	G	25.668697	87.941187	Normal

$$Y = 0 * X^2 + 0.969 * X + 74.60$$

$$X = 2615$$

$$Y = 2723$$

(R) RURAL ROAD

Good Average Poor
 <4000 4001-5000 >5000

Sum IRI	106136
Average IRI	2793.05

04/25	15:59:11	33	0.1	310	20.2	3100	3202	G	25.668856	87.953589	Normal
04/25	15:59:52	33	0.1	290	10.1	2900	3003	G	25.668786	87.953764	Normal
02/04/25	16:0:38	33	0.1	220	10.1	2200	2303	G	25.668713	87.954571	Normal
02/04/25	16:1:17	33	0.1	310	10.1	3100	3203	G	25.668076	87.954762	Normal
02/04/25	16:2:23	33	0.1	260	10.1	2615	2723	G	25.662389	87.958682	Normal

Am
08/04/2025
H.E.

Res
08/04/2025
S.E.

[Signature]
Executive Engineer
Rural Works Department
Works Division, Barsoi

Name of Customer : M/S A B C L Construction
 Name of Work/ Road : L032-RATAPOKHAR TO DHACHNA
 Lab Job number : 33
 Date : 02-04-2025
 Section No. : 33

Test Date :	02-04-2025	Road Name :	L032-RATAPOKHAR TO DHACHNA
Machine No :	404	Road Type :	(R) RURAL ROAD
Start S No :		Side :	
Start E No :		Interval	
Weather :		UIV Range :	1218 To 5000 1000 mm/km
Start Location :		Dist Range :	0 To 39 0.1 * 1000 m
End Location :		Equation :	$Y = 0 * X^2 + 0.969 * X + 74.60$

Print


Generate Report and Graph

Redraw Graph

Map View

File : D:\Dachna\dxs. Section No. : 33. Eqn : $Y = 0 * X^2 + 0.969 * X + 74.60$

Name of Customer : M/S A B C L Construction. Name of Work/ Road : L032-RATAPOKHAR TO DHACHNA (VR32). Le

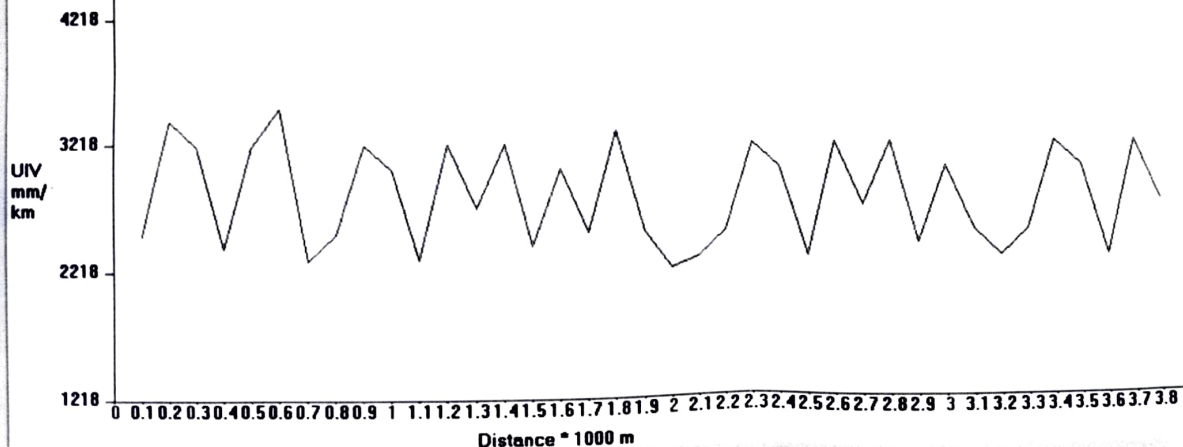

Executive Engineer
 Rural Works Department
 Works Division, Barsoi

08/04/2025
 J-E.

08/04/25
 AE

L032 - Ratan Pokhar to Daadana (VR-32)

Schedule XLV-Form No. 134

MR-3054

Executive Engineer

Rural Works Department

DIVISION

Works Division, Barsoi

SUB-DIVISION

BARSOI

MB-NO:-22-86

Measurement Book

M/S-ABCL Construction

OK

60/-

Name of Work-

Situation of Work-

Agency by which work is executed-

Date of Measurement-

No. and date of agreement

(These four lines should be repeated at the commencement of the measurement relating to each work)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of work:- Repair of Road from					
1032-Ratanpokhar To Dhachna					
Agency:- M/s ABCL Construction					
Agreement No:- 21MBD/2024-25					
Date of Commencement:- 06.11-2024					
Date of completion:- 05-08-2025					

Record Measurement

① clearing and grubbing
road land - E11

$$2 \times 15 \times 30 \text{ m} \times 1.00 \text{ m} = 900.00 \text{ m}^2$$

$$2 \times 10 \times 30 \text{ m} \times 1.00 \text{ m} = 600.00 \text{ m}^2$$

$$2 \times 12 \times 30 \text{ m} \times 1.00 \text{ m} = 720.00 \text{ m}^2$$

$$2 \times 10 \times 30 \text{ m} \times 1.00 \text{ m} = 600.00 \text{ m}^2$$

$$2 \times 15 \times 30 \text{ m} \times 1.00 \text{ m} = 900.00 \text{ m}^2$$

$$2 \times 15 \times 30 \text{ m} \times 1.00 \text{ m} = 900.00 \text{ m}^2$$

$$2 \times 20 \times 30 \text{ m} \times 1.00 \text{ m} = 1200.00 \text{ m}^2$$

$$2 \times 15 \times 30 \text{ m} \times 1.00 \text{ m} = 900.00 \text{ m}^2$$

$$2 \times 14 \times 30 \text{ m} \times 1.00 \text{ m} = 840.00 \text{ m}^2$$

$$2 \times 1 \times 20 \text{ m} \times 1.00 \text{ m} = 40.00 \text{ m}^2$$

$$\text{Total} = 7600.00 \text{ m}^2$$

$$= 0.76 \text{ Hect.}$$

Continuation



Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(20) 20 Road marking on C.C Surface - el2					
60.00 m ² O.V.T M.B.P. (18)					
@ 1005.95/m ² - R.					60357.00
(21) 21 Pl & fixing of typical M1654 information board -					
4.0 Nos O.V.T M.B.P. (18)					
@ 11945.30/each - R.					47781.00
(22) 22 Painting on Parapet wall - el2					
192.88 m ² O.V.T M.B.P. (19)					
@ 139.16/m ² - R.					26841.00
(23) 23 Plastering with (1:4) on blw - el2					
192.88 m ² O.V.T M.B.P. (19)					
Unit to 192.64 m ² @ 253.34/m ² - R.					48803.00
(24) 24 Brick masonry work in cement mortar 1:3 Parapet - el2:					
4.22 m ³ O.V.T M.B.P. (19)					
Unit to 4.21 m ³ @ 6233.01/m ³ - R.					26241.00
					R. 1191176.00
Add 18 X. G. ST @ - R.					2144012.00
Add 1 X. L. Cess @ - R.					119112.00
Add 10 X. S. fee @ - R.					138949.00
C.O. - R.					14313249.00

[illegible]
