



कार्यपालक अभियंता का कार्यालय ग्रामीण कार्य विभाग, कार्य प्रमंडल, मढ़ौरा।

E-Mail – eerwd.marhaura@yahoo.com

पत्रांक:- 548(अनु०)

मढ़ौरा/दिनांक:- 16/04/2025

प्रेषक:-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, मढ़ौरा।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण, बिहार, पटना।

विषय:- शीर्ष **MR-3054** योजनान्तर्गत बिहार ग्रामीण पथ नई अनुस्क्षण नीति-2018 के तहत स्वीकृत पथ में कराये गये कार्य का आवंटन मॉग के संबंध में।

प्रसंग:- भवदीय के पत्रांक:-113 अनु०, दिनांक:-10-01-2020

महाशय,

उपरोक्त विषयक प्रासंगिक पत्र के संबंध में कहना है कि इस कार्य प्रमंडल, अंतर्गत शीर्ष-**3054 (MR-3054)** अंतर्गत बिहार ग्रामीण पथ नई अनुस्क्षण नीति-2018 के तहत संवेदक जे०के० एण्ड कम्पनी के द्वारा पथ में किये गये कार्य का अधियाचना उक्त प्रासंगिक पत्र द्वारा प्राप्त विहित प्रपत्र में भरकर आवंटन मॉग हेतु अधियाचना-पत्र सादर समर्पित की जा रही है।

अतः अनुरोध है कि अधियाचना प्रपत्र में दर्शाये गये पथवार राशि कॉलम सं०-18 के अनुरूप पथ में आवंटन उपलब्ध कराने की कृपा की जाय ताकि संबंधित संवेदक द्वारा पथ में कराये गये कार्य का भुगतान किया जा सकें।


अनु०-1) अधियाचना प्रपत्र।


2) 19 ए प्रपत्र।

3) BOMP Indicator Report संलग्न।

विश्वासभाजन


15/4/25


15/04/25
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, मढ़ौरा।


15/4/25

FORM GER-19-A

(See Government of India'S Decision (I) below Rule -150)

Form of Utilization Certificate up to the Month of March-2025


PIU:- Executive Engineer RWD Works Division, Marhaura

SL No	Name of Scheme	Sanction No & Date with Amount (in Lacs Rs.)	Amount Received (in lacs Rs.)	Particulars
1	Construction of Rural Roads under MR-3054 Rural Road Maintenance Policy-2018 (Ledger ID-7069)	सचिव ब्राडा के पत्रांक-29 we दिनांक-30-03-2025	10760.54279	Certified that out of Rs- 10760.54279 Lacs received during the Years, 2018-19 & 2019-20, 2020-21, 2021-22, 22-23, 23-24 & 2024-25 in favour of E.E., R.W.D. Works Division Marhaura Sum of Rs- 10714.22499 Lacs has been utilized for the Purpose of MR-3054 New Maint. Policy-2018 Scheme as given in the margin for Which it was Sanctioned and that the balance of Rs-46.31780 Lacs remaining unutilized at CFMS the end of the period under report.


15/4/25


Sr. DAO

R.W.D. (W) Division Marhaura


15/04/25

Executive Engineer

R.W.D. (W) Division Marhaura


15/4/25

Requisition Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of works Division:- Rural Work Department, Work Division, Marhaura.

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA) Total		Agreement Amount (In Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (In Lakh)	up-to-date expenditure as per MIS (In Lakh)	Requisition against work done. (In Lakh)	
					Length (In Km.)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/SA/MAR/24/0001 MR-N/23-24 Marhaura/01	Saran jila antargat amnaur prakhand me dorlahi kethal P.C.C path se mahrauli mahadalit tola hote hue aphar bank tak path nirmaan.	31306505001	Lt. - No-6115 Date-04-12-2023	2.470	146.91000	111.08038	18.07852	03/MR-3054-N /MBD/ 2024-25 22-08-2024	21-05-2025		3126.14	25 mm	5%	63.24381	63.24381	47.25585	Work Completed
2	RM/SA/MAR/24/0001 MR-N/23-24 Marhaura/01	Jalalpur Shivganj PMGSY Path To Pakridih baniya Tola	31306512019	Lt. - No-6115 Date-04-12-2023	1.200	86.59000	68.59394	7.08893	03/MR-3054-N /MBD/ 2024-25 22-08-2024	21-05-2025		3019.83	25 mm	5%	39.07092	39.07092	27.91029	Work Completed
3	RM/SA/MAR/24/0001 MR-N/23-24 Marhaura/01	Amnour Firojpur PMGSY Path To Uttar Tola Tak	31306513010	Lt. - No-6115 Date-04-12-2023	1.400	79.33000	59.12531	9.61231	03/MR-3054-N /MBD/ 2024-25 22-08-2024	21-05-2025		3179.85	25 mm	5%	32.34969	32.34969	26.57749	Work Completed
4	RM/SA/MAR/24/0001 MR-N/23-24 Marhaura/01	L062-Salkhua Madhoura PMGSY Rd. to Manourpur (VR41)	31306502030	Lt. - No-6115 Date-04-12-2023	1.091	65.41200	49.27845	8.30197	03/MR-3054-N /MBD/ 2024-25 22-08-2024	21-05-2025		3050.45	25 mm	5%	25.54185	25.54185	21.72014	Work Completed
5	RM/SA/MAR/24/0001 MR-N/23-24 Marhaura/01	L045-Repura Rasulpur rd. to Shikarpur (VR26)	31306502024	Lt. - No-6115 Date-04-12-2023	1.010	41.86800	28.07923	9.27163	03/MR-3054-N /MBD/ 2024-25 22-08-2024	21-05-2025		2721.63	25 mm	5%	21.46628	21.46628	6.26135	Work Completed
6	RM/SA/MAR/24/0001 MR-N/23-24 Marhaura/01	L068-Beldehi Amnour Main Rd. to Balha Mahi River (VR47)	31306502034	Lt. - No-6115 Date-04-12-2023	0.780	52.32800	40.80178	5.04816	03/MR-3054-N /MBD/ 2024-25 22-08-2024	21-05-2025		2999.25	25 mm	5%	36.58979	36.58979	4.19073	Work Completed

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA) Total		Agreement Amount (In Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Alloted Amount (In Lakh)	up-to-date expenditure as per MIS (In Lakh)	Requisition against work done. (In Lakh)	Remarks
					Length (In Km.)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
7	RM/SA/MAR/24/0001 MR-N/23-24 Marhaura/01	Katsa Jogani PMGSY Path To Dasai Sah Tola Tak	31306512020	Lt.- No-6115 Date-04-12-2023	1.400	59.96500	40.50470	10.73996	03/MR-3054-N /MBD/ 2024-25 22-08-2024	21-05-2025		2774.64	25 mm	5%	31.27367	31.27367	8.92581 ✓	Work Completed
8	RM/SA/MAR/24/0001 MR-N/23-24 Marhaura/01	KATSA MARHAURA PMGSY PATH TO RAHIMPUR KURMI TOLA.	31306512018	Lt.- No-6115 Date-04-12-2023	0.900	51.23800	38.39203	6.77279	03/MR-3054-N /MBD/ 2024-25 22-08-2024	21-05-2025		2954.55	25 mm	5%	21.58164	21.58164	16.59971 ✓	Work Completed
Total:-															271.11765	271.11765	159.44137	

1. Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.
2. Up-to-date Physical Progress has been Uploaded in MIS.

15/04/25

15/04/25
Executive Engineer
Rural Work Department
Work Division, Marhaura
15/04/25

Steco Analyzer

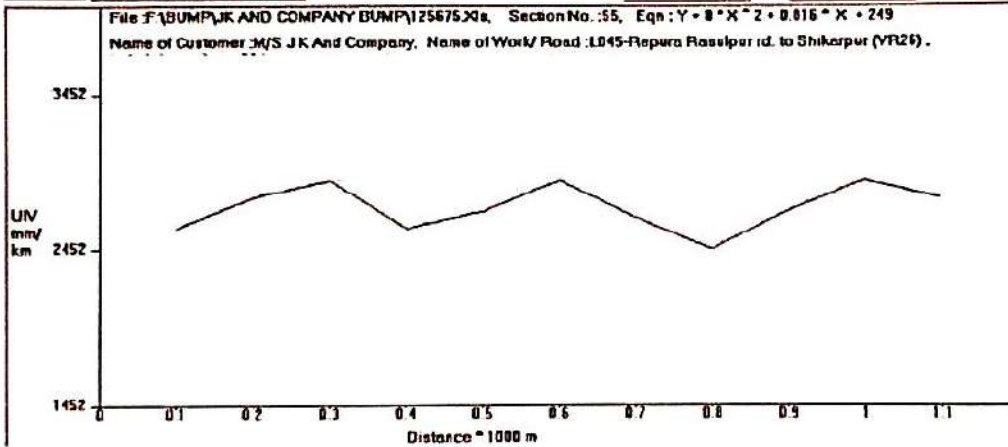
Name of Customer : M/S J.K. And Company
 Name of Work/ Road : asulpur rd to Shikarpur (VR26)
 Lab Job number : 394
 Date : 07/10/2024
 Section No. : 55

Test Date : 07/10/2024 Road Name : asulpur rd to Shikarpur (VR26)
 Machine No : Road Type : (R) RURAL ROAD
 Start S No : Side : Interval
 Start E No :
 Weather : UV Range : 1452 To 4000 1000 mm/km
 Start Location : Dist Range : 0 To 12 01 = 1000 m
 End Location : Equation : $Y = 0 \cdot X^2 + 0.815 \cdot X + 249$

Print Generate Report and Graph

Redraw Graph

Map View



Chaudhary
 07/10/24
 76

Shikarpur
 07/10/24

Shikarpur
 07/10/24

Name of Customer :M/S J K And Company

Name of Work/ Road :L045-Repura Rasulpur rd. to Shikarpur (VR26)

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI CATEGORY mm/km	ROAD	Latitude	Longitude	Event	
7/10/24	11:00:05	55	0.1	140	30.1	1400	2586 G		25.89974	84.8809	Normal	$Y = 0 \cdot X^2 + 0.815 \cdot X + 249$
7/10/24	11:00:20	55	0.1	280	30.5	2800	2789 G		25.90036	84.87952	Curve	X = 0
7/10/24	11:00:33	55	0.1	220	30.2	2200	2895 G		25.89997	84.87941	Normal	Y = 249
7/10/24	11:00:47	55	0.1	320	30.1	3200	2587 G		25.89979	84.88061	Normal	
7/10/24	11:01:00	55	0.1	110	25.8	2500	2698 G		25.90055	84.8796	Curve	(R) RURAL ROAD
7/10/24	11:01:14	55	0.1	190	30.5	1900	2897 G		25.90134	84.87998	Normal	Good Average Poor
7/10/24	11:01:30	55	0.1	220	30.7	2200	2657 G		25.90172	84.88029	Curve	<4000 4001-5000 >5001
7/10/24	11:01:45	55	0.1	270	30.3	2700	2452 G		25.902	84.88051	Normal	
7/10/24	11:02:02	55	0.1	270	27.9	2700	2698 G		25.90231	84.88088	Curve	
7/10/24	11:02:15	55	0.1	300	25.8	3000	2895 G		25.90242	84.88073	Normal	
7/10/24	11:02:28	55	0.01	310	28.8	3100	2784 G		25.9025	84.88086	Normal	
Length			1.01			IRI Value	2721.63					

CS/ans/6/24
07/10/24
-6

CS/ans/6/24
07/10/24

Ans/6/24
07/10/24
EE

Lab Job number :384

Date :07/10/2024

Name of Customer :M/S J K And Company

Name of Work/ Road :L045-Repura Rasulpur rd. to Shikarpur (VR26)

Sr.no Location of Corrected U.I Road category
test(in km) value(mm/km)

1	0.1	2586 G
2	0.2	2789 G
3	0.3	2895 G
4	0.4	2587 G
5	0.5	2698 G
6	0.6	2897 G
7	0.7	2657 G
8	0.8	2452 G
9	0.9	2698 G
10	1	2895 G
11	1.01	2784 G

Shankar
07/10/24
76

Shankar
07/10/24

Shankar
07/10/24
EE



NAME OF ROAD:- REPURA RASULPUR ROAD TO SHIKARPUR
L045

Schedule XLV-Form No. 134

M.B. NO:- 996

Executive Engineer
Rural Work's Department
Works Division, Marhaura

DIVISION

MIR 3054 - NMP 2018.

AMNOUR.

SUB-DIVISION

(S) 24/0004
Measurement Book

J. K. And Company

2nd & Final Bill

8

Sch. XLV—Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of work :- M/R to Road from					
Repura-Rasulpur Road to					
Shikarpur					
Agency :- M/S J.K. & Company					
Agreement No. :- 03/M.R-305A-N					
/MBP/2024-25					
Date of Commence :- 22.08.2024					
Date of Completion :- 21.05.2025					
Record entry					
①	Construction of Subgrade				
	& Earthen Shoulders				
	with approved material				

-do-do all complete Job					
10X2X	25X	1.120X	$\frac{0.71+0.31}{2}$	$= 187.6 \text{ m}^3$	
10X2X	30X	1.0X	$\frac{0.35+0.31}{2}$	$= 201.0 \text{ m}^3$	
10X2X	30X	1.10X	$\frac{0.38+0.31}{2}$	$= 227.7 \text{ m}^3$	
6X2X	20X	1.25X	$\frac{0.34+0.31}{2}$	$= 87.75 \text{ m}^3$	
4X2X	10X	0.5X	0.15	$= 6.0 \text{ m}^3$	
					710.05 m^3

②

Retro reflectorised
traffic signs providing
and erecting -do-do
all Complete Job

$$03 \times 1.20 \times 0.80 = 2.88 \text{ m}^3$$

③

Providing & Fixing
of retro-reflectorised

Continuation

Abstract of cost

11

Sch. XLV—Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
1/1	Clearing & Grubbing of road land -do-do all complete Job				
TMBP-01	0.1518 Ha	@	76926.08/Ha		R 11677.00
2/3	Construction of G.S.B G.R-II -do-do all Complete Job				
TMBP-01	6.05 m ³	@	2555.30/m ³		R 15460.00
3/4	Prov. laying & Spreading WBM Gr-2 -do-do all Complete Job				
TMBP-01,02	7.49 m ³	Limit	7.46 m ³		
		@	R 5671.58		R 42316.00
4/5	Prov. Laying & Spreading WBM Gr-3 -do-do all Complete Job				
TMBP-02	36.05 m ³	@	5172.96/m ³		R 186485.00
5/6	Prov. & applying Primer Coat with (RS-1) -do-do all Complete Job				
TMBP-03	480.67 m ²	@	R 5736/m ²		R 27571.00
G/7	Pro. & applying tack Coat -do-do -all Complete Job				
TMBP-03	3637.50 m ²	@	R 1647/m ²		R 59910.00

Continuation

Gor 34349.00

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
				BFR -	343419.00
7/8	Proof laying 25mm thick				
	S.D.B.C - do - do - all				
	Complete Job				
TMBP-03	90.94 m ³	@ R	14702.93/m ³	R	13,37,084.00
8/9	Construction of D.L.C				
	Subbase - do - do				
	all complete Job				
TMBP-02	0.45 m ³	@ R	5256.28/m ³	R	2365.00
9/10	Construction of Panel				
	Complete RCC m-30				
	- do - do - all complete Job				
TMBP-02	18.75 m ³	@ R	9276.08/m ³	R	173987.00
10/11	Proof Fixing RCC m-15				
	grade km ² 200m Stone				
	- do - do - all complete Job				
TMBP-03	Km Stone -				
	2 m ³	@	2919.48 each	-	5839.00
TMBP-03	200m Stone -				
	04 m ³	@	814.80 each	-	3259.00
11/17	Proof Fixing Logo of mms				
	Sign board - do - do -				
	all complete Job				
TMBP-03	03 m ³	@ R	10933.08 each	R	32799.00

Sch. XLV—Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
				BFR	18,98,692.00
12/02	Construction of Subgrade of earthen shoulders with approved material - do - do - all complete Job				
TMBP-08	710.05 m ³	@ 264.72 / m ³			- R 187964.00
13/12	Retro reflectorised traffic Signs providing and erecting - do - do - all - Complete Job				
TMBP-08	2.88 m ²	@ 14998.19 / m ²			- R 43197.00
14/13	Pack Fixing of retro- reflectorised Cautionary Mandatory Sign - do - do - all complete Job				
(i)	600mm equilateral and triangle				
TMBP-09	05 Nos	@ 4439.41 each			- R 22197.00
(ii)	600mm circular				
TMBP-09	01 Nos	@ 4310.23 each			- R 4310.00
(iii)	600mm x 450mm rectangular				
TMBP-09	03 Nos	@ 4165.70 each			- R 12497.00
(iv)	900mm Side octagon				
TMBP-09	01 Nos	@ 8635.01 each			- R 8635.00
				C.O.R	21,77,492.00

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
15/14	RCC m-s grade boundary Pillars/Jucal Stone - do do all complete Job				B.F.R 21,77,992.00
TMBP-09	16 Nos @ 677.86 each - R 10845.00				
16/15	Planting of trees by the Road Side -do-do-all complete Job				
TMBP-09	49 Nos @ 1305.10 each - R 63950.00				
17/16	Provd laying of hot applied thermoplastic -do-do-all complete Job				
TMBP-09	For BT Portion and Pedestrian crossing 194.75m ² @ 886.50/m ² - R 172646.00 For portion				
TMBP-09	08m ² @ 988.82/m ² - R 7911.00 HPC 600mm Parapet repair				
18	Brick masonry work in cement mortar (1:3) in Parapet - do-do-all complete Job				
TMBP-10	2.02m ³ @ 6553.81/m ³ - R 13239.00 C.R 24,46,983.00				

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
19.	Plastering with Cement mortar (1:4) on brick work - do-do all complete Job.				BFR 2446083.00
TMBP-10	14.40 m ²	@	200.42 / m ²	- R	2886.00
20.	Painting two coats & including Primer coat - do-do - all Complete Job.				
TMBP-10	14.40 m ²	@	136.59 / m ²	- R	1967.00
				RS:	2450936.00
				Add GST (18%) - (+)	441168.00
				Add Labour Cess (4%) +	24509.00
				Add S. Fee - (+)	17838.00
				RS.	2934451.00
				Less (5.51%) below (-)	161688.00
				Less for Previous Payment	2146628.00
				RS.	626135.00
	 02/04/2023 J.F.				 02/04/23
					CSP 15/04/23 EE
