

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, महनार (वैशाली)

पत्रांक
प्रेषक ,

725 (अंक)

/महनार/दिनांक :- 12/04/2025

सेवा में,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, महनार

नोडल पदाधिकारी,
3054 एम0आर0 कोषांग,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय :- मुख्यमंत्री ग्रामीण सड़क उन्नयन योजना (MMGSUY) के तहत
निर्मित पथ की राशि की अधियाचना पत्र समर्पित करने के संबंध में।

महाशय,


उपरोक्त विषय के संदर्भ में मुख्यमंत्री ग्रामीण सड़क उन्नयन योजना
(MMGSUY) से निर्मित पथ के लिए राशि की अधियाचना विहित प्रपत्र में
समर्पित की जा रही है।

विदित है कि अधियाचित पथ का कार्य संतोषप्रद है। अधियाचित पथ
में आवंटन देने की कृपा की जाये।

अनु0:-1. अधियाचना विहित प्रपत्र।

विश्वासभाजन


12/04/25


कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, महनार

Office of The Executive Engineer, Rural Works Department, Works Division Mahnar

Requisition formate for Scheme Head- MMGSUY																				
S.No.	Package No	Project ID As per MIS	Name of Road	A.A. Letter No & Date	Administrativ Approval (A.A.)		Agreement Amount (in Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen content in Percentage	Total Previous Allotted Amount (in Lakh)	Up-tp-Date Expenditure as per MIS (in lakh)	Value of work done (in lakh)	Current Demand (in lakh)	Remarks
					Length (in K.M.)	Amount (in lakh)	Construction (in lakh)	5 Years Maintenance (in lakh)												
1	2	3	4	5	6		7		8	9	10	11	12	13	14	15	16	17	18	19
1	MMGSUY/23-24 Mahnar/04	3150770280007	Raghopur Ke Virpur Me Utkarmit High School Se Tapeswar Singh k Ghar Hote hue Suresh Singh K ghar tak	18/12/2023	1.500	147.24000	137.11402	5.48732	12.09.2024	09.05.2025	-	Surface Complete	3058.60	PCC- 125	Grading-M30	82.05701	82.05701	135.74821	53.69120	
2	MMGSUY/23-24 Mahnar/04	3150770280009	Raghopur Virpur Me RCD Road 10 No. Ward se Sukhdeo Choudhary Ke ghar Se Narayan Shah k Ghar tak	18/12/2023	0.550	68.52000	64.15964	2.20715	12.09.2024	09.05.2025	-	Surface Complete	3142.66	PCC- 125	Grading-M30	38.57982	38.57982	63.53024	24.95042	
3	MMGSUY/23-24 Mahnar/04	3150770280010	PCC Road Dhirendrera Rai K Ghar Se Jawahar Rai Rustumpur Tenparaiya Tola	18/12/2023	1.075	114.18000	106.38749	4.19851	12.09.2024	09.05.2025	-	Surface Complete	3148.54	PCC- 125	Grading-M30	63.69375	63.69375	105.49975	41.80600	
4	MMGSUY/23-24 Mahnar/04	3150770280011	Ramjanki Math Se Das Tola hote hue Narashiya PCC Sadak Tak	18/12/2023	0.800	95.98000	90.03437	2.92735	12.09.2024	09.05.2025	-	Surface Complete	3041.63	PCC- 125	Grading-M30	54.01719	54.01719	89.38587	35.36868	
5	MMGSUY/23-24 Mahnar/04	3150770280012	Ranjay Singh Kapda Dukan via Post office to Kashi Chowk	18/12/2023	0.640	82.85000	77.68931	2.5361	12.09.2024	09.05.2025	-	Surface Complete	3084.86	PCC- 125	Grading-M30	46.84466	46.84466	76.59377	29.74911	
6	MMGSUY/23-24 Mahnar/05	5150770280025	L028-L022 to Rampur Karari Barari (VR9)	19/12/2023	4.960	490.53000	490.52227	18.78304	24/09/2024	23/06/2025	-	3 km work completed	3090.28	PCC- 125	Grading-M30	98.00000	98.00000	289.39879	191.39879	
7	MMGSUY/23-24 Mahnar/03	3150770280004	Chandpura Mahrani Sthan PCC Road via Devvindra Rai Mukhiya House to Mukesh Jha	18/12/2023	0.400	41.18000	37.97729	1.44651	24/09/2024	23.06.2025	-	PCC Work in progress	2304.84	PCC- 125	Grading-M30	8.00000	8.00000	37.70904	29.70904	

Requisition formate for Scheme Head- MMGSUY																				
S.No.	Package No	Project ID As per MIS	Name of Road	A.A. Letter No & Date	Administrativ Approval (A.A.)		Agreement Amount (in Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen content in Percentage	Total Previous Allotted Amount (in Lakh)	Up-tp-Date Expenditure as per MIS (in lakh)	Value of work done (in lakh)	Current Demand (in lakh)	Remarks
					Length (in K.M.)	Amount (in lakh)	Construction (in lakh)	5 Years Maintenance (in lakh)												
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19		
8	MMGSUY/23-24 Mahnar/03	3150770280022	Registery Tola Raghopur Purbi Path to Samudaik Bhawan Chandan Choudhary ke Ghar hote huye Middle School RCD Path	18/12/2023	1.500	153.08000	141.09351	5.42312	24/09/2024	23.06.2025	-	PCC Work in progress	3097.40	PCC- 125	Grading- M30	76.15567	76.15567	135.47299	59.31732	
9	MMGSUY/23-24 Mahnar/02	3150770280019	ADALPUR CHOWK TO BHATTAHI	18/12/2023	4.700	431.15000	350.43921	43.47845	09.08.2024	07.08.2025	-	GSB Gr-III Completed	3390.36	0.00	0.00	70.00000	70.00000	207.22254	137.22254	
10	MMGSUY/23-24 Mahnar/02	3150770280001	L040 - Bilandpur Dhadhua to Malahi Chuk Bajo Malahi (VR33)	18/12/2023	5.650	508.25000	418.65743	45.44359	09.08.2024	07.08.2025	-	B.T & PCC work Completed	3357.00	Bitumen- 25 mm PCC- 125	Bitumen- 5.019 % Grading- M30	211.93696	205.58431	281.94698	70.01002	


 Sr. Divisional Accounts Officer
 Rural Works Department,
 Works Division, Mahnar


 Executive Engineer,
 Rural Works Department,
 Works Division, Mahnar

GFR 12-B
[See Rule 256 (2)]

FORM OF UTILIZATION CERTIFICATE

(1) Certified that out of the Loan of Rs.174994908.00, Sanctioned under Letter No-31, dated-08-04-2025, in favour of Executive Engineer, RWD, Works Division, Mahnar, during the year 2024-25, an amount of Rs. 155049702.00, has been utilized for the purpose for which it was sanctioned, and that the balance of Rs. 19945206.00, remaining unutilized at the end of the year Zero has been surrendered to the Government (vide No....., dated.....) / will be adjusted towards the loan payable during the next financial year.

(2) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.

Kinds of checks exercised

- 1.
- 2.
- 3.
- 4.

Signature.....

Designation.....

Date.....

See See
12/4/25

[Signature]
Executive Engineer
RWD Works Div. Mahnar

Lab Job number :37

Date :22-02-2025

Name of Customer :Wakil Ray

Name of Work/ Road :Raghopur Ke Virpur Me Utkarmit High School Se
Tapeswar Singh k Ghar Hote hue Suresh Singh K ghar tak

Sr.no	Location of test (in km)	Corrected U.I value (mm/km)	Road catagory
1	0.100	2884	G
2	0.200	3175	G
3	0.300	2981	G
4	0.400	3078	G
5	0.500	3272	G
6	0.600	2884	G
7	0.700	2787	G
8	0.800	3175	G
9	0.900	3078	G
10	1.000	3078	G
11	1.100	2981	G
12	1.200	3175	G
13	1.300	2981	G
14	1.400	3272	G
15	1.500	3078	G
Average IRI Value		3058.60	

ma
22/1/25
SC

22/02/25
नगरपालिका आभार
ग्रामीण कार्य विभाग
कार्य प्रमण्डल महानगर

Lab Job number :37
Date :22-02-2025

Name of Customer :Wakil Ray

Name of Work/ Road :Raghopur Ke Virpur Me Utkarmit High School Se Tapeswar Singh k Ghar Hote hue Suresh Singh K ghar tak

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
22/ 2/ 25	13: 35: 7	37	0.1	290	0	2900	2884	G	25.53207	85.46869	Normal
22/ 2/ 25	13: 35: 46	37	0.1	320	10.1	3200	3175	G	25.53166	85.46930	Normal
22/ 2/ 25	13: 36: 18	37	0.1	300	10.1	3000	2981	G	25.53133	85.46986	Normal
22/ 2/ 25	13: 36: 53	37	0.1	310	10.1	3100	3078	G	25.53121	85.47023	Normal
22/ 2/ 25	13: 37: 26	37	0.1	330	20.2	3300	3272	G	25.53099	85.47117	Normal
22/ 2/ 25	13: 37: 56	37	0.1	290	20.2	2900	2884	G	25.53135	85.47204	Curve
22/ 2/ 25	13: 38: 25	37	0.1	280	20.2	2800	2787	G	25.53216	85.47254	Normal
22/ 2/ 25	13: 38: 48	37	0.1	320	10.1	3200	3175	G	25.53230	85.47199	Normal
22/ 2/ 25	13: 39: 15	37	0.1	310	10.1	3100	3078	G	25.53249	85.47126	Curve
22/ 2/ 25	13: 39: 51	37	0.1	310	10.1	3100	3078	G	25.53313	85.47064	Normal
22/ 2/ 25	13: 40: 26	37	0.1	300	10.1	3000	2981	G	25.53344	85.46996	Normal
22/ 2/ 25	13: 40: 49	37	0.1	320	10.1	3200	3175	G	25.53379	85.46911	Normal
22/ 2/ 25	13: 41: 21	37	0.1	300	10.1	3000	2981	G	25.53340	85.46872	Curve
22/ 2/ 25	13: 41: 53	37	0.1	330	20.2	3300	3272	G	25.53297	85.46845	Normal
22/ 2/ 25	13: 42: 32	37	0.1	310	10.1	3100	3078	G	25.53252	85.46806	Normal

$$Y = 0 * X^2 + 0.969 * X + 74.60$$

$$X = 3100$$

$$Y = 3078$$

(R) RURAL ROAD


Good Average Poor
<4000 4001-5000 >5001

179
22/11/25
SC

28/02/25
नयपालक अभियन्ता
ग्रामीण कार्य विभाग
कार्य प्रमण्डल महानगर

File :D:\Bump Integrator\MMGSUY\Raghopur Ke Virpur Me Utkarmit High School Se Tapeswar Singh k Ghar Hote hue

Name of Customer :Wakil Ray. Name of Work/ Road :Raghopur Ke Virpur Me Utkarmit High School Se Tapeswar Sin

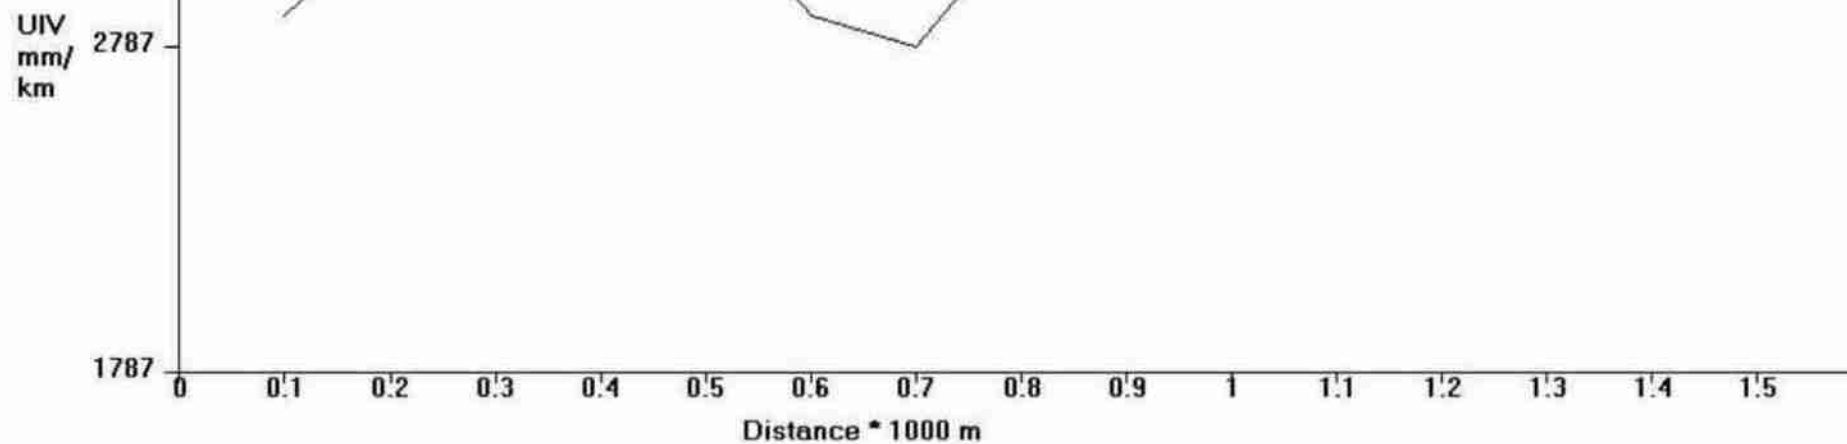

ma
22/1/25
SC

28/01/25
नरेशपालक आभेयन्त
ग्रामीण कार्य विभाग
कार्य प्रमण्डल महानगर
