

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, गोपालगंज-1

पत्रांक:-623 3330

/ गोपालगंज

दिनांक: 17/04/2025

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, गोपालगंज-1

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार, पटना।

विषय:- शीर्ष मुख्यमंत्री ग्रामीण सड़क उन्नयन योजना (सामान्य) अन्तर्गत में अधियाचित राशि का आवंटन उपलब्ध कराने के संबंध में।


महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि शीर्ष मुख्यमंत्री ग्रामीण सड़क उन्नयन योजना (सामान्य) अन्तर्गत राशि की माँग संलग्न विहित प्रपत्र में पथवार की जा रही है।

अतः भवदीय से अनुरोध है कि विहित प्रपत्र के कॉलम-18 में अंकित कुल राशि का आवंटन उपलब्ध कराने की कृपा की जाय। अधियाचित राशि के संदर्भ में C & P किये मापी पुस्तिका की छाया प्रति, एवं उपयोगिता प्रमाण-पत्र संलग्न कर आवश्यक कार्रवाई हेतु समर्पित किया जा रहा है।

अनु०-यथोक्त।

विश्वासभाजन


17/4/25

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,

कार्य प्रमण्डल, गोपालगंज-1

17.4.25

Requisition Format for Scheme MMGSUY (General/SC/ST)

Name of the Works Division :- Gopalganj-1

Sl. No.	Package No.	Project ID as per MIS	Name of Road	AA Length (in km.)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (VBM/WBM/SDBC etc.)	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allocated Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MMGSUY/23-24 Gopalganj-1/01	3140690280001	Babhi Khass to Naharpur	7.680	696.310	644.14439	10/MBD (MMGSUY) 2024-25 dt. 18.09.2024	17.09.2025	24.02.2025	BM/SDBC	773.81	75	5.03	392.86121	392.86121	637.25744	244.39623	Completed
2	MMGSUY/23-24 Gopalganj-1/01	3140690280004	L042 Malpura to Harizan Toia Paththrauli	3.800	260.660	258.31049	10/MBD (MMGSUY) 2024-25 dt. 18.09.2024	17.09.2025	24.02.2025	BM/SDBC	2639.60	75	5.03	136.30597	136.30597	256.30581	119.99984	Completed
3	MMGSUY/23-24/ Gopalganj-1/02	3140690280002	Babu Jannanah se Chaurawa	4.270	600.130	581.67664	09/MBD (MMGSUY) 2024-25 dt. 18.09.2024	17.09.2025	31.03.2025	BM/SDBC	1201.93	75	5.02	477.03825	477.03825	571.19087	94.15262	Completed
4	MMGSUY/23-24 Gopalganj-1/03	3140690280003	TDS Thawe NH-85 TDS to Gawandari Dhaningra Path (OTTI6)	8.850	1195.870	1190.20429	11/MBD (MMGSUY) 2024-25 dt. 18.09.2024	17.09.2025	-	BM/SDBC	1916.26	75	5.02	328.47646	328.47646	1078.75815	750.28169	Surface Completed

It is certified that Physical & Financial Progress has been updated in MIS.

Note :-

1. Above Signed Copy along with Forwarding Letter & Utilisation Certificate must be uploaded in MIS.
2. Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed (As Applicable).

D.A.O.
R.W.D. Works Division
Gopalganj-1

17/4/25

Executive Engineer
R.W.D. Works Division
Gopalganj-1

17/4/25

GFR 12-B
[See Rule 256 (2)]

FORM OF UTILIZATION CERTIFICATE

(1) Certified that out of the Loan of Rs.133468189.00 Sanctioned under MMGSUY GEN dated 27.03.2025, in favour of Executive Engineer, RWD Works Division Gopalganj-1, during the year 2024-25, an amount of Rs.133468189.00 has been utilized for the purpose for which it was sanctioned, and that the balance of Rs.0.00 remaining unutilized at the end of the year 2025 has been surrendered to the Government (vide No..... dated.....) will be adjusted towards the loan payable during the next financial year.


(2) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.

Kinds of checks exercised

- 1.
- 2.
- 3.
- 4.


D.A.O.

R.W.D. Works Division,
Gopalganj-1


Executive Engineer,
R.W.D. Works Division,
Gopalganj-1
17.4.25

Road Name-L042 - Malpura to Harizan Tola Pathkhauji

Cont.Name-Shailcon Construction

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI CATEGORY mm/km ROAD	Latitude	Longitude	Event
1/2/25	10:45:10	59	0.1	100	10.1	1000	1064 G	26.537123	84.10111	Normal
1/2/25	10:45:46	59	0.1	120	10.1	1200	1228 G	26.537818	84.1017	Normal
1/2/25	10:46:22	59	0.1	280	10.1	2800	2533 G	26.538615	84.102137	Normal
1/2/25	10:47:0	59	0.1	340	20.2	3400	3023 G	26.538798	84.103063	Normal
1/2/25	10:48:8	59	0.1	290	20.2	2900	2615 G	26.53893	84.104007	Normal
1/2/25	10:48:8	59	0.1	220	20.2	2200	2044 G	26.539602	84.104528	Normal
1/2/25	10:48:43	59	0.1	330	30.3	3300	2941 G	26.539887	84.105218	Normal
1/2/25	10:49:0	59	0.1	240	30.3	2400	2207 G	26.539737	84.106228	Normal
1/2/25	10:49:18	59	0.1	270	30.3	2700	2452 G	26.539585	84.107205	Normal
1/2/25	10:49:18	59	0.1	310	30.3	3100	2778 G	26.539342	84.108232	Normal
1/2/25	10:50:0	59	0.1	290	30.3	2900	2615 G	26.538988	84.10909	Normal
1/2/25	10:50:0	59	0.1	350	20.2	3500	3104 G	26.538727	84.109982	Normal
1/2/25	10:50:28	59	0.1	260	30.3	2600	2370 G	26.538563	84.11101	Normal
1/2/25	10:51:3	59	0.1	340	30.3	3400	3023 G	26.538252	84.112423	Normal
1/2/25	10:51:3	59	0.1	400	20.2	4000	3512 G	26.538155	84.11335	Normal
1/2/25	10:51:39	59	0.1	310	30.3	3100	2778 G	26.537635	84.114123	Normal
1/2/25	10:51:39	59	0.1	380	20.2	3800	3349 G	26.536978	84.114628	Normal
1/2/25	10:52:0	59	0.1	230	30.3	2300	2125 G	26.536393	84.114965	Normal
1/2/25	10:52:14	59	0.1	220	30.3	2200	2044 G	26.536297	84.115842	Normal
1/2/25	10:52:14	59	0.1	350	20.2	3500	3104 G	26.536158	84.116835	Normal
1/2/25	10:52:14	59	0.1	330	30.3	3300	2941 G	26.535958	84.117845	Normal
1/2/25	10:52:14	59	0.1	310	20.2	3100	2778 G	26.53548	84.118552	Normal
1/2/25	10:53:0	59	0.1	370	20.2	3700	3268 G	26.53509	84.119258	Normal
1/2/25	10:53:0	59	0.1	440	20.2	4400	3839 G	26.534668	84.12005	Normal
1/2/25	10:53:25	59	0.1	310	30.3	3100	2778 G	26.534595	84.120975	Normal
1/2/25	10:53:25	59	0.1	300	30.3	3000	2696 G	26.534365	84.122037	Normal
1/2/25	10:53:25	59	0.1	200	30.3	2000	1880 G	26.53441	84.123013	Normal
1/2/25	10:54:0	59	0.1	280	30.3	2800	2533 G	26.534108	84.123972	Normal

$$Y = 0 * X^2 + 0.816 * X + 249$$

$$X = 1000$$

$$Y = 3069$$

(R) RURAL ROAD

Good Average Poor
<4000 4001-5000 >5001

IRI Value

Average IRI-2639.60

11/03/25
me

11/03/25
ce

1/2/25	10:54:0	59	0.1	340	20.2	3400	3023 G	26.533357	84.124443	Normal
1/2/25	10:54:35	59	0.1	380	20.2	3800	3349 G	26.533015	84.124932	Normal
1/2/25	10:55:10	59	0.1	330	10.1	3300	2941 G	26.533248	84.125875	Normal
1/2/25	10:55:10	59	0.1	250	10.1	2500	2288 G	26.533848	84.126548	Normal
1/2/25	10:55:46	59	0.1	270	20.2	2700	2452 G	26.533835	84.127423	Normal
1/2/25	10:56:0	59	0.1	230	20.2	2300	2125 G	26.53448	84.128063	Normal
1/2/25	10:56:0	59	0.1	380	10.1	3800	3349 G	26.534907	84.128872	Normal
1/2/25	10:56:21	59	0.1	230	20.2	2300	2125 G	26.53469	84.129813	Normal
1/2/25	10:56:21	59	0.1	210	20.2	2100	1962 G	26.534797	84.130807	Normal
1/2/25	10:56:21	59	0.081	280	20.2	3457	3069 G	26.534868	84.13111	Normal

1103/25
AE

113/25
EG

Name of Customer: Shaleen Construction
 Name of Work/ Road: L042 - Mapur to Haren Tola
 Lab Job number: 55
 Date: 07-02-2025
 Section No.: 55

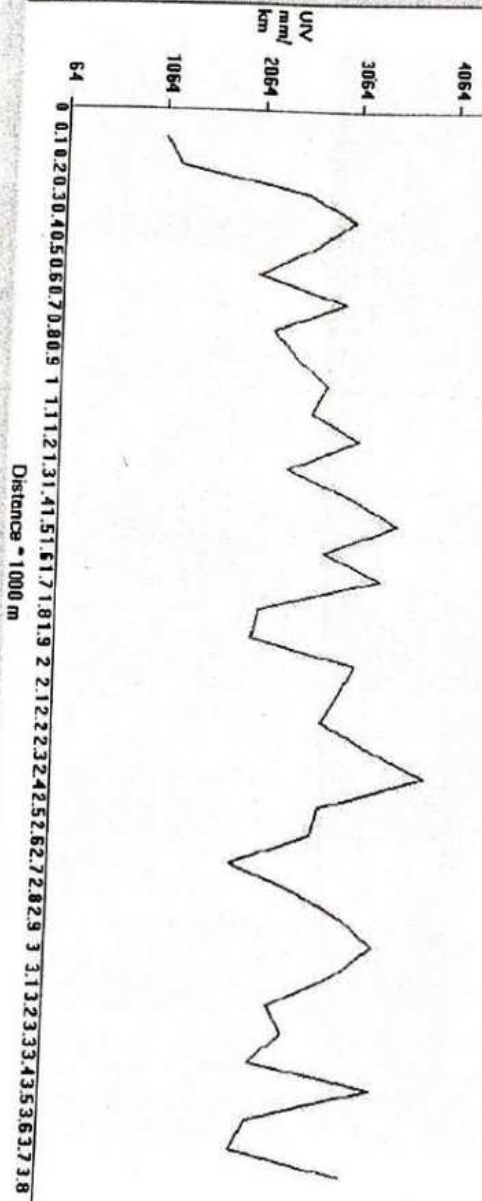
Test Date: 07-02-2025 Road Name: Pura to Horizon Tola Pathkhali
 Machine No.: 456 Road Type: (R) RURAL ROAD
 Start S No.: Side: Interval:
 Start E No.:
 Weather:
 Start Location: L042 - Mapur U/V Range: 64 To 5000 1000 mm/km
 Dist Range: 0 To 39 0.1 * 1000 m
 End Location: 04 Pathkhali Equation: $Y = 0 * X^2 + 0.01E * X + 249$

Print Generate Report and Graph

Redraw Graph

Map View

File: D:\Gopalgeni-1\Graph\Mapur se Haren Tola Pathkhali\Mapuraxlsx Section No.: 55, Egn: Y = 0 * X^2 +
 Name of Customer: Name of Work/ Road: Lab Job number:



Wishu
11/03/25
 are

Wishu
11/3/25
