



कार्यपालक अभियंता का कार्यालय ग्रामीण कार्य विभाग, कार्य प्रमंडल, मढ़ौरा।

E-Mail – eerwd.marhaura@yahoo.com

पत्रांक:- 601/अ-20

मढ़ौरा/दिनांक:- 25.04.25.

प्रेषक:-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, मढ़ौरा।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण, बिहार, पटना।

विषय:- शीर्ष **MR-3054** योजनान्तर्गत बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत स्वीकृत पथ में कराये गये कार्य का आवंटन मॉग के संबंध में।

प्रसंग:- भवदीय के पत्रांक:-113 अनु0, दिनांक:-10-01-2020

महाशय,

उपरोक्त विषयक प्रासंगिक पत्र के संबंध में कहना है कि इस कार्य प्रमंडल, अंतर्गत शीर्ष-**3054 (MR-3054)** अंतर्गत बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत संवेदक श्री राजु कुमार सिंह एवं युगलब्रील कन्स्ट्रक्शन प्रा0लि0 के द्वारा पथ में किये गये कार्य का अधियाचना उक्त प्रासंगिक पत्र द्वारा प्राप्त विहित प्रपत्र में भरकर आवंटन मॉग हेतु अधियाचना-पत्र सादर समर्पित की जा रही है।

अतः अनुरोध है कि अधियाचना प्रपत्र में दर्शाये गये पथवार राशि कॉलम सं0-18 के अनुरूप पथ में आवंटन उपलब्ध कराने की कृपा की जाय ताकि संबंधित संवेदक द्वारा पथ में कराये गये कार्य का भुगतान किया जा सकें।

अनु0-यथोक्त।

विश्वासभाजन


24/4/25

24/04/25
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, मढ़ौरा।
24/4/25


FORM GER-19-A

(See Government of India'S Decision (I) below Rule -150)
Form of Utilization Certificate up to the Month of March-2025
PIU:- Executive Engineer RWD Works Division, Marhaura


SL No	Name of Scheme	Sanction No & Date with Amount (in Lacs Rs.)	Amount Received (in lacs Rs.)	Particulars
1	Construction of Rural Roads under MR-3054 Rural Road Maintenance Policy-2018 (Ledger ID-7069)	सचिव ब्राडा के पत्रांक-29 वे दिनांक-30-03-2025	10760.54279	Certified that out of Rs- 10760.54279 Lacs received during the Years, 2018-19 & 2019-20, 2020-21, 2021-22, 22-23, 23-24 & 2024-25 in favour of E.E., R.W.D. Works Division Marhaura Sum of Rs- 10714.22499 Lacs has been utilized for the Purpose of MR-3054 New Maint. Policy-2018 Scheme as given in the margin for Which it was Sanctioned and that the balance of Rs-46.31780 Lacs remaining unutilized at CFMS the end of the period under report.



Sr. DAO
R.W.D. (W) Division Marhaura



Executive Engineer
R.W.D. (W) Division Marhaura




Requisition Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of works Division:- Rural Work Department, Work Division, Marhaura.

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA) Total		Agreement Amount (In Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Alloted Amount (In Lakh)	up-to-date expenditure as per MIS (In Lakh)	Requisition against work done. (In Lakh)	Remarks
					Length (In Km.)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/SA/MAR/24/0005 MR-N/23-24 Marhaura/05	Padampur Pakki Sadak To Timuhani Manager Rai Ke Ghar Tak.	31306512031	Lt.- No-583 Date-05-12-2023	1.400	86.65000	69.58099	10.70266	08/MR-3054-N- /MBD/2024-25 Dt-11-09-2024	10.06.2025	20-03-2025	2975.57	25mm	5%	68.32597	68.32597	0.36626	Work Completed
2	MR-N/23-24 Marhaura/08 RM/SA/MAR/24/0008	Mashrakh Mela Pmgsty Road To Mashrakh Purbi Tola Tak	31306512007	Lt.- No-31 Date-03-01-2024	0.670	49.74800	40.84166	3.87960	15/MR-3054-N- (MBD/2024-25) Dt-25-10-2024	24-07-2025	20-03-2025	2588.00	25mm	5%	0.00000	0.00000	40.78128	Work Completed
3	MR-N/23-24 Marhaura/11 RM/SA/MAR/23/0007	Chavaniya Mahadalit Tola PMGSY Path Kadam Tola Tak.	31306513016	Lt.- No-2178 Date-20-10-2022	3.200	183.27600	149.55651	31.00790	13/MR-3054-N- (MBD/2024-25) Dt-18-10-2024	17-07-2025		3180.37	25mm	5%	86.39320	86.39320	62.79099	Work Completed
4	MR-N/23-24 Marhaura/08 RM/SA/MAR/24/0009	Kawalpura PMGSY Path To Mahadeva	31306512029	Lt.- No-270 Date-22-01-2024	0.900	77.60000	62.46772	7.40175	07/MR-3054-N- /MBD/2024-25 Dt-11-09-2024	10-06-2025	21-03-2025	3119.33	25mm	5%	60.54253	60.54252	0.13461	Work Completed
5	MR-N/23-24 Marhaura/08 RM/SA/MAR/24/0009	Bahadurpur High School To Bairagi Harijan Tola tak	31306513019	Lt.- No-270 Date-22-01-2024	1.500	119.93000	96.49559	11.35940	07/MR-3054-N- /MBD/2024-25 Dt-11-09-2024	10-06-2025	21-03-2025	3015.93	25mm	5%	84.92517	84.92413	9.93089	Work Completed
Total:-															300.18687	300.18582	114.00403	

1. Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.

2. Up-to-date Physical Progress has been Uploaded in MIS.


 Executive Engineer
 Rural Work Department
 Work Division, Marhaura

Steco Analyze


Name of Customer: Raju Kumar Singh
 Name of Work/ Road: Mashrakh mela PMGSY Road
 Lab Job number: 70
 Date: 20-03-2025
 Section No.: 70

Test Date: 20-03-2025 Road Name: Road to Mashrakh Purwi to tal
 Machine No: 384 Road Type: (R) RURAL ROAD
 Start S No: Side:
 Start E No: Interval
 Weather: IIV Range: 1233 To 4000 1000 mm/km
 Start Location: Dist Range: 0 To 0.8 0.1 * 1000 m
 End Location: Equation: $Y = 0 * X^2 + 0.969 * X + 74.60$

Print Generate Report and Graph

Redraw Graph

Map View

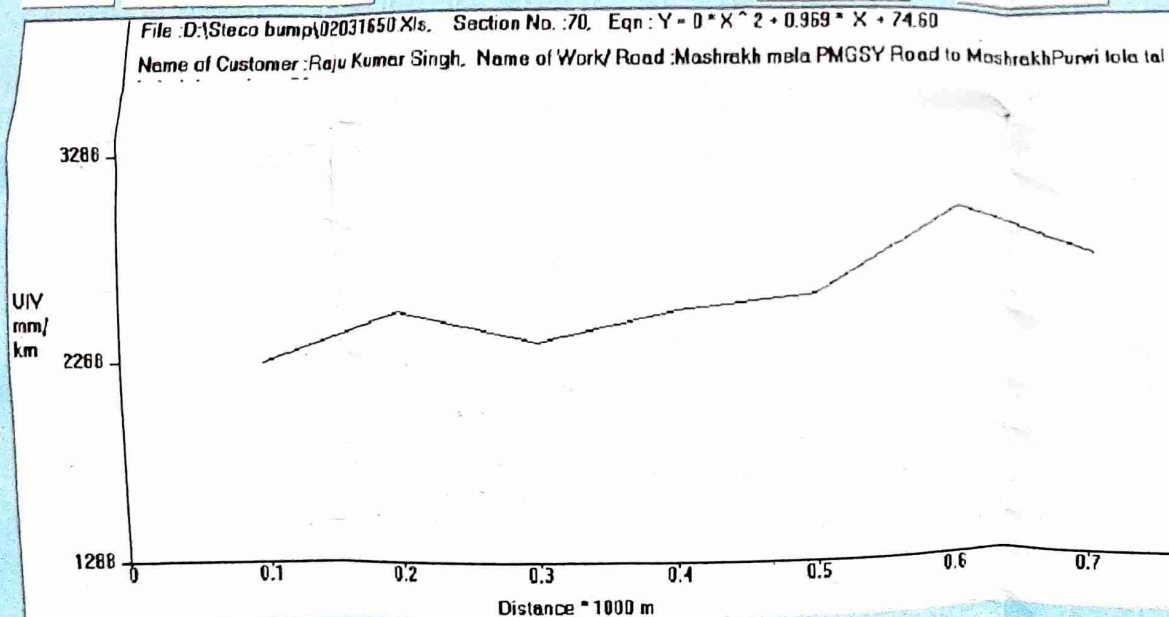

[Signature]
 20-03-25

[Signature]
 20-3-25
 A-E

Name of Road- Mashrakh mela PMGSY Road to MashrakhPurwi tola tak

Date	Time	Section	Length	Bumps	Speed	OR	IRI	TEGORY		Latitude	ongitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD				
20/ 3/ 25	16: 46: 4	70	0.1	230	10.1	2500	2288	G		26.10114	84.81311	Normal
20/ 3/ 25	16: 47: 0	70	0.1	230	10.1	2700	2525	G		26.10109	84.8136	Normal
20/ 3/ 25	16: 47: 25	70	0.1	200	30.3	2600	2370	G		26.10105	84.81411	Normal
20/ 3/ 25	16: 47: 49	70	0.1	210	20.2	2700	2525	G		26.10074	84.81567	Curve
20/ 3/ 25	16: 48: 0	70	0.1	250	30.3	2800	2607	G		26.10054	84.81667	Normal
20/ 3/ 25	16: 48: 24	70	0.1	240	30.2	3200	3025	G		26.10021	84.81845	Normal
20/ 3/ 25	16: 49: 0	70	0.1	200	20.2	2900	2780	G		26.10018	84.81926	Normal
Total			0.700	Average IRI			2588					

$$Y = 0 * X^2 + 0.969 * X + 74.60$$

$$X = 2288$$

$$Y = 2780$$

(R) RURAL ROAD

Good Average Poor
 <4000 4001-5000 >5001

IRI value=2588

Machine ID=384

[Signature]
 20/03/25

[Signature]
 20-3-25
 A-E

MASHRAKH MELA PMWSY ROAD TO MASHRAKH
PURBI TOLA TAK.

Schedule XLV-Form No. 134

Executive Engineer
Rural Works Department
Works Division Marhaura

DIVISION

MashraKh

SUB-DIVISION

RAJU KUMAR SINGH

Measurement Book

1024

1st & final Bill

1

Name of work—

Situation of work—

Agency by which work is executed—

Date of measurement—

No. and date of agreement.

(These four lines should be repeated at the commencement of the measurements relating to each work.)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of work:- Const. of Road from					
"Mashraikh mela pmgsy Road TO					
Mashraikh Purbi tola tar (mmgsuy					
Agency :- Raju Kr Singh.					
Agreement No:-					
Agreement Value:-					
Date of Start:-					
Date of Compl:-					
Date of Entry:- 28/09/2025					

1) Clearing & Grubbing Rd					
Landel — do —					
$2 \times 22 \text{ mtr} \times 30.0 \times 0.75 = 990.0 \text{ m}^2$					
$2 \times 10 \text{ mtr} \times 0.75 = 15.0 \text{ m}^2$					
Total = 1005.0 m ²					
So $\frac{1005.0}{10000} = 0.0101 = 1.01 \text{ Hect}$					
2) Const. of Granular Sub. Base (G.S.B.)					
by P/V well graded material					
Spreading — do —					
$2 \times 3.36 \times 0.43 \times 0.175 = 1.2128 \text{ m}^3$					
$4 \text{ mtr} \times 2.96 \times 1.01 \times 0.175 = 2.093 \text{ m}^3$					
$5 \text{ mtr} \times 3.20 \times 1.06 \times 0.175 = 2.968 \text{ m}^3$					

Continuation Total = 6.273 m³

Limit Qty = 6.272 m³

[Signature]
28/09/25
JE

ABSTRACT OF COST

7

Sch. XLV—Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
1) Clearing & Grubbing Rd Land		do			
Qty = 1.01 Hect. (vide TMB, Pg-1)					
@ 76,926.08 Rs/Hect.					Rs 777020
2) Const. of Sub-grade & Earthwork					
Shoulder		do			
Qty = 203.95 m ³ (vide TMB, Pg-5)					
@ 264.72 Rs/m ³					Rs 53,99020
3) Const. of Granular Sub-Base with well graded Material					
(vide TMB, Pg-1)					
Qty = 6.272 m ³ (vide TMB, Pg-1)					
@ 2,792.74 Rs/m ³					Rs 17,51620
4) P.V., Laying, Spreading & Comp. of					
Stone Agg. (vide TMB, Pg-2)					
Qty = 4.545 m ³ (vide TMB, Pg-2)					
@ 6,214.0 Rs/m ³					Rs 28,24320
5) P.V., Laying, Spreading & Comp. of					
Stone Agg. (vide TMB, Pg-3)					
Qty = 13.155 m ³ (vide TMB, Pg-3)					
@ 5,651.14 Rs/m ³					Rs 74,34120
6) Const. of Dry lean cement concrete					
Concrete		do			
Qty = 2.025 m ³ (vide TMB, Pg-3)					
@ 5,662.19 Rs/m ³					Rs 11,46620
7) Const. of Panel Concrete with (M-30) concrete					
Concrete		do			
Qty = 128.67 m ³ (vide TMB, Pg-4)					
Qty = 188.47 m ² (vide TMB, Pg-4)					
Total Qty = 317.16 m ³ Continuation					
@ 9681.78 Rs/m ³					Rs 30,70,67320

Sch. XLV—Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
8) Kilometre Stone					
$Qty = 2.0 \text{ No}$ (vide TMB, Pg-5)					
@ 3,021.78 Rs/No					Rs 6,044.20
9) 200 mm Stone					
$Qty = 3.0 \text{ No}$ (vide TMB, Pg-5)					
@ 832.99 Rs/No					Rs 2,499.20
10) Direction & Place Identification					
$Qty = 2.88 \text{ m}^2$ (vide TMB, Pg-5)					
@ 15,063.02 Rs/m ²					Rs 43,381.20
11) Retro-Reflective Traffic Signs					
(i) 600 mm equl & Triangle					
$Qty = 4.0 \text{ Nos}$ (vide TMB, Pg-6)					
@ 4,487.28 Rs/No					Rs 17,949.20
(ii) 600 mm Circular					
$Qty = 1.0 \text{ No}$ (vide TMB, Pg-6)					
@ 4358.10 Rs/No					Rs 4358.20
(iii) 600 mm x 450 mm Rectangular					
$Qty = 1.0 \text{ No}$ (vide TMB, Pg-6)					
@ 4213.57 Rs/No					Rs 4214.20
(iv) 900 mm Side Octagon					
$Qty = 1.0 \text{ No}$ (vide TMB, Pg-6)					
@ 8,682.94 Rs/No					Rs 8,683.20
12) Road marking with hot Applied thermoplastic Compound					
$Qty = 134.0 \text{ m}^2$ (vide TMB, Pg-6)					
@ 988.82 Rs/m ²					Rs 1,32,502.20

Continuation

[illegible]

Continuation
