

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, त्रिवेणीगंज।

पत्रांक1595...../त्रिवेणीगंज,
प्रेषक,

दिनांक ...18.08.2025/

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, त्रिवेणीगंज।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह- सचिव,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय :- MR-3054 (New Maintenance Policy-2018) योजनान्तर्गत राशि विमुक्ति हेतु
अधियाचना समर्पित करने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि MR-3054 (New Maintenance Policy-2018) योजनान्तर्गत अधियाचना इस पत्र के साथ संलग्न विहित प्रपत्र में तैयार कर समर्पित की जा रही है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

विश्वासभाजन

(Signature)
कार्यपालक अभियंता

ग्रामीण कार्य विभाग

कार्य प्रमंडल, त्रिवेणीगंज।


(Signature)
14.8.25

Rural Works Department

Requisition Format for Scheme Head- MR (3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Division :- Triveniganj


S. No	Package No	Name of Road	Project ID as per MIS	Administ rative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (In Lacs)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (In mm/km)	Thicknes s of Bitumen Layer (In mm)	Value of Bitumen Content in Percenta ge	Previous Total Alloted Amount (in Lakh)	Up-to-date expenditure as per MIS (In Lakh)	Requisition against work done (In Lakh)	Remarks
					Length (in Km.)	Amount of (In Lacs)	Initial Rectification and Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/23-24-TRIVENIGA NJ/06.	L059- Triveniganj Pratapganj PWD Road to Yadav Tola Oriaha. (ODR34)	21005102029	1086 01.03.24	1.600	81.31	77.87632	11.96983	08 MBD/MR-3054-2024-25 12.11.24	15.11.2025	Complete	3434	25	5.01	0.00000	0.00000	49.09636	
2		Raghunath PWD No-42 to Mehta Tola Ward No-04 tak.	21005112028		0.860	62.89	84.13886	15.41588			Complete	3366	25	5.01	0.00000	0.00000	54.01122	
3		Jadia Anil Mehta Kamat ke ghar to Nahar Par kar Sharma Tola Tak.	21005112035		1.930	87.93	56.42207	5.19419			Complete	3508	25	5.01	0.00000	0.00000	54.96618	
Total					4.390	232.130	218.43725	32.57990							0.00000	0.00000	158.07376	


 Executive Engineer
 R.W.D. (W.D.) Triveniganj


FORM GFR - 19 - A
(See Government of India's Decision (i) below Rule - 150)
Form of Utilization Certificate up to 14.08.2025
(Programming Fund)

Sl. N.	Name of Scheme	Sanction No. & Date with Amount (in Lac.)	Total Amount Received (in Lac.)	Particulars
1	2	3	4	5
1.	Construction of Rural Road under MR-3054 (Bihar Rural Road Maintenance Policy)	Total Allotment received vide Secretary-cum-Empowered Officer BRRDA, Additional CEO, Patna. Letter No-69 Dated-06.05.2024	Rs- 12414.85452	Total Allotment Rs.- 12414.85452 Lakh CFMS Expenditure Rs.- 12254.01022 Lakh Balance Rs.- 160.84430 Lakh
		Total	12414.85452	
2.	Certified that I have satisfied myself that the condition on which the grants in aid sanctioned have been duly fulfilled / are being fulfilled and that I have Exercised the following Checks to see that the money was actually utilized for the purpose for which it was sanctioned . i) Works have been supervised by Executive Engineer / Superintending Engineer. ii) Periodical inspection has been conducted by A.E. / Executive Engineer / Superintending Engineer. iii) Construction materials have been tested. iv) Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer / Executive Engineer. v) All other Codal formalities have been observed.			


Sr. D.A.O.
RWD, Works Division, Triveniganj


Executive Engineer
RWD, Works Division, Triveniganj
14.8.25

Analyzer

Name of Customer : RKS Engicon PVT LTD
 Name of Work/ Road : 142 Mehta toal Ward No -04 tak
 Lab Job number : 01
 Date : 01-08-2025
 Section No. : 76

Test Date : 01-08-2025 Road Name : Raghunathpur PWD N042 Meh
 Machine No : 491 Road Type : (R) RURAL ROAD
 Start S No : Side : 1
 Start E No : Interval
 Weather : UIV Range : 1888 To 4000 1000 mm/km
 Start Location : PWD Dist Range : 0 To 1 0.1 * 1000 m
 End Location : Ward No 04 Equation : test

Print

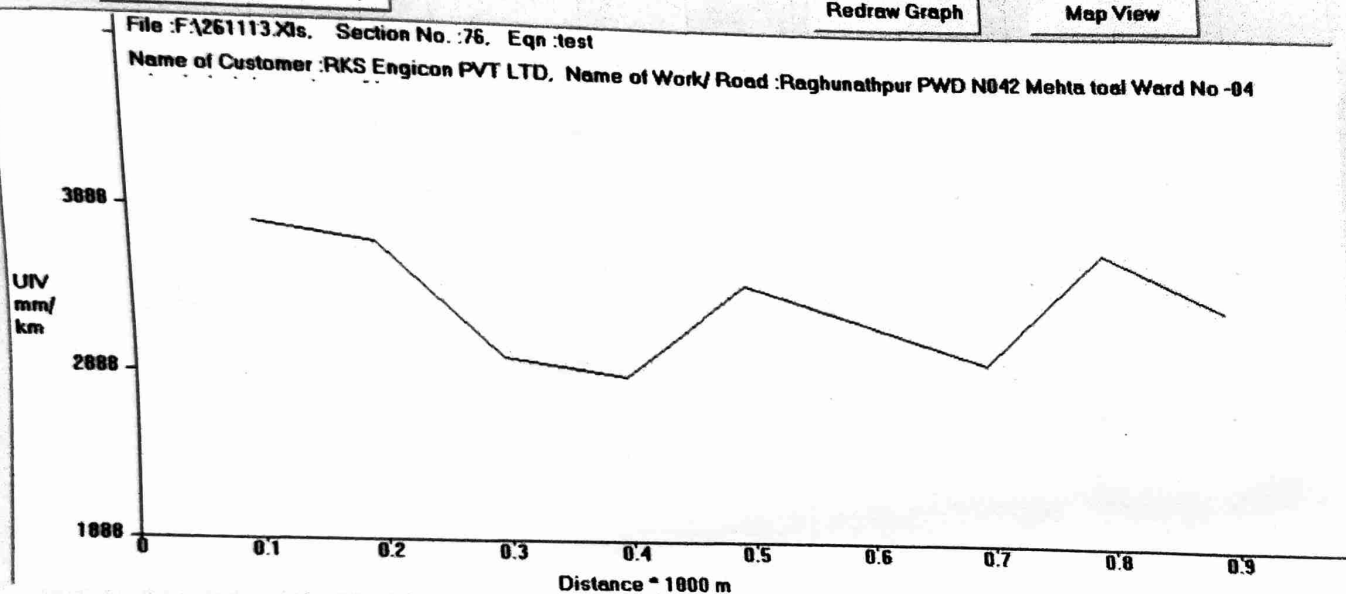
Generate Report and Graph

Redraw Graph

Map View

File : F:\261113.Xls, Section No. : 76, Eqn : test

Name of Customer : RKS Engicon PVT LTD, Name of Work/ Road : Raghunathpur PWD N042 Mehta toal Ward No -04



13/8/25
 3.5

13/8/25
 A-E

14/8/25

Name of Raod:-Raghunathpur PWD N042 to Mehta tola Ward O-04 tak

Name of Contractor's:- RKS Engicon PVT. LTD.

		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
01/08/25	13:39:0	76	0.1	330	0	3300	3571	G	26.102973	87.037585	Normal
01/08/25	13:39:0	76	0.1	350	30.3	3500	3798	G	26.103231	87.037598	Normal
01/08/25	13:39:31	76	0.1	340	30.3	3400	3684	G	26.102323	87.0374	Normal
01/08/25	13:40:0	76	0.1	280	20.2	2800	3002	G	26.101444	87.037527	Normal
01/08/25	13:40:6	76	0.1	270	30.3	2700	2888	G	26.100391	87.037083	Normal
01/08/25	13:40:41	76	0.1	320	20.2	3200	3457	G	26.100398	87.037059	Normal
01/08/25	13:41:0	76	0.1	300	20.2	3000	3230	G	26.0973	87.036368	Normal
01/08/25	13:41:16	76	0.1	280	30.3	2800	3002	G	26.096614	87.036736	Normal
01/08/25	13:41:52	76	0.1	340	30.3	3400	3684	G	26.102323	87.0374	Normal
01/08/25	13:42:12	76	0.1	310	20.2	3100	3343	G	26.095527	87.037226	Normal
					Average IRI=		3365.9				

$$Y = 0 * X^2 + 0.998 * X + 109.5$$

$$X = 3700$$

$$Y = 4025$$

(R) RURAL ROAD

Good Average Poor
 <4000 4001-5000 >5001

[Signature]
 13/8/25

[Signature]
 13/8/25
 A-E

[Signature]
 14/8/25

(MR-3054)

Raghunath PWD No-42 to Mehta tola ward No-04 Tak

Schedule XLV-Form No. 134

Executive Engineer
RWD (W) Divn. Triveniganj

DIVISION

Triveniganj

SUB-DIVISION

RKS Bogicon Pvt Ltd.

MB NO-1145

MEASUREMENT BOOK

Schedule PLV-Form No. 134

NOTES

REFERENCE TO P.W.A CODE CHRI. VII

Paras 30 & 31

In recording detailed measurements, the following general instruction should be carefully observed :—

- [a] Subject to such subsidiary orders as may be laid down by the local Government detailed measurement should be recorded only by Executive of Assistant Engineer or by Executive subordinate in-charge or work to whom measurement book have been supplied to the Executive Engineer for the purpose :
- [b] All measurements should be neatly taken down in a measurement book Form 23, issued for the purpose in where else.
- [c] Each set of measurement should commence with entries stating—
 - [i] In the case of bills for work done :—
 - (a) Full name of work as given in estimate.
 - (b) Situation of work (c) Name of contractor.
 - (c) Number and date of his agreement, and
 - (d) Date of measurement.
 - [ii] In the case of bills for supply of materials :—
 - [a] Name of supplier,
 - [b] Number and date of his agreement for order
 - [c] Purpose of supply in one of the following forms applicable to the case—
 - [i] "Stock" (for all supply for stock purpose)
 - [ii] "Purchase for direct issue to the work (full name of work as given in estimate may be mentioned)
 - [iii] "Purchases" or (full name of work as given in estimate) issued to contractor.....on.....and

- [d] Date of measurements and should end with the dated initials of the officer marking the measurement, (See all paragraph 25)

A suitable abstract should than be prepared which/ Should collect in the case of measurements for work done the total quantities of each district item of work relating to each sanctioned Sub-head.

- [e] As all payment for work suppliers based on the quantities recorded in the measurement book it is incumbent upon the person taking the measurements to record the quantities clearly and accurately. If measurements are taken in connection with a running contract account on which work has been previously measured he is further responsible (1) that reference to the last set of measurement is recorded and (2) that if the entire job or contract has been completed the fact is recorded prominently just above his initials.
- [f] Entries should be record continuously in the measurement book No, blank pages may be left and no page be turn out. any page left blank in advertently must be cancelled by diagonal lines, The cancellation being attested, See also paragraph 335 or the public Work Department Code.
- [g] No entry may be erased, of a mistake is made it should be correct (and deleted) by the responsible officer in the manner prescribed in paragraph 335 of the Public Work Department Code. When any measurements are cancelled, the cancellation must be supported by the dated initials of the officer ordering the cancellation or by a reference to his measurements in either case the reason for cancellation should be recorded.

Each measurement book should be provided with an index which should be kept up to date.

1st on A/C Bill

1.

Name of work -

Situation of work -

Agency by which work is executed -

Date of measurement -

No. and date of agreement.

(These four lines should be repeated at the commencement of the measurements relating to each work).

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of work →	Raghunath PWD				
No. 42 To Mehla Tola					
Ward No. 4 Tak.					
Agency →	RKS Engkon Pvt Ltd.				
Agreement No. →	08/ABD/2024-25				
Date of Commencement →					
Date of Completion →					
RECORD-ENTRY					

(1/1) Clearing & Grubbing
Road land (By
manual means)
— Do — E5 —

2 Nos x 15 Nos x 30.0m x 1.0m = 900m²
2 Nos x 15 Nos x 30.0m x 1.0m = 900m²
2 Nos x 10 Nos x 30.0m x 1.0m = 600m²
2 Nos x 14 Nos x 30.0m x 1.0m = 840m²
2 Nos x 10 Nos x 30.0m x 1.0m = 600m²
2 Nos x 1 Nos x 10.0m x 1.0m = 20m²

Total = 3860m²
Say = 0.386 Ha.

Continuation

Sch.XLV-Form No. 134

Particulars	Details of actual measure				Contents of area
	No.	L.	B.	D.	
(2/9)	Construction of dry lean cement concrete				
	— Do — Et —				
	1 Nos	3.13 m	1.39 m	0.1 m	$0.43 m^3$
	3 Nos	3.29 m	1.51 m	0.1 m	$1.49 m^3$
	1 Nos	2.81 m	1.43 m	0.1 m	$0.40 m^3$
	4 Nos	3.93 m	1.26 m	0.1 m	$1.98 m^3$
	2 Nos	3.13 m	1.41 m	0.1 m	$0.88 m^3$
	1 Nos	2.89 m	1.33 m	0.1 m	$0.384 m^3$
	4 Nos	4.85 m	1.21 m	0.1 m	$1.96 m^3$
	2 Nos	2.59 m	1.53 m	0.1 m	$0.818 m^3$
	3 Nos	1.98 m	1.52 m	0.1 m	$0.90 m^3$
	2 Nos	1.8 m	1.4 m	0.1 m	$0.504 m^3$
	2 Nos	2.60 m	1.50 m	0.1 m	$0.78 m^3$
	Total qty =				$10.526 m^3$
	Limit to =				$10.463 m^3$
(3/9)	Construction of Panel concrete				
	Pavement (PCC) M30				
	— Do — Et —				
	1 Nos	10 Nos	30.0 m	3.75 m	$1125 m^2$
	1 Nos	10 Nos	30.0 m	3.75 m	$1125 m^2$
	1 Nos	10 Nos	30.0 m	3.75 m	$1125 m^2$
	1 Nos	1 Nos	30.0 m	3.75 m	$112.5 m^2$
					$3487.5 m^2$

Continuation

[illegible]

Continuation

ABSTRACT OF COST

4

Sch.XLV-Form No. 134

Particulars	Details of actual measure				Contents of area
	No.	L.	B.	D.	
(1/1) Clearing and grubbing Road and (By Manual means)					
	—	DO	—	ET	—
Qty. Vide TMBP - (1)					
	$0.386 \text{ Ha} @ \text{Rs } 76926.08 / \text{Ha} = \text{Rs } 29693.00$				
(2/8) Construction of dry lean cement					
	—	DO	—	ET	—
Qty. Vide TMBP - (2)					
	$10.463 \text{ m}^3 @ \text{Rs } 6538.52 / \text{m}^3 = \text{Rs } 68,413.00$				
(3/9) Construction of Panel Concrete Pavement (PCC)					
	—	DO	—	ET	—
Qty. Vide TMBP - (2) & (3)					
	$435.93 \text{ m}^3 @ \text{Rs } 10470.53 / \text{m}^3 = \text{Rs } 45,64418.00$				
	$\text{Rs } 46,2524.00$				
Add 18% GST = (+)	$\text{Rs } 83,39254.00$				
Add 1% - License = (+)	$\text{Rs } 46628.00$				
Add S. Fee = (+)	$\text{Rs } 47455.00$				
	$\text{Rs } 55,95858.00$				

Continuation

[illegible]
