

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, समस्तीपुर
e-mail- eerwdsamastipur@gmail.com

पत्रांक 2732 (अप्र) दिनांक 02/12/2025

प्रेषक:- कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, समस्तीपुर।

सेवा में,
अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय:- शीर्ष RRSMP (SC) मद में आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषयक शीर्ष RRSMP (SC) योजनान्तर्गत निर्मित/निर्माणाधीन पथों का विहित प्रपत्र में अधियाचना पत्र संलग्न कर भेजा जा रहा है।

अतः अनुरोध है कि संलग्न अधियाचना पत्र के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय।

अनु0-यथोक्त।

विश्वासभाजन

कार्यपालक अभियंता

ग्रामीण कार्य विभाग

कार्य प्रमंडल, समस्तीपुर

GFR 12-B

[See Rule 256(2)]


FORM OF UTILIZATION CERTIFICATE

(1) Certified that out of the Loan of Rs.456640229.00, Sanctioned under RRSMP(SC) Letter No. 97 dated 04.11.2025, in favor of EXECUTIVE ENGINEER, RURAL WORKS DEPARTMENT, WORKS DIVISION, SAMASTIPUR, during the year 2025-26, an amount of Rs. 456639058.00, has been utilized for the purpose for which it was sanctioned, and that the balance of Rs. 1171.00, remaining unutilized till date year 2025-26.

(2) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.

Kinds of checks exercised

- 1
- 2
- 3
- 4

16-12-2025
2-12-2025

Executive Engineer
RWD, Works Division
Samastipur

Requisition Format for Scheme MMGSUY/RRSMP (SC)

Name of the Works Division :- Samastipur

Sl. No.	Package No.	Project ID as per MIS	Name of Road	AA Length (in km.)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WBM/WM/ BM/SDBC etc.)	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allocated Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RRSMP/24-25 Samastipur/04	6201010300028	T04 Dhabhar to Jagdishpur Tak	1.080	66.604	51.71921	01(CMBD)2025-26 dt.25.04.2025	24.04.2026	-	PCC	2787	25	5.0	29.830	29.830	36.810	6.98031	Complete
2		6201010300011	T01 Sankar Chowk To Gopalpur Harjan Tola Hote Hue Gopalpur Garh Tola Tak	2.740	185.882	140.55722			-	PCC, BT	2858	25	5.0	100.776	100.776	106.707	5.93101	Complete
3		6201010300024	L046-X Road L045 to Garha (ODR46)	0.700	77.353	59.83992			-	PCC	2856	25	5.0	44.936	44.926	48.715	3.78850	Complete
4		6201010300016	Balika High School Rampur To Rampur Utrari Tola Via Dih tola Malha tola	2.030	130.895	98.19190			-	PCC, BT	2887	25	5.0	60.108	60.108	75.606	15.49782	Complete
5		6201010300033	L063-SH to Madhurabpur (ODR63)	0.880	58.325	46.79623			-	PCC	2916	25	5.0	19.54621	19.54621	44.340	24.99379	Complete
6		6201010300036	T06 to BASWARI	0.780	57.039	42.28674			-	PCC		25	5.0	35.420	35.420	40.388	5.16806	Complete
7		6201010300039	Dukharan chowk to Panchayat bhawan tak	0.500	27.689	22.13284			-	PCC	3097	25	5.0	17.362	17.362	20.567	3.20539	Complete
8		6201010300012	Mukhay sadak MMGSY Yogi Rai ke ghar to Balha hat tak	2.570	164.16	124.41535			-	PCC, BT		25	5.0	83.207	83.207	96.838	13.63177	Complete
9		6201010300023	L057-X Road L055 to Ojha Tola (ODR56)	1.160	78.366	63.31631			-	PCC, BT	2892	25	5.0	54.264	54.264	60.702	6.43790	Complete
10		6201010300025	Panchkhutta chowk to Kabristan tak	1.250	75.753	59.30888			-	PCC, BT	2869	25	5.0	50.753	50.753	56.458	5.70569	Complete
11		6201010300007	Repair of road from Saidpur Chaulk to Baswan Village	1.570	240.313	175.29862			-	PCC, BT		25	5.0	125.749	125.749	170.375	44.62652	Complete

Sl. No.	Package No.	Project ID as per MIS	Name of Road	AA Length (in km.)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WBM/WMM/BM/SDBC etc.)	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allotted Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
12	RRSMP/24-25 Samastipur/04	6201010300013	Repair of road from Varsinghpur Chauk to Jhauri Ghat	0.920	140.14600	121.15656	01(CMBD)/2025-26 dt.25.04.2025	24.04.2026	-	PCC, BT		25	5.0	71.334	71.334	119.119	47.78509	Complete
13		6201010300018	Pvd Karia Chowk Sa to Haralgan Tola	2.100	109.72100	86.54049			-	PCC, BT	3046	25	5.0	73.556	73.556	81.788	8.23258	Complete
14		6201010300029	SH50 to Jamalpur Tira Panchayat	0.920	62.80100	50.79988			-	PCC, BT	2836	25	5.0	44.202	44.202	48.812	4.60965	Complete
15		6201010300045	Kalyanpur chowk to Madhuban(Kishanpur Rlystation)	5.020	1042.18900	928.67840			-	PCC, BT	2673	25	5.0	314.749	314.749	812.146	497.39768	Complete
16	RRSMP/24-25 Samastipur/05	6201010300022	SH to Bhagwanpur middle school	1.300	80.632	59.71793	02(CMBD)/2025-26 dt.05.05.2025	04.05.2026	-	PCC, BT	2823	25	5.0	40.144	40.144	45.558	5.41387	Complete
17		6201010300021	L050-SH to Gopalpur (ODR50)	1.300	85.285	72.43856			-	PCC, BT	2798	25	5.0	59.051	59.051	64.614	5.56247	Complete
18		6201010300037	X ROAD L029 to RAMBHADRAPUR	0.740	48.589	39.92969			-	PCC	2872	25	5.0	35.034	35.034	38.290	3.25557	Complete
19		6201010300034	L028-SH to Bakhari (ODR28)	0.840	56.833	45.74561			-	PCC	3035	25	5.0	38.687	38.687	43.719	5.03200	Complete
20		6201010300027	L072-SH to Belsandi (ODR72)	1.120	73.591	59.69544			-	PCC, BT	2981	25	5.0	53.584	53.584	56.961	3.37697	Complete
21		6201010300019	Rambhadrapur Railway Station Ke Njdik To Islampur	1.600	105.445	80.16356			-	PCC, BT	2775	25	5.0	52.713	52.713	59.407	6.69391	Complete

Alumina
9.12.2025

Divisional Accounts Officer
RWD, Works Division Samastipur


Alumina
20.11.25

Executive Engineer
RWD, Works Division Samastipur

अधियाचना हेतु प्रमाण पत्र

प्रमाणित किया जाता है कि R.R.S.M.P.(S.C.) योजनान्तर्गत :-

1. पथ/पुल L063-SH to Madhwaripur (O.D.R-63) में कराये गये कार्य की गुणवत्ता जाँच की गयी है जो निर्धारित मानक/विशिष्टियों के अनुरूप है।
2. अद्यतन कराये गये कार्य की मापी संबंधित मापी पुस्तिका में दर्ज है जिसका सत्यापन कर लिया गया है।


13/11/25
कनीय अभियंता
ग्रामीण कार्य विभाग
कार्य प्रशाखा, कल्याणपुर


13/11/25
सहायक अभियंता
ग्रामीण कार्य विभाग


24/11/25
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल, कल्याणपुर कार्य प्रमंडल, समस्तीपुर

Name of Customer : Anjan Kumar
 Name of Work/ Road : L063 - SH to Madhurabpur (OD)
 Lab Job number : 30
 Date : 10-09-2025
 Section No. : 30

Test Date : 10-09-2025
 Machine No : 396
 Start S No :
 Start E No :
 Weather :
 Start Location :
 End Location :
 Road Name : L063 - SH to Madhurabpur (OD)
 Road Type : (R) RURAL ROAD
 Side :
 UIV Range : 1690 To 4000 mm/km
 Dist Range : 0 To 1 0.1 * 1000 m
 Equation : $Y = 0.0002 \cdot X^2 + 0.959 \cdot X + 74.60$

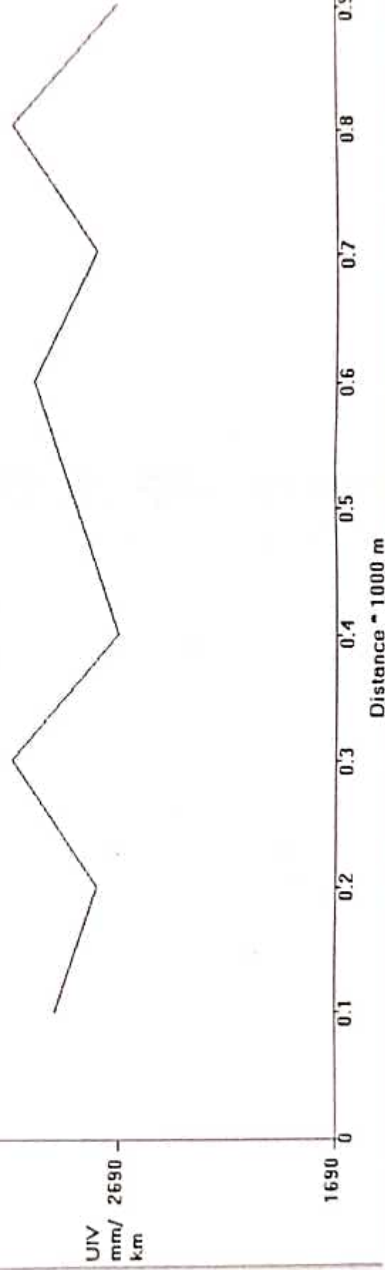
Print

Redraw Graph

Map View

File : E:\Samastipur Division\BUMP DATA\anjan kumar\L063 - SH to Madhurabpur\10092251.Xls, Section No. 30.

Name of Customer : Anjan Kumar, Name of Work/ Road : L063 - SH to Madhurabpur (ODR46), Lab Job number : 30



10/09/25
 Anjan

10/11/25
 Anjan

Lab Job number :30

Date :10-09-2025

Name of Customer :Anjani Kumar

Name of Work/ Road :L063 - SH to Madhurabpur (ODR46)

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	IRI		CATEGORY ROAD	Latitude	Longitude	Event
						mm/km	mm/km				
10/9/25	14:20:21	30	0.1	300	10.1	3000	2981	G	25.976209	85.736135	Normal
10/9/25	14:20:27	30	0.1	280	20.2	2800	2787	G	25.975429	85.73798	Normal
10/9/25	14:21:2	30	0.1	320	10.1	3200	3175	G	25.974612	85.735444	Normal
10/9/25	14:21:2	30	0.1	270	10.1	2700	2690	G	25.973934	85.735091	Normal
10/9/25	14:21:38	30	0.1	290	20.2	2900	2884	G	25.973338	85.735342	Normal
10/9/25	14:22:13	30	0.1	310	10.1	3100	3078	G	25.972811	85.735785	Normal
10/9/25	14:22:13	30	0.1	280	40.4	2800	2787	G	25.972412	85.736656	Normal
10/9/25	14:22:48	30	0.1	320	20.2	3200	3175	G	25.972235	85.737619	Normal
10/9/25	14:22:48	30	0.1	270	10.1	2700	2690	G	25.972235	85.737619	Normal

Total UIV 26247

Average UIV 2916

$$Y = 0 * X^2 + 0.959 * X + 74.50$$

$$X = 2700$$

$$Y = 2690$$

(R) RURAL ROAD

Good Average Poor

<4000 4001-5000 >5001

10/9/25

10/9/25
