

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, समस्तीपुर
e-mail- eerwdsamastipur@gmail.com

पत्रांक 2733(अम) दिनांक. 02/12/25

प्रेषक:- कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, समस्तीपुर।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय:- शीर्ष RRSMP (Gen) मद में आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषयक शीर्ष RRSMP (Gen) योजनान्तर्गत निर्मित/निर्माणाधीन पथों का
विहित प्रपत्र में अधियाचना पत्र संलग्न कर भेजा जा रहा है।

अतः अनुरोध है कि संलग्न अधियाचना पत्र के अनुसार आवंटन उपलब्ध कराने की कृपा
की जाय।

अनु०-यथोक्त।

विश्वासभाजन

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, समस्तीपुर

2-12-2025

GFR 12-B

[See Rule 256(2)]

FORM OF UTILIZATION CERTIFICATE


(1) Certified that out of the Loan of Rs.668885771.00, Sanctioned under RRSMP(Gen.) Letter No.-102 dated 18.11.2025, in favor of EXECUTIVE ENGINEER, RURAL WORKS DEPARTMENT, WORKS DIVISION, SAMASTIPUR, during the year 2025-26, an amount of Rs 658913833.00, has been utilized for the purpose for which it was sanctioned, and that the balance of Rs.9971938.00, remaining unutilized till date year 2025-26.

(2) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.

Kinds of checks exercised

- 1
- 2
- 3
- 4


Executive Engineer
RWD, Works Division
Samastipur


2.12.2025

Requisition Format for Scheme MMGSUY/RRSMP (General)

Name of the Works Division :- Samastipur

Sl. No.	Package No.	Project ID as per MIS	Name of Road	AA Length (in km.)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WBM/WM, M/BM/SDBC etc.)	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allotted Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RRSMP/24-25 Samastipur/10	6201010350060	Maharajan Mukhay marg to State Tubewell Malihpur tak	2.410	156.130	116.72189	27(CMBD)25-26 Dt-13.08.2025	25.09.2026	In Progress	PCC, DLC	-	-	-	-	-	67.93769	67.93769	In Progress
2		6201010350089	Mahaanth Kalishthan House (Sari) To Anandi Lal Ray House (Sari)	1.200	96.243	76.71654				PCC, DLC	-	-	-	-	-	65.05156	65.05156	In Progress
3		6201010350091	Krishti Bazar Samiti Sari to Ramnath Singh House Sari (L045)	1.400	89.721	70.70635				PCC, DLC	-	-	-	-	-	20.54496	20.54496	In Progress
4		6201010350104	RAM NAGAR To SARI TOLE SANICHARI	1.090	69.910	59.45696				PCC, DLC	-	-	-	-	-	51.16049	51.16049	In Progress
5		6201010350132	Sanichura Ashan To U.M. Vidyalaya Begampur Hindi Purab L045	0.600	39.091	33.11119				PCC, DLC	-	-	-	-	-	21.92452	21.92452	In Progress
6		6201010350082	L051-L051 to Kishumpura (VR70)	1.670	108.246	82.237				PCC	-	-	-	-	-	45.77160	45.77160	In Progress
7		6201010350356	Repair of road from T02 Paroriya to Mohiddinpur	6.500	1169.910	1096.167				PCC, DLC	-	-	-	-	-	206.63999	206.63999	In Progress
8	RRSMP/24-25 Samastipur/09	6201010350179	Dharnapur chowk to chakhusin Tak	1.500	90.720	71.134	07(CMBD)25-26 Dt-19.06.2025	28.06.2026	In Progress	PCC	-	-	-	-	-	54.83815	54.83815	In Progress
9		6201010350161	Musapur bhumiur Tola to Sanichura Ashan	0.430	22.03800	17.42731				PCC	-	-	-	1.827	1.827	16.39786	14.57051	In Progress
10		6201010350352	Samastipur to Pusa main road Bela se kon Bajitpur via Punash	8.500	1399.490	1232.665				GSB, WMM, Culvert	-	-	-	44.923	44.923	189.75126	144.82794	In Progress
11	RRSMP/24-25 Samastipur/12	6201010350142	Rahua Panchayat met(S76)Airtel lawar to Rahua Panchayat Nandlal Paswan ke ghar tak	0.500	28.242	22.568	15(CMBD)25-26 Dt-23.07.2025	28.04.2026	In Progress	PCC, DLC	-	-	-	-	-	17.55188	17.55188	In Progress
		6201010350198	Ilmanagar To Kishanpur Railway Station	13.830	2236.076	2080.296				GSB, WMM, Culvert	-	-	-	355.123	355.123	475.07383	119.95130	In Progress



Sl. No.	Package No.	Project ID as per MIS	Name of Road	AA Length (in km.)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WBM, WM, M, BM, SDBC etc.)	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allocated Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
12	RRSMP/25-26 Samastipur/01	6201010350212	RWD Path Hajipurwa Pramod Singh Ke Ghar Se Sonar Toli Tak	0.750	60.347	48.551	09(CNIBD)25-26 Dt-02.07.2025	05.06.2026	In Progress	PCC	3030	25	5.0	-	-	37.34110	37.34110	In Progress
13		6201010350214	RWD path Madanpur Ram Narayan Sah ke Ghar Se PMGSY Path Ganesha Ram ke Ghar Tak	0.420	33.629	27.100				PCC				-	-	21.26725	21.26725	
14		6201010350223	RCD path Hanuman Mandir se Musepur se RWD Path Musepur Tak	0.600	45.174	36.042				PCC	3062	25	5.0	-	-	29.82586	29.82586	In Progress
15	RRSMP/24-25 Samastipur/03	6201010350049	L0576-T02 to Fatehpur Bala (VR56)	2.970	184.534	155.625	22(CMBD)25-26 Dt-29.08.2025	25.04.2026	In Progress	PCC, DLC	-	-	-	-	-	48.04972	48.04972	In Progress
16		6201010350050	L029-T06 to Kasha Ahar (VR29)	2.200	177.494	142.279				PCC, DLC	-	-	-	-	-	77.50537	77.50537	In Progress
17		6201010350052	T06 To Madhopur Digharua via Palghamburpur	2.490	156.225	119.123				PCC, DLC	-	-	-	-	-	61.92614	61.92614	In Progress
18		6201010350059	T02 NH (Bangan Thana) To Kabaull buso ajwa Tak	2.160	138.031	104.357				PCC, DLC	-	-	-	-	-	32.12534	32.12534	In Progress
19		6201010350071	T02 NH Ward no-05 to fatehpur bala ward no-11(Morwa Sima)	1.630	104.016	81.583				PCC, DLC	-	-	-	-	-	9.87528	9.87528	In Progress
20		6201010350074	L045-T02 to Dhi Tola Rahimabad (VR45)	1.660	103.938	80.949				PCC, DLC	-	-	-	-	-	27.46039	27.46039	In Progress
21		6201010350076	L059 Kabir chowk to Bhona chowk Dhibara chowk	1.600	100.774	73.221				PCC, DLC	-	-	-	-	-	69.54077	69.54077	In Progress
22		6201010350078	L044-L044 Anganwari Kendra to Munnichak (VR44)	1.620	100.582	82.941				PCC, DLC	-	-	-	-	-	-	-	In Progress
23		6201010350094	T02 NH To Pasi Tola	0.960	59.460	46.820				PCC, DLC	-	-	-	-	-	-	-	In Progress
24		6201010350097	L049-T02 to Kabaull Baso (VR49)	0.980	56.399	44.837				PCC, DLC	-	-	-	-	-	12.97712	12.97712	In Progress
25		6201010350100	T04 Asari To Musalman Chowk Ward No. 11	0.850	53.410	42.847				PCC, DLC	-	-	-	-	-	23.31314	23.31314	In Progress

Sl. No.	Package No.	Project ID as per MIS	Name of Road	AA Length (in km)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WBM W/M, M BM, SDBC etc.)	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allocated Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
26	RRSMP/25-26 Samastipur/05	6201010350255	Tajpur Sahpur Baghauni RWD Path MD Usaid ke ghar ke nikar se sabhar Tola jane wali sadak	0.300	22.283	18.082	14(CMBD)25-26 Dt-14.07.2025	05.06.2026	In Progress	PCC	-	-	-	-	-	-	11.05275	In Progress
27		6201010350279	NH 28 Rajwa Se Bahadur Nagar	1.200	78.796	63.619					-	-	-	-	-	-	48.09146	In Progress
28	RRSMP/24-25 Samastipur/06	6201010350007	Reeta to Dinmanpur	3.950	273.611	238.642	11(CMBD)25-26 Dt-05.07.2025	28.05.2026	In Progress	PCC, DLC	-	-	-	83.363	83.36275	165.70315	82.34040	In Progress
29		6201010350009	Repair of road from T01 to Khairi	3.100	197.928	152.698					-	-	-	25.361	25.36117	78.71900	53.35783	In Progress
30		6201010350196	Dakuri Chowk To Bishwanathpur	20.450	1729.207	1476.325					-	-	-	0	0	272.42155	272.42155	In Progress
31		6201010350024	L064 Tinbutiya to Kheda Siman	1.230	80.877	61.136					-	-	-	13.298	13.29830	33.51671	20.21841	In Progress
32	RRSMP/24-25 Samastipur/11	6201010350101	L023-T01 to Ganga Tola (VR232)	1.150	75.139	59.662	08(CMBD)25-26 Dt-25.06.2025	24.04.2026	In Progress	PCC	-	-	-	42.421	42.421	56.77374	14.35236	In Progress
33		6201010350121	Dasur Indal Paswan ke Ghar to L022 Ram Biksh Gupta ke Ghar Tak	0.660	49.127	39.789					-	-	-	26.569	26.569	38.22793	11.65864	In Progress
34		6201010350138	Dasur Math me rampur paswan ke ghar to Dasur math trinuhani tak	0.500	33.525	27.052					-	-	-	20.834	20.834	25.97694	5.14336	In Progress
35		6201010350056	BHADEN TO BASANTPUR RAMAN	2.560	185.882	165.146					-	-	-	64.633	64.63271	90.56082	25.92811	In Progress



Sl. No.	Package No.	Project ID as per MIS	Name of Road	AA Length (in km)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WBM W/M M/BM SDBC etc.)	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allocated Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
36	RRSMP/24-25 Samastipur/11	6201010350197	Repair of Road from Sainulpur To Lavhatta Nakla	12.100	137.897	1653.322	08(CMBD)25-26 Dt-25.06.2025	24.04.2026	In Progress	Box cutting, GSB,WMM	-	-	-	481.799	481.799	733.44965	251.65099	In Progress
37		6201010350079	Lavhatta Chowk To Lavhatta	1.550	111.644	89.014				PCC	-	-	-	66.128	66.128	78.45304	12.32517	In Progress
38		6201010350126	T03 Belahi uchayn vidyalay To Raj ratan singh ke ghar tak	0.700	42.957	34.109				PCC	-	-	-	24.535	24.535	28.90506	4.37042	In Progress
		6201010350122	Purnabi Puchhim Tola me Ramlagan Mahito House To Ram Sundar House	0.900	48.673	38.904				PCC	-	-	-	29.722	29.722	35.33398	5.61205	In Progress
39		6201010350062	Sainulpur Chowk Laxmi Mahito Ke Ghar to Hanuman Chowk	2.260	144.967	110.962				PCC	-	-	-	74.825	74.825	82.98639	8.16165	In Progress
40	RRSMP/24-25 Samastipur/08	6201010350174	L039 se to Ramchandra Ram	1.700	105.409	78.175	16(CMBD)25-26 Dt-26.08.2025	26.06.2026	In Progress	PCC	-	-	-	-	-	45.83940	45.83940	In Progress
41		6201010350188	Ramnathpur Chowk to Salmi Tola via Danda Chowk	1.200	69.617	53.793				PCC	-	-	-	-	-	21.04187	21.04187	In Progress
42		6201010350194	In Korbadda village Shiv Mandir to Talma tola via Ram Jatan Mahito house	1.000	60.996	50.162				PCC	-	-	-	-	-	36.07160	36.07160	In Progress
43	RRSMP/25-26 Samastipur/04	6201010350201	Sobhit Sah ke Ghar se Sambhupatti Post Office tak	0.450	33.596	27.202	26(CMBD)25-26 Dt-19.09.2025	12.08.2026	In Progress	PCC	-	-	-	-	-	19.52035	19.52035	In Progress

Neeraj
2.12.2025

Divisional Accounts Officer
RWD, Works Division Samastipur


[Signature]
22/12/25
Executive Engineer
RWD, Works Division Samastipur



31/10/25
Ravi Ranjan Kumar
JE Kasimpur

31/10/25
Ravi Ranjan Kumar

31/10/25
Ravi Ranjan Kumar

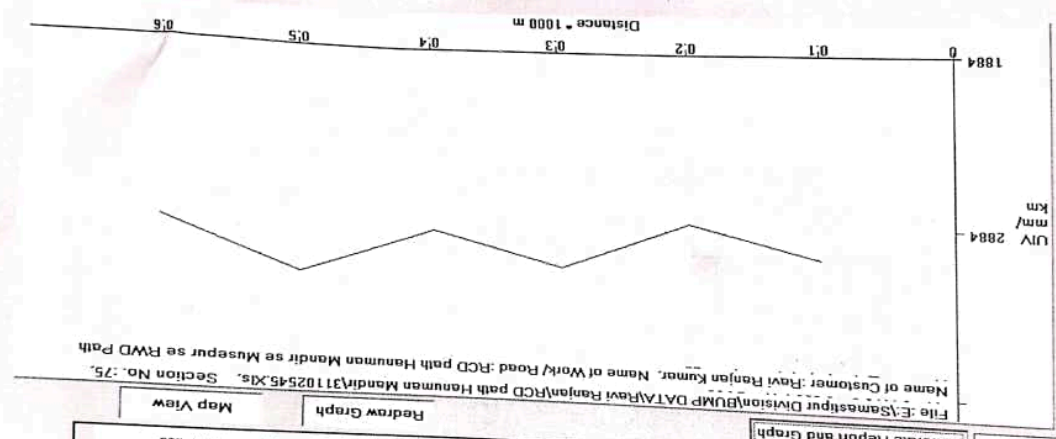

Test Date :	31-10-2025	Road Name :	RCD path Hanuman Mandir se
Machine No :	396	Road Type :	(R) RURAL ROAD
Start S No :		Side :	
Weather :		U/V Range :	1884 To 4000
Start Location :		Dist Range :	0 To 0.1
End Location :		Equation :	$Y = 0.0000X^2 + 0.969X + 74.60$
		Interval	mm/km
			1000
			* 1000 m

Name of Customer :	Ravi Ranjan Kumar
Name of Work :	RCD path Hanuman Mandir se Musepur se RWD Path
Lab Job number :	75
Date :	31-10-2025
Section No. :	75

Lab Job number :75

Date :31-10-2025

Name of Customer :Ravi Ranjan Kumar

Name of Work/ Road :RCD path Hanuman Mandir se Musepur se RWD Path Musepur Tak

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	IRI		CATEGORY ROAD	Latitude	Longitude	Event
						mm/km	mm/km				
31/ 10/ 25	17: 13: 27	75	0.1	310	0	3100	3078	G	25.885163	85.781428	Normal
31/ 10/ 25	17: 13: 27	75	0.1	290	30.3	2900	2884	G	25.886028	85.781082	Normal
31/ 10/ 25	17: 14: 2	75	0.1	320	10.1	3200	3175	G	25.886575	85.780697	Normal
31/ 10/ 25	17: 14: 2	75	0.1	300	10.1	3000	2981	G	25.887798	85.78083	Normal
31/ 10/ 25	17: 14: 38	75	0.1	330	20.2	3300	3272	G	25.888302	85.78119	Normal
31/ 10/ 25	17: 15: 13	75	0.1	300	10.1	3000	2981	G	25.888468	85.781275	Normal

Total UIV 18371
Average UIV 3062

$$Y = 0 * X^2 + 0.969 * X + 74.60$$

$$X = 3000$$

$$Y = 2981$$

(R) RURAL ROAD

Good <4000 Average 4001-500 Poor >5001

Arif
31/10/2024
JE Kalyanpur-01

31/10/25
AE

31/10/25

अध्याचना हेतु प्रमाण पत्र

प्रमाणित किया जाता है कि RRSMP (GEN) योजनान्तर्गत :-

1. प्रथम/पुल RCD Path Hanuman Mandir Se Murepur Se में कराये गये कार्य की गुणवत्ता जाँच की गयी है जो निर्धारित मानक/विशिष्टियों के अनुरूप है।
RWD Path Murepur Tal
2. अद्यतन कराये गये कार्य की मापी संबंधित मापी पुस्तिका में दर्ज है जिसका सत्यापन कर लिया गया है।

अमित
31/10/2024
कनौज अभियंता

ग्रामीण कार्य विभाग
कार्य प्रशाखा, कलमणपुर-01

SKS
31/10/2024
सहायक अभियंता

ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल, कलमणपुर

Ph
31/10/24
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, समस्तीपुर
