

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, गोपालगंज-1

पत्रांक:- 2066 अ.क.

/ गोपालगंज

दिनांक:- 09 / 12 / 2025

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, गोपालगंज-1

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार, पटना।

विषय:- शीर्ष RRSMP (General) अन्तर्गत में अधियाचित राशि का आवंटन उपलब्ध कराने के संबंध में।


महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि शीर्ष RRSMP (General) अन्तर्गत राशि की माँग संलग्न विहित प्रपत्र में पथवार की जा रही है।

अतः भवदीय से अनुरोध है कि विहित प्रपत्र के कॉलम-18 में अंकित कुल राशि का आवंटन उपलब्ध कराने की कृपा की जाय। अधियाचित राशि के संदर्भ में C & P किये मापी पुस्तिका की छाया प्रति, एवं उपयोगिता प्रमाण-पत्र संलग्न कर आवश्यक कार्रवाई हेतु समर्पित किया जा रहा है।

अनु०-यथोक्त।

विश्वासभाजन



कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, गोपालगंज-1

68-12-25

Requisition Format for Scheme RRSMP (General)

Name of the Works Division :- Gopalganj-1

Sl. No.	Package No.	Project ID as per MIS	Name of Road	AA Length (in km.)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WB/M/W MM/ BM /SDBC etc.)	Value of IRI (in mm/ km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Amount Allotted (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RRSMP/24/25 Gopalganj-1/05	5140690350048	PMGSY Road to Karmaini Gaji Pandey tola (Uttar tola)	1.350	60.700	61.31678	04/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	25.10.2025	SDBC	2184.35	25	5.03	37.62389	37.62389	44.67783	7.05394	
2	RRSMP/24/25 Gopalganj-1/05	5140690350044	Sipaya Polytechnic to Roop Chhap	1.000	54.250	54.81048	04/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	25.10.2025	SDBC	2163.40	25	5.02	32.69693	32.69693	39.72123	7.02430	
3	RRSMP/24/25 Gopalganj-1/05	5140690350077	PWD Road Kuchakote to Barwa tola	3.300	154.190	156.16417	04/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	18.11.2025	SDBC	2124.96	25	5.02	50.81540	50.81540	112.67410	61.85870	
4	RRSMP/24/25 Gopalganj-1/05	5140690350040	Balwanwa NH-28 to Balwanwa	0.850	39.690	40.05753	04/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	18.11.2025	SDBC	2698.66	25	5.02	17.05256	17.05256	30.45714	13.40458	
5	RRSMP/24/25 Gopalganj-1/05	5140690350051	Belwa Briti Middle School to Ghoda Chat Lalbegi	1.600	94.560	95.64389	04/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	12.11.2025	SDBC	2398.25	25	5.01	37.80983	37.80983	67.61204	29.80221	
6	RRSMP/24/25 Gopalganj-1/06	5140690350049	PMGSY Road Gopalpur to Rampur Bhaishahi Chaudhari Tola	1.500	71.600	72.56905	07/CMBD (MMGSUY)2 025-26 dt. 20.05.2025	19.05.2026	-	SDBC	2740.93	25	5.02	0.00000	0.00000	52.39926	52.39926	

It is certified that Physical & Financial Progress has been updated in MIS.

Note :-

- 1 Above Signed Copy along with Forwarding Letter & Utilisation Certificate must be uploaded in MIS.
- 2 Signed Hard Copy and Soft Copy of recorded IRI is enclosed (As Applicable).

R.W.D. Works Division
Gopalganj-1

[Signature]
D.A. 8/12/25

Executive Engineer
R.W.D. Works Division
Gopalganj-1
08/12/25

[Signature]
08/12/25

GFR 12-B

[See Rule 256 (2)]

FORM OF UTILIZATION CERTIFICATE

(1) Certified that out of the Loan of Rs.468206853.00 Sanctioned under MMGSUY/RRSMP GEN dated 08.12.2025, in favour of Executive Engineer, RWD Works Division Gopalganj-1, during the year 2025-26, an amount of Rs.454125580.00 has been utilized for the purpose for which it was sanctioned, and that the balance of Rs.14081273.00 remaining unutilized at the end of the year 2025 has been surrendered to the Government (vide No..... dated.....) will be adjusted towards the loan payable during the next financial year.

(2) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.

Kinds of checks exercised

- 1.
- 2.
- 3.
- 4.



D.A.O.

R.W.D. Works Division,
Gopalganj-1




Executive Engineer,
R.W.D. Works Division,
Gopalganj-1

As
08.12.25

अधियाचना हेतु प्रमाण पत्र

- प्रमाणित किया जाता है कि **MMGSUY (RRSMP GEN)** योजनान्तर्गत
1. पथ/पुल **Belwa Brit Middle School to Ghoda Ghat Lalbegi** में कराये गये कार्य की गुणवत्ता जाँच की गयी है जो निर्धारित मानक/विशिष्टियों के अनुरूप है।
 2. अद्यतन कराये गये कार्य की मापी संबंधित मापी पुस्तिका में दर्ज है जिसका सत्यापन कर लिया गया है।



सहायक अभियंता
ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल कुचायकोट।



कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल गोपालगंज-1

RRSMP GEN COPY

Name of Road:- Belwa Brit Middle School to Ghoda Chat Lalbegi

Name of Contractor:- M/s Pawan and Tiwari Construction J.V.

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
6/11/25	14: 18: 28	10	0.1	230	0	2300	2431 G		26.251027	84.732945	Normal
6/11/25	14: 18: 28	10	0.1	200	10.1	2000	2172 G		26.250243	84.733315	Normal
6/11/25	14: 19: 4	10	0.1	210	10.1	2100	2258 G		26.249715	84.73414	Normal
6/11/25	14: 19: 4	10	0.1	210	10.1	2100	2258 G		26.24922	84.734763	Normal
6/11/25	14: 19: 39	10	0.1	270	10.1	2700	2775 G		26.248765	84.73542	Normal
6/11/25	14: 20: 0	10	0.1	230	10.1	2300	2431 G		26.248722	84.736447	Normal
6/11/25	14: 20: 0	10	0.1	240	10.1	2400	2517 G		26.248482	84.737407	Normal
6/11/25	14: 20: 14	10	0.1	250	10.1	2500	2603 G		26.248345	84.738282	Normal
6/11/25	14: 20: 14	10	0.1	200	20.2	2000	2172 G		26.247468	84.738	Normal
6/11/25	14: 21: 0	10	0.1	230	20.2	2300	2431 G		26.246773	84.738872	Normal
6/11/25	14: 21: 0	10	0.1	180	10.1	1800	2000 G		26.246507	84.73983	Normal
6/11/25	14: 21: 25	10	0.1	250	10.1	2500	2603 G		26.24634	84.740807	Normal
6/11/25	14: 21: 25	10	0.1	220	10.1	2200	2344 G		26.246172	84.74182	Normal
6/11/25	14: 21: 25	10	0.1	270	10.1	2700	2775 G		26.24601	84.742827	Normal
6/11/25	14: 22: 0	10	0.1	260	10.1	2600	2689 G		26.245985	84.74377	Normal
6/11/25	14: 22: 0	10	0.1	170	10.1	1700	1913 G		26.245847	84.74473	Normal
		AVERAGE		2398.25							

$$Y = 0 * X^2 + 0.862 * X + 448.5$$

$$X = 1700$$

$$Y = 1913$$

(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

IRI Value
Average IRI-2398.25

Robert 8/11/25

AE

Signature


Name of Customer : [M/S Pawan and Tansen Construc
Name of Work/ Road : [Belwa Brit Middle School to Gih
Lab Job number : 10
Date : 06-11-2025
Section No. : 10

Test Date : 06-11-2025
Machine No : 413
Start S No :
Start E No :
Weather :
Start Location :
End Location :
Road Name : [Belwa Brit Middle School to Gih
Road Type : (R) RURAL ROAD
Side :
Interval
UV Range : 913 To 4000 mm/km
Dist Range : 0 To 1.7 0.1 * 1000 m
Equation : $Y = 0 * X^2 + 0.862 * X + 448.5$

Print Generate Report and Graph

Redraw Graph Map View

File : C:\Users\labhim\OneDrive\Desktop\Bump Report\1.Xls, Section No. : 10, Eqn : $Y = 0 * X^2 + 0.862 * X +$
Name of Customer : , Name of Work/ Road : , Lab Job number :

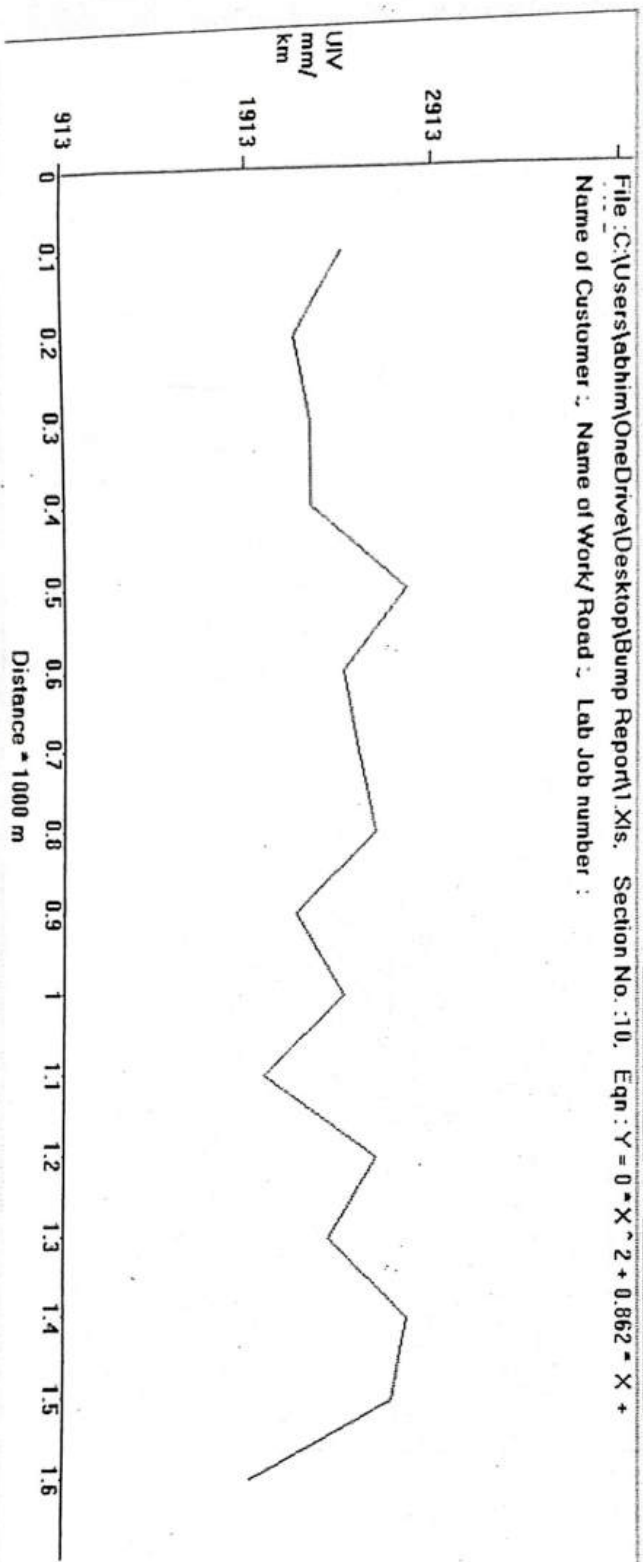

Produced by 06/11/25

PC

Shree 09/11/25
