

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, झांझा ।

पत्रांक-3464(अनु०)

दिनांक- 23/12/2025

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, झांझा ।

सेवा में,

नोडल पदाधिकारी,
3054 एम.आर. कोषांग,
ग्रामीण कार्य विभाग, बिहार, पटना ।

विषय- RRSMP (ग्रामीण सड़क सुदृढीकरण एवं प्रबंधन कार्यक्रम) के क्रियान्वित पथों के भुगतान हेतु अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषयक प्रासंगिक पत्र के संबंध में कहना है कि कार्य प्रमण्डल झांझा अन्तर्गत RRSMP (ग्रामीण सड़क सुदृढीकरण एवं प्रबंधन कार्यक्रम) के पथ में पूर्ण कराये गये कार्यों का भुगतान हेतु अधियाचना विहित प्रपत्र में तैयार कर आवश्यक कार्रवाई हेतु समर्पित की जाती है। सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।

अनु०- 1. अधियाचना विहित प्रपत्र में।

2. Recorder IRI की प्रतिहस्ताक्षरित प्रति।

विश्वासभाजन

Amar
23/12/25

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,

कार्य प्रमण्डल झांझा ।
23/12/25

Position Format for Scheme RRSMP (SC)

of the Works Division :- Jhajha

Sl. No.	Package No.	Project ID as per MIS	Name of Road	AA Length (in km.)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WBM/W MM/BM/S DBC etc.)	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allotted Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
	RRSMP/24-25 Jhajha/06		RRSMP/24-25 Jhajha/03															
		3080420360100	Chakal Garbhudih More To Bichkorba Cakal Basbutti Road	6.600	510.63000	514.82328	04/CMBD/4515 MMGSUY (RRSMP)/2025-26 / 13.07.2025	12.05.2026	BM Work Completed	BM Work Completed		50mm	3.40%	102.56487	102.56487	264.20536	161.64049	BM Work Completed
		3080420360113	L069-Rangania To Binjha	2.600	111.66800	109.14916	04/CMBD/4515 MMGSUY (RRSMP)/2025-26 / 13.07.2025	12.05.2026	Road Surface Work Completed	Road Surface Work Completed	2976.42	25mm	4.83%	0.00000	0.00000	62.70663	62.70663	Road Surface Work Completed
		3080420360127	L135-Jhajha Sono PWD Road Bhitra To Kurkutta	2.890	175.04700	172.74315	05/CMBD/4515 MMGSUY (RRSMP)/2025-26/ 13.07.2025	12.05.2026	Road Surface Work Completed	Road Surface Work Completed	2971.86	25mm	4.75%	43.96363	43.96363	86.50358	42.53995	Road Surface Work Completed
		3080420360133	Sardhodih To Jamui Chakai PWD Road Via Lohao Lakhani Kiyari Tak Path Nirman	6.080	417.32300	416.92447	05/CMBD/4515 MMGSUY (RRSMP)/2025-26/ 13.07.2025	12.05.2026	Road Surface Work Completed	Road Surface Work Completed	2906.44	25mm	4.81%	55.17657	55.17657	281.33951	226.16294	Road Surface Work Completed

It is certified that Physical & Financial Progress has been updated in MIS.

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
	Package No.	Project ID as per MIS	Name of Road	AA Length (in km.)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WBM/WMM/BM/SDBC etc.)	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allotted Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
RRSMP/24-25 Jhajha/03																		
5		3080420360134	L034-Sardhodih To Gorwa Mathihari (TRACK19)	0.800	33.93600	32.69601	05/CMBD/4515 MMGSUY (RRSMP)/2025-26/ 13.07.2025	12.05.2026	Road Surface Work Completed	Road Surface Work Completed	3306.38	25mm	4.73%	0.00000	0.00000	17.81915	17.81915	Road Surface Work Completed
6		3080420360122	L063-Near Kairi To Belakura (Track-49)	8.610	611.08500	618.33646		12.05.2026	Road Surface Work Completed	Road Surface Work Completed	2942.14	25mm	4.75%	414.95807	414.95807	474.55460	59.59653	Road Surface Work Completed
7		3080420360018	L026-Near Dahiriari to Karyasair (Track26)	1.400	56.66000	55.05201		12.05.2026	Road Surface Work Completed	Road Surface Work Completed	2968.21	25mm	4.78%	18.80034	18.80034	38.39522	19.59488	Road Surface Work Completed

It is certified that Physical & Financial Progress has been updated in MIS.

Note :-

- 1 Above Signed Copy along with Forwarding Letter & Utilisation Certificate must be uploaded in MIS.
- 2 Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed (As Applicable).

RWD, Works Division Jhajha

Senior D.A.O.

[Signature]
23.11.2025

Executive Engineer

RWD, Works Division Jhajha

[Signature]
23.11.2025



GFR 12 – B


[See Rule 256 (2)]

FORM OF UTILIZATION CERTIFICATE

- (1) Certified that out of the Loan Of Rs 4828.59834 lacs Sanctioned under RRSMP (SC) dated 16.12.2025 in favour of Executive Engineer, RWD Works Division Jhajha during the year 2025-2026 an amount of Rs 4828.59834 lacs has been Utilized for the purpose for which it was sanctioned , and that the balance of Rs 0.00 lac remaining Utilized at the end of the year 2025-2026 has been surrendered to the Government (Vide No NIL dated NIL)/ will be adjusted towards the load payable during the next financial year.
- (2) Certified that I have satisfied myself that the condition on which the loan was sanctioned have been duly fulfilled / are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made .

Kinds of checks exercised

- 1.
- 2.
- 3.
- 4.
- 5.


23/12/25


Sr Divisional Account Officer,
RWD Works Division,
Jhajha.



23/12/25
Executive Engineer,
RWD Works Division,
Jhajha.

अधियाचना हेतु प्रमाण-पत्र

प्रमाणित किया जाता है कि RRSMP (SC) योजनान्तर्गत :-

1. पथ / पुल L026-Near Dahiari to Karyasair (Track26) में कराये गए कार्य की गुणवत्ता जाँच की गयी है जो निर्धारित मानक / विशिष्टियों के अनुरूप है।
2. अद्यतन कराये गए कार्य की मापी सम्बंधित मापी पुस्तिका में दर्ज है जिसका सत्यापन कर लिया गया है।


कनीय अभियंता,
ग्रामीण कार्य विभाग
कार्य प्रशाखा-सोनो-2


सहायक अभियंता,
ग्रामीण कार्य विभाग,
कार्य अवर प्रमण्डल, सोनो।


कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, झांझा।

Name of Road- L026-Near Dahiari To Karyasair

Name of Contractor-Nitesh Kumar Singh

Package No- RRSMP/24-25 Jhjhha/03

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event			
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD						
21/ 12/ 25	9: 12: 12	74	0.1	310	30.3	3100	3165	G	24.64536	86.35181	Normal	$Y = 0 * X^2 + 0.936 * X + 278.4$		
21/ 12/ 25	9: 12: 31	74	0.1	290	30.3	2900	2936	G	24.64578	86.35194	Normal	X = 2985		
21/ 12/ 25	9: 12: 54	74	0.1	330	20.2	3300	3357	G	24.64732	86.35234	Normal	Y = 3072		
21/ 12/ 25	9: 13: 17	74	0.1	270	30.3	2700	2805	G	24.64845	86.35299	Normal			
21/ 12/ 25	9: 13: 39	74	0.1	260	30.3	2600	2712	G	24.64845	86.35299	Normal			
21/ 12/ 25	9: 13: 57	74	0.1	270	30.3	2700	2805	G	24.65014	86.35399	Normal	(R) RURAL ROAD		
21/ 12/ 25	9: 14: 19	74	0.1	340	20.2	3400	3460	G	24.65014	86.35399	Normal	Good	Average	Poor
21/ 12/ 25	9: 14: 40	74	0.1	250	30.3	2500	2618	G	24.65056	86.35545	Normal	<4000	4001-5000	>5001
21/ 12/ 25	9: 15: 02	74	0.1	260	30.3	2600	2712	G	24.65056	86.35545	Normal			
21/ 12/ 25	9: 15: 21	74	0.1	340	30.3	3400	3456	G	24.65025	86.3565	Normal			
21/ 12/ 25	9: 15: 42	74	0.1	330	20.2	3300	3357	G	24.65025	86.3565	Normal			
21/ 12/ 25	9: 16: 05	74	0.1	290	30.3	2900	2936	G	24.64922	86.35611	Normal			
21/ 12/ 25	9: 16: 27	74	0.1	230	30.3	2300	2431	G	24.64922	86.35611	Normal			
21/ 12/ 25	9: 16: 49	74	0.1	270	30.3	2700	2805	G	24.64878	86.35665	Normal			
Total			1.400	4040	394	40400	41555							
Average				288.57	28.136	2885.71	2968.21							

22/12/2025

22/12/25

22/12/25
A.E

22/12/25
Executive Engineer
Rural Works Department
Works Division, Jhjhha



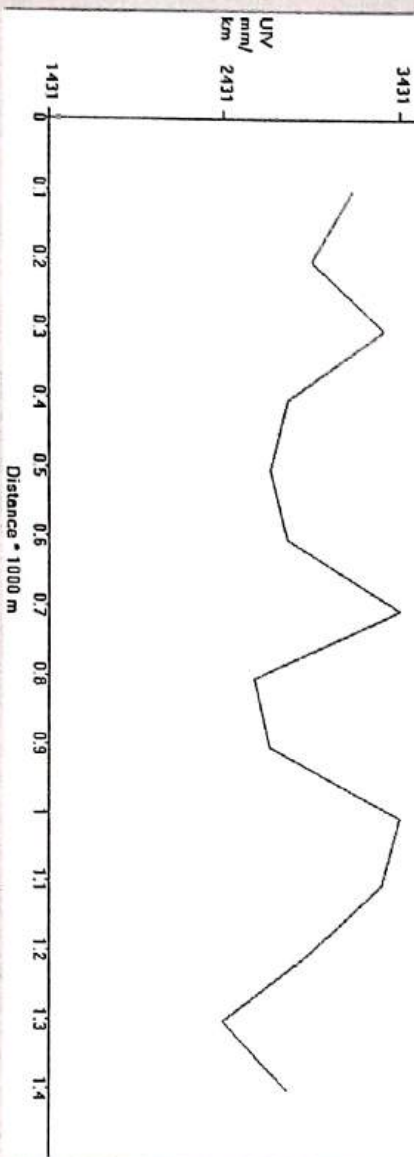
Name of Customer: Nishu Kumar Singh
 Name of Work: U25Hear Dahanu To Karyasar
 Road: 74
 Lab Job number: 74
 Date: 21-12-2025
 Section No. 74

Test Date: 21-12-2025 Road Name: U25Hear Dahanu To Karyasar
 Machine No: 435 Road Type: (R) RURAL ROAD
 Start S No: 0000 Side: Interval
 Start E No: 1400
 Weather: U25Hear Do
 Start Location: U25Hear Do U25Hear Range: 1431 To 4000 1000 mm/km
 End Location: Karyasar Dist Range: 0 To 15 0.1 = 1000 m
 Equation: $Y = 0 \cdot X^2 + 0.936 \cdot X + 278.4$

Print Generate Report and Graph

Redraw Graph Map View

File: F:\Bump Data Jhajha From February 2025\Nishu Kumar Singh (RRSMP SC) SonuRRSMP SC & Road on
 Name of Customer: Name of Work/Road: Lab Job number:



S.K.S.
22/12/2025

G. K. S.
22/12/25

Somesh
22/12/25
A.E.

Sanjay Kumar
Executive Engineer
Rural Works Department
Works Division, Jhajha
