



कार्यपालक अभियंता का कार्यालय ग्रामीण कार्य विभाग, कार्य प्रमंडल, मढ़ौरा।

E-Mail – eerwd.marhaura@yahoo.com

पत्रांक:- 1249/म-30

मढ़ौरा/दिनांक:- 08.07.20

प्रेषक:-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, मढ़ौरा।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण, बिहार, पटना।

विषय:- शीर्ष MR-3054 योजनान्तर्गत बिहार ग्रामीण पथ नई अनुस्क्षण नीति-2018 के तहत स्वीकृत पथ में कराये गये कार्य का आवंटन मॉग के संबंध में।

प्रसंग:- भवदीय के पत्रांक:-113 अनु0, दिनांक:-10-01-2020

महाशय,

उपरोक्त विषयक प्रासंगिक पत्र के संबंध में कहना है कि इस कार्य प्रमंडल, अंतर्गत शीर्ष-3054 (MR-3054) अंतर्गत बिहार ग्रामीण पथ नई अनुस्क्षण नीति-2018 के तहत संवेदक श्री ललन कुमार के द्वारा पथ में किये गये कार्य का अधियाचना उक्त प्रासंगिक पत्र द्वारा प्राप्त विहित प्रपत्र में भरकर आवंटन मॉग हेतु अधियाचना-पत्र सादर समर्पित की जा रही है।

अतः अनुरोध है कि अधियाचना प्रपत्र में दर्शाये गये पथवार राशि कॉलम सं0-18 के अनुरूप पथ में आवंटन उपलब्ध कराने की कृपा की जाय ताकि संबंधित संवेदक द्वारा पथ में कराये गये कार्य का भुगतान किया जा सकें।

अनु0-यथोक्त।

विश्वासभाजन

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, मढ़ौरा।
8/7/20

FORM GER-19-A

(See Government of India's Decision (I) below Rule -150)
Form of Utilization Certificate up to the Month of June-2025
PIU:- Executive Engineer RWD Works Division, Marhaura

SL No	Name of Scheme	Sanction No & Date with Amount (in Lacs Rs.)	Amount Received (in lacs Rs.)	Particulars
1	Construction of Rural Roads under MR-3054 Rural Road Maintenance Policy-2018 (Ledger ID-7069)	<u>सचिव ब्राडा के पत्रांक-45 we</u> <u>दिनांक-27-05-2025</u>	11723.78742	Certified that out of Rs- 11723.78742 Lacs received during the Years, 2018-19 & 2019-20, 2020-21, 2021-22, 22-23, 23-24 & 2024-25 in favour of E.E., R.W.D. Works Division Marhaura Sum of Rs- 11677.46962 Lacs has been utilized for the Purpose of MR-3054 New Maint. Policy-2018 Scheme as given in the margin for Which it was Sanctioned and that the balance of Rs-46.31780 Lacs remaining unutilized at CFMS the end of the period under report.




Sr. DAO

R.W.D. (W) Division Marhaura



Executive Engineer

R.W.D. (W) Division Marhaura



Requisition Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of works Division:- Rural Work Department, Work Division, Marhaura.

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA) Total		Agreement Amount (In Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allotted Amount (In Lakh)	up-to-date expenditure as per MIS (In Lakh)	Requisition against work done. (In Lakh)	Remarks
					Length (In Km.)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/23-24 Marhaura/11 RM/SA/MAR/ 24/0003	Gaurra Tejpuba Path (Brahm Sthan) To Chanda Bin Toli Tak	31306512025	Lt.- No-2178 Date-20-10-2022	1.600	92.47000	70.41542	12.06040	18/MR-3054-N- (MBD/2024-25) Dt-19-10-2024	18.07.2025		2650.00	N/A	N/A	65.00000	65.00000	5.41500	Work In Progress
2	MR-N/23-24 Marhaura/11 RM/SA/MAR/ 24/0003	Silauri Paharpur Pakki Sadak (Asoiya Chauk) to Pachim Tola tak	31306513035	Lt.- No-2178 Date-20-10-2022	1.500	93.40000	73.33475	9.62925	18/MR-3054-N- (MBD/2024-25) Dt-19-10-2024	18.07.2025		2833.00	N/A	N/A	68.00000	68.00000	5.29326	Work In Progress
3	MR-N/23-24 Marhaura/11 RM/SA/MAR/ 24/0003	Raspriya Singh (Brij Bihari Singh) Ke Ghar To Gandki Nadi Pull Via Lakshman Chowk Bhuwalpur	N313065024001	Lt.- No-2178 Date-20-10-2022	1.240	84.76000	67.99282	6.39670	18/MR-3054-N- (MBD/2024-25) Dt-19-10-2024	18.07.2025		2741.00	N/A	N/A	62.99282	62.99282	4.75650	Work In Progress
4	MR-N/23-24 Marhaura/11 RM/SA/MAR/ 24/0003	Dyalpur Gaura Bawansadak To Mashaha Ahir Tola Tak Path	31306513013	Lt.- No-2178 Date-20-10-2022	1.000	61.60300	46.54781	8.39790	18/MR-3054-N- (MBD/2024-25) Dt-19-10-2024	18.07.2025		2451.00	N/A	N/A	41.54781	41.54781	3.83871	Work In Progress
Total:-															237.54063	237.54063	20.32969	

1. Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.
2. Up-to-date Physical Progress has been Uploaded in MIS.

8/7/25

Shankar
8/7/25
Executive Engineer
Rural Work Department
Work Division, Marhaura
8/7/25

Name of Customer
Name of Work / (Job) To Check En Tox Tax
Hand
Lab Job number
Date
Section No


Test Date: 05/02/2022
Machine No: 75.8
Start S No:
Start E No:
Weather: 17°C/64°F
Start Location:
End Location:
Road Name: (R) RURAL ROAD
Road Type:
Side:
UTV Range: 1000
Dist Range: 1000
Equation: $Y = 0.015X^2 + 0.016X + 2.49$

Generate Report and Graph

File: C:\Users\Admin\Documents\Bump_05_03_2022\05-03-2022_124
Name of Customer: Laban Kumar, Name of Work/ Road: Gauran Topdha Pats (Haben Shan) To Chanda Him Tox Lok

Map View

Section Graph

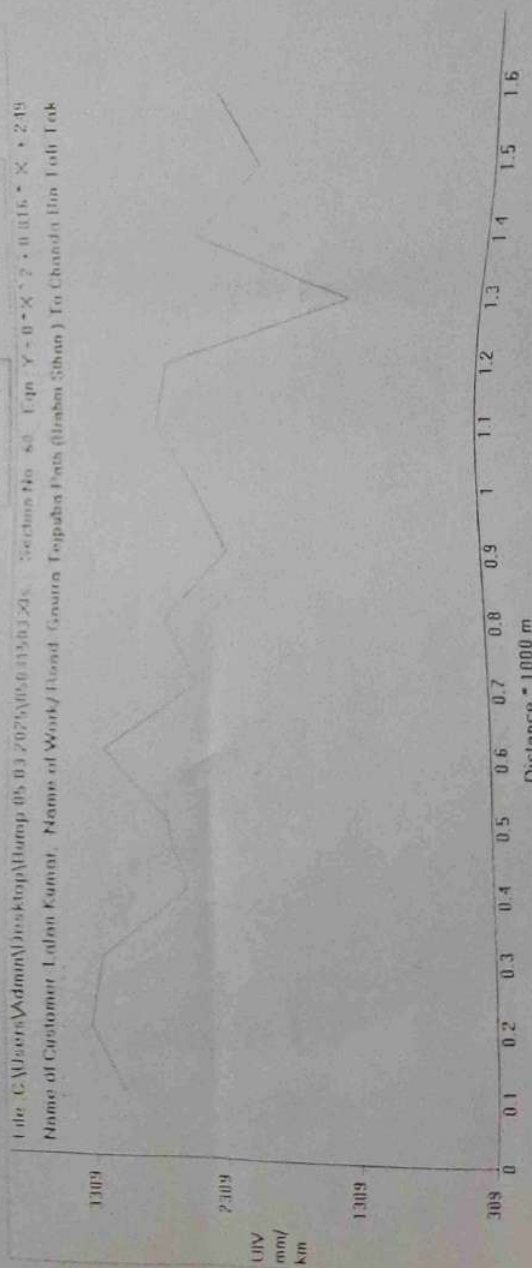

24/2/22
SILPA
EE

24/2/22
SILPA
EE

24/2/22
SILPA
EE

od Name:- Gaurra Tejpuba Path (Brahm Sthan) To Chanda Bin Toli Tak

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY	Latitude	Longitude	Event
5/3/25	14:31:0	60	0.1	350	20.2	3500	3104	ROAD	25.93974	84.814123	Normal
5/3/25	14:31:31	60	0.1	380	0	3800	3349	G	25.940097	84.814208	Speed Break
5/3/25	14:32:0	60	0.1	370	20.2	3700	3268	G	25.940823	84.813855	Normal
5/3/25	14:32:7	60	0.1	290	20.2	2900	2615	G	25.941522	84.813938	Normal
5/3/25	14:32:7	60	0.1	310	0	3100	2778	G	25.942255	84.813787	Normal
5/3/25	14:32:43	60	0.1	370	0	3700	3268	G	25.94298	84.813113	Speed Break
5/3/25	14:33:0	60	0.1	280	20.2	2800	2533	G	25.943478	84.812677	Normal
5/3/25	14:33:18	60	0.1	310	20.2	3100	2778	G	25.943805	84.812222	Normal
5/3/25	14:33:18	60	0.1	250	20.2	2500	2288	G	25.944248	84.811665	Normal
5/3/25	14:34:0	60	0.1	280	20.2	2800	2533	G	25.94493	84.810992	Normal
5/3/25	14:34:0	60	0.1	320	0	3200	2869	G	25.945457	84.81008	Speed Breaker
5/3/25	14:34:28	60	0.1	310	20.2	3100	2778	G	25.945857	84.809123	Normal
5/3/25	14:35:4	60	0.1	130	20.2	1300	1309	G	25.946332	84.80838	Normal
5/3/25	14:35:4	60	0.1	280	20.2	2800	2533	G	25.946585	84.807727	Normal
5/3/25	14:35:4	60	0.1	220	20.2	2200	2044	G	25.946682	84.806968	Normal
5/3/25	14:35:39	60	0.1	260	20.2	2600	2370	G	25.94664	84.806582	Normal
Total Length			1.600	Average IRI		2650					

$$Y = 0 * X^2 + 0.816 * X + 249$$

$$X = 2943$$

$$Y = 2650$$

(R) RURAL ROAD
Good <4000
Average 4001-5000
Poor >5001

24/3/23
EE

06/05/25
Raj

5/3/25
Raj

Graha Tejpurba PATH (Brahman Sthan) TO

CHANDA BIN TOLI TAK

Schedule XLV-Form No. 134

Executive Engineer
Public Works Department
Muzaffarpur
Works Division

M.B. No

1040

MUZAFFAR

DIVISION

Maxhouza

SUB-DIVISION

Lalan Kumax

MEASUREMENT BOOK

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
N/W - Gaurang - Tejpuram Path (Barhamsthan) To Chanda Bin - Tol Talk.					
Agency - Sri Lalan Kumar					
Agreement No - 18/MB-2024-N/MBD/2024					
Agreement Value -					
Date of work order - 13.10.2024					
Date of completion - 18-07-2025					
Date of measurement - 20/6/25					
Date of Actual completion - 20/6/25					
1) Const'n of Subgrade					
8 Earthen shoulder					
- do do - all complete					
Total -					
BT Port'n - 12	30		1.125	0.35 =	141.75 m ³
Both side	141.75 x 2				= 283.5 m ³
C.C Port'n	2	10	1.125	0.35 =	7.875 m ³
C.C Port'n 2x10	30		0.60	0.15 =	102.60 m ³
	2	11	0.60	0.15 =	1.98 m ³
	2x11	30	1.125	0.35 =	259.875 m ³
	2	12	1.125	0.35 =	9.45 m ³
	2x9	30	1.125	0.35 =	212.625 m ³
					877.905 m ³
2) Provide 20mm &					

Abstract of cost:-

1> Clearing and Grubbing

Road Land - do-do

as per complete job -

TMB - 14

$$0.241 \text{ Ha} @ 76926.08 / \text{Ha} = 18539 = \infty$$

2> Constn of subgrade

and earthen shoulder

- do-do - all complete

Job —

TMB - 19

$$877.905 \text{ M}^3 @ 264.72 / \text{M}^3 = 232399 = \infty$$

3> Providing C.I. S.B

grading - TI - do-do

all complete job: —

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
TMB- 14					
13.368 m ³ @ 2541.23/m ³ =					33973 = 0
4) Providing WBM					
Grade-II rat patches					
do-do-all complete job					
TMB- 14					
11.72 m ³ @ 5642.19/m ³ =					63035 = 0
5) Providing WBM					
Grade-3 do-do					
all complete job					
TMB- 15					
43.825 m ³ @ 5144.83/m ³ =					225462 = 0
6) Providing Prime					
coat - do-do all					
complete job					
TMB- 15					
422.73 m ³ @ 57.41/m ² =					24,269 = 0
7) Providing Tack					
coat - do-do all					
complete job					
TMB- 15					
2662.50 m ² @ 16.48/m ² =					43,878 = 0
8) Providing playing					
SDBC - do-do all					
complete job					
TMB- 15					
67.23 m ³ @ 14679.40/m ³ =					986896 = 0

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
9) Providing D.O.C					
- do do all complete job -					
TMB- 15					
8.85 m ³ @ 5250.31/m ³ =					46,465 =
10) Providing Panel					
Concrete Pavement					
PCCM-30 - do do -					
all complete job -					
TMB- 15					
394.145 m ³ @ 9270.16/m ³ =					3653764 =
11) Providing 1cm Stone					
200m post -					
(i) 1cm Stone					
TMB- 15, 20					
2 Nos					
1 Nos					
3 Nos @ 2918.59/Each =					8756 =
(ii) 200m post					
5 Nos @ 814.64/m =					4073.00
12) Providing Road					
sign - do do all					
complete job -					
TMB- 20					
2.88 m ² @ 14988.63/m ² =					43169 =
13) Providing Road					
traffic sign - do					
- do all complete job -					

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
TMB-16, 20					
(i) 600mm equilateral triangle					
6 Nos					
2 Nos					
8 Nos @ 4438.99/Each =					35512 = w
(ii) 600mm circular					
2 Nos @ 4309.82/Each =					8620 = w
(iii) 600mm x 450mm rectangular					
2 Nos					
1 Nos					
2 Nos @ 4165.29/Each =					8331 = w
(iv) 900mm Side octagon					
1 Nos					
1 Nos					
2 Nos @ 8634.65/Each =					17269 = w
14) Providing Boundary Pillar :-					
TMB-20					
24 Nos @ 8634.65/Each =					207232 =
15) Providing Planting of trees and their maintenance one year					
TMB-20					
36 Nos @ 1305110/Each =					46984 = w

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
16> Providing road marking - do - do all complete job -					
TMB - 16					
BT Portion -					
142m ² @ 886.50/m ² =					125883 =
CC Portion -					
173m ² @ 988.82/m ² =					171066 =
17> Providing Logo Board -					
TMB - 16, 20					
2 Nos @					
3 Nos @ 10932.25/each =					32797 =
					Rs 60,38,370 =
Add G.S.T 18% (+) Rs					10,86,907 =
Add 1% L.C (+) Rs					60,384 =
Add Seigniorage (+) Rs					20,952 =
					Rs 72,06,613 =
Below (4.25%) (-) Rs					3,06,281 =
					Rs 69,00,332 =
Less Previous Bill (-) Rs					62,56,210 =
					Rs 6,44,122 =
20/06/25					
20/6/25					
Certificate: -					
work has been completed					
proper specifications					
20/6/25					
Continuation					
