

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, महनार (वैशाली)

पत्रांक
प्रेषक ,

386(3420)

/महनार/दिनांक :- 28/02/25

सेवा में,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, महनार

नोडल पदाधिकारी,
3054 एम0आर0 कोषांग,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय :- मुख्यमंत्री ग्रामीण सड़क उन्नयन योजना (MMGSUY) के तहत
निर्मित पथ की राशि की अधियाचना पत्र समर्पित करने के संबंध में।

महाशय,

उपरोक्त विषय के संदर्भ में मुख्यमंत्री ग्रामीण सड़क उन्नयन योजना
(MMGSUY) से निर्मित पथ के लिए राशि की अधियाचना विहित प्रपत्र में
समर्पित की जा रही है।

विदित है कि अधियाचित पथ का कार्य संतोषप्रद है। अधियाचित पथ
में आवंटन देने की कृपा की जाये।

अनु0:-1. अधियाचना विहित प्रपत्र।

विश्वासभाजन

[Handwritten signature]
28/02/25

[Handwritten signature]
28/02/25
कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, महनार

[Handwritten signature]
28/2/25

Office of The Executive Engineer, Rural Works Department, Works Division Mahnar

Requisition formate for Scheme Head- MMGSUY (GEN)																				
S.No.	Package No	Project ID As per MIS	Name of Road	A.A. Letter No & Date	Administrativ Approval (A.A.)		Agreement Amount (in Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen content in Percentage	Total Previous Allotted Amount (in Lakh)	Up-to-Date Expenditure as per MIS (in lakh)	Value of work done (in lakh)	Current Demand (in lakh)	Remarks
					Length (in K.M.)	Amount (in lakh)	Construction (in lakh)	5 Years Maintenance (in lakh)												
	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19		
1	MMGSUY/23-24 Mahnar/04	3150770280007	Raghopur Ke Virpur Me Utikarmit High School Se Tapeswar Singh k Ghar Hote hue Suresh Singh K ghar tak	18/12/2023	1.500	147.24000	137.11402	5.48732	12.09.2024	09.05.2025	-	Surface Complete	3058.60	PCC- 125	Grading-M30	27.00000	19.90691	137.11402	110.11402	
2	MMGSUY/23-24 Mahnar/04	3150770280008	Raghopur Purbi Me Dimanath Paswan ke Ghar se Lakhan Deo Rai K ghar tak PCC Karya	18/12/2023	0.550	54.10000	50.37983	2.01378	12.09.2024	09.05.2025	-	Surface Complete	3110.33	PCC- 125	Grading-M30	10.00000	6.59415	50.37983	40.37983	
3	MMGSUY/23-24 Mahnar/04	3150770280009	Raghopur Virpur Me RCD Road 10 No. Ward se Sukhdeo Choudhary Ke ghar Se Narayan Shah k Ghar tak	18/12/2023	0.550	68.52000	64.15964	2.20715	12.09.2024	09.05.2025	-	Surface Complete	3142.66	PCC- 125	Grading-M30	13.00000	6.97758	64.15964	51.15964	
4	MMGSUY/23-24 Mahnar/04	3150770280010	PCC Road Dhirendrera Rai K Ghar Se Jawahar Rai Rustampur Tenparaiya Tola	18/12/2023	1.075	114.18000	106.38749	4.19851	12.09.2024	09.05.2025	-	Surface Complete	3148.54	PCC- 125	Grading-M30	21.00000	21.00000	106.38749	85.38749	
5	MMGSUY/23-24 Mahnar/04	3150770280011	Ramjanki Math Se Das Tola hote hue Narashiya PCC Sadak Tak	18/12/2023	0.800	95.98000	90.03437	2.92735	12.09.2024	09.05.2025	-	Surface Complete	3041.63	PCC- 125	Grading-M30	18.00000	18.00000	90.03437	72.03437	
6	MMGSUY/23-24 Mahnar/04	3150770280012	Ranjay Singh Kapda Dukan via Post office to Kashi Chowk	18/12/2023	0.640	82.85000	77.68931	2.5361	12.09.2024	09.05.2025	-	Surface Complete	3084.86	PCC- 125	Grading-M30	16.00000	7.30000	77.68931	61.68931	
7	MMGSUY/23-24 Mahnar/03	3150770280022	Registery Tola Raghopur Purbi Path to Samudaik Bhawan Chandan Choudhary ke Ghar hote huye Middle School RCD Path	18/12/2023	1.500	153.08000	141.09351	5.42312	24/09/2024	23.06.2025	-	PCC Work in progress	3097.40	PCC- 125	Grading-M30	28.00000	28.00000	124.34134	96.34134	
8	MMGSUY/23-24 Mahnar/02	3150770280018	CHAUSINLAN RAMPUR BHORPA	18/12/2023	4.290	308.02000	240.35019	36.21642	09.08.2024	07.08.2025	-	Surface Complete	2371.00	Bitumen-25 mm PCC- 125	Bitumen-5.019 % Grading-M30	238.35019	238.35019	240.35019	2.00000	

Requisition formate for Scheme Head- MMGSUY (GEN)																				
S.No.	Package No	Project ID As per MIS	Name of Road	A.A. Letter No & Date	Administrativ Approval (A.A.)		Agreement Amount (in Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen content in Percentage	Total Previous Allotted Amount (in Lakh)	Up-to-Date Expenditure as per MIS (in lakh)	Value of work done (in lakh)	Current Demand (in lakh)	Remarks
					Length (in K.M.)	Amount (in lakh)	Construction (in lakh)	5 Years Maintenance (in lakh)												
	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19		
9	MMGSUY/23-24 Mahnar/02	3150770280001	L040 - Bilandpur Dhadhua to Malahi Chak Bajo Malahi (VR33)	18/12/2023	5.650	508.25000	418.65743	45.44359	09.08.2024	07.08.2025	-	B.T & PCC work Completed	3357.00	Bitumen- 25 mm PCC- 125	Bitumen- 5.019 % Grading- M30	144.00000	137.64735	279.87392	135.87392	


 28/12/25
 Sr. Divisional Accounts Officer
 Rural Works Department,
 Works Division, Mahnar


 Executive Engineer,
 Rural Works Department,
 Works Division, Mahnar

GFR 12-B
[See Rule 256 (2)]

FORM OF UTILIZATION CERTIFICATE

(1) Certified that out of the Loan of Rs 130719364.00, Sanctioned under Letter No-11, dated 04-02-2025, in favour of Executive Engineer, RWD, Works Division, Mahnar during the year 2024-25 an amount of Rs 97536188.00 has been utilized for the purpose for which it was sanctioned, and that the balance of Rs 33183176.00 remaining unutilized at the end of the year..... has been surrendered to the Government (vide No....., dated.....)/ will be adjusted towards the loan payable during the next financial year.

(2) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.

Kinds of checks exercised

- 1.
- 2.
- 3.
- 4.

Signature.....

Designation.....

Date.....


DIVISION-I ACCOUNT OFFICER
A. W. D. WORK DIVISION
MAHNAR


Executive Engineer
RWD Works Div. Mahnar

TR-1/28/2/25

Name of Contractor :- Rajeev Kumar


Name of Work :-1040 - Biliandpur Dhadhua to Malahi Chak Bajo Malahi (VR33)

Date	Time	Section No.	Length in km	Bumps in mm	Rate	Speed	OR	IRI, TEGORY	Latitude	ongitude	Event
17/1/25	15: 40: 0	94	0.1	390	10.1	3900	3976 G	25.71923	85.42253	Normal	
17/1/25	15: 40: 30	94	0.1	380	10.1	3800	3890 G	25.71918	85.42162	Normal	$Y = 0 * X^2 + 0.860 * X + 622.7$
17/1/25	15: 41: 5	94	0.1	320	10.1	3200	3374 G	25.71934	85.42071	Normal	$X = 3800$
17/1/25	15: 41: 40	94	0.1	360	10.1	3600	3718 G	25.71958	85.41981	Normal	$Y = 3890$
17/1/25	15: 42: 16	94	0.1	220	10.1	2200	2514 G	25.71966	85.41901	Normal	
17/1/25	15: 43: 0	94	0.1	320	10.1	3200	3374 G	25.71881	85.41909	Normal	(R) RURAL ROAD
17/1/25	15: 43: 26	94	0.1	370	10.1	3700	3804 G	25.71795	85.41894	Normal	Good
17/1/25	15: 44: 1	94	0.1	290	10.1	2900	3116 G	25.71707	85.41899	Normal	Average
17/1/25	15: 44: 37	94	0.1	310	10.1	3100	3288 G	25.71621	85.41897	Normal	Poor
17/1/25	15: 45: 12	94	0.1	320	10.1	3200	3374 G	25.71535	85.41889	Normal	
17/1/25	15: 50: 0	94	0.1	220	10.1	2200	2514 G	25.71528	85.41891	Normal	
17/1/25	16: 20: 37	94	0.1	270	10.1	2700	2944 G	25.70785	85.43886	Normal	
17/1/25	16: 22: 0	94	0.1	300	10.1	3000	3202 G	25.70717	85.43835	Normal	
17/1/25	16: 22: 23	94	0.1	380	10.1	3800	3890 G	25.70641	85.43825	Normal	
17/1/25	16: 23: 0	94	0.1	370	10.1	3700	3804 G	25.70556	85.43838	Normal	
17/1/25	16: 24: 0	94	0.1	340	10.1	3400	3546 G	25.70488	85.43896	Normal	
17/1/25	16: 24: 9	94	0.1	230	10.1	2300	2600 G	25.70322	85.43931	Normal	
17/1/25	16: 25: 0	94	0.1	340	10.1	3400	3546 G	25.70245	85.43941	Normal	
17/1/25	16: 25: 19	94	0.1	280	10.1	2800	3030 G	25.70166	85.43946	Normal	
17/1/25	16: 26: 0	94	0.1	290	10.1	2900	3116 G	25.70158	85.43946	Normal	
17/1/25	16: 26: 30	94	0.005	380	10.1	3800	3890 G				
						IRI Value	3357				

Chandan
24/6/125

24/6/125
26

File :D:\BUMP\Rajeev\170124Dhadhuamalahi.Xls, Section No.:94, Eqn : $Y = 0 \cdot X^2 + 0.860 \cdot X + 622.7$
 Name of Customer :Rajeev Kumar, Name of Work Road :L:040-Bilandpur Dhadhua To Malahi Chak Bajo Malahi, Lab Job

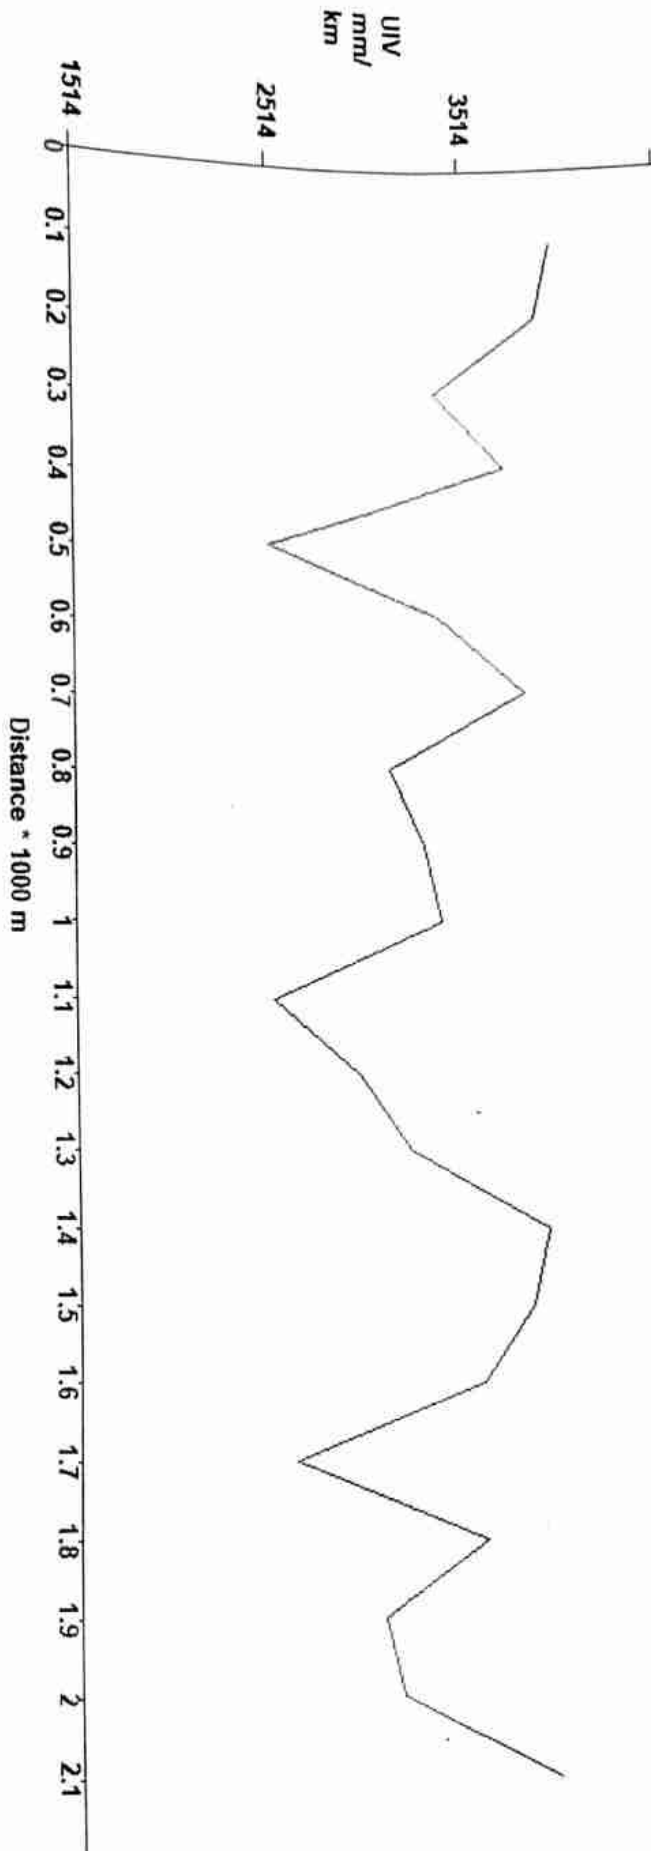

Dr. R. K. Singh
 24/11/25
 JC

Dr. R. K. Singh
 24/11/25
