

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल- डुमराँव।

पत्रांक:- 231, डुमराँव/

दिनांक:- 03/03/2025

प्रेषक,
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, डुमराँव।

सेवा में,
अपर मुख्य कार्यपालक पदाधिकारी-साह-सचिव
बिहार ग्रामीण पथ विकास अभिकरण,
बुद्ध मार्ग, पटना


विषय :- NEW MR 3054(बिहार ग्रामीण पथ अनुरक्षण निति-2018) योजनान्तर्गत राशि की अधियाचना के संबंध में।

महाशय,
उपर्युक्त विषय के संबंध में कहना है कि इस प्रमंडल अंतर्गत NEW MR 3054 मरम्मत (बिहार ग्रामीण पथ अनुरक्षण निति-2018) अन्तर्गत कराये गये कार्यों के भुगतान हेतु राशि की आवश्यकता है जिसका अधियाचना प्रपत्र के साथ संलग्न कर भेजा जा रहा है।


अतः अनुरोध है कि अधियाचित राशि उपलब्ध कराने की कृपा की जाए ताकि संवेदक द्वारा कराये गये कार्यों का भुगतान किया जा सके।

अनु०:- यथोक्त।

विश्वासभाजन


03/03/25

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल डुमराँव।

 03/03/25

Requisition Format for Scheme Head- MR (3054) Under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Name of Works Division:- RWD, Works Division, Dumraon.

St. No	Package No	Name of Road	Project ID as per MIS	Administrative Approval (AA Letter No & Date)	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No/Date	Date of Completion as per Agreement	Actual Date of Completion	Value of RRI (in mm/km)	Thickness of Bitumen (in mm)	Value of Bitumen content in Percentage	Previous Total Allowed Amount (in Lakh)	Up-to-date Expenditure as per MIS (in Lakh)	Requisition against work done (in lakh)	Remarks
					Length (in KM)	Amount (in Lakh)	Initial Rectification on Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
	RN/BU/ DUM/24/ 0003	PARAKORE-BELAHARI	10402002042	6120/04.12.2023	0.880	42.121	31.17444	6.6348	08 MBD/2024-25/27.09.2024	26.06.2025	06.12.2024	2956	25	5.06	28.49198	28.49198	2.25487	2nd & final Bill
	RN/BU/ DUM/24/ 0003	Kesadh Nahar Dangoli Pool Path via Pokhara Tola	NEA220001340	6120 /04.12.2023	3.830	169.368	107.74080	16.07460	08 MBD/2024-25/27.09.2024	26.06.2025	Ongoing	3294	25	5.02	81.03306	81.03306	26.26194	2nd on Acc Bill

1 Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.
2 Up-to-date Physical Progress has been Uploaded in MIS.

Sgt
29/7/24

03/03/25
Executive Engineer,
Rural Works Department,
Works Division, Dumraon

New Maintenance Policy 2018 Through CFMS

FIU:-RWD(W),Div:- Dumraon				
Sl No.	Name of Schemes	Sanctione No. & Date with Amount (in Rs Lakh)	Amount Received (in Rs. Lacs)	Particulars
1	Construction of Rural Roads under New Maintainance Policy 2018	Letter No:- 07, Dated:-22.01.2025	4111.46141	Certified that out of Rs.4111.46141 lacs received during the years in favours of Ex-Engineer , RWD(W), Div -Dumraon, Bihar. A sum of Rs 4090.50025 lacs has been utilized for the purpose of New Maintainance Policy 2018 Schemes as given in the margin for which it was sanctioned and that the balance of Rs.20.96116 lacs remaining unutilized at the end of the period under.

- (i) Construction of road works.
- (ii) Construction of CD works.

57+
09425

D. R. W.
03/03/25
Executive Engineer
R.W.D Work Division
D. R. W.
03/03/25

Name of Road:- PARAKORE - BELAHARI, Name of Contractor:- Ramanand Rai

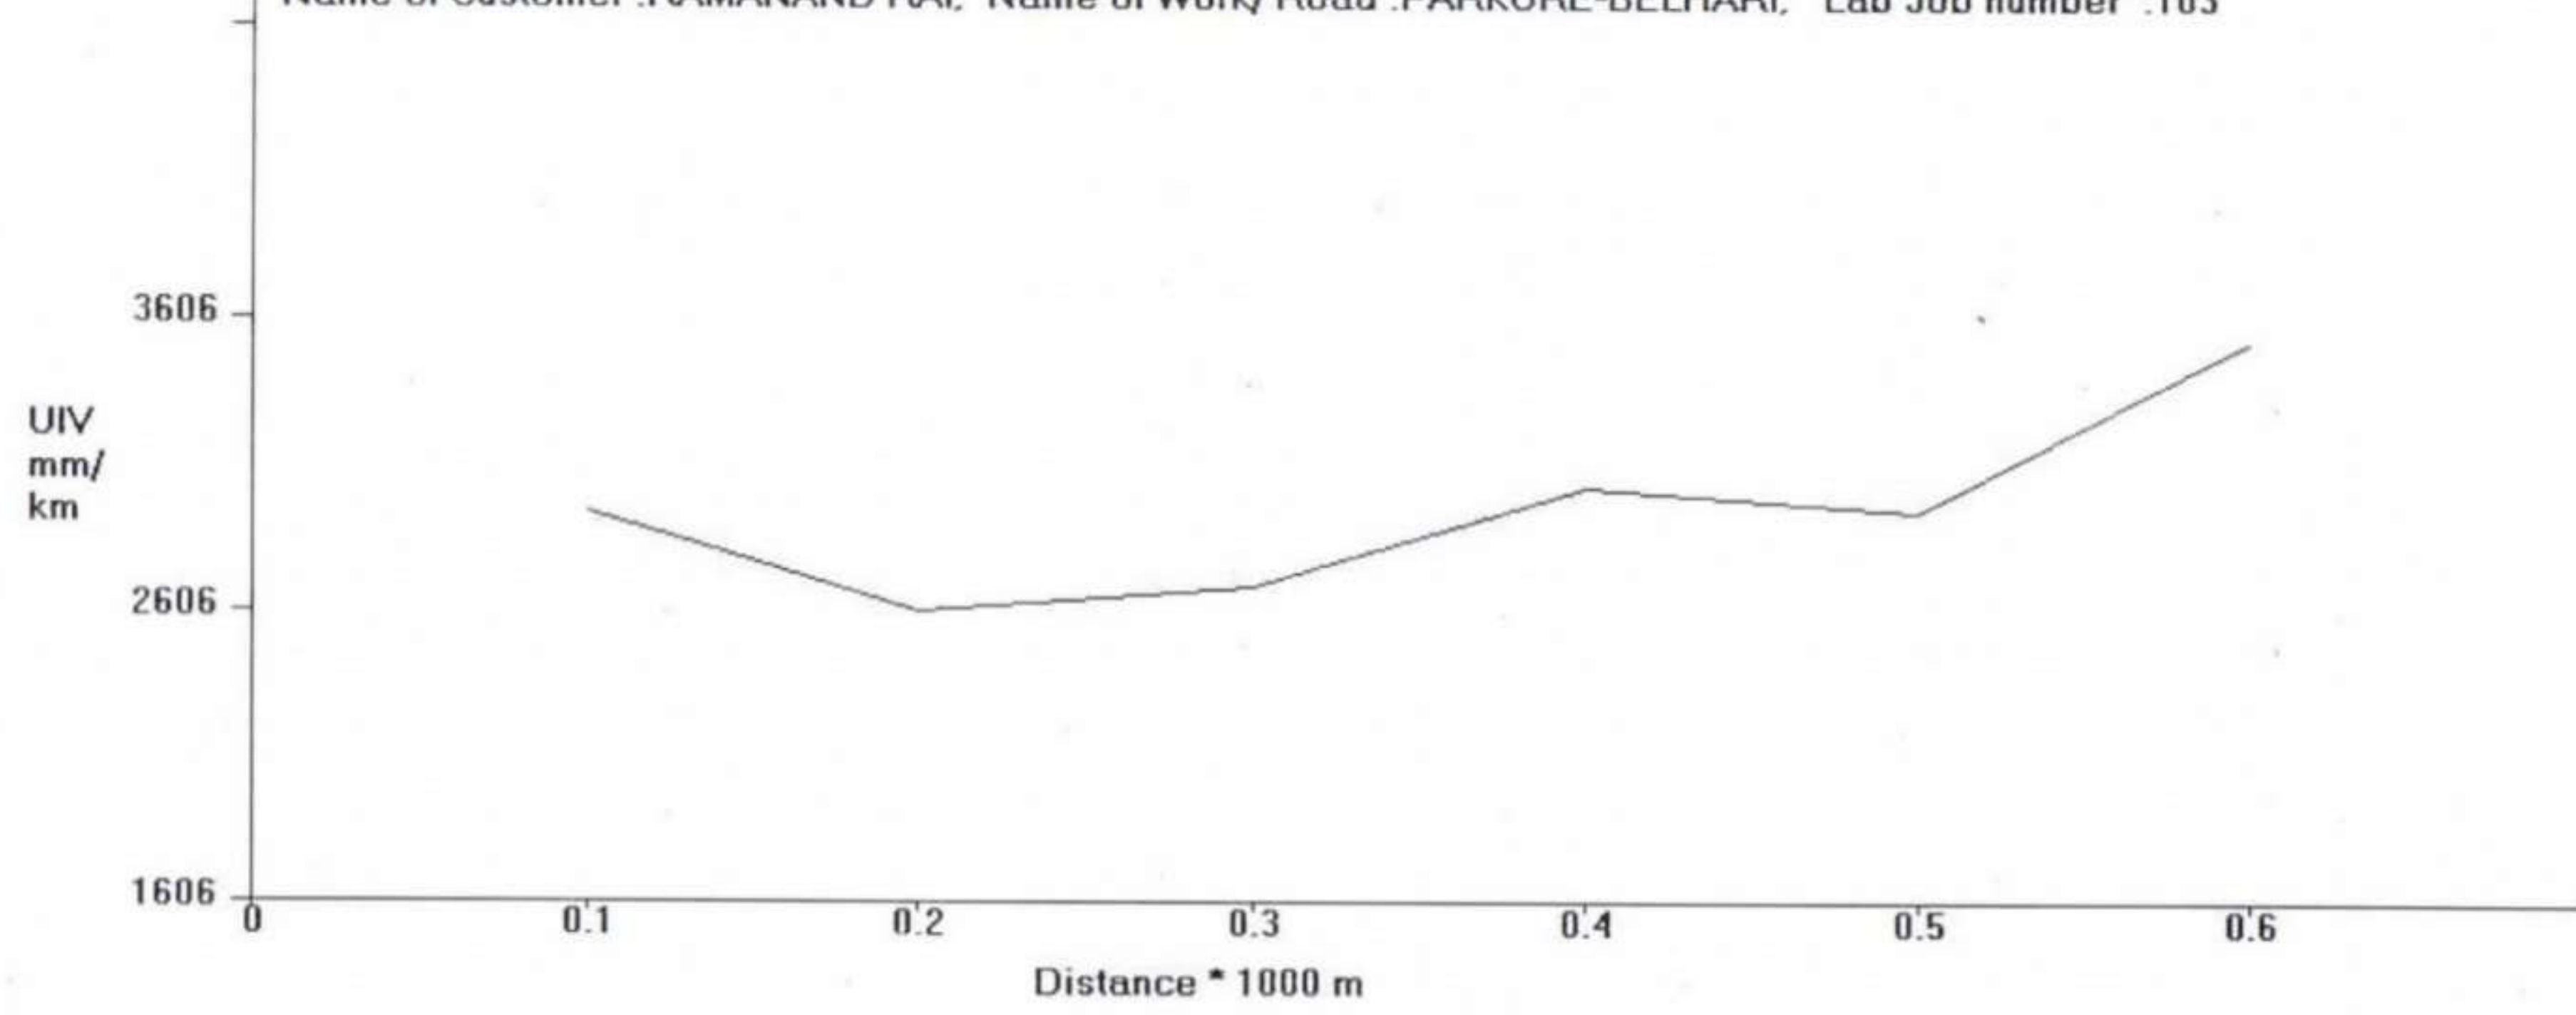
Date	Time	Section	Length	Bumps	Speed	OR		CATEGORY	IRI	Latitude	Longitude	Event				
		No.	in km	in mm	Rate	mm/km	UIV	ROAD					Y = 0 * X ^ 2 + 0.840 * X + 339.0			
21/ 11/ 24	11: 31: 21	103	0.1	310	10.1	3100	2942	G	3.95	25.43331	84.15084	Normal	X = 3800			
21/ 11/ 24	11: 31: 21	103	0.1	270	30.3	2700	2606	G	3.55	25.432806	84.150709	Normal	Y = 3530			
21/ 11/ 24	11: 32: 0	103	0.1	280	40.4	2800	2690	G	3.65	25.432363	84.150663	Normal				
21/ 11/ 24	11: 32: 0	103	0.1	320	40.4	3200	3026	G	4.05	25.430734	84.150005	Culvert				
21/ 11/ 24	11: 32: 31	103	0.1	310	30.3	3100	2942	G	3.95	25.430376	84.14987	Normal	RURAL ROAD			
21/ 11/ 24	11: 32: 31	103	0.1	380	20.2	3800	3530	G	4.65	25.429963	84.9755	Curve	Good	Average	Poor	
							Total IRI	17736								
							Avg_IRI	2956								

Dupt
21/11/2024
J.E

#1
21/11/24
AE

Dr. K. M.
21/11/24
EE

File :C:\Users\DELL\Desktop\STECO\Ramanand Rai\Parkore to belhri.xlsx, Section No. :103, Eqn : $Y = 0 * X^2 +$
Name of Customer :RAMANAND RAI, Name of Work/ Road :PARKORE-BELHARI, Lab Job number :103



Subb
21/11/2024
J.E

#1
21/11/24
AE

Subb
21/11/24

पत्र करणें देणें
Schedule XLV-Form No. 134
०१११-१३१५

M R- 3054/2018

Agreement-No-08 MBD/2024-25

54219
DIVISION

SUB-DIVISION

कार्य-प्रारंभ-की-दिनांक-१५-०९-२०२४
कार्य-प्रारंभ-की-दिनांक-१६-०६-२०२५

MEASUREMENT BOOK

दिनांक:- ११.११.२०२४

1290

Name of work—
 Situation of work—
 Agency by which work is executed—
 Date of measurement—
 No. and date of agreement.

(These four lines should be repeated at the commencement of the measurements relating to each work.)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of Work - Repair and maintenance of Road from Parturkore to Belhari					
Length of Road - 0.570 km					
Name of Agency - Ramnandan Rai					
Vill + P.O - Dharaoni, Dist - Chaziguri, (U.P)					
Package No - MR-N/22-24 Dmraon/06					
Agreement No - 08 MBD/2024-25					
Date of start of work - 27/03/2024					
Date of completion of work - 26/06/2024					
Agg. construction cost RS - 3,17,444.00					
Agg. maintenance cost RS - 66,348.30					
Total RS - 37,80,927.00					
Date of measurement - 20/11/24, 21/11/24					
Description of item					
① clearing and grubbing Road Land					
— do - do - all complete job as per E/I.					
	5	2	30.00	1.50	450.00 m ²
	5	2	30.00	1.50	450.00 m ²
	5	2	30.00	1.50	450.00 m ²
	4	2	30.00	1.50	360.00 m ²
					Pl ₁ = 1710.00 m ²
					= 0.17 Hg
② Dismantling of existing structure					
like culverts, bridge - do - do - all					

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
<u>Abstract of cost</u>					
(1) Clearing and grubbing Road Land					
- do - all complete job					
Qty vide P. No (6) in TMB					
item No (1)					
@ R 76926.08/Hq	0.17 Hq			R	13077=00
(2) Construction of Subgrade and					
earthen shoulder - do - all					
complete job					
Qty vide Page No (6) in TMB					
item No (2)					
@ R 264.72/H ³	184.73 m ³			R	48902=00
(3) Dismantling of existing str-do					
- do - all complete job					
Qty vide Page No (6) in TMB					
item No (2)					
@ R 687.18/H ³	0.81 m ³			R	557=00
(4) Dismantling of Brick/Tile - do					
- do - all complete job					
Qty vide P. No (6) in TMB					
item No (4)					
@ R 321.93/H ³	30.60 m ³			R	9880=00
(5) Removing all types of H-pipe do					
- do - all complete job					
Qty vide P. No (6) in TMB					
item No (5)					
@ R 356.13/H ³	7.50 m ³			R	2671=00
(6) Plr, laying, spreading and compaction					
of WBM - do - all complete job					
Qty vide P. No (6) in TMB					
item No (6)					
@ R 5272.58/H ³	160.31 m ³			R	845247=00

Continuation

R 920334=00

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
			B/F R ₁	-	920,334=∞
(7) Plr and applying of primer coat - do - do - all complete job					
Qty vide Page No (7) in TMB					
@ Rs 58.04/m ² Item No (7)		2152.00m ²	R ₃		1,24,902=∞
(8) Plr and applying of Taek coat do - do - all complete job					
Qty vide Page No (7) in TMB					
@ Rs 19.89/m ² Item No (8)		2152.00m ²	R ₃		42,803=∞
(9) Plr and laying of S.P.B.c - do - do - all complete job					
Qty vide Page No (9) in TMB					
@ Rs 14052.59/m ³ Item No (9)		53.80m ³	R ₃		756363=∞
(10) Plr and fixing of Rec Mis Kilomble store - d. - do - all complete job					
Qty vide P.No (11) in TMB					
Item No (1)					
@ Rs 2987.92/m ³ 2 m ³			R ₃		5976=∞
(11) Plr and fixing of Rec Mis 200m store - d. - do - all complete job					
Qty vide P.No (11) in TMB					
Item No (2)					
@ Rs 827.10/m ³ 3 m ³			R ₃		2481=∞
(12) Plr and fixing of 600mm equilateral triangle Sign board - do. - do - all complete job					
Qty vide P.No (11) in TMB					
Item No (2)(1)					
@ Rs 4558.38/m ² 4 m ²			R ₃		18,234=∞
Total B					187,093=∞

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
				B 1 F R ₃	18,71,093 = ∞
($\frac{13}{13}$) Plv and fixing of 600MM circular					
Sign board - do - do - all complete job					
				Qty vide P. No. (11) in TMB	
				item No. 2 (11)	
@ R 4354.27/M ²		10 M ²		B	43,543 = ∞
($\frac{14}{14}$) Plv and fixing of 600MM x 450MM					
Rectangle Sign board - do - do - all					
complete job					
				Qty vide Page No. (11) in TMB	
				item No. 2 (11)	
B 4210.20/M ²		4 M ²		B	16,841 = ∞
($\frac{5}{3}$) Plv and laying of foot path					
Road marking - do - do - all complete					
job					
				Qty vide P. No. (7) in TMB	
				item No. 60	
@ R 886.50/M ²		114.00 M ²		B	1,01,061 = ∞
($\frac{16}{16}$) Plv and fixing of typical HR (300)					
information sign board - do - do - all					
complete job					
				Qty vide Page No. (7) in TMB	
@ R 11127.72/M ²		1 M ²		B	11,128 = ∞
($\frac{17}{17}$) Plv and fixing of Guard					
stone, boundary pillar - do - do - all					
complete job					
				Qty vide P. No. (12) in TMB	
				item No. (3)	
@ R 702.35/M ²		40 M ²		B	28,094 = ∞
($\frac{18}{18}$) Planting of tree by the roadside					
- do - do - all complete job					
				Qty vide Page No. (12) in TMB	
				item No. (4)	
@ R 1305.10/M ²		57 M ²		B	74,391 = ∞
				B	21,46,151 = ∞

Sch. XLV—Form No. 134					
Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
			BIF B	25,57,670=∞	
			Add G.S. @ 18% ⊕ B	4,60,381=∞	
			Add L.C.E.S. @ 14% ⊕ B	25,577=∞	
			Add S.Fee ⊕ — B	32,287=∞	
			Total B-	30,75,915=∞	
Below 0.04% as Per Agreement (-) B(-)				1,230=∞	
			Total B,	30,74,685=∞	
Deduct previous payment (-) B				28,49,198=∞	
(vide P.N. ⑩)			Total B,	22,54,87=∞	
			<i>[Signature]</i>		
			06/12/2024		
			DE		
			AF		
