



कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, मढ़ौरा।

E-Mail - eerwd.marhaura@yahoo.com

पत्रांक:- 384/अ.30

मढ़ौरा/दिनांक:- 24.03.25

प्रेषक:-

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, मढ़ौरा।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण, बिहार, पटना।

विषय:- शीर्ष MR-3054 योजनान्तर्गत बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत स्वीकृत पथ में कराये गये कार्य का आवंटन मॉग के संबंध में।

प्रसंग:- भवदीय के पत्रांक:-113 अनु0, दिनांक:-10-01-2020

महाशय,

उपरोक्त विषयक प्रासंगिक पत्र के संबंध में कहना है कि इस कार्य प्रमंडल, अंतर्गत शीर्ष-3054 (MR-3054) अंतर्गत बिहार ग्रामीण पथ नई अनुरक्षण नीति-2018 के तहत संवेदक श्री ललन कुमार के द्वारा पथ में किये गये कार्य का अधियाचना उक्त प्रासंगिक पत्र द्वारा प्राप्त विहित प्रपत्र में भरकर आवंटन मॉग हेतु अधियाचना-पत्र सादर समर्पित की जा रही है।

अतः अनुरोध है कि अधियाचना प्रपत्र में दर्शाये गये पथवार राशि कॉलम सं0-18 के अनुरूप पथ में आवंटन उपलब्ध कराने की कृपा की जाय ताकि संबंधित संवेदक द्वारा पथ में कराये गये कार्य का भुगतान किया जा सकें।

अनु0-1) अधियाचना प्रपत्र।

2) 19 ए प्रपत्र।

3) BOMP Indicator Report संलग्न।

4) MB प्रति संलग्न।

विश्वासभाजन

24/3/25

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, मढ़ौरा।

24/3/25

FORM GER-19-A


(See Government of India's Decision (I) below Rule -150)
Form of Utilization Certificate up to the Month of March-2025
PIU:- Executive Engineer RWD Works Division, Marhaura

SL No	Name of Scheme	Sanction No & Date with Amount (in Lacs Rs.)	Amount Received (in lacs Rs.)	Particulars
1	Construction of Rural Roads under MR-3054 Rural Road Maintenance Policy-2018 (Ledger ID-7069)	सचिव ब्राडा के पत्रांक-02 we दिनांक-14-01-2025	11667.64926	Certified that out of Rs- 11667.64926 Lacs received during the Years, 2018-19 & 2019-20, 2020-21, 2021-22, 22-23, 23-24 & 2024-25 in favour of E.E., R.W.D. Works Division Marhaura Sum of Rs- 11627.55974 Lacs has been utilized for the Purpose of MR-3054 New Maint. Policy-2018 Scheme as given in the margin for Which it was Sanctioned and that the balance of Rs-40.08952 Lacs remaining unutilized at CFMS the end of the period under report.



Sr. DAO

R.W.D. (W) Division Marhaura



Executive Engineer

R.W.D. (W) Division Marhaura

Requisition Formate for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of works Division:- Rural Work Department, Work Division, Marhaura.

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA) Total		Agreement Amount (In Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Alloted Amount (In Lakh)	up-to-date expenditure as per MIS (In Lakh)	Requisition agalnst work done. (In Lakh)	Remarks
					Length (In Km.)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Years Routine Maintenance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/23-24 Marhaura/11 RM/SA/MAR/ 24/0003	Gaurra Tejpuba Path (Brahm Sihan) To Chanda Bin Toli Tak	31306512025	Lt.- No-2178 Date-20-10-2022	1.600	92.47000	70.41542	12.06040	18/MR-3054-N- (MBD/2024-25) Dt-19-10-2024	18.07.2025		2650.00	N/A	N/A	0.00000	0.00000	58.51813 ✓	Work In Progress
2	MR-N/23-24 Marhaura/11 RM/SA/MAR/ 24/0003	Silauri Paharpur Pakki Sadak (Asoiya Chauk) to Pachim Tola tak	31306513035	Lt.- No-2178 Date-20-10-2022	1.500	93.40000	73.33475	9.62925	18/MR-3054-N- (MBD/2024-25) Dt-19-10-2024	18.07.2025		2833.00	N/A	N/A	0.00000	0.00000	69.96235 ✓	Work In Progress
3	MR-N/23-24 Marhaura/11 RM/SA/MAR/ 24/0003	Raspriya Singh (Brij Bihari Singh) Ke Ghar To Gandki Nadi Pull Via Lakshman Chowk	N313065024001	Lt.- No-2178 Date-20-10-2022	1.240	84.76000	67.99282	6.39670	18/MR-3054-N- (MBD/2024-25) Dt-19-10-2024	18.07.2025		2741.00	N/A	N/A	0.00000	0.00000	57.60388 ✓	Work In Progress
4	MR-N/23-24 Marhaura/11 RM/SA/MAR/ 24/0003	Dyalpur Gaura Bawansadak To Mashaha Ahir Tola Tak Path	31306513013	Lt.- No-2178 Date-20-10-2022	1.000	61.60300	46.54781	8.39790	18/MR-3054-N- (MBD/2024-25) Dt-19-10-2024	18.07.2025		2451.00	N/A	N/A	0.00000	0.00000	33.90786 ✓	Work In Progress
Total:-															0.00000	0.00000	219.99222	

1. Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.
2. Up-to-date Physical Progress has been Uploaded in MIS.

[Handwritten Signature]

[Handwritten Signature]
24/3/25
Executive Engineer
Rural Work Department
Work Division, Marhaura

Road Name:- Silauri Paharpur Pakki Sadak (Asoiya Chauk) to Pachim Tola tak

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY	Latitude	Longitude	Event
5/3/25	14:11:20	59	0.1	320	10.1	3200	2860	G	25.920177	84.8384	Normal
5/3/25	14:12:32	59	0.1	310	10.1	3100	2779	G	25.92059	84.837238	Normal
5/3/25	14:13:7	59	0.1	320	10.1	3200	2860	G	25.920913	84.83677	Normal
5/3/25	14:13:43	59	0.1	330	30.3	3300	2942	G	25.921168	84.836312	Normal
5/3/25	14:13:43	59	0.1	310	20.2	3100	2779	G	25.921465	84.83574	Normal
5/3/25	14:14:18	59	0.1	340	0	3400	3023	G	25.92184	84.835318	Speed Breaker
5/3/25	14:16:4	59	0.1	320	10.1	3200	2860	G	25.922388	84.83502	Normal
5/3/25	14:16:4	59	0.1	310	10.1	3100	2779	G	25.922837	84.833955	Normal
5/3/25	14:16:39	59	0.1	280	10.1	2800	2534	G	25.923207	84.833047	Normal
5/3/25	14:17:0	59	0.1	260	20.2	2600	2371	G	25.92365	84.83276	Normal
5/3/25	14:17:13	59	0.1	270	20.2	2700	2452	G	25.924125	84.832172	Normal
5/3/25	14:17:13	59	0.1	290	20.2	2900	2615	G	25.924775	84.830975	Normal
5/3/25	14:18:0	59	0.1	360	0	3600	3186	G	25.92528	84.83002	Speed Breaker
5/3/25	14:18:24	59	0.1	360	20.2	3600	3186	G	25.926442	84.829443	Normal
5/3/25	14:18:24	59	0.1	370	0	3700	3268	G	25.926913	84.82867	Speed Breaker
Total Length			1.500	Average IRI			2833				

$$Y = 0 * X^2 + 0.816 * X + 249$$

$$X = 3.166$$

$$Y = 2833$$

(R) RURAL ROAD

Good Average Poor
 <4000 4001-5000 >5001

Done
 06/03/25
 AE

2/3/25
 EE

Done
 6/3/25
 AE

Name of Customer : Lalan Kumar
 Name of Work/ Road : Asoiya Chauk to Pachim Tola tal.
 Lab Job number : 59
 Date : 05/03/2025
 Section No. : 59


Test Date : 05/03/2025 Road Name : Asoiya Chauk to Pachim Tola tal.
 Machine No : 384 Road Type : (R) RURAL ROAD
 Start S No : Side : Interval
 Start E No :
 Weather : NORMAL UIV Range : 1371 To 4000 1000 mm/km
 Start Location : Dist Range : 0 To 1.6 0.1 * 1000 m
 End Location : Equation : $Y = 0 * X^2 + 0.816 * X + 249$

Print Generate Report and Graph

Redraw Graph

Map View

File C:\Users\Admin\Desktop\Bump 05.03.2025\05031503.Xls. Section No. : 59, Eqn : $Y = 0 * X^2 + 0.816 * X + 249$
 Name of Customer : Lalan Kumar, Name of Work/ Road : Silauri Paharpur Pakki Sadak (Asoiya Chauk) to Pachim Tola

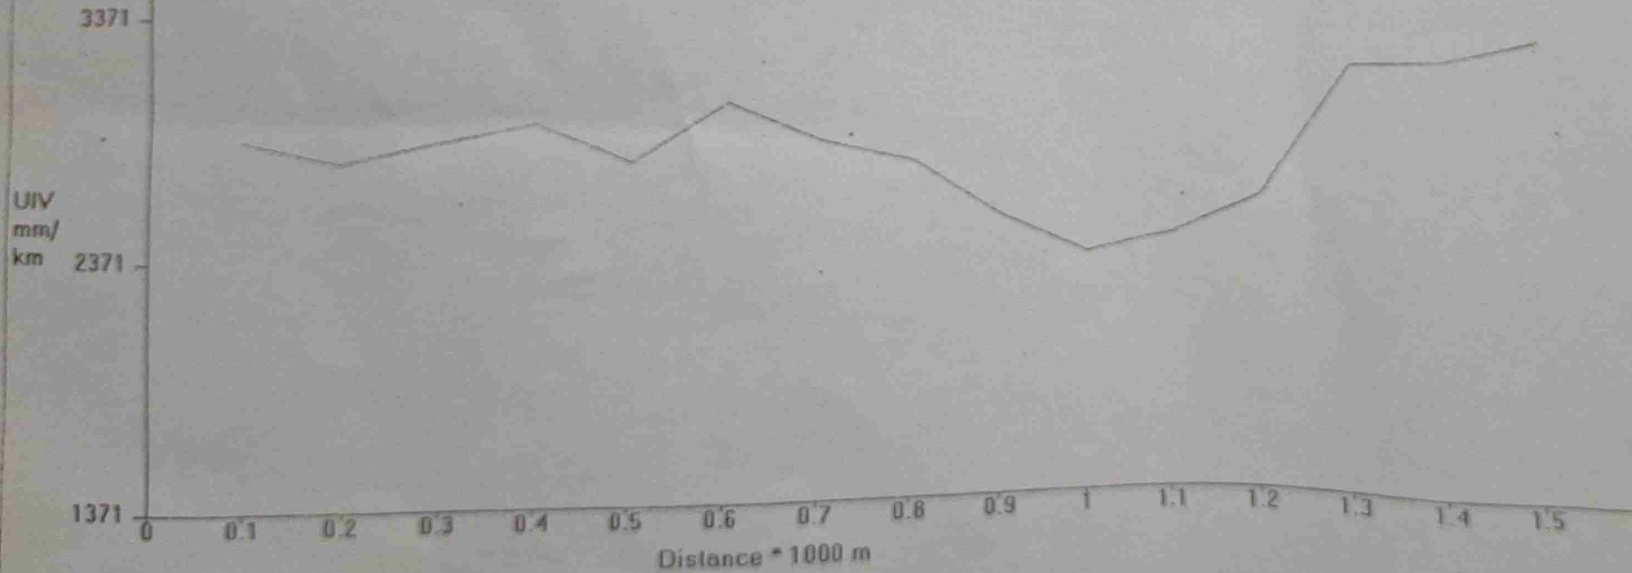

6/3/25
JE

06/03/25
AE

D
24/3/25
EE

SILAURI Paharpur Pakki Sadak (Asoiya Chowk)

Schedule XLV-Form No. 134

To Pachim TOLA TAK

MB NO 1041

Executive Engineer
Rural Works Department
Works Division, Silaura

MARHAUSA

DIVISION

Marhausa

SUB-DIVISION

Lalan Kumar

MEASUREMENT BOOK


1
Name of Work—
Situation of Work—
Agency by which work is executed—
Date of Measurement—
No. and date of agreement

(These four lines should be repeated at the commencement of the measurement relating to each work)

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
Name of work:— Silouni bahampur pakki sarak (gadiya chaur) To Pachim taluk.					
Agency:— Sri Lalun Kumar					
Agreement No:— 18/MR-3054-N-1/MBD/24-25					
Date of work order:— 19.10.2024					
Date of Completion:— 18.07.2025					
Situation:— on going (1 st on A/C Bill)					
Date of measurement:— 11/3/25					

1> clearing and grubbing road land:—					
2x10 30 0.75 =	450M ²				
2x10 30 0.75 =	450M ²				
2x10 30 0.75 =	450M ²				
2x10 30 0.75 =	450M ²				
2x10 30 0.75 =	450M ²				
	2250M ²				
	=	0.225Ha			
2> Logo of Project					
2	=	2Nos			
3> Providing G.S.B					
grading-TT Pot patch					
measurement:—					
2 3.35 1.10 0.175 =	1.98M ³				

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
	1	30	3.714	0.025	2.88 m ³
	1	30	3.60	0.025	2.70 m ³
	1	30	3.70	0.025	2.775 m ³
	1	30	3.6	0.025	2.70 m ³
	1	30	3.6139	0.025	2.81 m ³
	1	30	3.70	0.025	2.775 m ³
	1	30	3.75	0.025	2.81 m ³
	1	30	3.40	0.025	2.55 m ³
	1	10	2.4+2.3	0.025	0.71 m ³
					28.145 m ³
Mr.  22/03/25 AE					
B. Bhushan 22/03/25					

<u>Abstract of Cost:-</u>				
1) Clearing & Chubbing				
Road land :- TMB-L				
0.225 Ha				
@ 76926.08/Ha =				17308.37
2) Providing G.S.B				
grading - II Pot Patch				
TMB:- 2				
3.36 m ³				
As per A.A = 3.266 m ³				
@ 254133/m ³ =				8299.98
3) Providing WBM				
Grade - II Pot Patch				
TMB - 2				
3.27 m ³				
As per A.A = 3.119 m ³				
@ 5646.07/m ³ =				17610.09
4) Providing WBM grade-3				
Pot Patch TMB-2				

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
9.55 m ³ As per A/A					
9.486 m ³ @ 5744.83/m ³ =					48803.85
5> Provide prime coat TMB-4					
127.27 m ² As per A/A = 126.48 m ² @ 57.40/m ² =					7259.95
6> Provide & applying track coat: TMB-4					
1126.5 m ² As per A/A					
1106.25 m ² @ 16.48/m ² =					18231.00
7> Provide & laying SDBC: TMB-5					
28.145 m ³ As per A/A = 27.94 m ³ @ 14678.55/m ³ =					410118.69
8> Provide DL c					
TMB-2					
9.98 m ³ @					
As per A/A					
9.04 m ³ @ 522733/m ³ =					47255.06
9> Provide panel concrete Pavement:-					
TMB-3					
571.51 m ³ As per A/A					
570.49 m ³ @ 9247.18/m ³ =					5275423.72
10> Logo of Project					
TMB-01					
2 No @ 10926.09/					21852.18
14994.5/E =					29989.06
					5880299.74
C.O =					185872162.80
Below 4.25% =					-249566.91

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
					= 5622595.97
					B.F = Rs 58,72,162.89
					Add S.T 18% (H) Rs 10,56,909.32
					Add I.Y.L.C = (H) Rs 58,721.63
					Add reg no cumy p fee (H) Rs 8361.39
					<u>Rs 69,96,235.23</u>
					Say = Rs 69,96,235 = w
					(Kumar) 23/03/25 AE
					(Rajesh) 23/03/25
					C 20 24/03/25 EA
