

कार्यपालक अभियंता का कार्यालय
ग्रामीणकार्य विभाग, कार्यप्रमंडल, जमुई

पत्रांक- 557 (3180)

जमुई, दिनांक- 05/05/2025

प्रेषक :- कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, जमुई।

सेवामें,
नोडल पदाधिकारी,
"नई अनुरक्षणनीति 2018" (3054-MR)
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय :- 3054 (MR)नई अनुरक्षणनीति 2018 के अन्तर्गत निर्माण कराये गये योजनाओं के विरुद्ध में आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषयक के संबंध में सूचित करना है कि 3054 (MR)नई अनुरक्षणनीति 2018 के अंतर्गत संलग्न सूची में अंकित पथों में कालीकरण का कार्य पूर्ण हो चुका है। प्रमंडल के द्वारा कराये गये कार्य के भुगतान हेतु कुल राशि रु0 173.02842 (एक करोड़ तिहत्तर लाख दो हजार आठ सौ बियालीस रुपये) लाख मात्र आवंटन की अधियाचना विहित प्रपत्र में भरकर समर्पित की जाती है।

अतः अनुरोध है कि शीघ्र आवंटन उपलब्ध कराने की कृपा की जाय।

अनु0: यथोक्त।

विश्वासभाजन


05/05/25
कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, जमुई।
31/5/25

FORM GFR 19-A

(Government of India's Decision (I) below Rule-150)
Form of Utilisation Certificate as on 31.03.2025
MR 3054(Bihar Rural Road New Maintenance Policy-2018)

STATE-BIHAR
PIU - E.E.RWD (W), Div.- Jamui

Month: March-2025



Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in Rs. Lacs)	Amount Received (in Rs. Lacs)	Particulars
1	Construction of Rural Roads under MR 3054 (Bihar Rural Road New Maintenance Policy-2018)	F.Y. - 2024-2025 Vide Letter No-29 Dated- 30.03.2025	18942.03221	Certified that out of Rs18942.03221 Lacs received during the years 2024-2025 in favour of Executive Engineer, RWD (W), Div.- Jamui, Bihar, a sum of Rs 18938.35836 Lacs has been utilized for the purpose of MR Policy -2018 (3054) Schemes as given in the margin for which it was sanctioned and that the balance of Rs 3.67385 Lacs remaining unutilized at the end of the period under.
			18942.03221	

I Certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks exercised :-

- Works have been supervised by Executive Engineer/ Supertending Engineer.
- Periodical inspection has been conducted by Executive Engineer/ Supertending Engineer.
- Construction materials have been tested
- Measurements have been recorded in the MBs and test check conducted by the Assistant.
- All other codal formalities have been observed.


Sr.Accounts Officer
R.W.D Works Division
Jamui


Executive Engineer
R.W.D Works Division
Jamui

3/5/25

Office of The Executive Engineer, Rural Works Department, Works Division Jamui
Requisition formate for Scheme Head- MR-3054 Under Bihar Rural Road Maintenance Policy -2018 (Initial Rectification with Surface Renewal)

Sl.No.	Package No	Name of Road	Project ID As per MIS	A.A. Letter No & Date	Administrative Approval (A.A.)		Agreement Amount (in Lakh)		Agreement No & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen content in Percentage (Including waste Plastic)	Previous Total Alloted Amount (in Lakh)	Up-to-Date Expenditure as per MIS (in lakh)	Requisition against work done (in lakh)	Remarks
					Length (in K.M.)	Amount (in lakh)	Initial Rectification with Surface Renewal (in lakh)	5 Years Routine Maintenance										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/JA/JAM/23/0013	L074-Bujhayat to Masarhandi (TRACK74) RRP-II	Project ID- 20804102150	6120 / 04.12.2023	3.8	236.676	152.68468	45.71405	01(MBD)/2024-25	22.04.2025	17.04.2025	2963	25	5%	83.03020	83.03020	31.29908	Work Completed
2	RM/JA/JAM/23/0013	L089-PMGSY road Majhiyani to Jagarnadih (TRACK89)	Project ID- 20804102169	6120 / 04.12.2023	2.65	171.328	104.60843	30.5421	00(MBD)/2024-25	22.04.2025	11.04.2025	3185	25	5%	58.71585	58.71585	44.32621	Work Completed
3	RM/JA/JAM/23/0013	L067-Jhundo to Jituadih (TRACK67) RRP-II	Project ID- 20804102140	6120 / 04.12.2023	2	116.415	112.213	25.93466	01(MBD)/2024-25	22.04.2025	18.04.2025	2962	25	5%	63.11026	63.11026	6.77169	Work Completed
4	RM/JA/JAM/23/0013	L073-Jamui Kauwakol road to Bichkorba (TRACK73) RRP-II	Project ID- 20804102149	6120 / 04.12.2023	2.95	182.313	113.03329	35.22454	01(MBD)/2024-25	22.04.2025	16.04.2025	2993	25	5%	61.27282	61.27282	41.37874	Work Completed

[Handwritten signature]
03/12/25

[Handwritten signature]



5	RN/JA/JAM/23/0012	L041-Jamui Kharagpur PWD road to Darha (VR41) RRP- II	Project ID- 20804102121	6120 / 04.12.2023	4 600	274 404	168 97018	57.18529	02(MBD)/2024-25	22.04.2025	10.04.2025	3142	25	5%	152.63956	152.63956	14.70505	Work Completed
6	RN/JA/JAM/23/0012	Jamui Kharagpur PWD road Paro more to Lalmatia road	Project ID- 20804100840	6120 / 04.12.2023	9.486	437.577	275.6007	99.14307	02(MBD)/2024-25	22.04.2025	02.04.2025	3006	25	5%	240.60071	240.60071	34.54765	Work Completed

Sub
03/5/25

BS
3/5/25

Executive Engineer,
Rural Works Department,
Works Division, Jamui



Name of Work-L067-Jhundo to Jitradih (TRAC K6") RRP-II										Name of Contractor-Alok Kumar Singh	
Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
2/2/25	11:38:10	1	0.1	280	0	2800	2659	G	24.78991	86.22239	Normal
2/2/25	11:38:12	1	0.1	250	10.1	2500	2411	G	24.78924	86.223013	Normal
2/2/25	11:38:20	1	0.1	280	20.2	2800	2659	G	24.788673	86.22345	Normal
2/2/25	11:38:46	1	0.1	250	20.2	2500	2411	G	24.788102	86.22382	Normal
2/2/25	11:39:0	1	0.1	300	20.2	3000	2825	G	24.78777	86.224427	Normal
2/2/25	11:39:0	1	0.1	270	20.2	2700	2577	G	24.787308	86.224948	Normal
2/2/25	11:39:21	1	0.1	360	20.2	3600	3322	G	24.786853	86.22547	Normal
2/2/25	11:39:21	1	0.1	360	20.2	3600	3322	G	24.786593	86.226515	Normal
2/2/25	11:39:21	1	0.1	200	20.2	2000	1997	G	24.786715	86.226958	Normal
2/2/25	11:40:0	1	0.1	350	20.2	3500	3239	G	24.787095	86.227793	Normal
2/2/25	11:40:0	1	0.1	370	20.2	3700	3405	G	24.787462	86.228703	Normal
2/2/25	11:40:31	1	0.1	310	20.2	3100	2908	G	24.78773	86.229493	Normal
2/2/25	11:40:31	1	0.1	300	20.2	3000	2825	G	24.788122	86.230235	Normal
2/2/25	11:40:31	1	0.1	310	20.2	3100	2908	G	24.788378	86.230925	Normal
2/2/25	11:41:0	1	0.1	330	20.2	3300	3073	G	24.788048	86.231515	Normal
2/2/25	11:42:16	1	0.1	350	20.2	3500	3239	G	24.78669	86.232827	Normal
2/2/25	11:42:16	1	0.1	410	10.1	4100	3736	G	24.786177	86.233298	Normal
2/2/25	11:43:0	1	0.1	360	10.1	3600	3322	G	24.78566	86.234175	Normal
2/2/25	11:43:27	1	0.1	340	10.1	3400	3156	G	24.786148	86.234747	Normal
2/2/25	11:44:2	1	0.1	350	10.1	3500	3239	G	24.786987	86.235437	Normal
Length			2.0	Total IRI			59233				
				Average IRI			2962				

$$Y = 0 * X^2 + 0.823 * X + 341.6$$

$$X = 3500$$

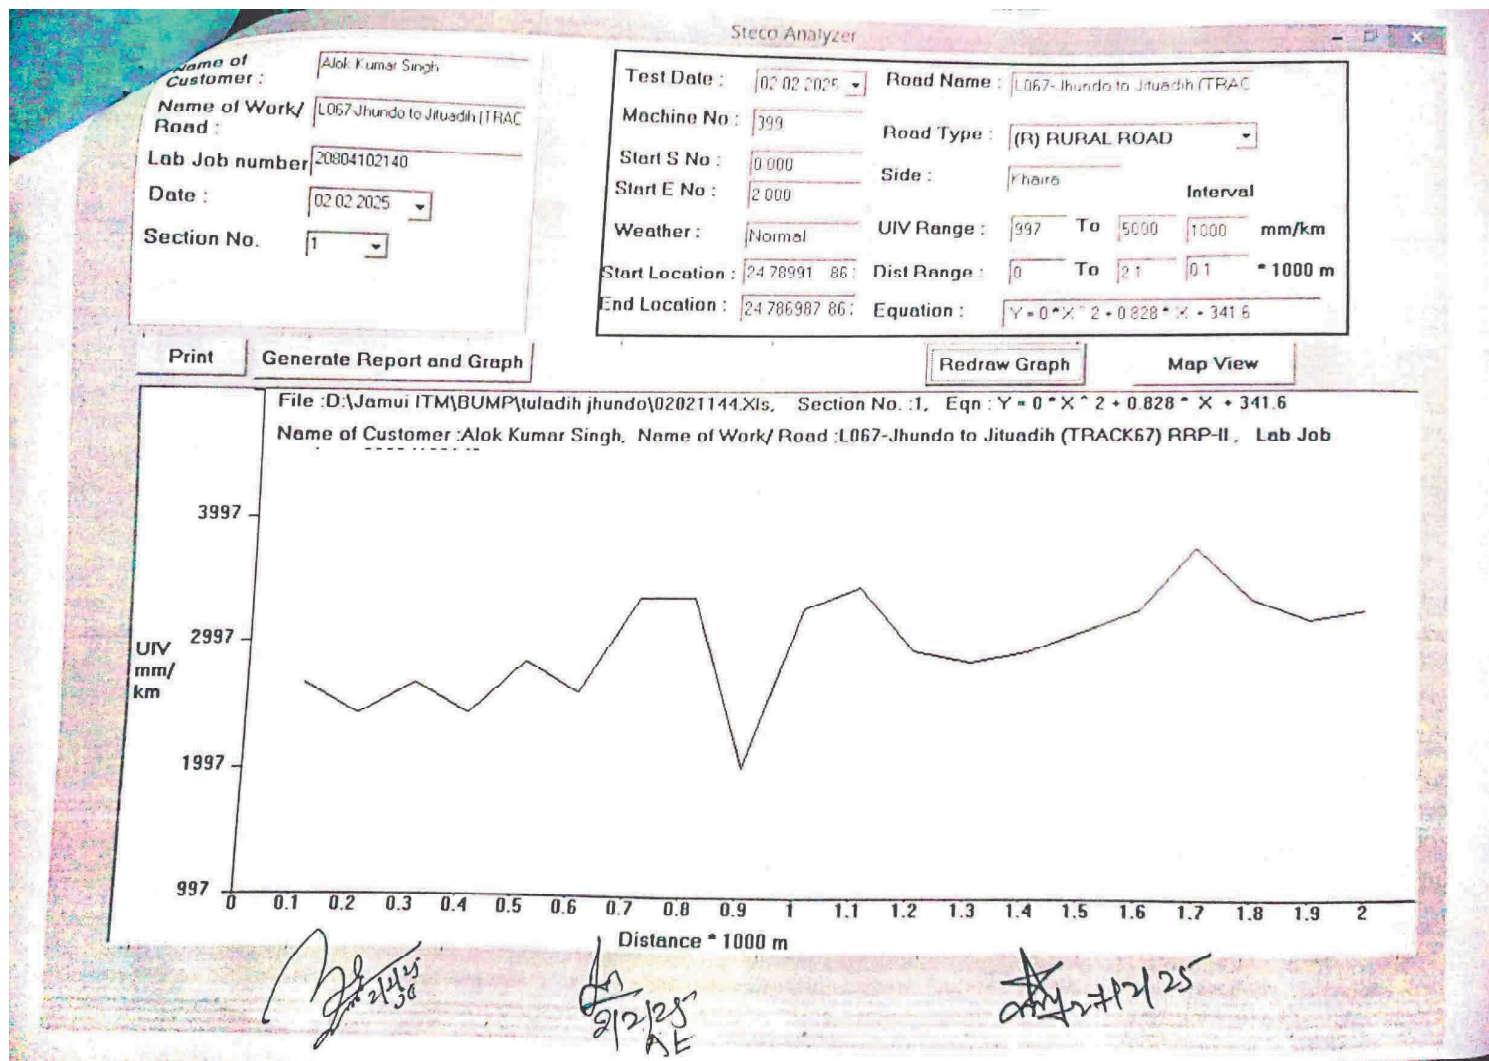
$$Y = 3239$$

(R) RURAL ROAD
Good Average Poor
<4000 4001-5000 >5001

J.E
27/2/25

A.E
9/2/25

A.E
27/2/25



(1) Earthwork in excavation for foundation —

$2 \times 2 \times 3.90 \times 1.15 \times 1.50 \times 2$	26.91 m^3
$2 \times 1 \times 5.35 \times 1.13 \times 0.365 \times 2$	4.41
Total	31.32 m^3

(2) Providing R.C.C M-15 of leveling course in shed —

$2 \times 2 \times 3.90 \times 1.15 \times 0.15 \times 2$	2.69 m^3
$2 \times 1 \times 5.31 \times 1.13 \times 0.25 \times 2$	3.00
Total	5.69 m^3

(3) Plinth / reinforced cement concrete in substructure complete —



Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
$2 \times 2 \times 3.60 \times 6.40 + 1.00 \times 2.78 = 28.02 \text{ m}^2$					
less $2 \times 2 \times 0.785 \times 6.40 \times 2 = 10.53 \text{ m}^2$					
					Net area = 26.874 m^2
(4) Providing & laying R.C.C.					
pipe N/3 600 mm dia.					
$2 \times 3 \times 2.50 = 15.00 \text{ m}$					
(5) Painting two coats					
including primer					
$2 \times 4 \times 3.60 \times 0.60 = 17.28 \text{ m}^2$					
$2 \times 2 \times 3.60 \times 0.40 = 5.76 \text{ m}^2$					
$2 \times 4 \times 6.15 \times 0.60 = 29.52 \text{ m}^2$					
$2 \times 2 \times 6.15 \times 0.40 = 9.84 \text{ m}^2$					
$4 \times 4 \times 0.40 \times 0.60 = 3.84 \text{ m}^2$					
Total = 66.24 m^2					
(6) kilometre stone					2.00 nos.
(7) 200 m stone post					8.00 nos.
(8) Direction & place sign.					
$3 \times 1.20 \times 0.80 = 2.88 \text{ m}^2$					
(9) 600 mm equilateral triangle					2.00 nos.
(10) 600 mm circular					2.00 nos.
(11) 600 x 450 mm Rectangular					3.00 nos.
(12) 900 mm wide octagon					2 nos.
(13) Boundary Pillar					30.00 nos.
(14) Maintenance band					1.00 m.
(15) Planting of tree & shrub.					80.00 nos.

Continuation

18/9/25

2nd on A/C B/M

Abstract of est.

19



Sch. XLV-Form No. 134

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
(1/1) clearing & grubbing road land.					
avg width by - (10)					
0.286 ha					
@ 76926.08/ha					2200/200
(2/2) construction of subgrade					
8 center shoulder.					
avg width by - (10)					
833.76 m					
@ 173.51/m					144666/200
(3/3) Granular sub base with well graded material					
avg width by - (10)					
148.23 m					
@ 1974.00/m					292606/200
(4/4) WBM Grading - 3					
avg width by - (10)					
298.091 m					
@ 3631.75/m					1082592/200
(5/5) Prime coat (Low Porosity)					
avg width by - (10)					
3984.547 m					
@ 57.57/m					228815/200

Continuation Rs. 1770680/200



less 2.32%	165,244.20
less Premium Payment	69,881.95
THAT (15)	631,026.20
	6,771,692.00

08/04/18
 JE

18 APR
 AL

Scanned with OKEN Scanner
