

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, चकिया, (पूर्वी चम्पारण)।

पत्रांक: 874/अनु0 / चकिया, दिनांक: 19/05/2025

प्रेषक

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, चकिया।

सेवा मे,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास एजेंसी,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषय- विभाग के नई निति रख-रखाव 2018 M.R (3054) योजना के अन्तर्गत निर्माणाधीन कार्य के लिए निधि उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में विभाग के नई निति रख-रखाव 2018 M.R (3054) योजना के अन्तर्गत निर्माणाधीन कार्य के लिए पथवार मांगी जाने वाली आवंटन की सूची पत्र के साथ भवदीय के अवलोकनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अतः संलग्न सूची के अनुसार आवंटन उपलब्ध कराने की कृपा की जाय।

- अनु0:- 1. आवंटन की सूची।
2. मापी पुस्त की छाया प्रति।
3. Bump Test Integrator Machine

विश्वासभाजन,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल-चकिया।

ज्ञापांक- 874 दिनांक- 19-05-2025

प्रतिलिपि-नोडल पदाधिकारी (3054), ग्रामीण कार्य विभाग, बिहार, पटना को सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।

- अनु0:- 1. आवंटन की सूची।
2. मापी पुस्त की छाया प्रति।
3. Bump Test Integrator Machine

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल-चकिया।

**OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, Chakia.**

Requisition Format for Scheme Head- MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division : Chakia

SI No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval ((AA) Latter No. & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Alloted Amount (in lakh)	up-to- date expenditure as per MIS (in Lakh)	Requisition against work done. (in Lakh)	Remarks
					Length (in Km)	Amount of (in Lakh)	Initial Rectification with Surface Renewal (in lakh)	5 Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/EA/CHA/24/0002	PWD Chakiya Kesariya Mela Chowk to Lakshmipur	31708412020	Latter No.6116 Date- 04.12.2023	2.480	118.690	86.74864	24.39026	1 MBD/2024-25 Date - 29.08.2024	28.05.2025	Work in Progress	2404.00	25	5.00	85.34908	85.34908	0.97498	Work in Progress
					2.480	118.690	86.74864	24.390							85.34908	85.34908	0.97498	

- 1 Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.
- 2 Up-to-date Physical Progress has been uploaded in MIS.


Executive Engineer,
Rural Works Department,
Works Division, Chakia.

19/05/25

Form GER 19-A
(See Government of India's decision (1) bellow Rule - 150)
Form of utilization certificate up to the month up to 05/2025
M.R. (3054) New maintenance Policy-2018.

PIU - RWD , W.D- CHAKIA


SL. NO	Name of Scheme	Sanction No. / Date with Amount (in RS. Lachs)	Amount Received (in RS. Lacks)	particulars
1	M.R. (3054) New maintenance Policy-2018	13191.35483	13191.35483	Certified that out of Rs.13191.35483 Lakh Receive upto the Month, May-25 (F.Y 2025-26) executive engineer RWD, (W) DIV, chakia a sum of RS.12710.35515 Lakh has been utilized for the perpose of M.R. (3054) New maintenance Policy-2018 'CFMS' Schemes given in the margin for which it was sanctioned and that the balance of Rs.480.99968 lakh remaining unutilized at this end of the (up to 05/2025)

2. Certificate that I have satisfied myself that the conditions on which the grand's-in-aid was sanctioned have been duly fulfilled/ate being fulfilled and that have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned kinds of cheks exercised:-

- Works have been supervised by Executive Engineer/ Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
- Construction materials have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant.

3. Physical Progress achieved :-

- Construction of M.R. (3054) New maintenance Policy-2018 (Details in Progress report)
- Construction of Road Works. (.....Do.....)


Executive Engineer,
Rural Works Department,
Works Division, Chakia.


Name of work : PWD Chakia Kesariya Mela Chowk to Lakshmipur

Name of customer : Hari Kishore Prasad Gupta

(R)Rural Road			
Good		Average	Poor
< 4000		4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
26/11/24	10:40:10	36	0	0	0.0 cm	0.0 Km/Hr	0.0 mm/Km	205	0.37	Good	26.5535727	N	84.9210291	E	Normal
26/11/24	10:41:30	36	100	100	23.0 cm	13.8 Km/Hr	2300.0 mm/Km	2337	3.22	Good	26.3493785	N	84.9428614	E	Normal
26/11/24	10:41:51	36	100	200	21.0 cm	17.0 Km/Hr	2100.0 mm/Km	2152	2.99	Good	26.3494858	N	84.9428491	E	Normal
26/11/24	10:42:05	36	100	300	25.0 cm	25.4 Km/Hr	2500.0 mm/Km	2522	3.45	Good	26.3494341	N	84.9428273	E	Normal
26/11/24	10:42:19	36	100	400	22.0 cm	26.7 Km/Hr	2200.0 mm/Km	2244	3.11	Good	26.3494917	N	84.9429363	E	Normal
26/11/24	10:42:35	36	100	500	26.0 cm	22.5 Km/Hr	2600.0 mm/Km	2615	3.56	Good	26.3495488	N	84.9425484	E	Normal
26/11/24	10:42:55	36	100	600	25.0 cm	18.2 Km/Hr	2500.0 mm/Km	2522	3.45	Good	26.3466542	N	84.9424134	E	Normal
26/11/24	10:43:16	36	100	700	24.0 cm	16.6 Km/Hr	2400.0 mm/Km	2430	3.34	Good	26.3465982	N	84.9428058	E	Normal
26/11/24	10:43:55	36	100	800	24.0 cm	19.6 Km/Hr	2400.0 mm/Km	2430	3.34	Good	26.3465411	N	84.9428884	E	Normal
26/11/24	10:44:15	36	100	900	31.0 cm	17.4 Km/Hr	3100.0 mm/Km	3079	4.12	Good	26.3465398	N	84.9428911	E	Normal
26/11/24	10:44:40	36	100	1000	29.0 cm	15.0 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.3465354	N	84.9429317	E	Normal
26/11/24	10:45:02	36	100	1100	23.0 cm	15.8 Km/Hr	2300.0 mm/Km	2337	3.22	Good	26.3464997	N	84.9430237	E	Normal
26/11/24	10:45:33	36	100	1200	32.0 cm	11.5 Km/Hr	3200.0 mm/Km	3171	4.23	Good	26.3454646	N	84.9442554	E	Normal
26/11/24	10:45:56	36	100	1300	26.0 cm	16.0 Km/Hr	2600.0 mm/Km	2615	3.56	Good	26.3423811	N	84.9442064	E	Normal
26/11/24	10:46:17	36	100	1400	24.0 cm	17.2 Km/Hr	2400.0 mm/Km	2430	3.34	Good	26.3420742	N	84.9438289	E	Normal
26/11/24	10:46:40	36	100	1500	30.0 cm	15.6 Km/Hr	3000.0 mm/Km	2986	4.01	Good	26.3419485	N	84.9439192	E	Normal
26/11/24	10:47:09	36	100	1600	29.0 cm	12.6 Km/Hr	2900.0 mm/Km	2893	3.9	Good	26.3412323	N	84.9442252	E	Normal
26/11/24	10:47:33	36	100	1700	21.0 cm	14.8 Km/Hr	2100.0 mm/Km	2152	2.99	Good	26.3413290	N	84.9444687	E	Normal
26/11/24	10:47:56	36	100	1800	21.0 cm	15.5 Km/Hr	2100.0 mm/Km	2152	2.99	Good	26.3385656	N	84.9435574	E	Normal
26/11/24	10:48:18	36	100	1900	30.0 cm	16.3 Km/Hr	3000.0 mm/Km	2986	4.01	Good	26.3380437	N	84.9435567	E	Normal
26/11/24	10:48:33	36	100	2000	23.0 cm	22.9 Km/Hr	2300.0 mm/Km	2337	3.22	Good	26.3373311	N	84.9435084	E	Normal

Name of work	: PWD Chakia Kesariya Mela Chowk to Lakshmipur
Name of customer	: Hari Kishore Prasad Gupta

(R)Rural Road				
Good	Average		Poor	
< 4000	4001 - 5000		> 5000	

26/11/24	10:48:52	36	100	2100	23.0 cm	19.6 Km/Hr	2300.0 mm/Km	2337	3.22	Good	26.3371933	N	84.9439024	E	Normal
26/11/24	10:49:05	36	100	2200	23.0 cm	25.7 Km/Hr	2300.0 mm/Km	2337	3.22	Good	26.3367924	N	84.9434907	E	Normal
26/11/24	10:49:19	36	100	2300	22.0 cm	26.2 Km/Hr	2200.0 mm/Km	2244	3.11	Good	26.3377570	N	84.9392149	E	Normal
26/11/24	10:49:37	36	100	2400	21.0 cm	32.0 Km/Hr	2100.0 mm/Km	2152	2.99	Good	26.3390561	N	84.9376994	E	Normal
26//2114	10:49:48	36	100	2500	26.0 cm	31.5 Km/Hr	2600.0 mm/Km	2615	3.56	Good	26.3391578	N	84.9374171		

Avg IRI-2404

[Handwritten signature]
mm/hr

[Handwritten signature]
26/11/24

[Handwritten signature]
26/11/24
2E.

Name of Customer: Hari Kishore Prasad Gupta , Machine no: 19191 , Road: PWD Chakia Kesariya Mela Chowk to Lakshmipur , Date: 26-11-24 , Section No: 36 , Equation: $Y = 0.927 X + 204.8$

4100

3125

2150

1175

200

0

0.1

0.2

0.3

0.4

0.5

0.6

0.7

0.8

0.9

1

1.1

1.2

1.3

1.4

1.5

1.6

1.7

1.8

1.9

2

2.1

2.2

2.3

2.4

2.5

2.6

Distance*1000 m

for 26/11/24
26/11/24

for 26/11/24
26/11/24

for 26/11/24
26/11/24

3rd and final Bill

Sch. XLV-Form No.134

26

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	

Name of Work - Construction of road from PWD Chakia Kesaria Mda Chowk to Lakshiniga (MR-3054)

Agency - Hanikishore Prasad Gupta,

Agreement No - 01 MBD / 2024-25.

Agreement value - 1,11,19,037.00

Construction Cost - 86,78,791.00

Maintenance Cost - 24,40,246.00

Date of Start - 29/08/2024.

Date of Completion - 28/05/2025.

Actual date of Completion - 16/12/2024.

Record Entry

① Construction of Subgrade and Earthen Shoulder.

$$2 \times 2 \times 30 \times 0.9(\text{av}) \times 0.300(\text{av}) = 32.4 \text{ m}^3$$

$$2 \times 5 \times 30 \times 1.00(\text{av}) \times 0.45(\text{av}) = 135 \text{ m}^3$$

$$2 \times 2 \times 30 \times 0.9(\text{av}) \times 0.35(\text{av}) = 37.8 \text{ m}^3$$

$$2 \times 1 \times 30 \times 0.9(\text{av}) \times 0.300(\text{av}) = 16.2 \text{ m}^3$$

$$2 \times 2 \times 30 \times 1.00(\text{av}) \times 0.45(\text{av}) = 54.0 \text{ m}^3$$

$$2 \times 1 \times 20 \times 0.9(\text{av}) \times 0.300(\text{av}) = 10.8 \text{ m}^3$$

$$286.20 \text{ m}^3$$

② Planting of Trees by

$$\text{Road Side} = 0.6 \text{ Nos.}$$

[Signature]

[Signature]

[Signature]

Continuation

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	

Abstract of Cost

① Cleaning and grubbing road land.

$$QVTMB, P-21(1) = 0.496 \text{ Ha}$$

$$@Rs-76926=08/\text{Ha} \quad Rs = 38155200$$

② Construction of Subgrade and Earthen Shoulder

$$QVTMB, P-21(2) = 1836.00 \text{ m}^3$$

$$@Rs-QVTMB, P-26(1) = 286.20 \text{ m}^3$$

$$2122.2 \text{ m}^3$$

$$@Rs-256=09/\text{m}^3 \quad Rs = 54347400$$

③ Providing Granular subbase

$$QVTMB, P-22(3) = 32.13 \text{ m}^3$$

$$@Rs-3654=57/\text{m}^3 \quad Rs = 117421200$$

④ Providing, laying, spreading and Compacting WBM grade-2

$$QVTMB, P-22(4) = 66.67 \text{ m}^3$$

$$@Rs-5784=22/\text{m}^3 \quad Rs = 385634200$$

⑤ Providing, laying, spreading and Compacting WBM grade-2

$$QVTMB, P-22(5) = 138.85 \text{ m}^3$$

$$@Rs-5042=04/\text{m}^3 \quad Rs = 700087200$$

⑥ Providing Prime Coat with Emulsion (SS1)

$$QVTMB, P-22(6) = 1851.33 \text{ m}^2$$

$$@Rs-57=07/\text{m}^2 \quad Rs = 105655200$$

Continuation

$$BF = 1890426200$$

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
⑦ Providing laying and rolling mix Seal.					
QVTMB, P-22 ⑦ = 2455.61 m ²					
@ Rs-261 = 52/m ²					Rs- 642191=00
⑧ Providing Tack Coat with emulsion (Rs-1)					
QVTMB, P-22 ⑧ = 11848.61 m ²					
@ Rs-19 = 60/m ²					Rs- 232233=00
⑨ Providing laying SDBC					
QVTMB, P-23 ⑨ = 234.819 m ³					
@ Rs-15107 = 61/m ³					Rs- 3547554=00
⑩ Providing and fixing KM Stone.					
QVTMB, P-23 ⑩ = 04 Nos.					
@ Rs-3377 = 67/each					Rs- 13511=00
⑪ Providing and fixing 200 mm Stone.					
QVTMB, P-23 ⑪ = 10 Nos.					
@ Rs-890 = 43/each					Rs- 8904=00
⑫ 600 mm equilateral					
QVTMB, P-23 ⑫ = 08 Nos.					
@ Rs-4630 = 07/each					Rs- 37041=00
⑬ 600 mm Circular					
QVTMB, P-23 ⑬ = 08 Nos.					
@ Rs-6079 = 69/each					Rs- 48638=00
Continuation B.F = 6420498=00					

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
⑭ 600 mm X 450 mm.					
② VTMB, P-23 ⑭ = 04 Nos.					
@ Rs - 5090 = 92/each					Rs - 20364.00 ✓
⑮ Planting of Trees by the Road Side.					
② VTMB, P-23 ⑮ = 07 ^{74 Nos.} Nos.					
② VTMB, P-26 ⑮ = 06 Nos.					
					80 Nos. ✓
@ Rs - 1305 = 10/each					Rs - 104408.00 ✓
⑯ Providing and laying Road Marking.					
② VTMB, P-23 ⑯ = 496.00 m ²					
@ Rs - 886 = 50/m ²					Rs - 439704.00 ✓
⑰ Providing & fixing MMSY informatory sign board.					
② VTMB, P-24 ⑰ = 03 Nos.					
@ Rs - 17262 = 05/each					Rs - 5786.00 ✓
⑱ Brick masonry work in cm (1:3) in parapet.					
② VTMB, P-24 ⑱ = 14.40 m ³					
@ Rs - 9102 = 68/m ³					Rs - 131079.00 ✓
⑲ Plastering with cm (1:4)					
② VTMB, P-24 ⑲ = 100.89 m ²					
@ Rs - 246 = 37/m ²					Rs - 24831.00 ✓

Continuation

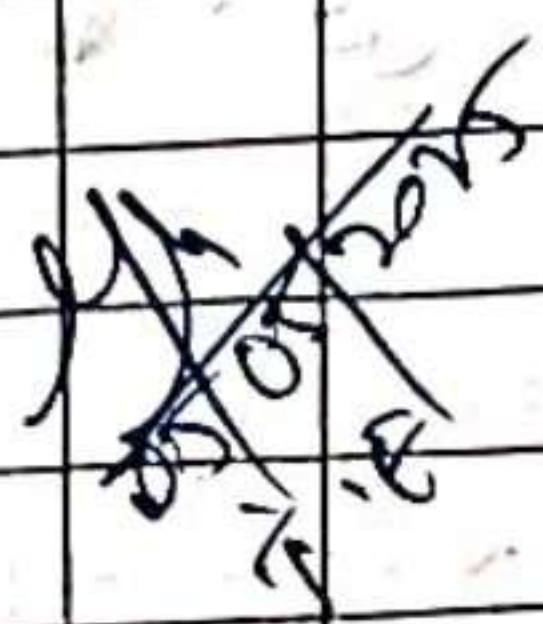
B.F = 7192670.00

Particulars	Details of actual measurement				Contents of area
	No.	L.	B.	D.	
②② Painting two Coat PrimoCoat.					
QVTMB, P-24 ②② = 100.80/m ²					
@ Rs - 129 = 46/m ²					Rs - 13050200
					Rs = 7205720:00
Add 1% labourers					(+) Rs = 7205720:00
Add 18% GST					(+) Rs = 129702920:
Add Seniorage fee					(+) Rs = 61918:00
					Rs = 8636724:00
Less 0.05% below					(-) Rs = 4318200
					Rs = 8632406:00

Less Previous Payment
by Page NO-②② Rs (-) = 7751000:00

Less Previous Payment
by Page NO-②③ Rs (-) = 783908:00

Rs = 97498:00

 05/05/2025
 05/05/2025
 05/05/2025 (T.S.)
