

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, खगड़िया

पत्रांक.....737..... खगड़िया

दिनांक :- 28 / 5 / 25

प्रेषक,

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, खगड़िया

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव,
बिहार ग्रामीण पथ विकास अभिकरण (ब्राडा), पटना।

विषय :- New MR (New Maintenance Policy 2018) अंतर्गत पथ में निर्माण कार्यों का आवंटन उपलब्ध कराने के संबंध में।

महाशय,


उपर्युक्त विषय के संबंध में कहना है कि **New MR (New Maintenance Policy 2018)** अंतर्गत पथ में निर्माण कार्यों के भुगतान हेतु संलग्न विवरणी के अनुसार **रु०-0.64154 लाख** राशि की आवश्यकता है।

अतः अनुरोध है कि उक्त राशि का आवंटन उपलब्ध कराया जाए, ताकि संवेदक को भुगतान किया जा सके।

सूचनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित।

अनु०-यथोक्त।

विश्वासभाजन



कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, खगड़िया



Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road maintenance Policy 2018 (Initial Rectification and Surface Renewal)

Month-May 2025

Division : Khagaria

Package no.	Name of Block	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in percentage	Previous Total Alloted Amount (Lac)	up to date expenditure as per MIS (in Lac)	Requisition Against work done (In lac)	Remarks
					Length (In Km)	Amount (in Lac)	Initial Rectification with Surface Renewal (in lac)	5 years Routine Maintenance (in lac)										
RM/KH/KHA/24/0002	Khagaria	L071-TO2 MATHURA PUR TO KAMALPUR (TRACK27)	20904502078	Lt-6120, Dt-04/12/2023	1.600	102.69	86.4512	7.8425	25MBD/2023-24 Dt-15/03/2024	14/12/2024	24/07/2024	3593	25 mm	5%	85.200	85.200	0.64154	Completed
																	Total	0.64154

Handwritten signature

Executive Engineer
RWD Works Division, Khagaria

Handwritten signature

FORM GFR 19A

(See Government of India's Decision (1) below Rule-150)

Form of Utilization Certificate up to the month- May 2025

New MR (New Maintenance Policy 2018)

S. No.	Name of Scheme	Sanction No & Date with Amount (in Lacs Rs.)	Amount Received (in Lacs Rs.)	Particulars
1	Construction of Rural Roads under New MR (New Maintenance Policy 2018)	-----	289.71249 (Through CFMS)	Certified that Rs. 289.71249 Lacs which was received during the year 2024-25 in favor of E.E., R. W.D(W), Division Khagaria Bihar & a sum of Rs. 289.65723 lacs has been utilized for the purpose of New MR (New Maintenance Policy 2018) schemes as given in the margin for which it was sanctioned and that the balance of Rs 0.05526 Lacs remaining unutilized at the end of the period under.

2. certified that I have satisfied myself that the conditions on which the grants-in-aid was sanctioned have been duly fulfilled and that I have exercised the following checks to see that the money was actually utilized for the propose for which it was sanctioned.

Kind of checks exercised-

- Works have been supervised by Executive Engineer/Superintending Engineer.
- Periodical inspection has been conducted by Executive Engineer/Superintending Engineer
- Construction material have been tested.
- Measurements have been recorded in the MBs and test check conducted by the Assistant.
- All other codal formalities have been observed

3. Physical Progress achieved:

- construction of Road Works
- Construction of CD Works

Executive Engineer

RWD (W) Div, Khagaria

28/5/25
Sd/-

Deviation Report

Name of work :- Construction of repair road from L071-T02 Mathorapur to Kamalpur

Agency Name :- Kishore Kumar Singh

Agreement no :- 25 MBD/2024

Date of start :- 15-03-2024


Date of Complition :- 14-12-2024

Actual date of completion :- 24-07-2024


Construction cost as per BOQ- 86,45,983=00

Sl. No.	Item Name	Agreement Qty.	Actual Qty. as per site Construction	Varitation Qty.	Percentage (%)	Varitation Amount
1	Panel Cement Concrete Pavement Construction of Unrainforced- do- do all Complete Job	591.80	597.655	5.855	1.00%	53916.00
				GST	@18%	9705.00
				L-Cess	@1%	539.00
				Less 0.01% Bellow (-)		64,160.00
						6.00
						Rs. 64,154.00

लिक पथ को जोड़ने के कारण PCC के Qty में बढ़ोतरी हुई है। यह लिक पथ मुख्य सड़क को जोड़ती थी, जिसकी स्थिति खराब एवं जर्जर थी, जिससे कुछ बड़ी आबादी को आवागमन से सुविधा मिल सके। जो जनहीत को देखते हुए अतिआवश्यक था।


24/7/2024
कनीय अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रशाखा, खगड़िया।


सहायक अभियंता,
ग्रामीण कार्य विभाग,
कार्य अवर प्रमंडल, खगड़िया।


कार्यप्रमुख अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, खगड़िया।

Name of Road - L071-T02 MATHURAPUR TO KAMALPUR (TRACK27)

Batch Name - RM/KH/KHA/24/0002											
Name of Contractor -Kishor Kumar Singh											
Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
21/4/24	13:12:0	64	0.1	350	0	3500	3520	G	25.517007	86.459073	Normal
21/4/24	13:12:32	64	0.1	310	10.1	3100	3161	G	25.51672	86.459998	Normal
21/4/24	13:13:7	64	0.1	390	10.1	3900	3880	G	25.516385	86.46069	Normal
21/4/24	13:14:0	64	0.1	390	10.1	3900	3880	G	25.515528	86.460572	Normal
21/4/24	13:15:28	64	0.1	370	10.1	3700	3700	G	25.514915	86.4601	Normal
21/4/24	13:16:3	64	0.1	380	20.2	3800	3790	G	25.51403	86.46002	Normal
21/4/24	13:16:39	64	0.1	310	20.2	3100	3161	G	25.513375	86.460252	Normal
21/4/24	13:17:14	64	0.1	350	20.2	3500	3520	G	25.513318	86.461312	Normal
21/4/24	13:17:49	64	0.1	360	20.2	3600	3610	G	25.513023	86.462172	Normal
21/4/24	13:21:0	64	0.1	370	20.2	3700	3700	G	25.512882	86.463013	Normal
21/4/24	13:21:56	64	0.1	350	20.2	3500	3520	G	25.513093	86.463652	Normal
21/4/24	13:22:0	64	0.1	350	20.2	3500	3520	G	25.51269	86.462999	Normal
21/4/24	13:22:56	64	0.1	380	10.1	3800	3790	G	25.512714	86.462998	Normal
21/4/24	13:23:14	64	0.1	390	20.2	3900	3880	G	25.51279	86.463356	Normal
21/4/24	13:23:56	64	0.1	330	20.2	3300	3341	G	25.512352	86.464132	Normal
21/4/24	13:24:23	64	0.087	350	20.2	3500	3520	G	25.512437	86.463698	Normal
						Total	57493				
						Average	3593.31				

$$Y = 0 * X^2 + 0.898 * X + 377.8$$

$$X = 3500$$

$$Y = 3520$$

(R) RURAL ROAD

Good Average Poor


<4000 4001-5000 >5001

21/4/24

21/4/24

21/4/24

File : E:\BUMP INDICATOR\21041406.Xls, Section No. : 64, Eqn : $Y = 0 * X^2 + 0.898 * X + 377.8$
 Name of Customer : Kishor Kumar Singh, Name of Work/ Road : L071-T02 MATHURAPUR TO KAMALPUR Lab Job

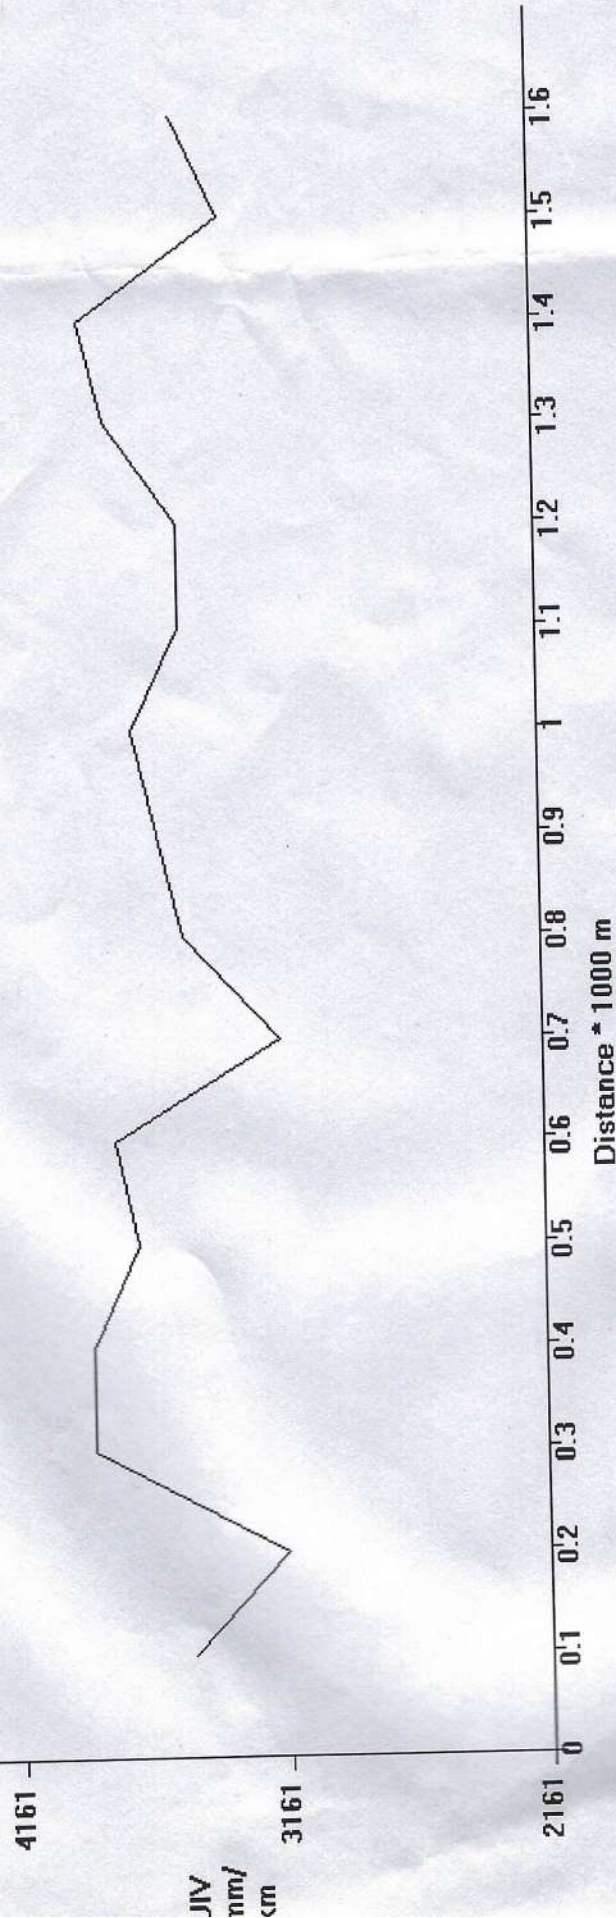

21/4/24
 [Signature]

21/4/24
 [Signature]

21/4/24
 [Signature]
