

कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

पत्रांक 5840 अक

दिनांक : 18/11/25

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी-सह-सचिव
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।

विषय: शीर्ष RRSMP (Gen) अंतर्गत वित्तीय वर्ष 2025-26 में व्यय हेतु आवंटन की मांग।

महाशय,

उपर्युक्त विषय के संबंध में शीर्ष RRSMP (Gen) अंतर्गत वित्तीय वर्ष 2025-26 में व्यय हेतु संलग्न विवरणी के अनुसार 149.65066 (एक करोड़ उनचास लाख पैसठ हजार छेयासठ) रुपये का आवंटन उपलब्ध कराने की कृपा की जाये ताकि किये गये कार्यों का भुगतान किया जा सके।

अनुलग्नक:- यथोक्त

विश्वासभाजन


कार्यपालक अभियंता

ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

18/11/25
19/11/25

GFR 12-B
[See Rule 256 (2)]

FORM OF UTILIZATION CERTIFICATE

(1) Certified that out of the Loan of Rs. Nil, Sanctioned under RRSMP (GEN), dated....., in favour of **Executive Engineer, RWD Works Division Muzaffarpur East-1** during the year 2025-26, an amount of Rs. Nil, has been utilized for the purpose for which it was sanctioned, and that the balance of Rs. Nil, remaining unutilized at the end of the year 2025-26 has been surrendered to the Government (vide No....., dated.....)/ will be adjusted towards the loan payable during the next financial year.

(2) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.

Kinds of checks exercised

- 1.
- 2.
- 3.
- 4.


Sr. D.A.O.
R.W.D. Works Division
Muzaffarpur East-1


Executive Engineer
R.W.D. Works Division
Muzaffarpur East-1

Requisition Format for Scheme RRSMP (General)

The Works Division :- Muzaffarpur East-1

Package No.	Project ID as per MIS	Name of Road	AA Length (in km.)	Administrative Approval (Construction work) Amount (in lakh)	Agreement (Construction work) Amount (in lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WBM / WMM / SBC/PC etc.)	Value of (in m/m/ km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allocated Amount (in lakh)	Upto date Expenditure as per MIS (in lakh)	Value of Work Done (in lakh)	Current Demand (in lakh)	Remarks
1	RRSMP/24-25 Muzaffarpur East-1/04	Mulhapur To Hartha Tak Path	4.750	230.45900	231.91079	01CMBO/ 2025-26 29.04.2025	28.04.2026	—	SDBC	2314.479	25mm	5.02	63.72826	63.72826	102.48160	38.75334	
2	RRSMP/24-25 Muzaffarpur East-1/04	BARGAW MALANG CHOWK (MASJID CHOWK) to BISHUNPUR HARLIAN TOLA	0.750	33.35700	33.27249	01CMBO/ 2025-26 29.04.2025	28.04.2026	29.10.2025	Work Complete	2545.00	—	—	28.94250	28.94250	30.25413	1.31163	
3	RRSMP/24-25 Muzaffarpur East-1/04	LOS2-T02 to madhupur Lakhraj (VR16)	1.150	54.23500	54.44272	01CMBO/ 2025-26 29.04.2025	28.04.2026	30.10.2025	Work Complete	2201.667	25mm	5.02	17.47795	17.47795	38.54114	21.06319	
4	RRSMP/24-25 Muzaffarpur East-1/04	LOS7-Rawara Devan Road Sundarpur Ratwara Harjan tola (VR24)	1.200	54.83700	55.13673	01CMBO/ 2025-26 29.04.2025	28.04.2026	12.11.2025	Work Complete	2129.00	25mm	5.02	14.21956	14.21956	35.76784	21.54828	
5	RRSMP/24-25 Muzaffarpur East-1/04	LOS4-T02 to Muzaffarpur labraj (VR18)	1.430	70.20100	70.51674	01CMBO/ 2025-26 29.04.2025	28.04.2026	09.11.2025	Work Complete	2104.667	25mm	5.02	9.61490	9.61490	46.81599	37.20109	
6	RRSMP/24-25 Muzaffarpur East-1/04	RATWARA HANJUMAN CHOWK to MEGH RATWARA	1.550	74.36900	74.66598	01CMBO/ 2025-26 29.04.2025	28.04.2026	12.11.2025	Work Complete	2070.125	25mm	5.02	20.62161	20.62161	50.39474	29.77313	
		Total														149.65066	

It is certified that Physical & Financial Progress has been updated in MIS.

RRWD, Works Division, Muzaffarpur East-1

Senior-D.A.O./D.A.O.

Executive Engineer

RRWD, Works Division, Muzaffarpur East-1

Note :-

- 1 Above Signed Copy along with Forwarding Letter & Utilisation Certificate must be uploaded in MIS.
- 2 Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed (As Applicable).

17/11/2025

अधियाचना हेतु प्रमाण पत्र

प्रमाणित किया जाता है कि RRSMP (GEN) योजनान्तर्गत:-

1. पथ/मुल्ल Mutlupur To Hattha Tak Path में कराये गये कार्य की गुणवत्ता जाँच की गयी है जो निर्धारित मानक/विशिष्टियों के अनुरूप है।
2. अद्यतन कराये गये कार्य की मापी संबंधित मापी पुस्तिका में दर्ज है जिसका सत्यापन कर लिया गया है।

[Signature]
17/11/25
(56)

कनीय अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रशाखा बंदरा

[Signature]
12/11/25

सहायक अभियंता
ग्रामीण कार्य विभाग
कार्य अवर प्रमंडल बंदरा

[Signature]
18/11/25

कार्यपालक अभियंता
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पूर्वी-1

Name of Contractor:- Abs Infra Solution Prop Babli Singh

Name of Road:- Mutlupur To Hathha Tak Path

Date	Time	Section	Length	Bumps	Speed	OR	CATEGORY	IRI	Latitude	Longitud	Event	
		No.	in km	in mm	Rate	mm/km	UIV	ROAD				
9/11/25	15:27:13	16	0.1	220	0	2200	2162	G	3	26.58487	85.66306	Y = 0 * X ^ 2 + 0.989 * X - 13.58
9/11/25	15:28:0	16	0.1	180	10.1	1800	1766	G	2.51	26.59487	85.66288	Normal
9/11/25	15:28:24	16	0.1	240	10.1	2400	2360	G	3.25	26.6052	85.66281	Culvert
9/11/25	15:29:0	16	0.1	190	10.1	1900	1865	G	2.63	26.61488	85.66276	Normal
9/11/25	15:29:0	16	0.1	220	10.1	2200	2162	G	3	26.62377	85.6631	Normal
9/11/25	15:30:0	16	0.1	210	10.1	2100	2063	G	2.88	26.63397	85.66332	Normal
9/11/25	15:30:10	16	0.1	250	10.1	2500	2458	G	3.37	26.64187	85.66348	Normal
9/11/25	15:30:45	16	0.1	220	10.1	2200	2162	G	3	26.65092	85.66377	Normal
9/11/25	15:31:0	16	0.1	190	10.1	1900	1865	G	2.63	26.6584	85.66436	Normal
9/11/25	15:31:20	16	0.1	230	10.1	2300	2261	G	3.13	26.66472	85.66497	Normal
9/11/25	15:31:30	16	0.1	200	10.1	2000	1964	G	2.76	26.50208	85.66507	Normal
9/11/25	15:32:0	16	0.1	210	10.1	2100	2063	G	2.88	26.67275	85.66551	Normal
9/11/25	15:32:20	16	0.1	220	10.1	2200	2162	G	3	26.67592	85.66594	Normal
9/11/25	15:32:24	16	0.1	230	10.1	2300	2261	G	3.13	26.67892	85.66658	Normal
9/11/25	15:33:0	16	0.1	200	10.1	2000	1964	G	2.76	26.686	85.6669	Normal
9/11/25	15:33:34	16	0.1	180	10.1	1800	1766	G	2.51	26.6944	85.66734	Normal
9/11/25	15:34:0	16	0.1	190	10.1	1900	1865	G	2.63	26.7018	85.66776	Normal
9/11/25	15:34:10	16	0.1	220	10.1	2200	2162	G	3	26.7075	85.6681	Normal
9/11/25	15:34:45	16	0.1	170	20.2	1700	1667	G	2.38	26.7128	85.6684	Normal
9/11/25	15:35:0	16	0.1	220	10.1	2200	2162	G	3	26.72077	85.66879	Normal
9/11/25	15:35:10	16	0.1	240	10.1	2400	2360	G	3.25	26.72427	85.66891	Normal
9/11/25	15:35:20	16	0.1	220	10.1	2200	2162	G	3	26.729	85.66921	Normal
9/11/25	15:35:45	16	0.1	200	10.1	2000	1964	G	2.76	26.73723	85.66961	Normal
9/11/25	15:35:55	16	0.1	200	10.1	2000	1964	G	2.76	26.74057	85.66985	Normal
9/11/25	15:36:0	16	0.1	180	10.1	1800	1766	G	2.51	26.74582	85.67019	Normal
9/11/25	15:36:31	16	0.1	200	10.1	2000	1964	G	2.76	26.7538	85.67076	Normal
9/11/25	15:36:41	16	0.1	240	10.1	2400	2360	G	3.25	26.7553	85.67111	Normal
9/11/25	15:37:6	16	0.1	210	10.1	2100	2063	G	2.88	26.7605	85.67135	Normal
9/11/25	15:37:6	16	0.1	220	10.1	2200	2162	G	3	26.7683	85.67187	Normal
9/11/25	15:38:0	16	0.1	200	10.1	2000	1964	G	2.76	26.77675	85.67247	Normal

Speed Breaker

Muthupur

Babli Singh


Date	Time	Section	Length	Bumps	Speed	OR		CATEGO RY	IRI	Latitude	Longitud e	Event		
9/11/25	15:38:16	16	0.1	240	10.1	2400	2360	G	3.25	26.78442	85.67298	Normal		
9/11/25	15:38:26	16	0.1	200	10.1	2000	1964	G	2.76	26.79092	85.67316	Normal		
9/11/25	15:38:52	16	0.1	200	10.1	2000	1964	G	2.76	26.7938	85.67328	Normal		
9/11/25	15:39:0	16	0.1	180	10.1	1800	1766	G	2.51	26.8025	85.67359	Culvert		
9/11/25	15:39:27	16	0.1	200	10.1	2000	1964	G	2.76	26.81198	85.67386	Normal		
9/11/25	15:40:2	16	0.1	240	10.1	2400	2360	G	3.25	26.8206	85.67434	Normal		
9/11/25	15:40:2	16	0.1	260	10.1	2600	2557	G	3.49	26.8258	85.67502	Normal		
9/11/25	15:41:0	16	0.1	240	10.1	2400	2360	G	3.25	26.83343	85.67549	Normal		
9/11/25	15:41:13	16	0.1	250	10.1	2500	2458	G	3.37	26.84238	85.67593	Normal		
9/11/25	15:41:23	16	0.1	220	10.1	2200	2162	G	3	26.84648	85.67612	Normal		
9/11/25	15:41:48	16	0.1	230	10.1	2300	2261	G	3.13	26.85065	85.67648	Normal		
9/11/25	15:42:0	16	0.1	250	10.1	2500	2458	G	3.37	26.85832	85.67715	Speed Breaker		
9/11/25	15:42:23	16	0.1	220	10.1	2200	2162	G	3	26.86532	85.67791	Normal		
9/11/25	15:43:0	16	0.1	200	10.1	2000	1964	G	2.76	26.87188	85.67872	Normal		
9/11/25	15:43:34	16	0.1	220	10.1	2200	2162	G	3	26.8774	85.67963	Normal		
9/11/25	15:44:0	16	0.1	200	10.1	2000	1964	G	2.76	26.88352	85.68025	Normal		
9/11/25	15:44:10	16	0.1	240	10.1	2400	2360	G	3.25	26.88702	85.68057	Normal		
9/11/25	15:44:59	16	0.05	120	10.1	2400	2360	G	3.25	26.89058	85.68111	Normal		
						Avg: -	2114.479							

Gruber
17/11/25
GE

Chaffin
19/11/25
KE

18/11/25

File : C:\Users\amc\Desktop\ABS INFRA\12\09111547.xls. Section No.: 16. Eqn : $Y = 0 \cdot X^2 + 0.989 \cdot X - 13.58$
 Name of Customer : Name of Work/ Road : Lab Job number :

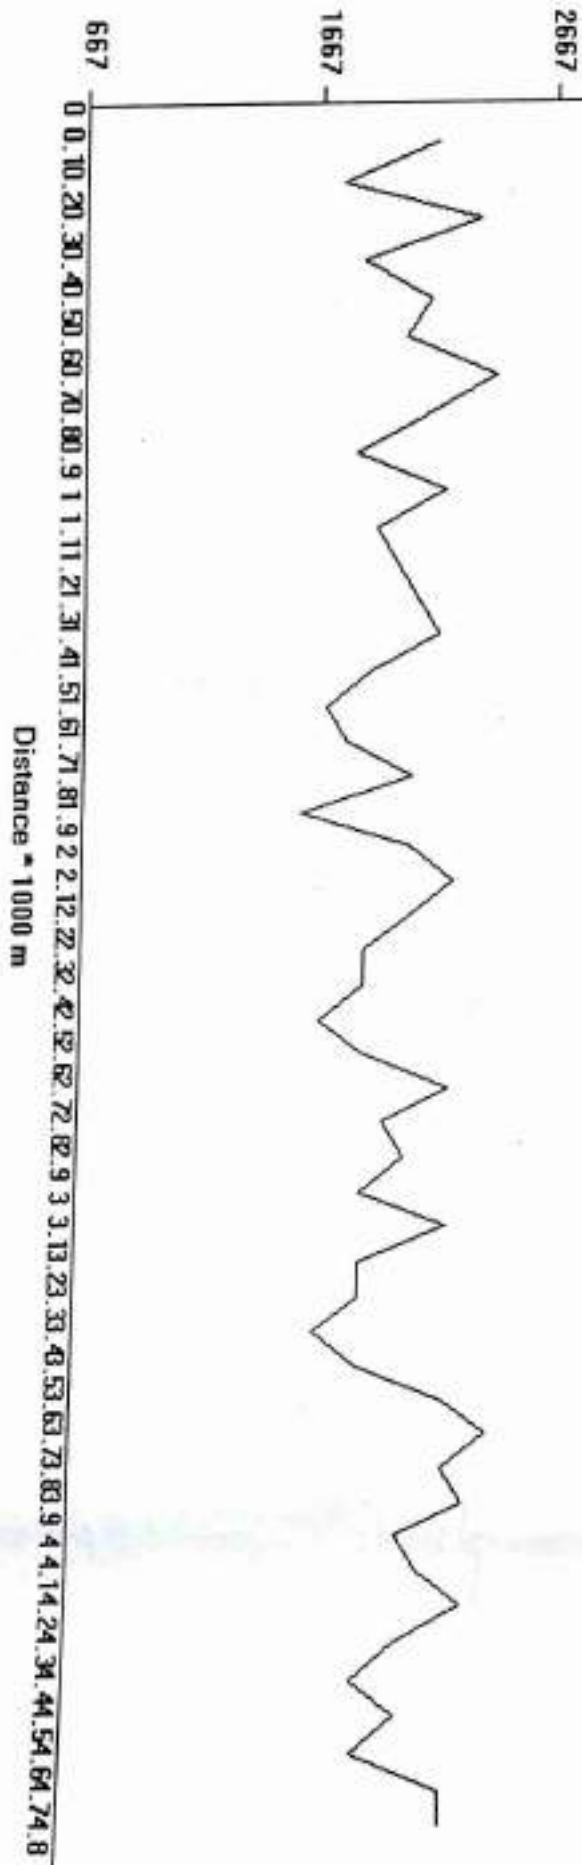

Chakher
17/11/15
56

Chaitan
17/11/15
A2

Yash
17/11/15
135
